

■ Remaining Level of Effort
 Actual Work
 Actual Level of Effort
 Remaining Work
 ◆ ◆

C8 - 3 MONTH ROLLING PROGRAMME, 01 DEC-16 UPDATE


Date	Revision	Checked	Appro...
01-Dec-16	Working Programme with RAB3 Baseline	SGJ	

Activity ID	Activity Name	2016										2017														
		November					December					January					February					March				
		31	07	14	21	28	05	12	19	26	02	09	16	23	30	06	13	20	27	06	13	20	27			
Roof Slab																										
North Structure																										
RAB-22-0270	022 - Construct R/F Suspended Slab at +11.00mPD Bay 1 (240m²) (Approx 3																									
RAB-22-0300	022 - Construct R/F Suspended Slab at +11.00mPD Bay 2 (240m²) (Approx 3																									
Cure and Strip																										
RAB-22-0250	022 - Cure and Strip False/Formwork - 1/F N																									
Middle Structure																										
RAB-22-0340	022 - Construct R/F Suspended Slab at +11.00mPD Bay 1 (240m²) (Approx 3																									
Cure and Strip																										
South Structure																										
RAB-22-0430	022 - Construct R/F Suspended Slab at +11.00mPD Bay 1 (240m²) (Approx 3																									
RAB-22-0580	022 - Construct R/F Suspended Slab at +11.00mPD Bay 2 (240m²) (Approx 3																									
Cure and Strip																										
RAB-22-0510	022 - Cure and Strip False/Formwork																									
ABWF/E&M																										
Internal Finishes																										
North																										
Middle																										
South																										
Specialist Installations																										
RAB-22-0990	022 - Kennels Installation (42No) South																									
RAB-22-1050	022 - Install HR and SPR Glass Reinforced Polyester Water Tanks (G/F Nor																									
Window Wall																										
RAB-22-7090	022 - Install Window Wall Cast In Items (North)																									
RAB-22-7130	022 - Install Window Wall Cast In Items (South)																									
East																										
West																										
Dog Swimming Pool																										
RAB-22-0160	022 - Setting out of Dog Swimming Pool																									
RAB-22-0170	022 - Excavate for Dog Swimming Pool																									
RAB-22-0200	022 - RC Structure																									
RAB-22-0220	022 - Construct Staircase																									
Utilities and Drainage																										
North																										
Middle																										
South																										
Testing & Commissioning																										
Statutory Submissions & Approvals (Day 670 Completion)																										
Water Supplies Department (WSD)																										
Commencement																										
RAB-WSD-794	022 - Submit WWO 46 Pt. I & II																									
RAB-WSD-814	022 - WSD Issue WWO 46 Pt. III																									
Completion																										
Fire Services Water (FS)																										
Commencement																										
RAB-WSD-824	022 - Submit WWO 46 Pt. I & II																									
RAB-WSD-844	022 - WSD Issue WWO 46 Pt. III																									

■ Remaining Level of Effort ■ Actual Work ■
■ Actual Level of Effort ■ Remaining Work ◆ ◆

C8 - 3 MONTH ROLLING PROGRAMME, 01 DEC-16 UPDATE

Date	Revision	Checked	Appro...
01-Dec-16	Working Programme with RAB3 Baseline	SGJ	

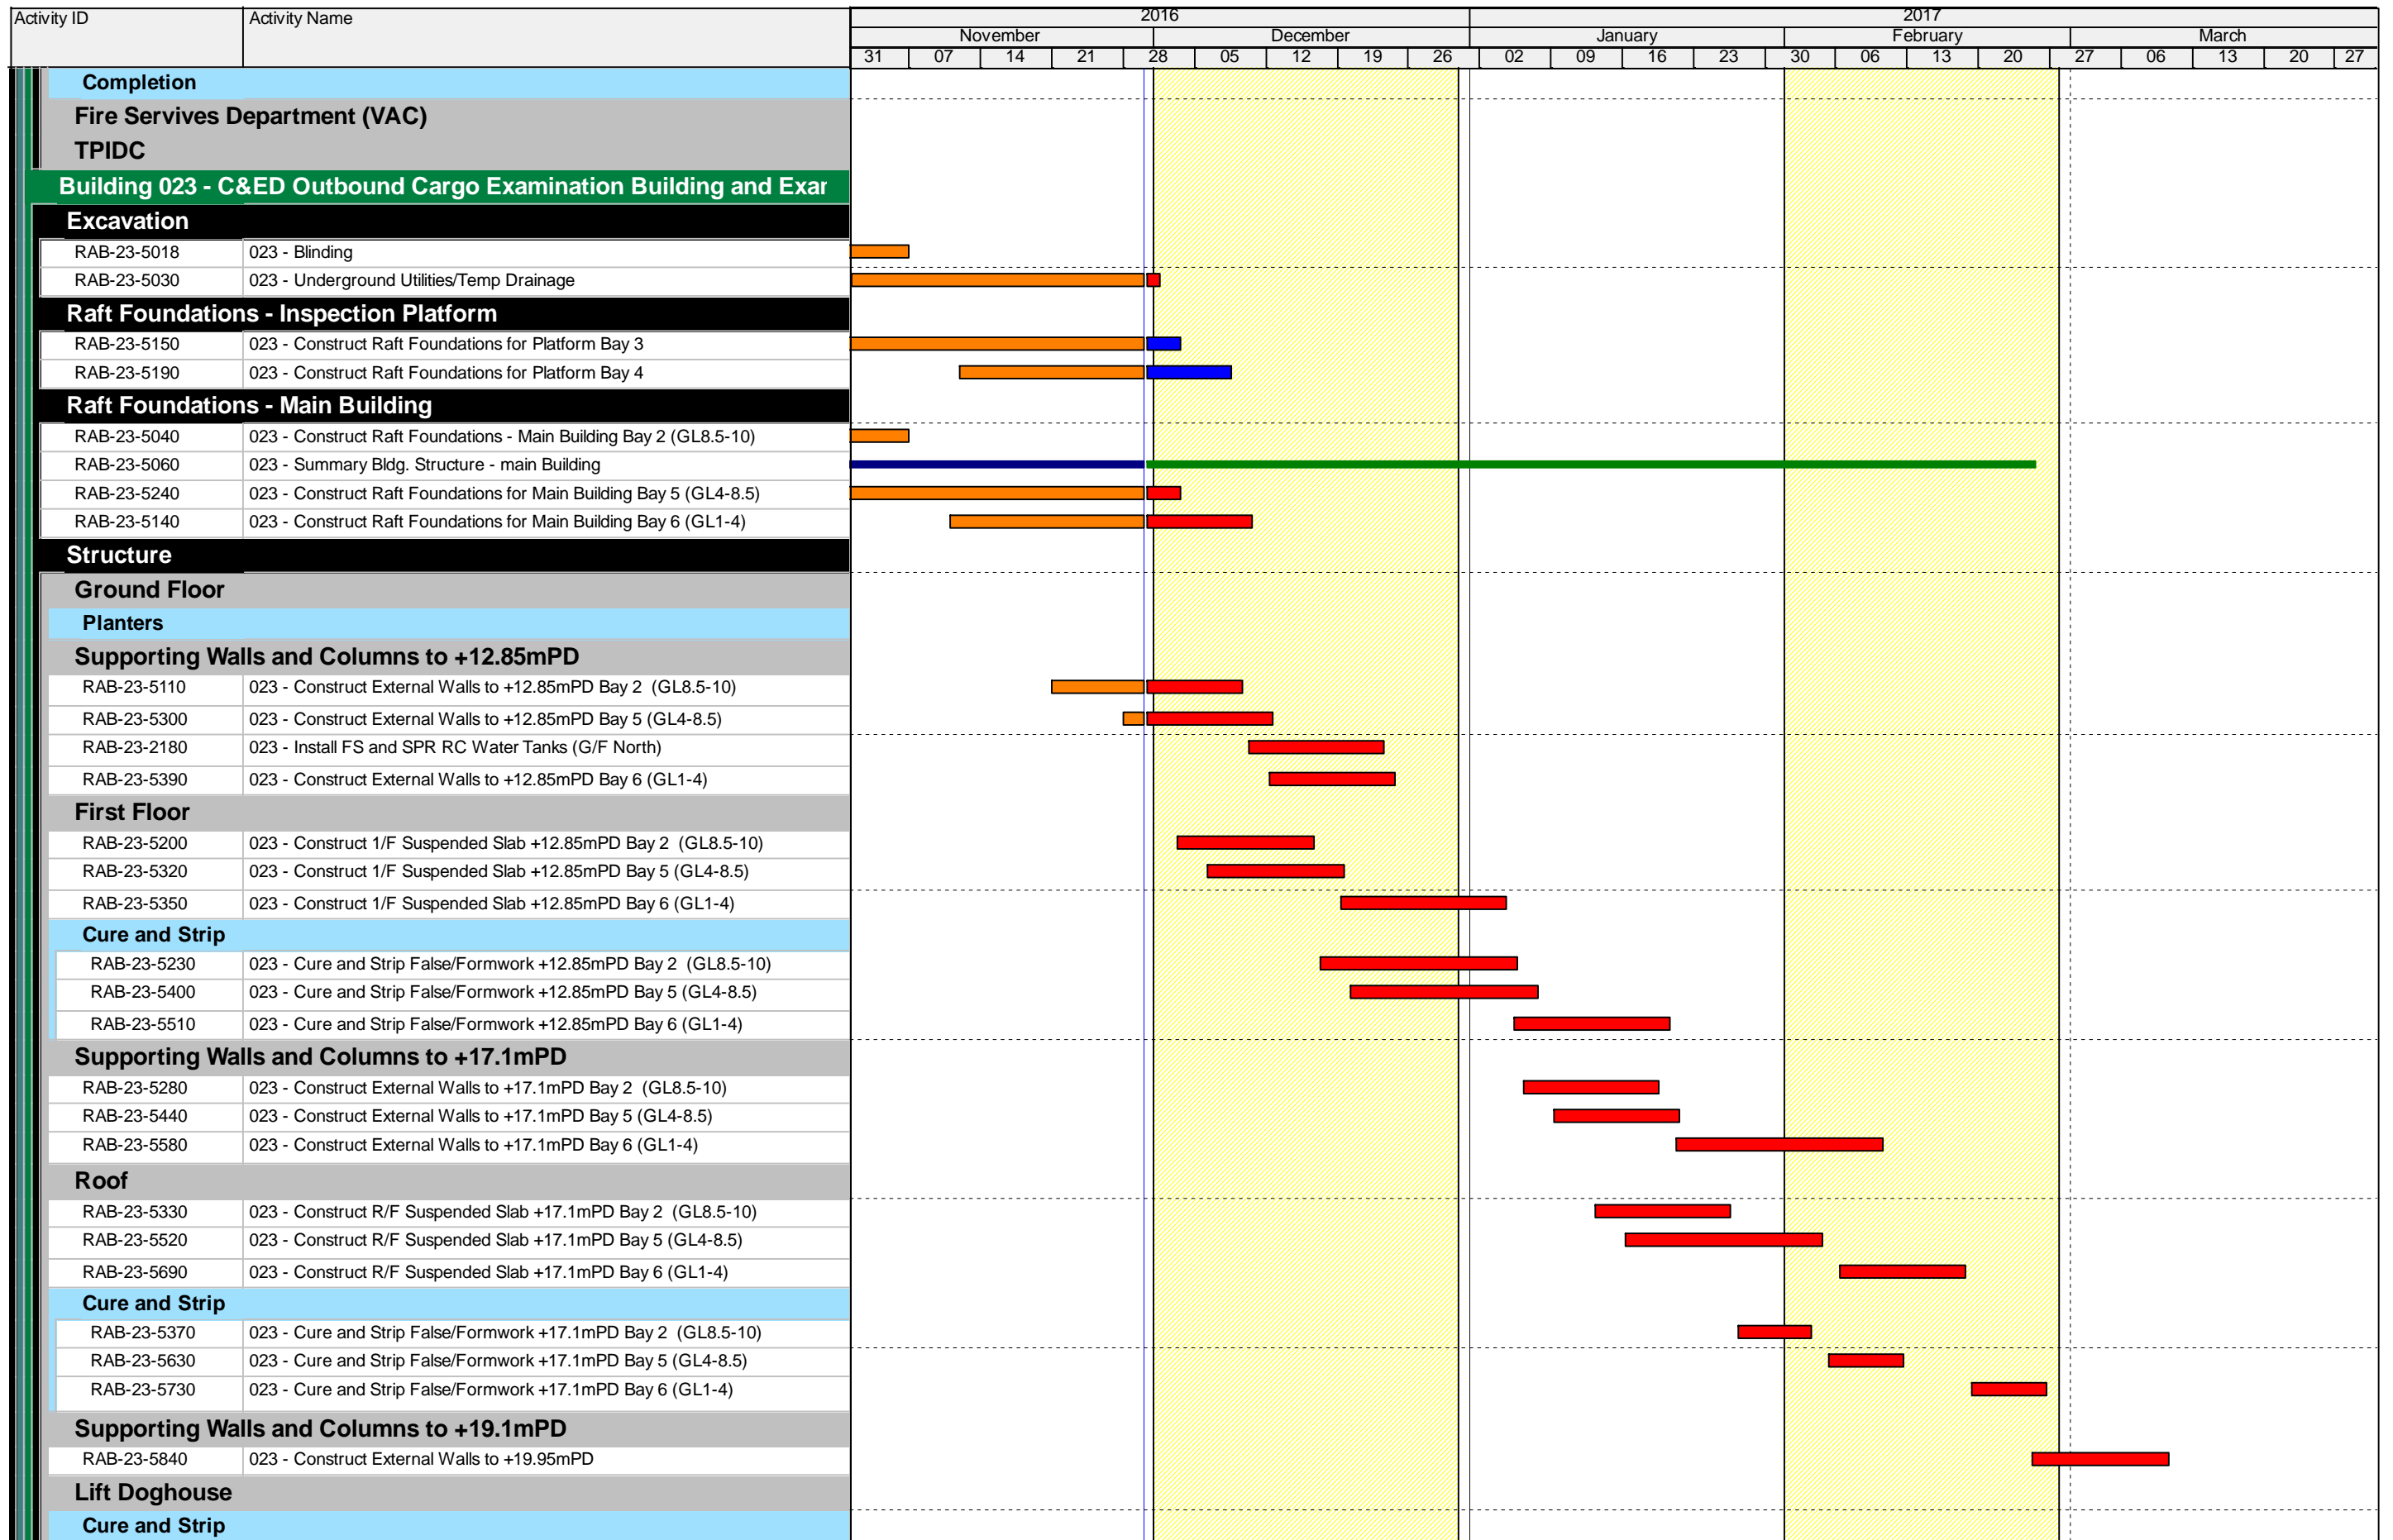

■ Remaining Level of Effort
■ Actual Work
■
■ Actual Level of Effort
■ Remaining Work
◆
◆

C8 - 3 MONTH ROLLING PROGRAMME, 01 DEC-16 UPDATE


Date	Revision	Checked	Appro...
01-Dec-16	Working Programme with RAB3 Baseline	SGJ	

Activity ID	Activity Name	2016										2017														
		November					December					January					February					March				
		31	07	14	21	28	05	12	19	26	02	09	16	23	30	06	13	20	27	06	13	20	27			
ABWF/E&M																										
North																										
Internal Finishes																										
Ground Floor																										
Building 023																										
RAB-23-5420	023 - Construct Blockwork Walls to G/F North (932m³), North																									
RAB-23-5660	023 - SUMMARY ABWF & MEP KD3A, N&S																									
RAB-23-5450	023 - ABWF and MEP works to Degree 1 for others (KD3A) G/F, North																									
RAB-23-5600	023 - ABWF and MEP works to Degree 2 for others (KD3B) G/F, North																									
RAB-23-5760	023 - SUMMARY ABWF & MEP KD3B, N&S																									
First Floor																										
Building 023																										
RAB-23-5540	023 - Construct Blockwork Walls to F/F North (932m³), North																									
RAB-23-5640	023 - ABWF and MEP works to Degree 1 for others (KD3A) 1/F, North																									
Interface Section for KD3E & KD3E																										
External Finishes																										
Roof Finishes																										
Green Roof																										
South																										
Internal Finishes																										
Ground Floor																										
Building 023																										
RAB-23-5570	023 - Construct Blockwork Walls to G/F South (932m³) - S																									
RAB-23-5670	023 - ABWF and MEP works to Degree 1 for others (KD3A) G/F - S																									
Interface Areas																										
First Floor																										
Building 023																										
RAB-23-5770	023 - Construct Blockwork Walls to F/F South (932m³) - S																									
Interface Areas																										
External Finishes																										
Facade																										
RAB-23-5680	023 - Erect Scaffolding around Building - S																									
RAB-23-5700	023 - Install External Louvers /Windows/Doors - S																									
At Grade																										
Window Wall																										
RAB-23-7140	023 - Install Window Wall Cast In Items in 1/F Slab - S																									
RAB-23-7100	023 - Install Window Wall Cast In Items in Base Slab - S																									
East																										
West																										
Roof Finishes																										
RAB-23-5710	023 - Leveling screed - (753m²) - S																									
Roof Level Dog House																										
Building 023																										
Specialist Installations																										
Metal Canopy																										
RAB-23-6170	023 - Install Steel Support Columns (30 No)																									

- Remaining Level of Effort
- Actual Level of Effort
- Actual Work
- Remaining Work

C8 - 3 MONTH ROLLING PROGRAMME, 01 DEC-16 UPDATE


Date	Revision	Checked	Appro...
01-Dec-16	Working Programme with RAB3 Baseline	SGJ	

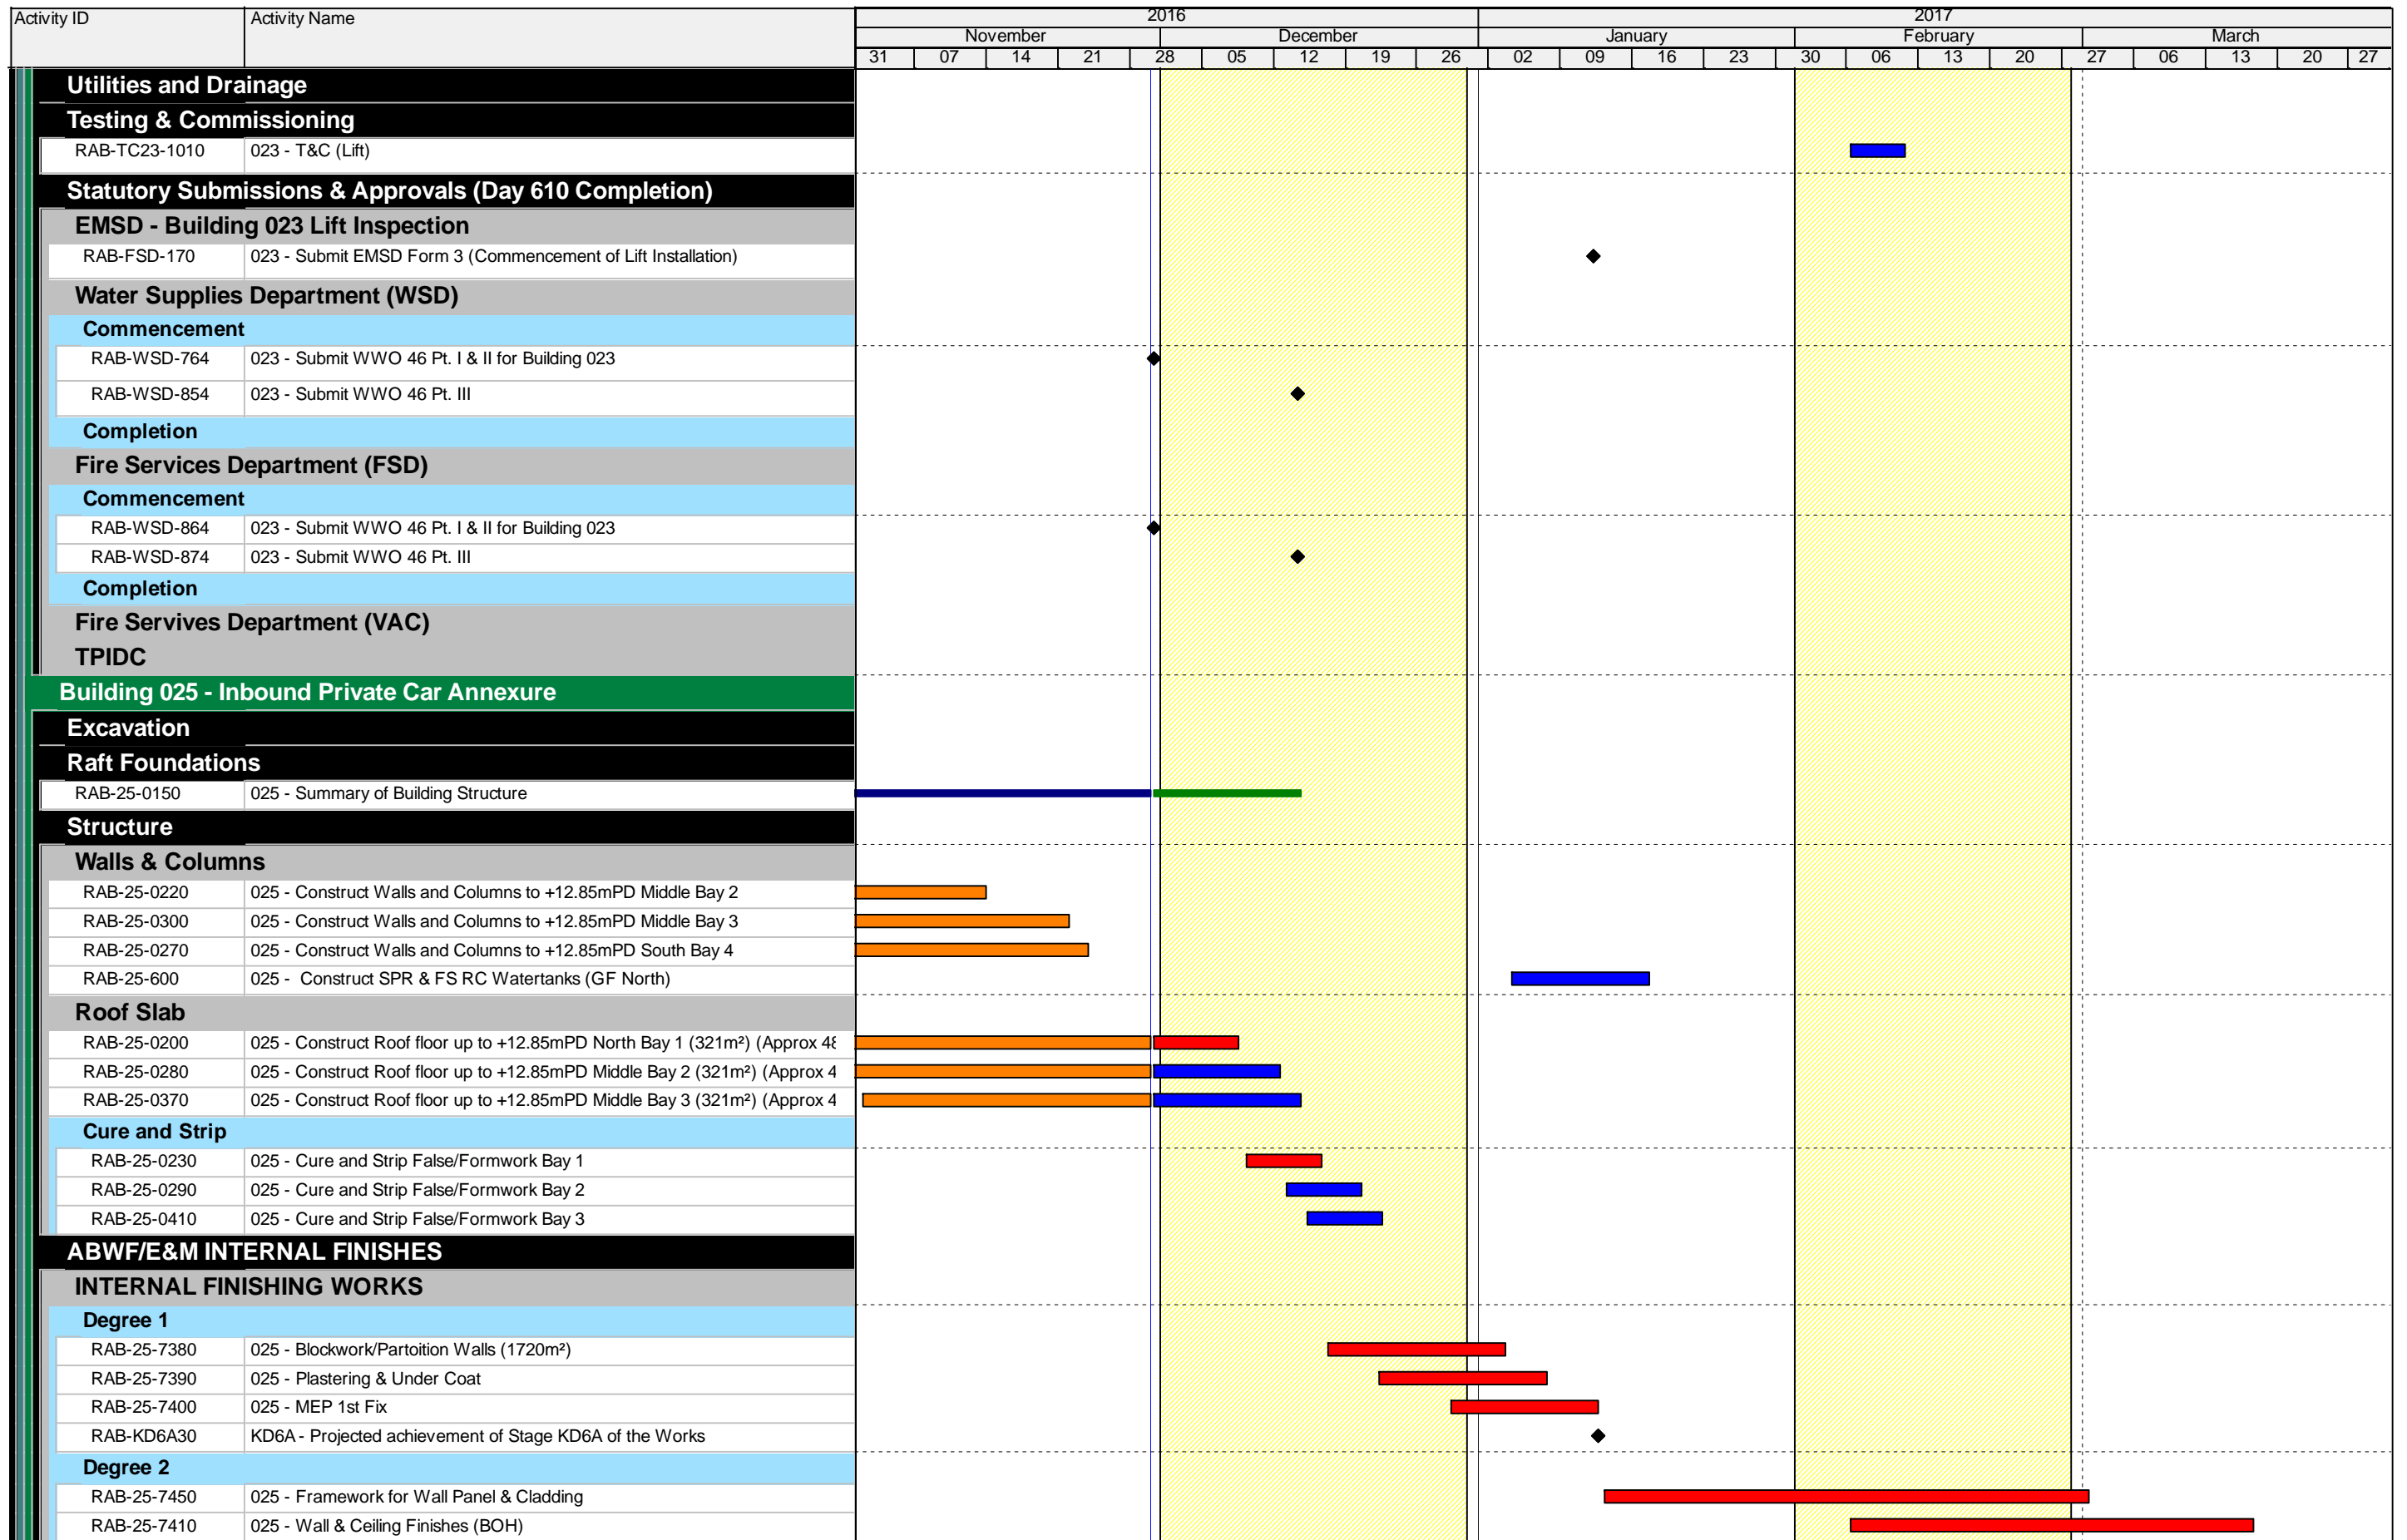

■ Remaining Level of Effort
 ■ Actual Work
 ■
 ■ Actual Level of Effort
 ■ Remaining Work
 ◆ ◆

C8 - 3 MONTH ROLLING PROGRAMME, 01 DEC-16 UPDATE


Date	Revision	Checked	Appro...
01-Dec-16	Working Programme with RAB3 Baseline	SGJ	

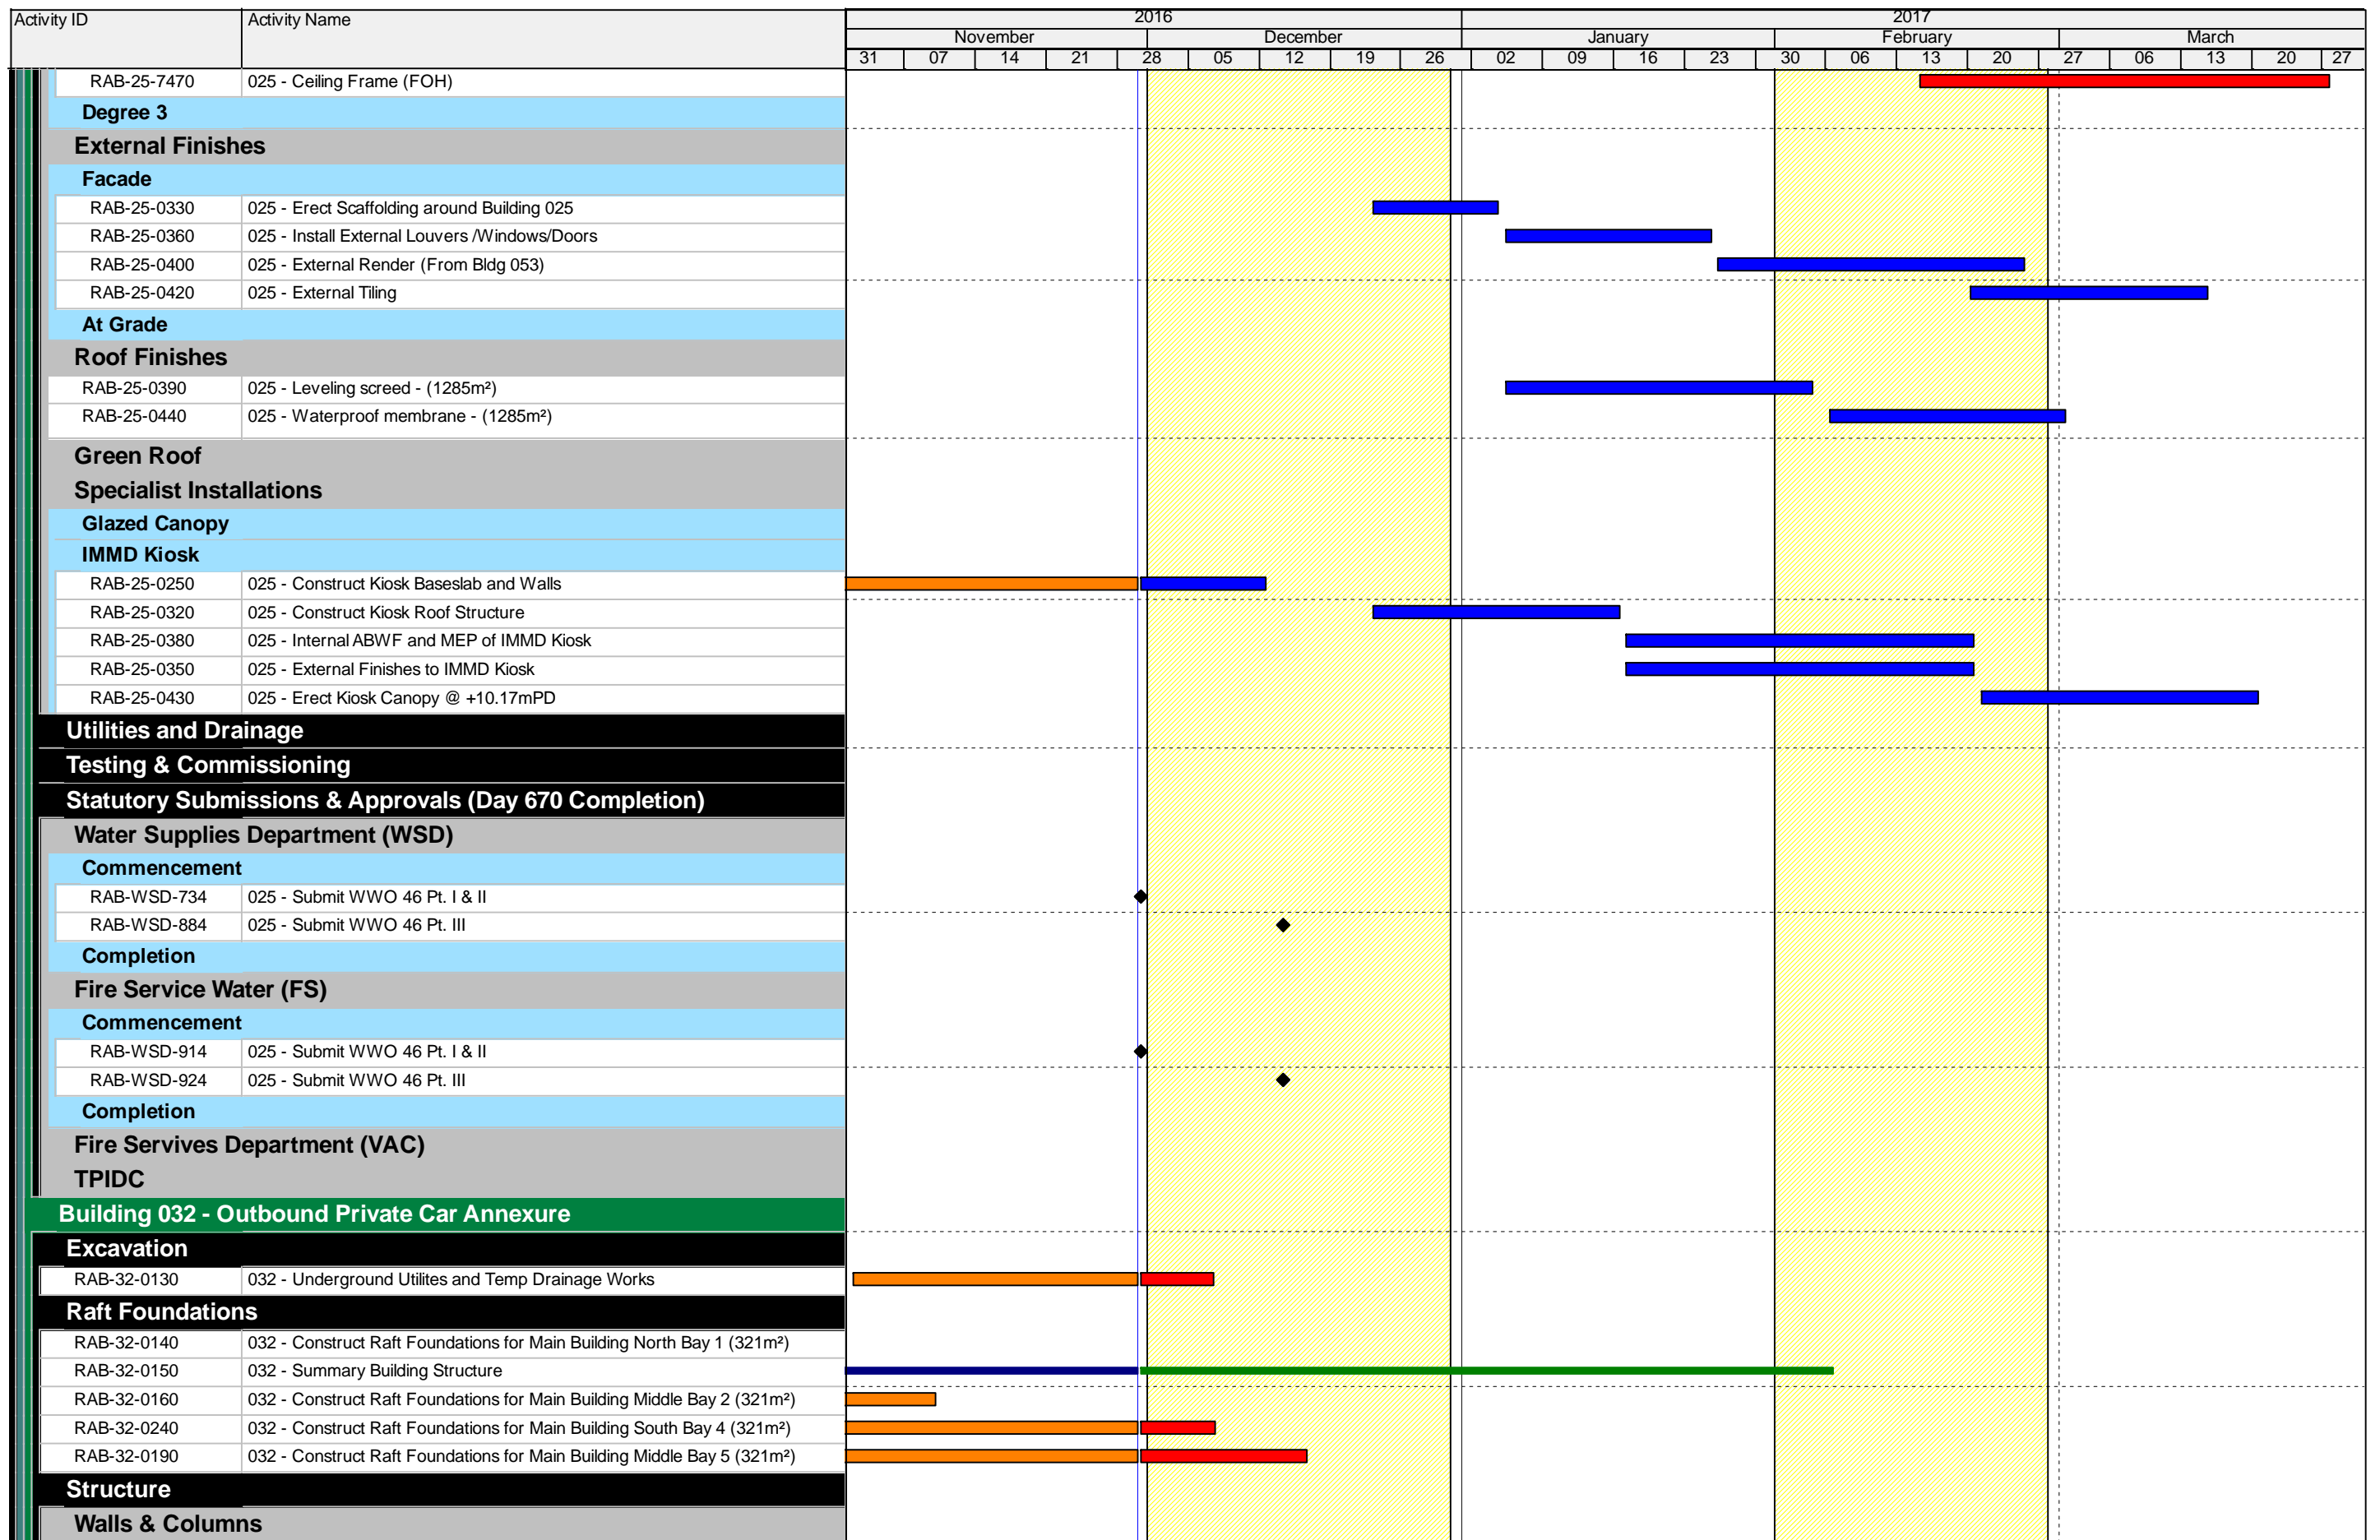

■ Remaining Level of Effort ■ Actual Work ■
■ Actual Level of Effort ■ Remaining Work ◆ ◆

C8 - 3 MONTH ROLLING PROGRAMME, 01 DEC-16 UPDATE


Date	Revision	Checked	Appro...
01-Dec-16	Working Programme with RAB3 Baseline	SGJ	

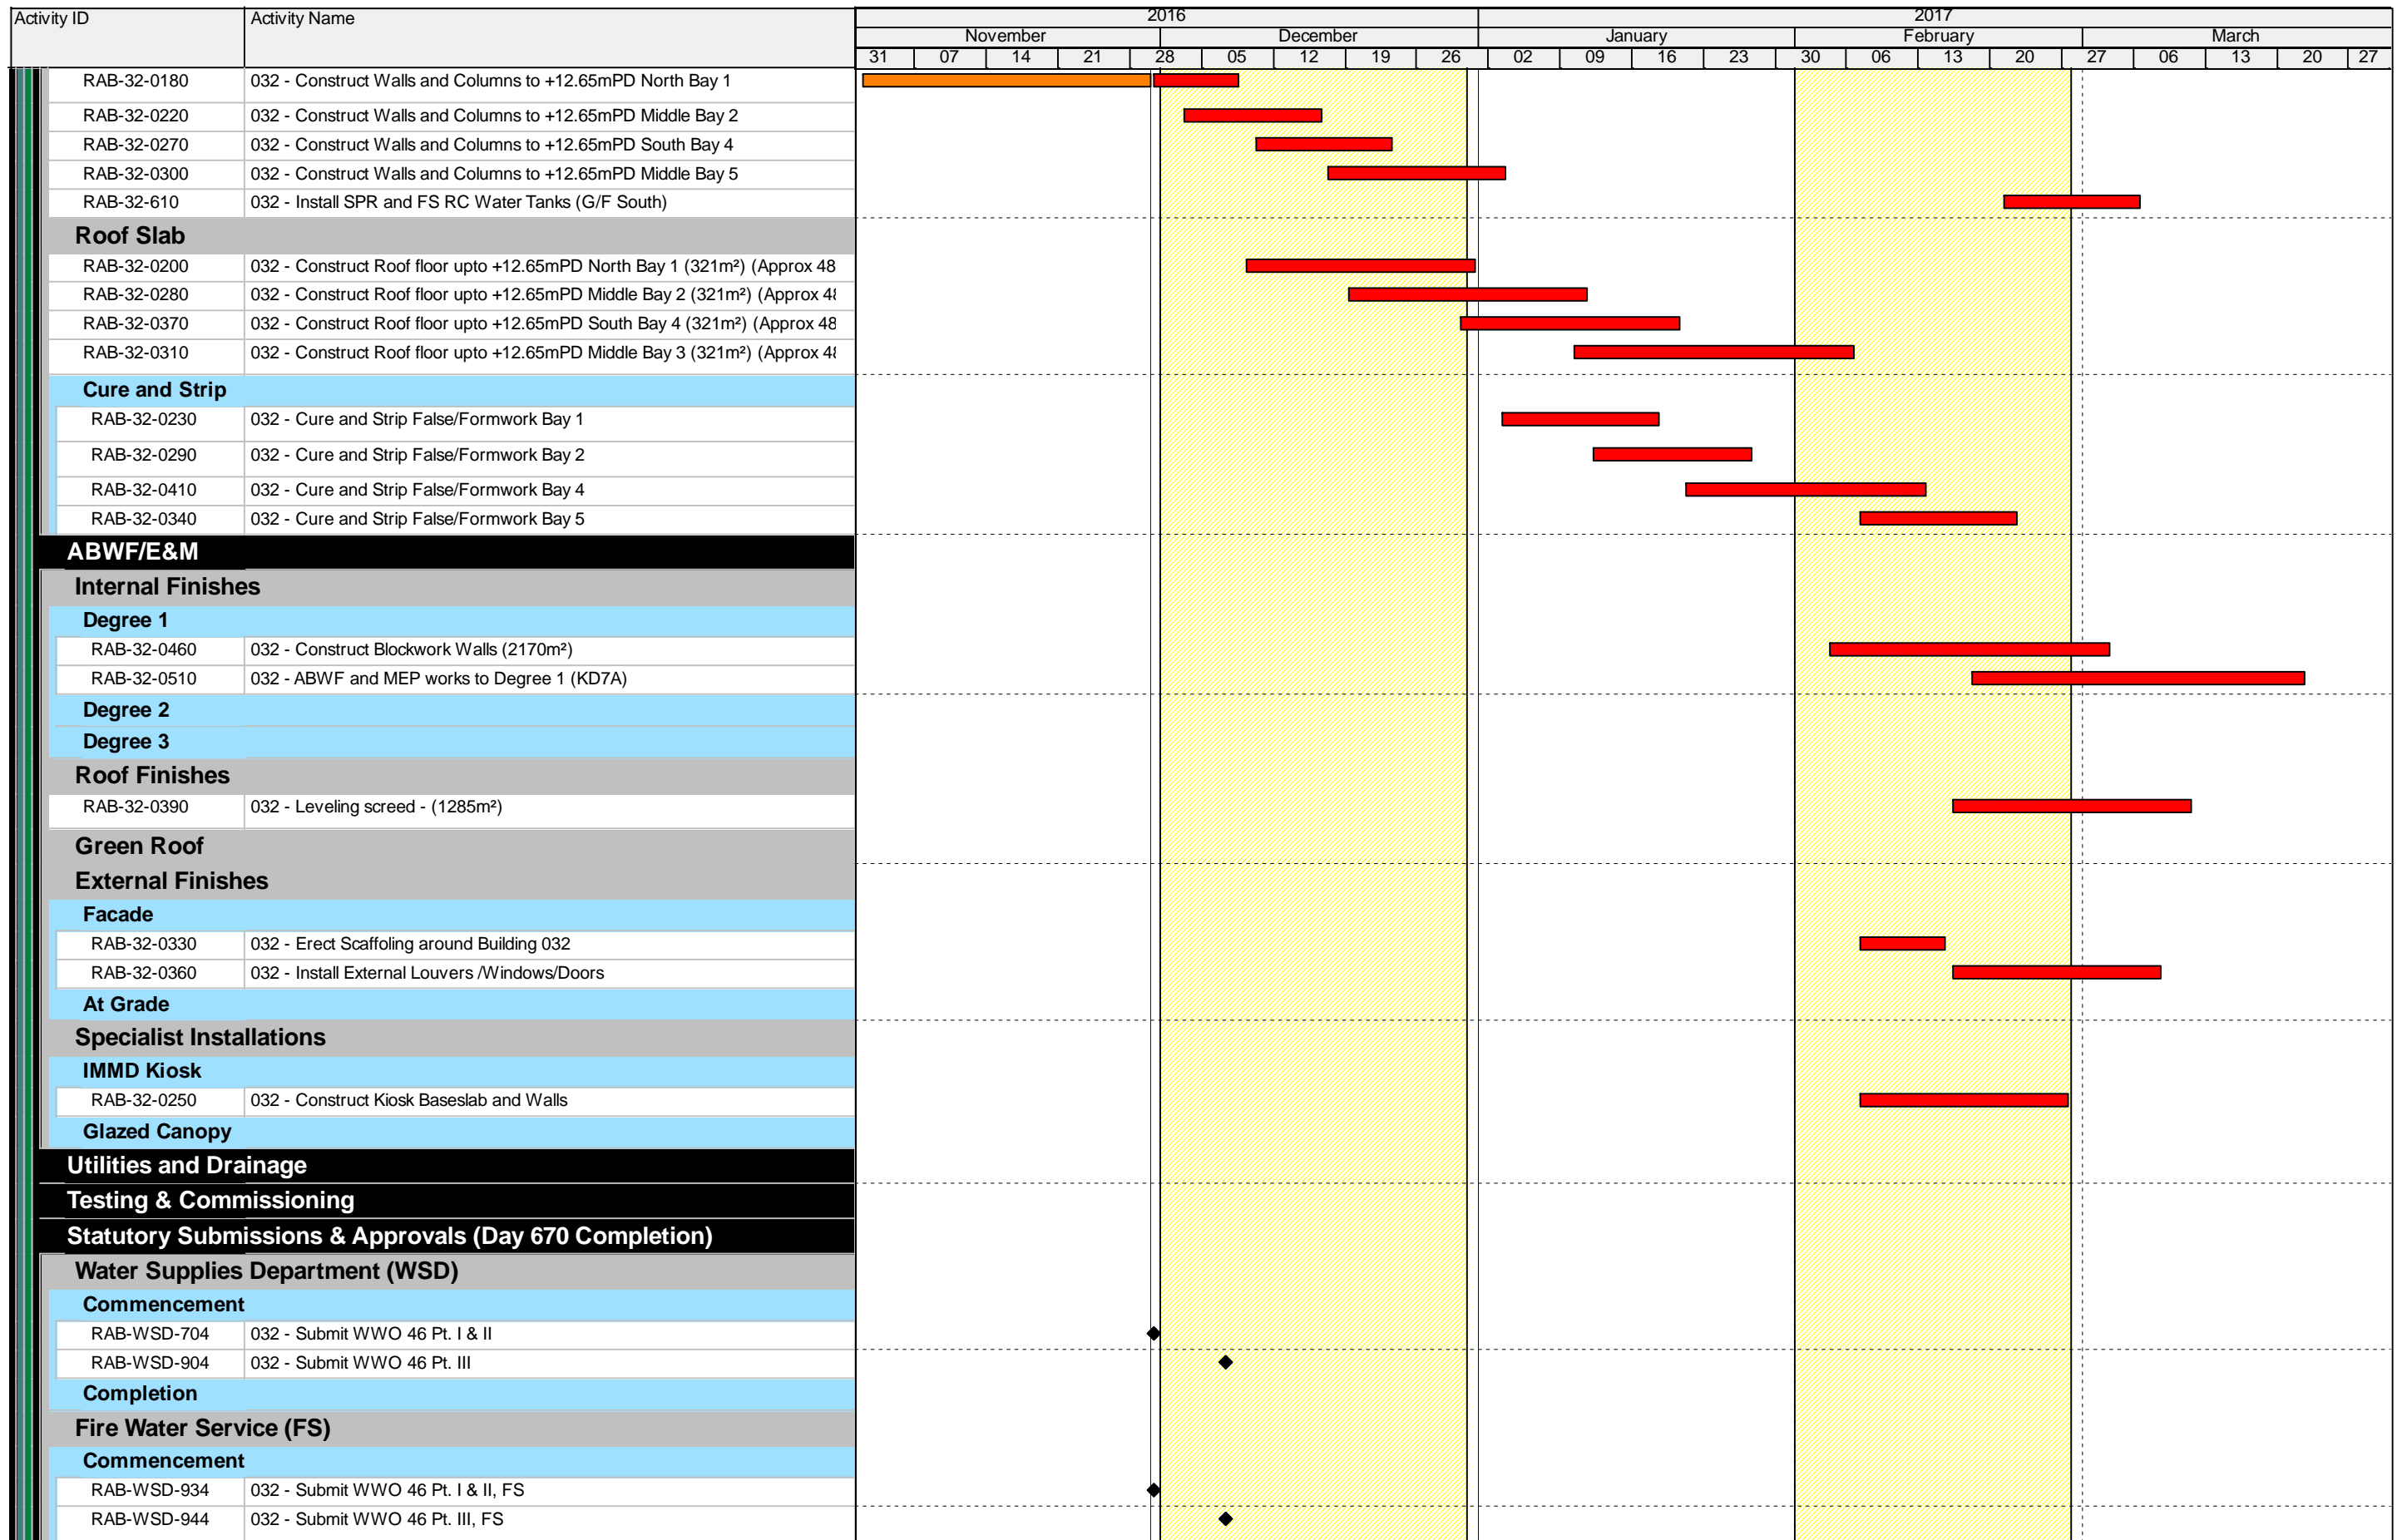

■ Remaining Level of Effort Actual Work
■ Actual Level of Effort Remaining Work ◆ ◆

C8 - 3 MONTH ROLLING PROGRAMME, 01 DEC-16 UPDATE


Date	Revision	Checked	Appro...
01-Dec-16	Working Programme with RAB3 Baseline	SGJ	

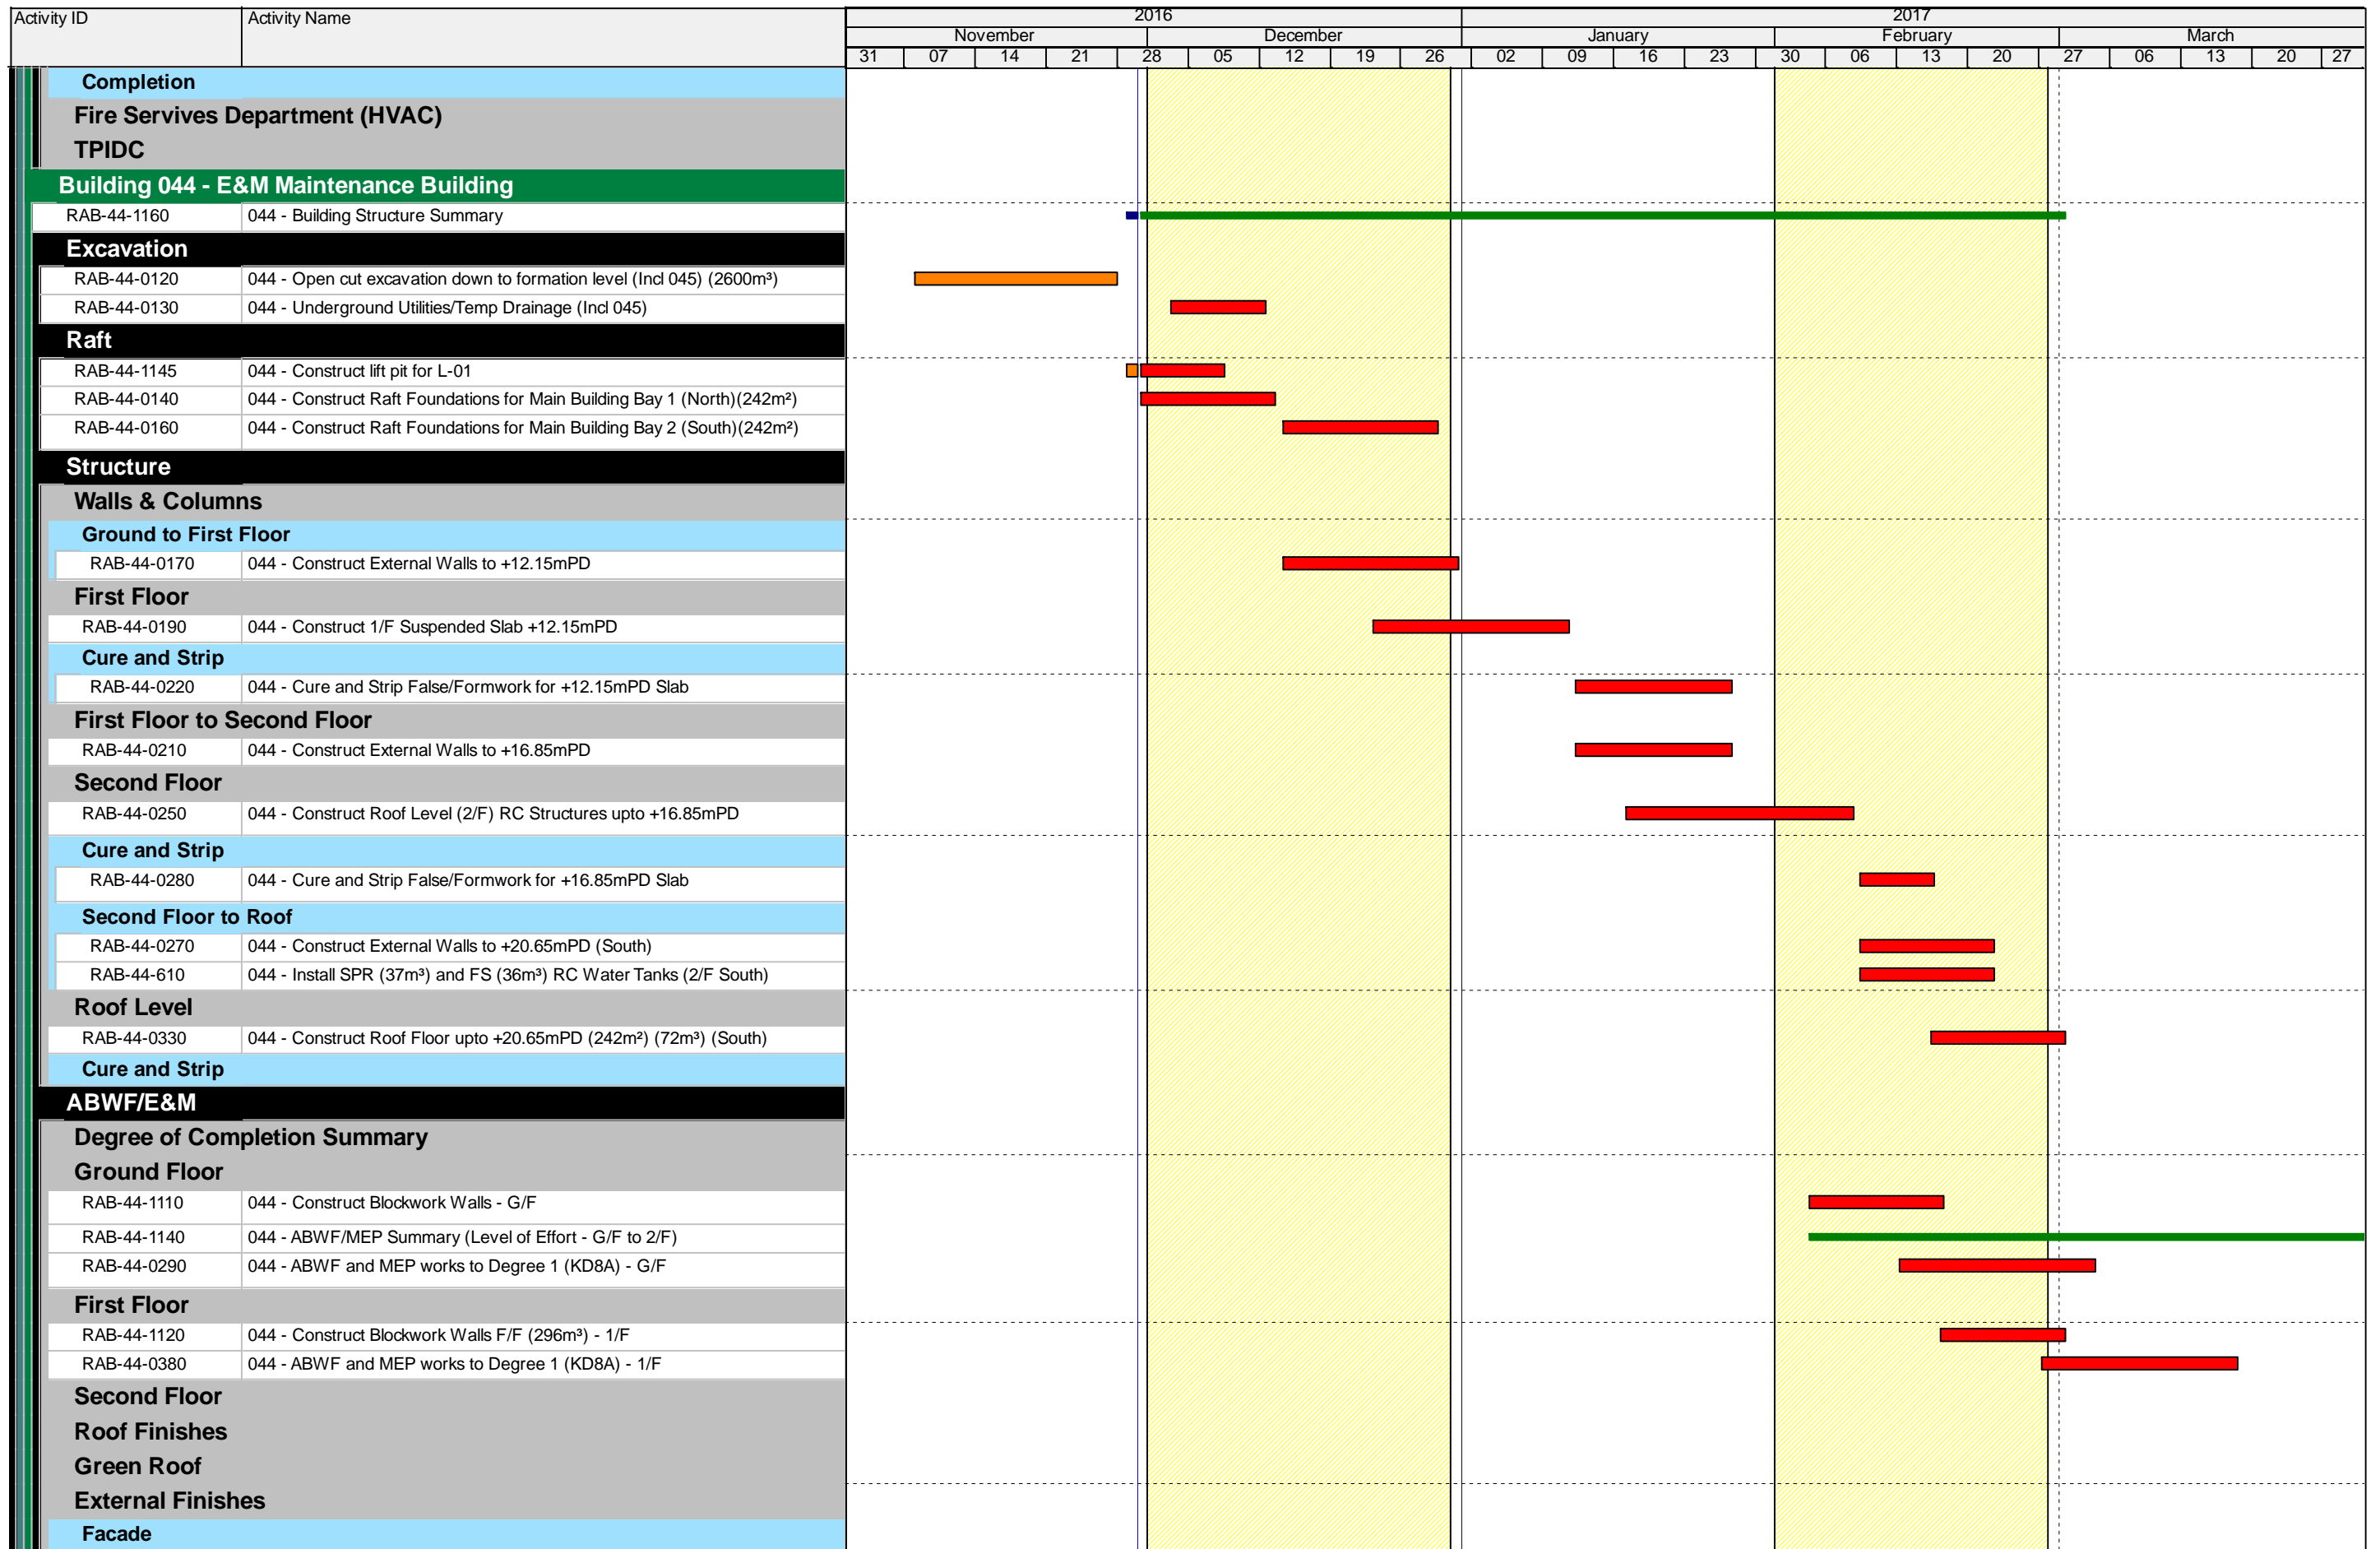

■ Remaining Level of Effort
 Actual Work
 ■ Actual Level of Effort
 Remaining Work
 ◆ ◆

C8 - 3 MONTH ROLLING PROGRAMME, 01 DEC-16 UPDATE

Date	Revision	Checked	Appro...
01-Dec-16	Working Programme with RAB3 Baseline	SGJ	

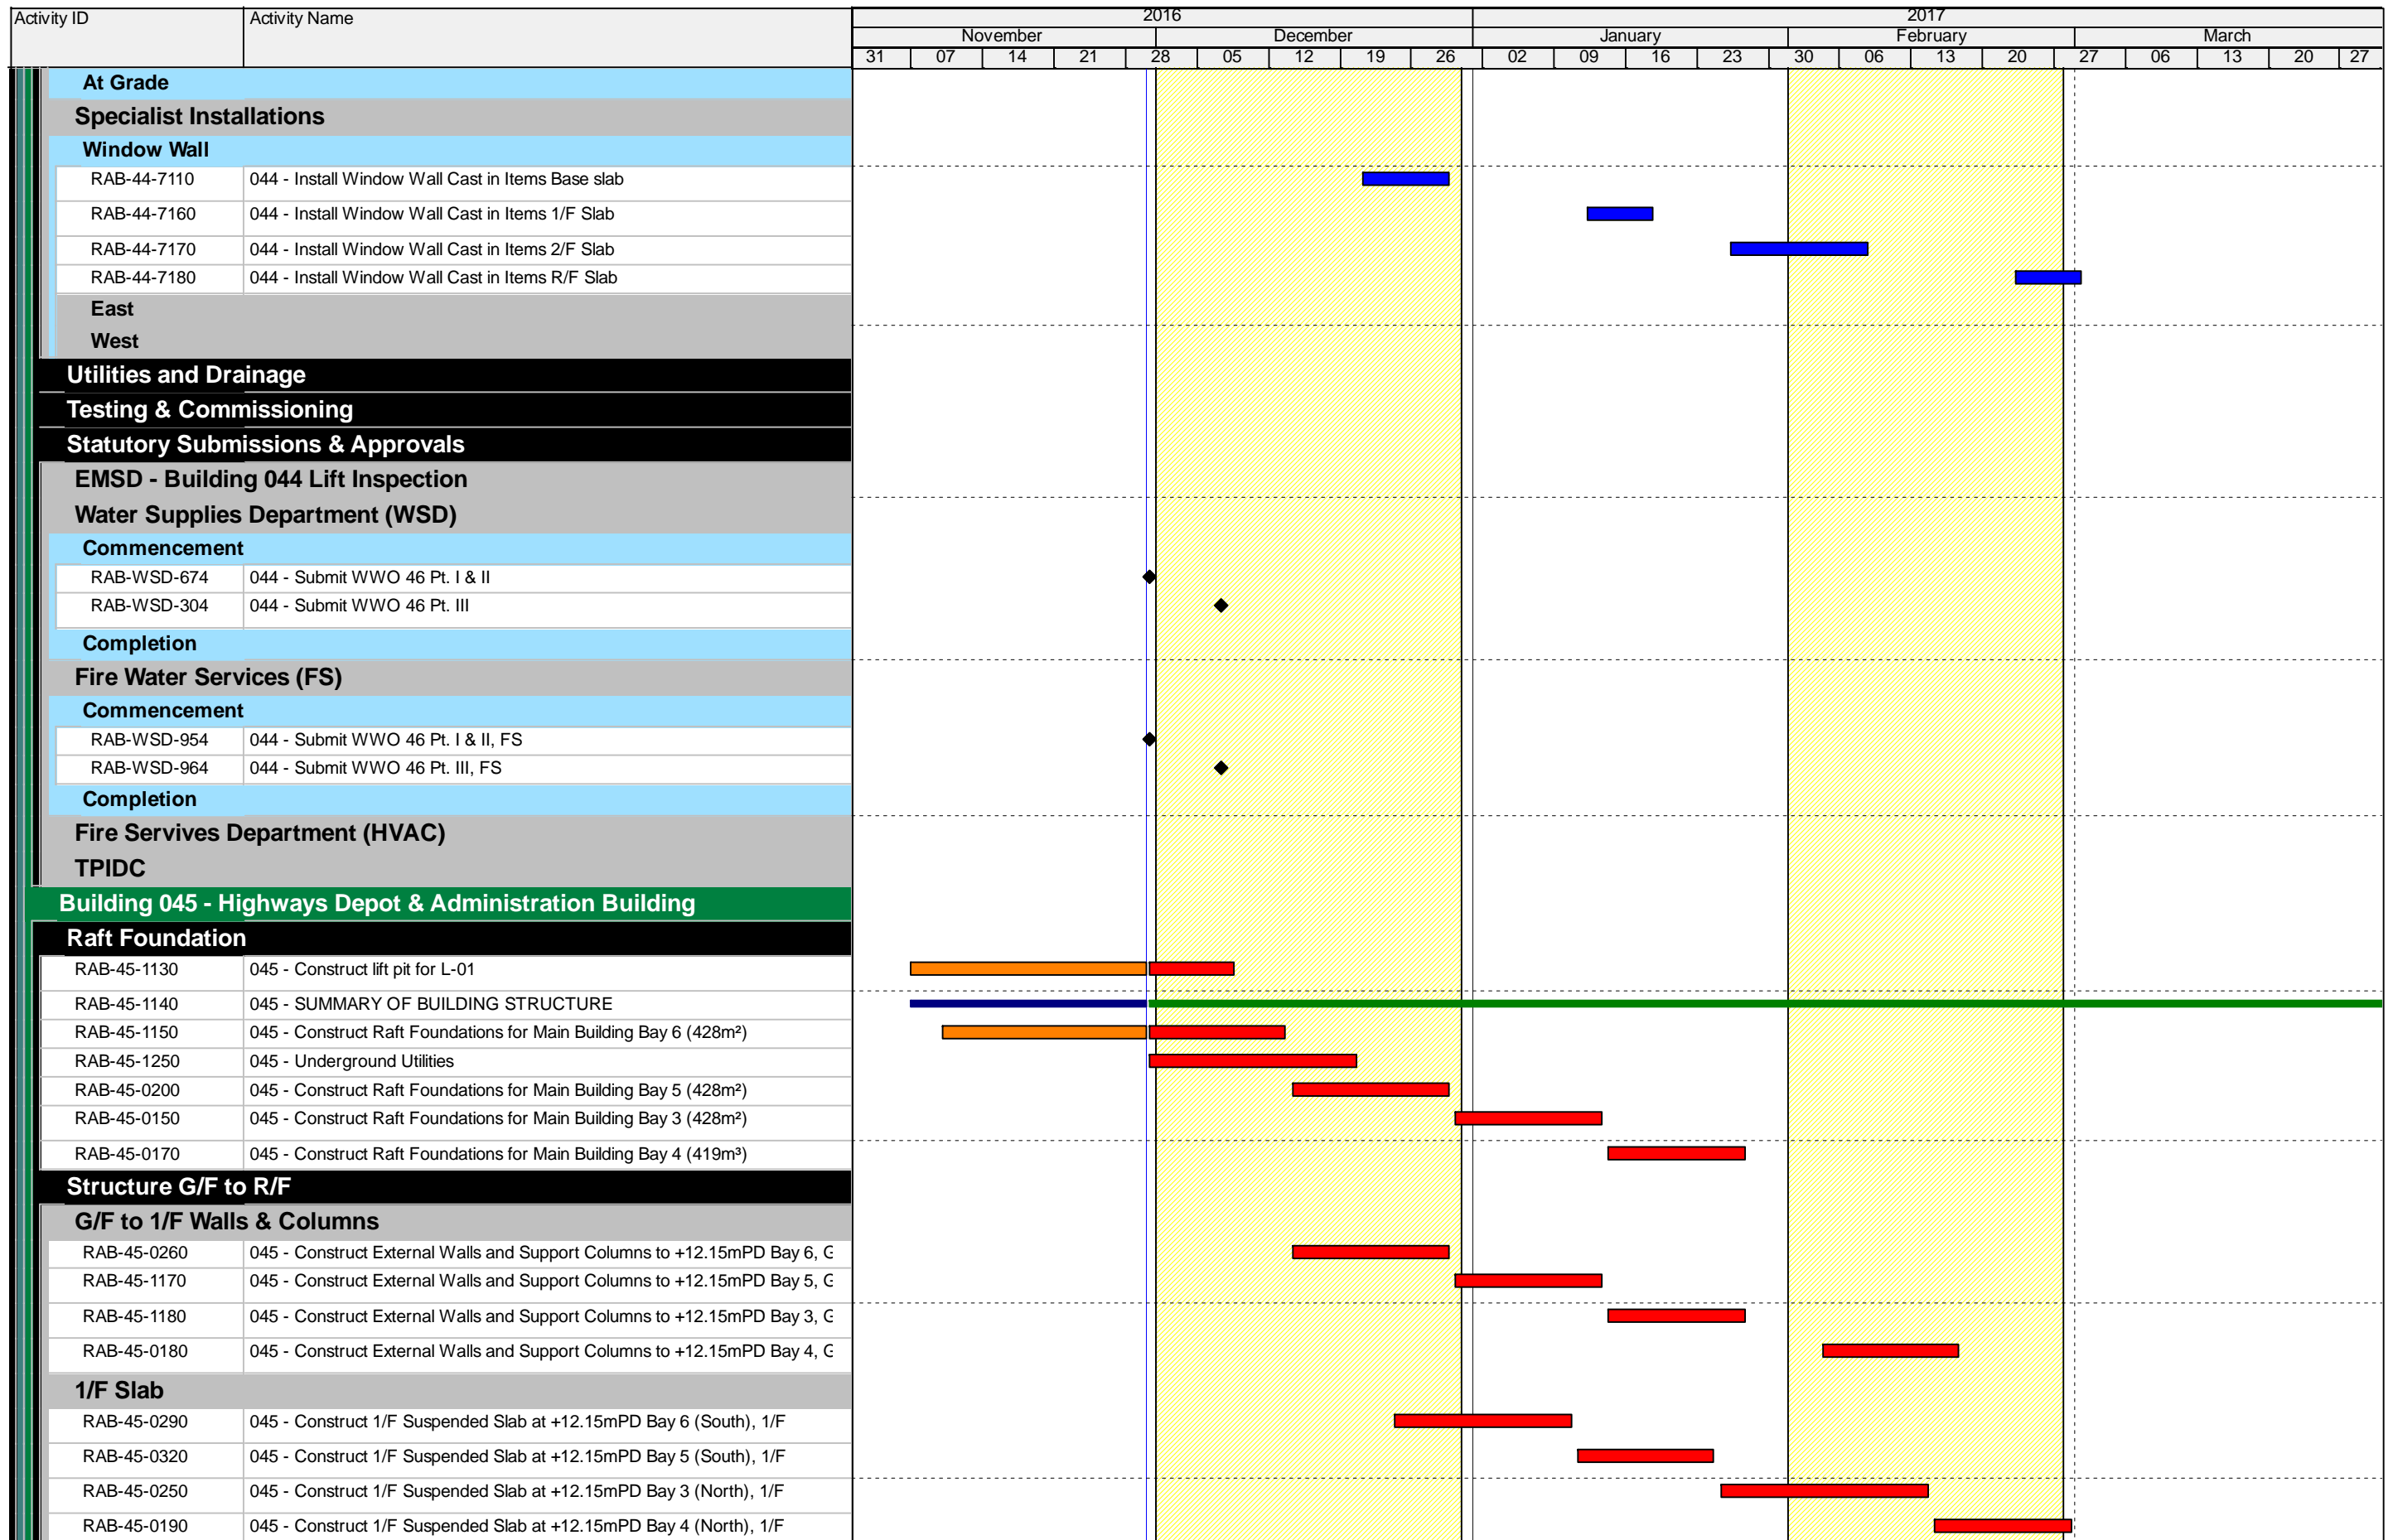

■ Remaining Level of Effort
 ■ Actual Work
 ■ [Actual Work]
 ■ Actual Level of Effort
 ■ Remaining Work
 ◆ ◆

C8 - 3 MONTH ROLLING PROGRAMME, 01 DEC-16 UPDATE


Date	Revision	Checked	Appro...
01-Dec-16	Working Programme with RAB3 Baseline	SGJ	

Activity ID	Activity Name	2016										2017														
		November					December					January					February					March				
		31	07	14	21	28	05	12	19	26		02	09	16	23	30	06	13	20	27		06	13	20	27	
Cure and Strip																										
RAB-45-0310	045 - Cure and Strip False/Formwork +12.15mPD Bay 6 (South),G/F-1/F																									
RAB-45-0350	045 - Cure and Strip False/Formwork +12.15mPD Bay 5 (South),G/F-1/F																									
RAB-45-0270	045 - Cure and Strip False/Formwork +12.15mPD Bay 3 (Middle),G/F-1/F																									
1/F to 2/F Walls & Columns																										
RAB-45-0300	045 - Construct External Walls and Support Columns to +16.55mPD Bay 6 (S																									
RAB-45-0420	045 - Construct External Walls and Support Columns to +16.55mPD Bay 5 (S																									
RAB-45-1200	045 - Construct External Walls and Support Columns to +16.7mPD Bay 3 (Mi																									
2/F Slab																										
RAB-45-0470	045 - Construct 2/F Suspended Slab +16.55mPD Bay 6 (South) (285m²) (ap																									
RAB-45-0520	045 - Construct 2/F Suspended Slab +16.55mPD Bay 5 (South) (285m²) (ap																									
Cure and Strip																										
RAB-45-0370	045 - Cure and Strip False/Formwork +16.55mPD Bay 6 (South), 1/F-2F																									
RAB-45-0510	045 - Cure and Strip False/Formwork +16.55mPD Bay 5 (South), 1/F-2F																									
2/f to R/F Walls & Columns																										
RAB-45-0610	045 - Construct External Walls to +20.65mPD Bay 5 & 6, 2/F-R/F																									
RAB-45-1110	045 - Construct SPR (37m³) and FS (36m³) RC Water Tanks (2/F South), 2/I																									
Roof Level Slab																										
Cure and Strip																										
ABWF/E&M																										
Degree of Completion Summary																										
South Section																										
North Section																										
Specialist Installations																										
Window Wall																										
RAB-23-7120	045 - Install Window Wall Cast in Items G/F																									
RAB-23-7190	045 - Install Window Wall Cast in Items F/F																									
RAB-23-7200	045 - Install Window Wall Cast in Items 2/F																									
East																										
West																										
Utilities and Drainage																										
Testing & Commissioning																										
Statutory Submissions & Approvals (Day 670 Completion)																										
EMSD - Building 045 Lift Inspection																										
RAB-FSD-230	045 - Submit EMSD Form 3 (Commencement of Lift Installation)																									
Generator Set - Design																										
Generator Set - DG Licence																										
Water Supplies Department (WSD)																										
Commencement																										
RAB-WSD-644	045 - Submit WWO 46 Pt. I & II																									
RAB-WSD-634	045 - Submit WWO 46 Pt. III																									
Completion																										
Fire Services Department (FSD)																										
Commencement																										
RAB-FSD-620	045 - Submit WWO 46 Pt. I & II																									
RAB-WSD-974	045 - Submit WWO 46 Pt. III																									

- Remaining Level of Effort
- Actual Level of Effort
- Actual Work
- Remaining Work
- ◆
- ◆

C8 - 3 MONTH ROLLING PROGRAMME, 01 DEC-16 UPDATE


Date	Revision	Checked	Appro...
01-Dec-16	Working Programme with RAB3 Baseline	SGJ	

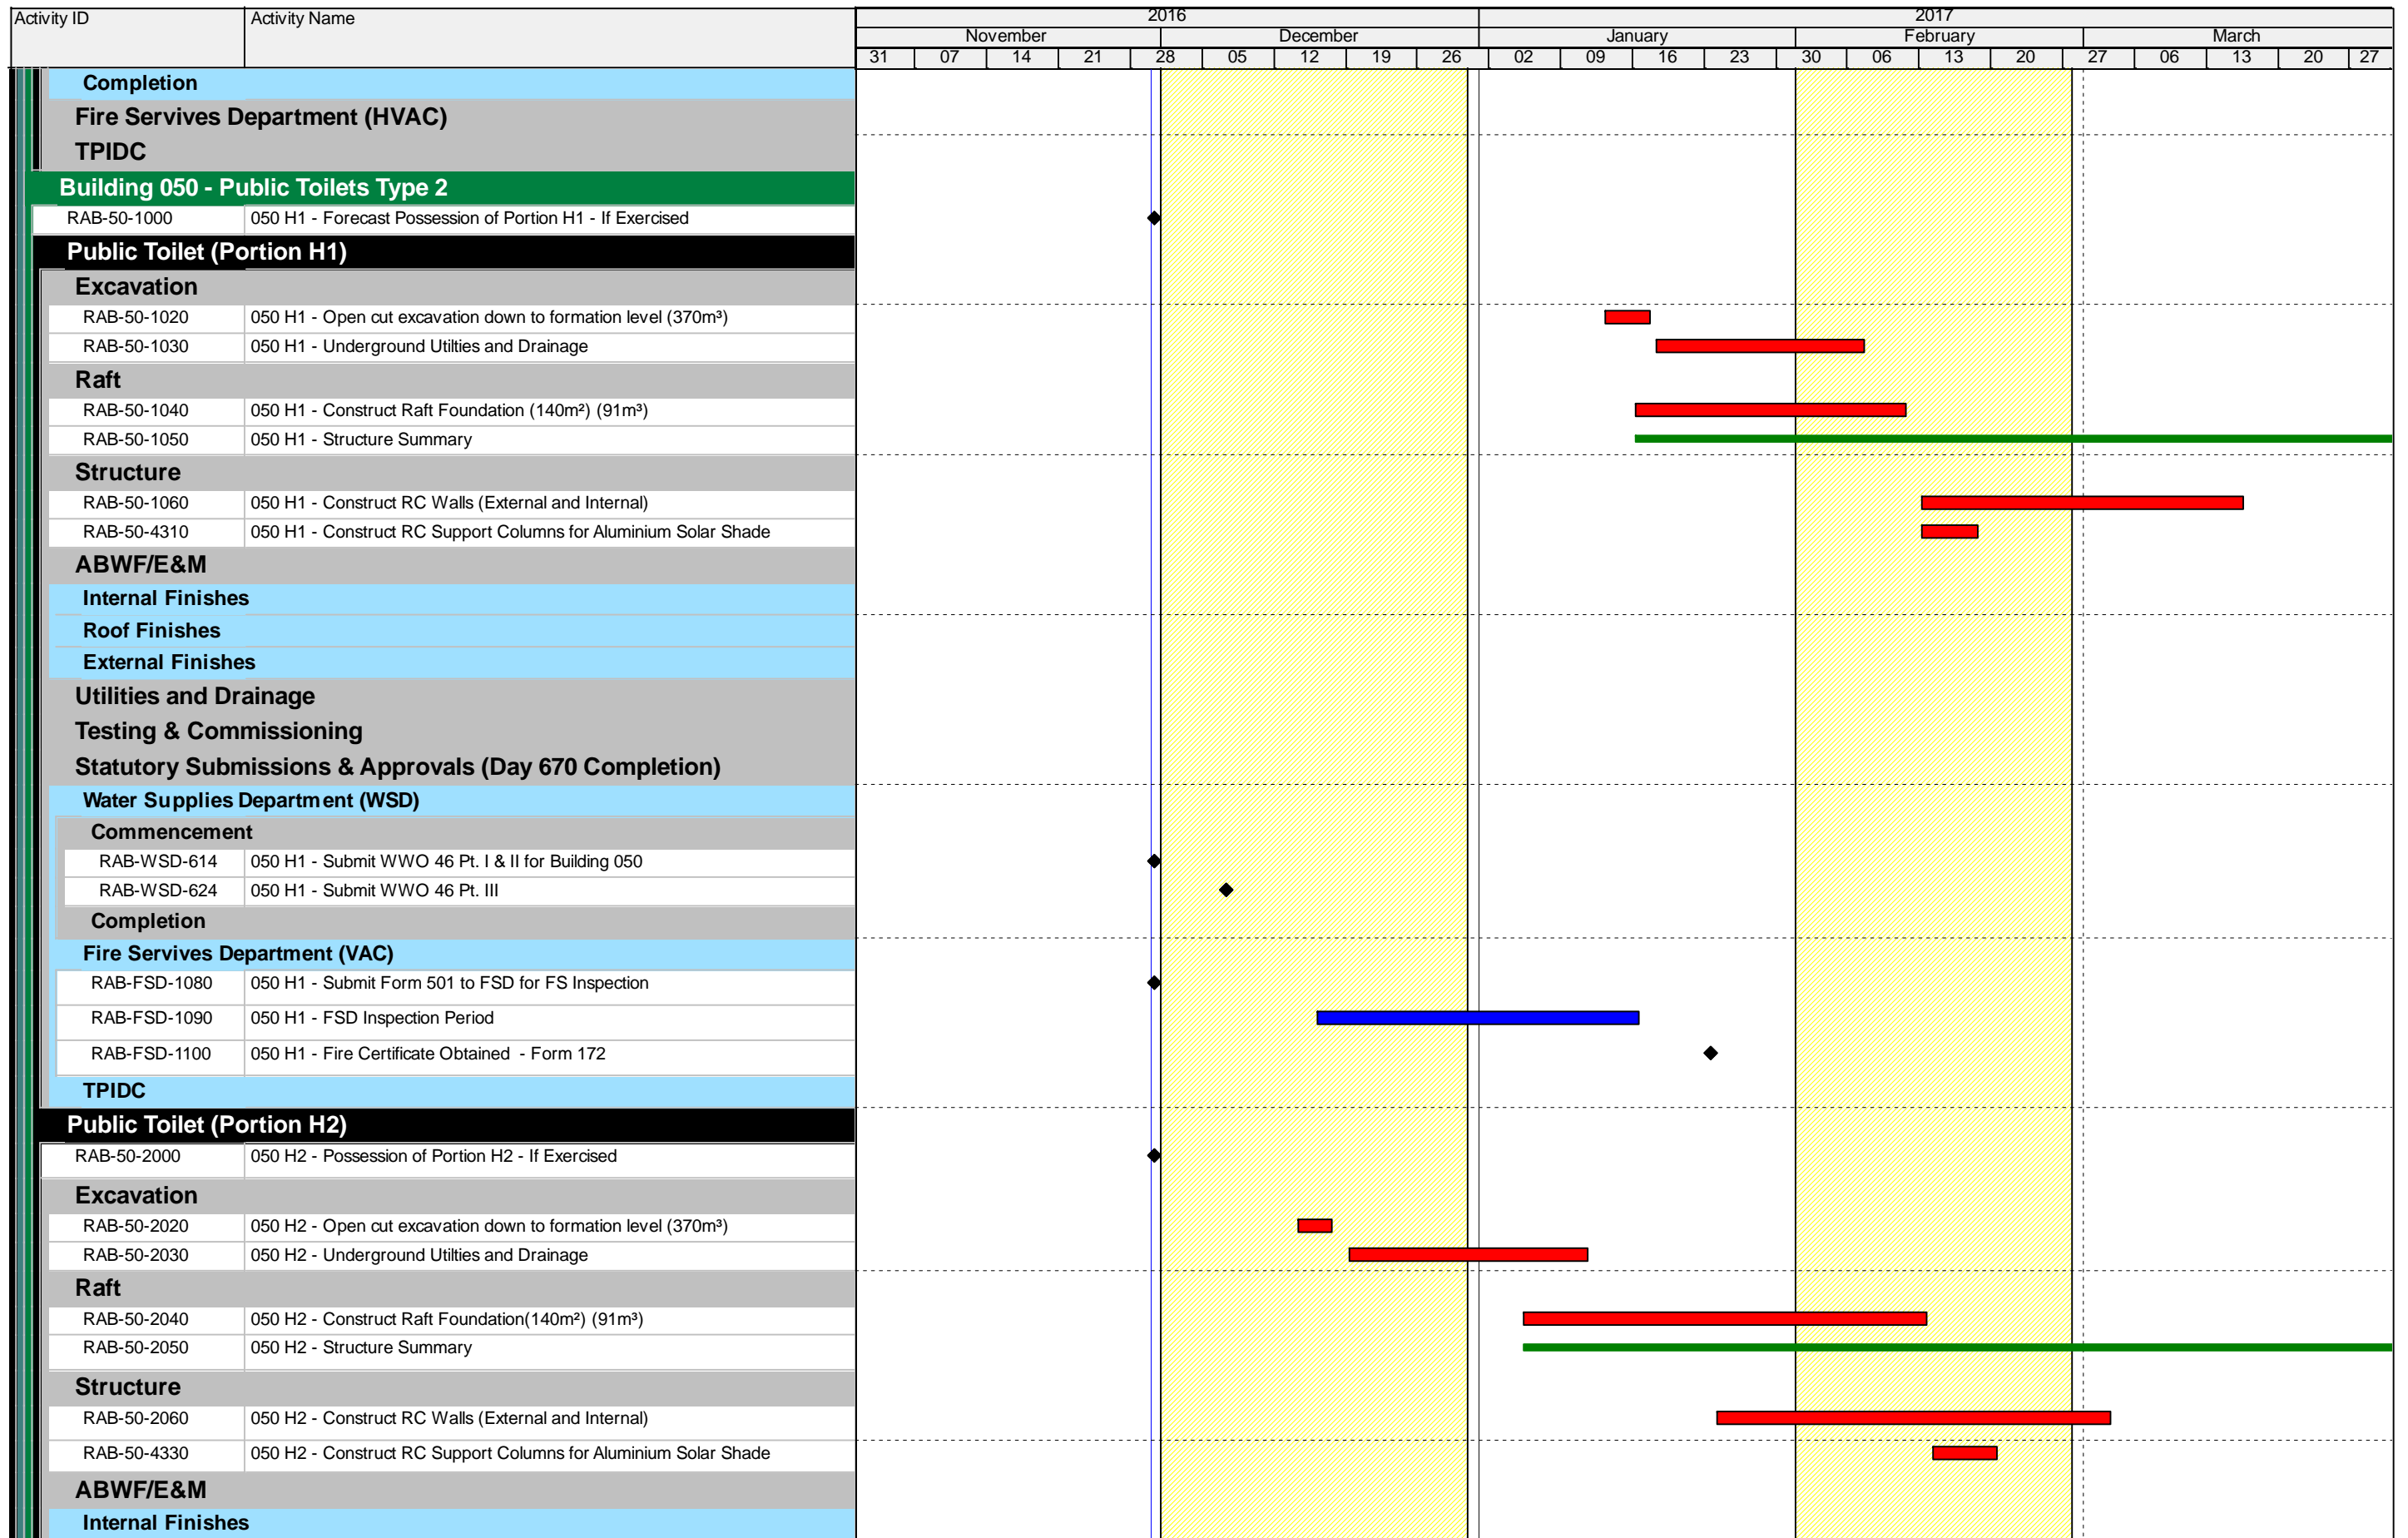

■ Remaining Level of Effort ■ Actual Work ■
■ Actual Level of Effort ■ Remaining Work ◆ ◆

C8 - 3 MONTH ROLLING PROGRAMME, 01 DEC-16 UPDATE


Date	Revision	Checked	Appro...
01-Dec-16	Working Programme with RAB3 Baseline	SGJ	

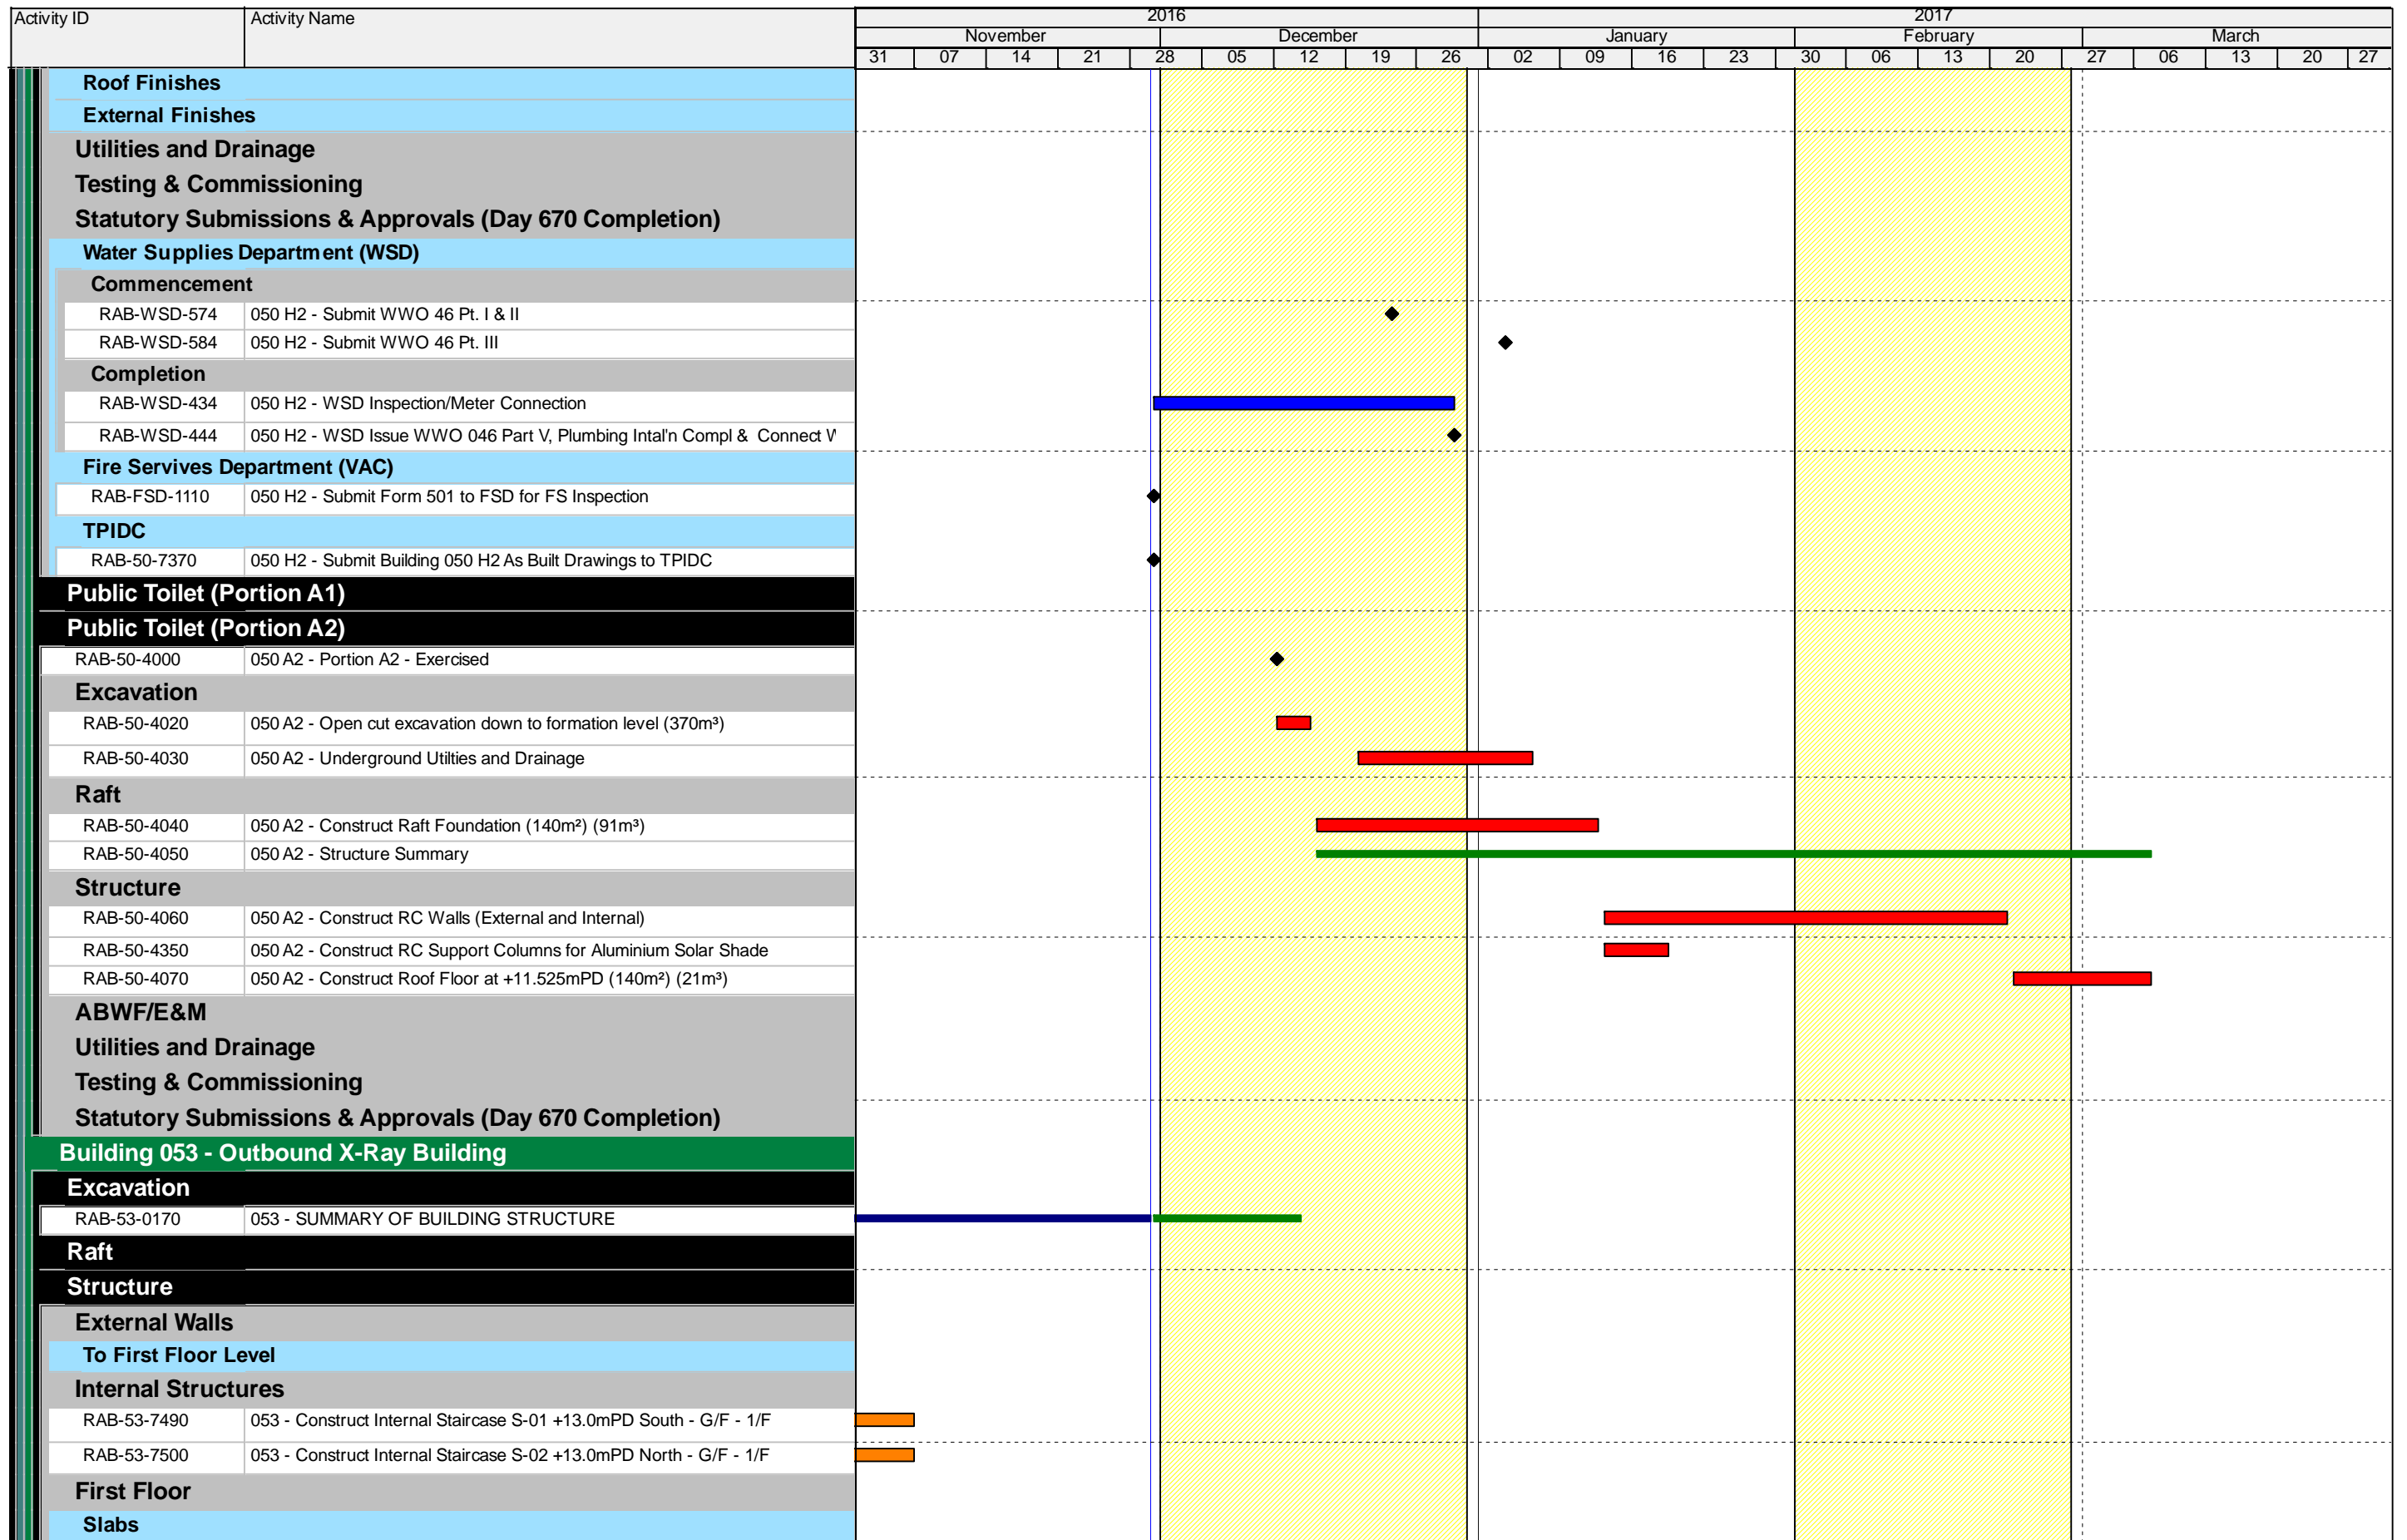

■ Remaining Level of Effort
■ Actual Work
■
■ Actual Level of Effort
■ Remaining Work
◆
◆

C8 - 3 MONTH ROLLING PROGRAMME, 01 DEC-16 UPDATE

Date	Revision	Checked	Appro...
01-Dec-16	Working Programme with RAB3 Baseline	SGJ	

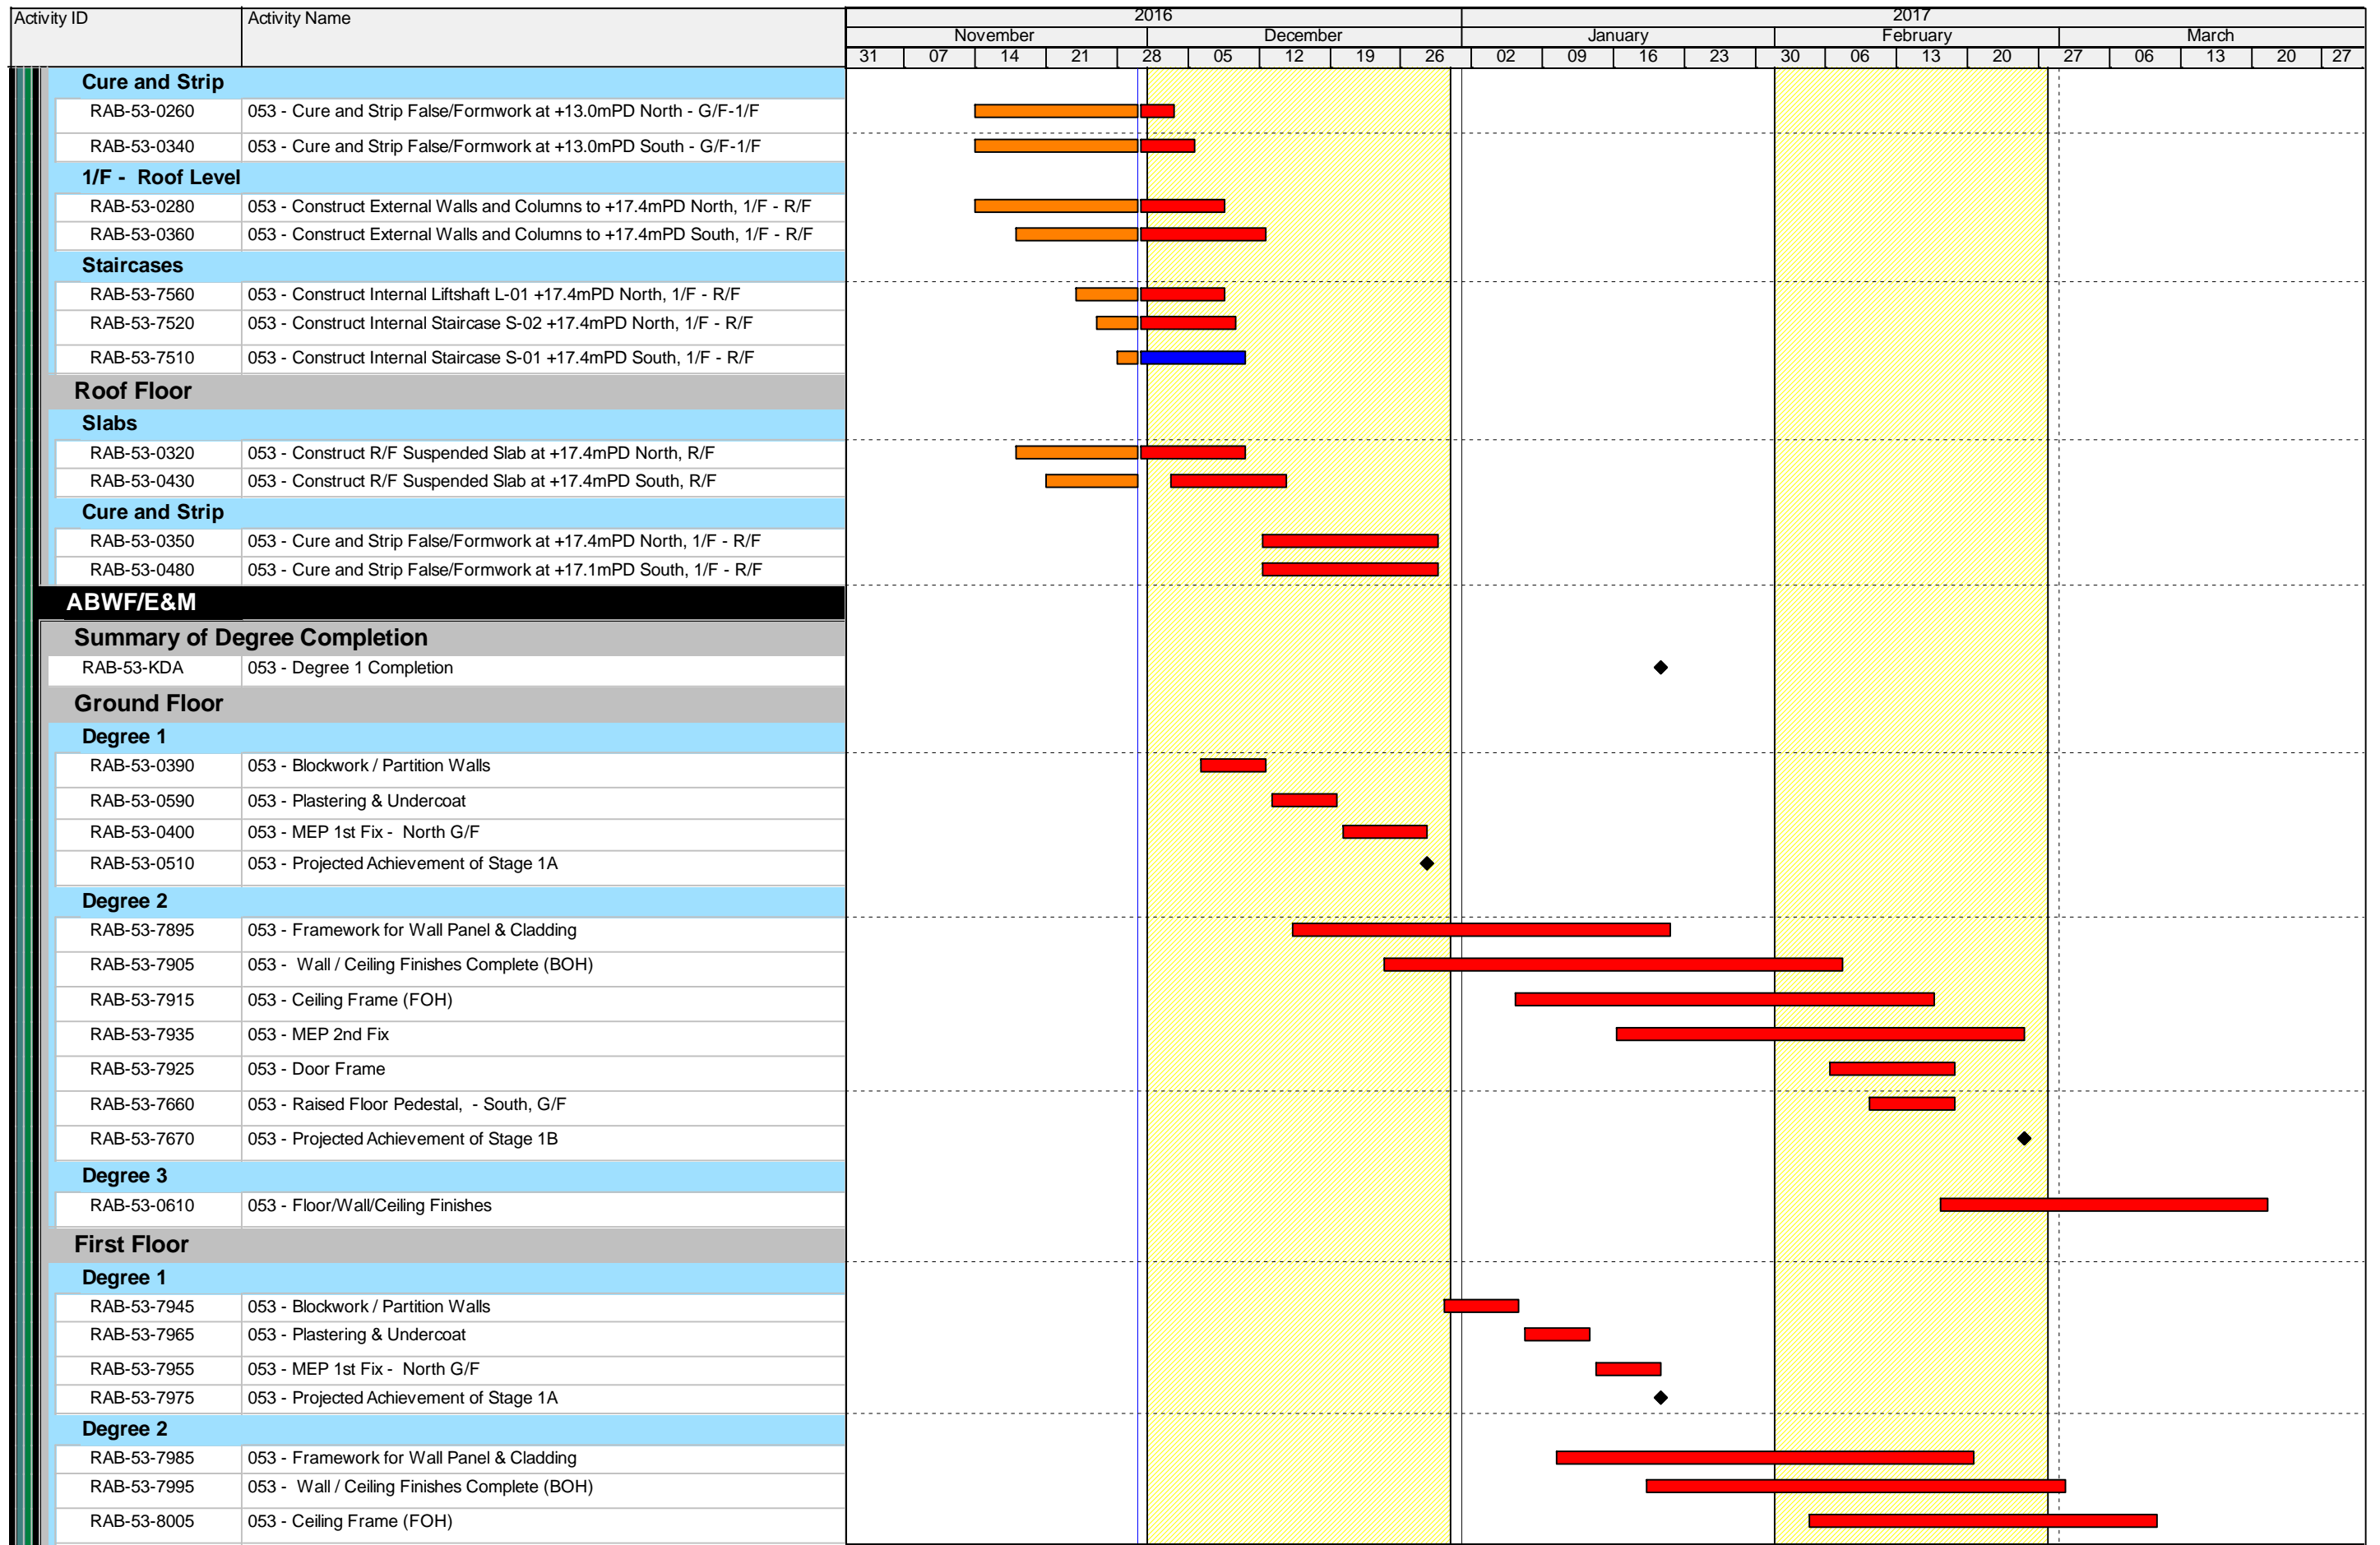

■ Remaining Level of Effort
■ Actual Work
■ Actual Level of Effort
■ Remaining Work
◆ Milestone

C8 - 3 MONTH ROLLING PROGRAMME, 01 DEC-16 UPDATE


Date	Revision	Checked	Appro...
01-Dec-16	Working Programme with RAB3 Baseline	SGJ	

Activity ID	Activity Name	2016										2017																					
		November					December					January					February					March											
		31	07	14	21	28	05	12	19	26		02	09	16	23	30	06	13	20	27		06	13	20	27								
RAB-53-8035	053 - MEP 2nd Fix																																
Degree 3																																	
External Finishes																																	
External Facade																																	
RAB-53-0410	053 - Erect External Scaffolding																																
RAB-53-0440	053 - Install External Louvers /Windows/Doors																																
RAB-53-0450	053 - External Render (465m²) (From Bldg 053)																																
At Grade																																	
Roof Finishes																																	
RAB-53-0420	053 - Leveling Screed - (490m²)																																
RAB-53-0460	053 - Waterproof Membrane - (490m²)																																
RAB-53-670	053 - Insulation Board - (490m²)																																
RAB-53-0490	053 - Top Screed - (490m²)																																
RAB-53-0520	053 - Install Roof Tiles - (490m²)																																
Spacialist Installations																																	
RAB-53-0600	053 - Install Lift (1 nos)																																
Glazed Canopy																																	
Utilities and Drainage																																	
RAB-53-7595	053 - Construct Permanent Drainage and Manholes (Approx 135m)																																
RAB-53-7620	053 - Install Fresh Water Mains																																
RAB-53-7610	053 - Install Flushing Water Mains																																
RAB-53-7605	053 - Utilites and Common Telecom Ducting																																
Testing & Commissioning																																	
Statutory Submissions & Approvals (Day 470 Completion)																																	
EMSD - Building 053 Lift Inspection																																	
RAB-FSD-140	053 - Submit EMSD Form 3 (Commencement of Lift Installation)																																
Water Supplies Department (WSD)																																	
Commencement																																	
RAB-WSD-494	053 - Submit WWO 46 Pt. I & II																																
RAB-WSD-504	053 - Submit WWO 46 Pt. III																																
Completion																																	
RAB-WSD-100	053 - Submit WWO 46 Pt. IV																																
RAB-WSD-102	053 - WSD's Processing/Inspection/Meter Connection																																
Fire Water Services (FSD)																																	
Commencement																																	
RAB-FSD-770	053 - Submit WWO 46 Pt. I & II																																
RAB-FSD-840	053 - Submit WWO 46 Pt. III																																
Completion																																	
RAB-FSD-410	053 - Submit WWO 46 Pt. I V																																
RAB-FSD-420	053 - FSD Inspection Period																																
Fire Servives Department (VAC)																																	
RAB-FSD-1140	053 - Submit Form 501 to FSD for FS Inspection																																
TPIDC																																	
RAB-53-7460	053 - Submit Building 053 As Built Drawings to TPIDC																																
Building 058 - Outbound X-Ray Scan Tunnel																																	
Excavation																																	

- Remaining Level of Effort
- Actual Level of Effort
- Actual Work
- Remaining Work
- ◆
- ◆

C8 - 3 MONTH ROLLING PROGRAMME, 01 DEC-16 UPDATE


Date	Revision	Checked	Appro...
01-Dec-16	Working Programme with RAB3 Baseline	SGJ	

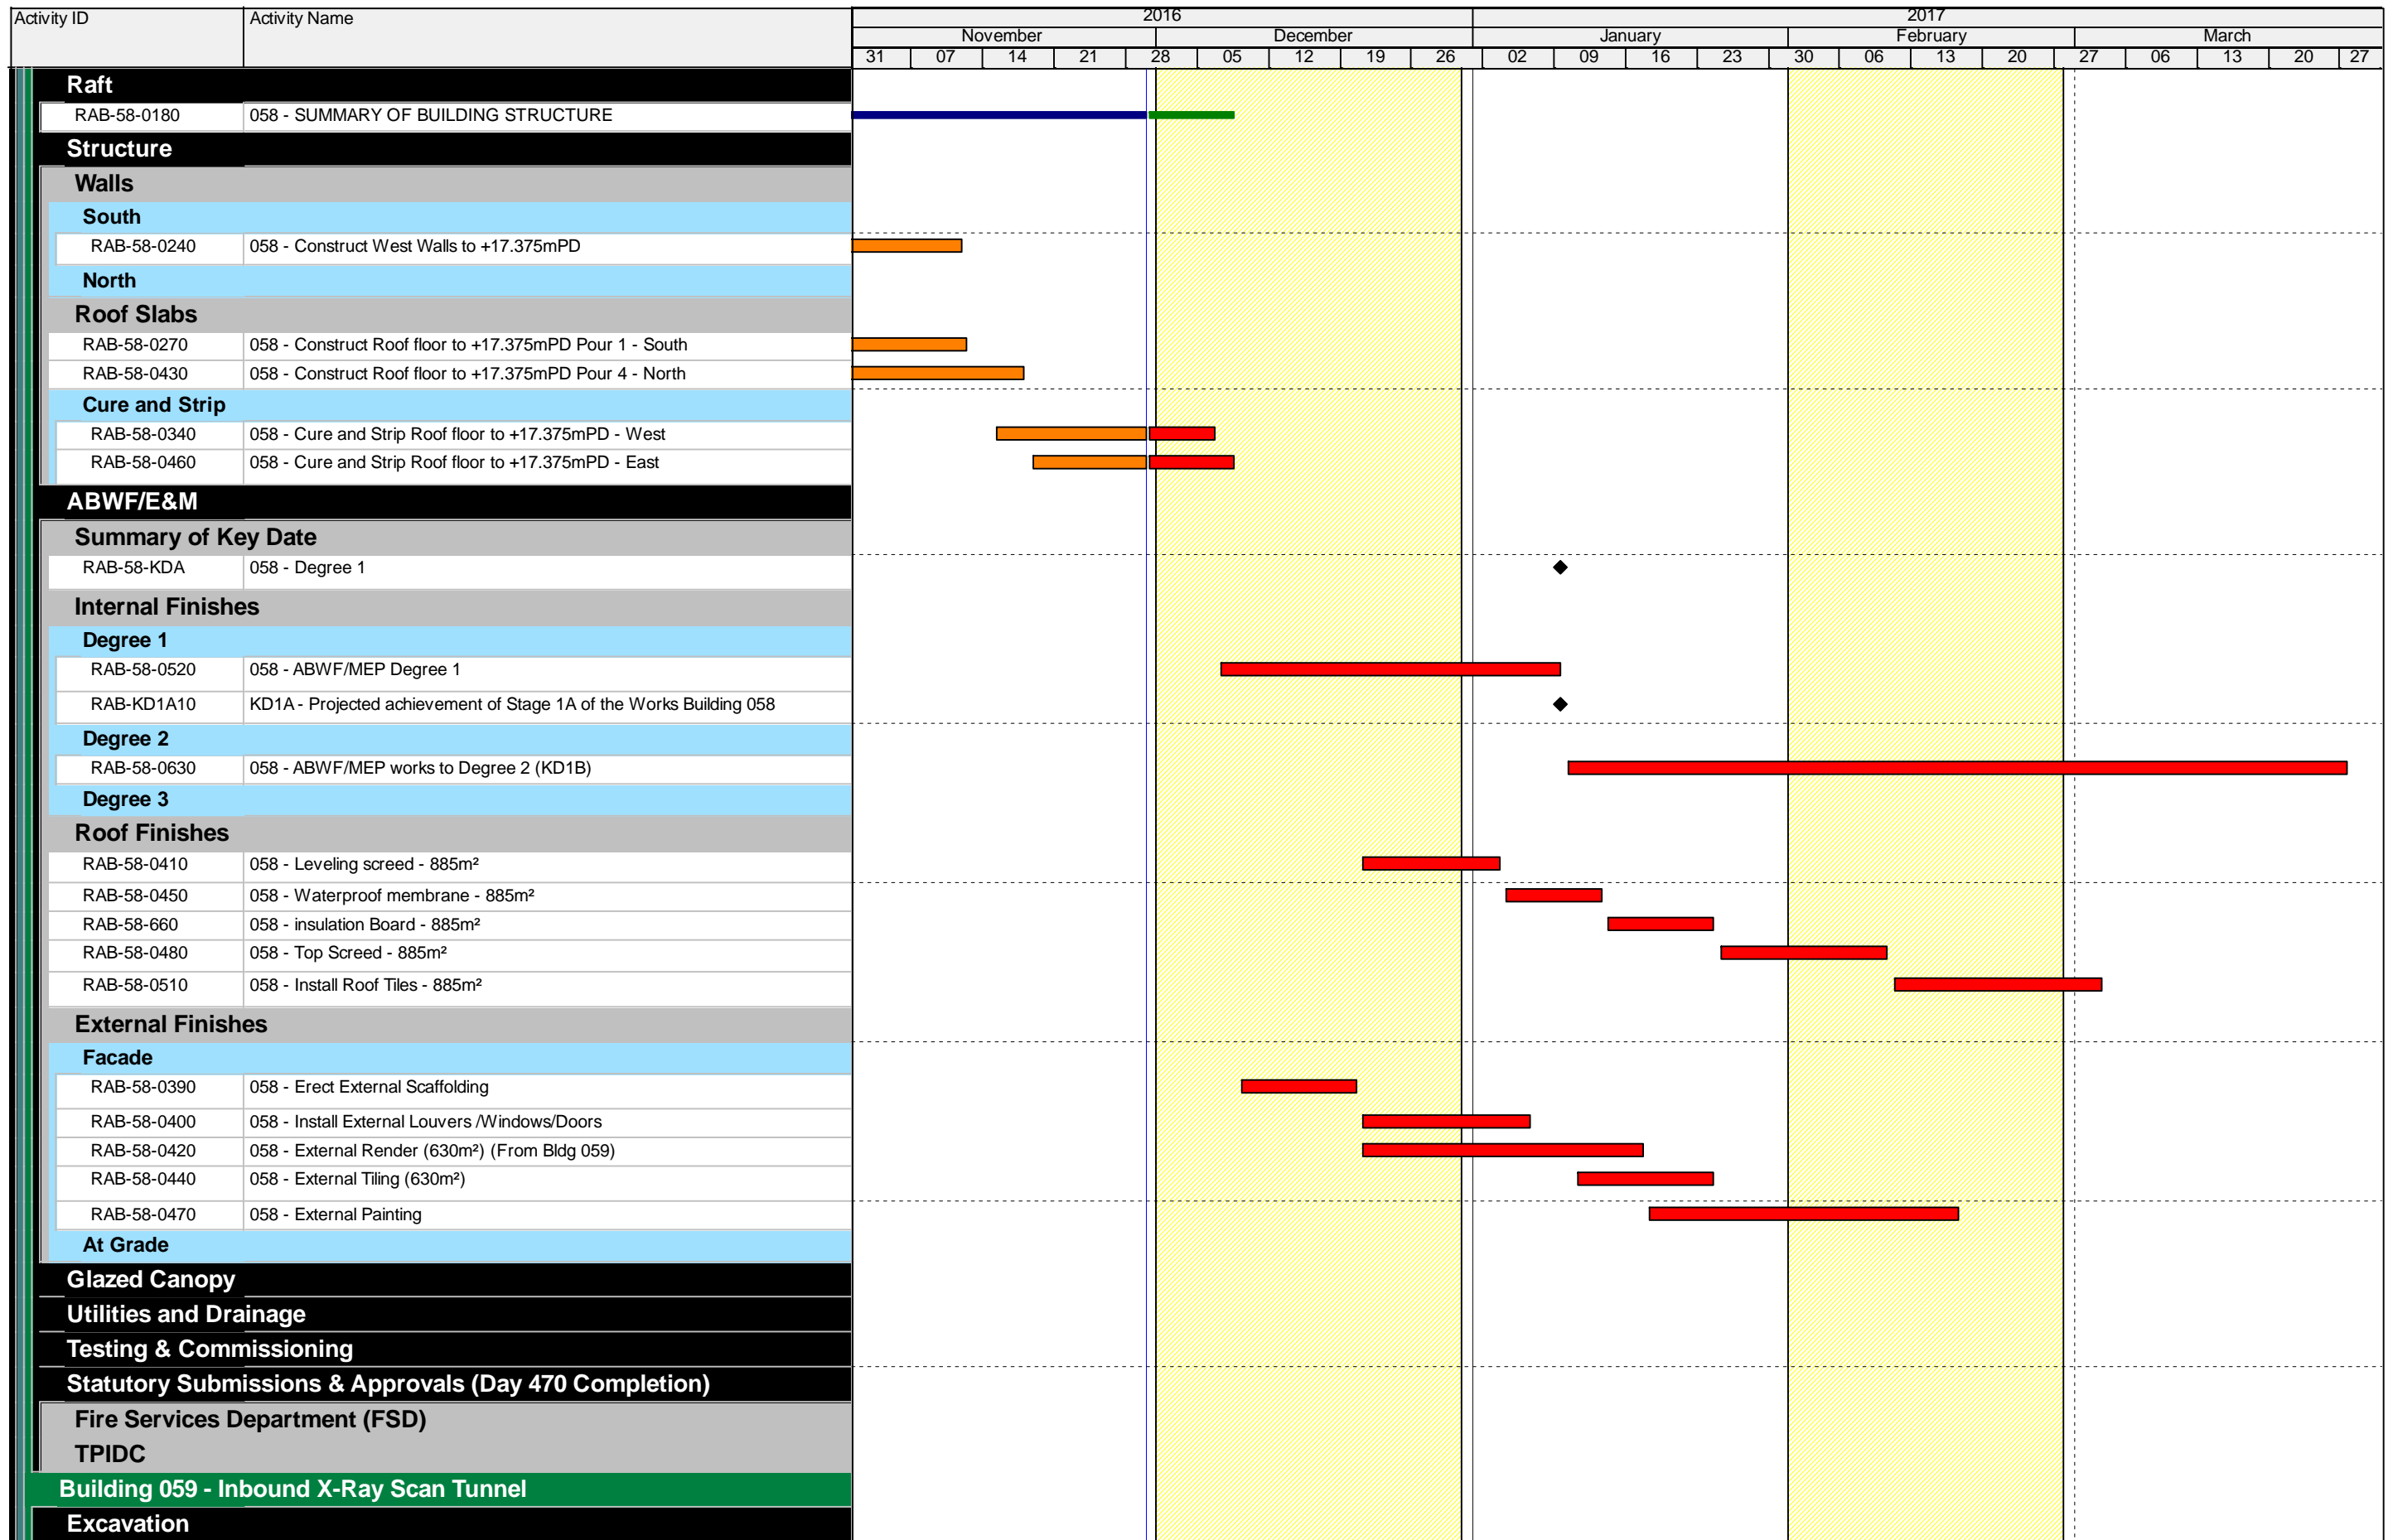

■ Remaining Level of Effort
■ Actual Work
■
■ Actual Level of Effort
■ Remaining Work
◆
◆

C8 - 3 MONTH ROLLING PROGRAMME, 01 DEC-16 UPDATE

Date	Revision	Checked	Appro...
01-Dec-16	Working Programme with RAB3 Baseline	SGJ	

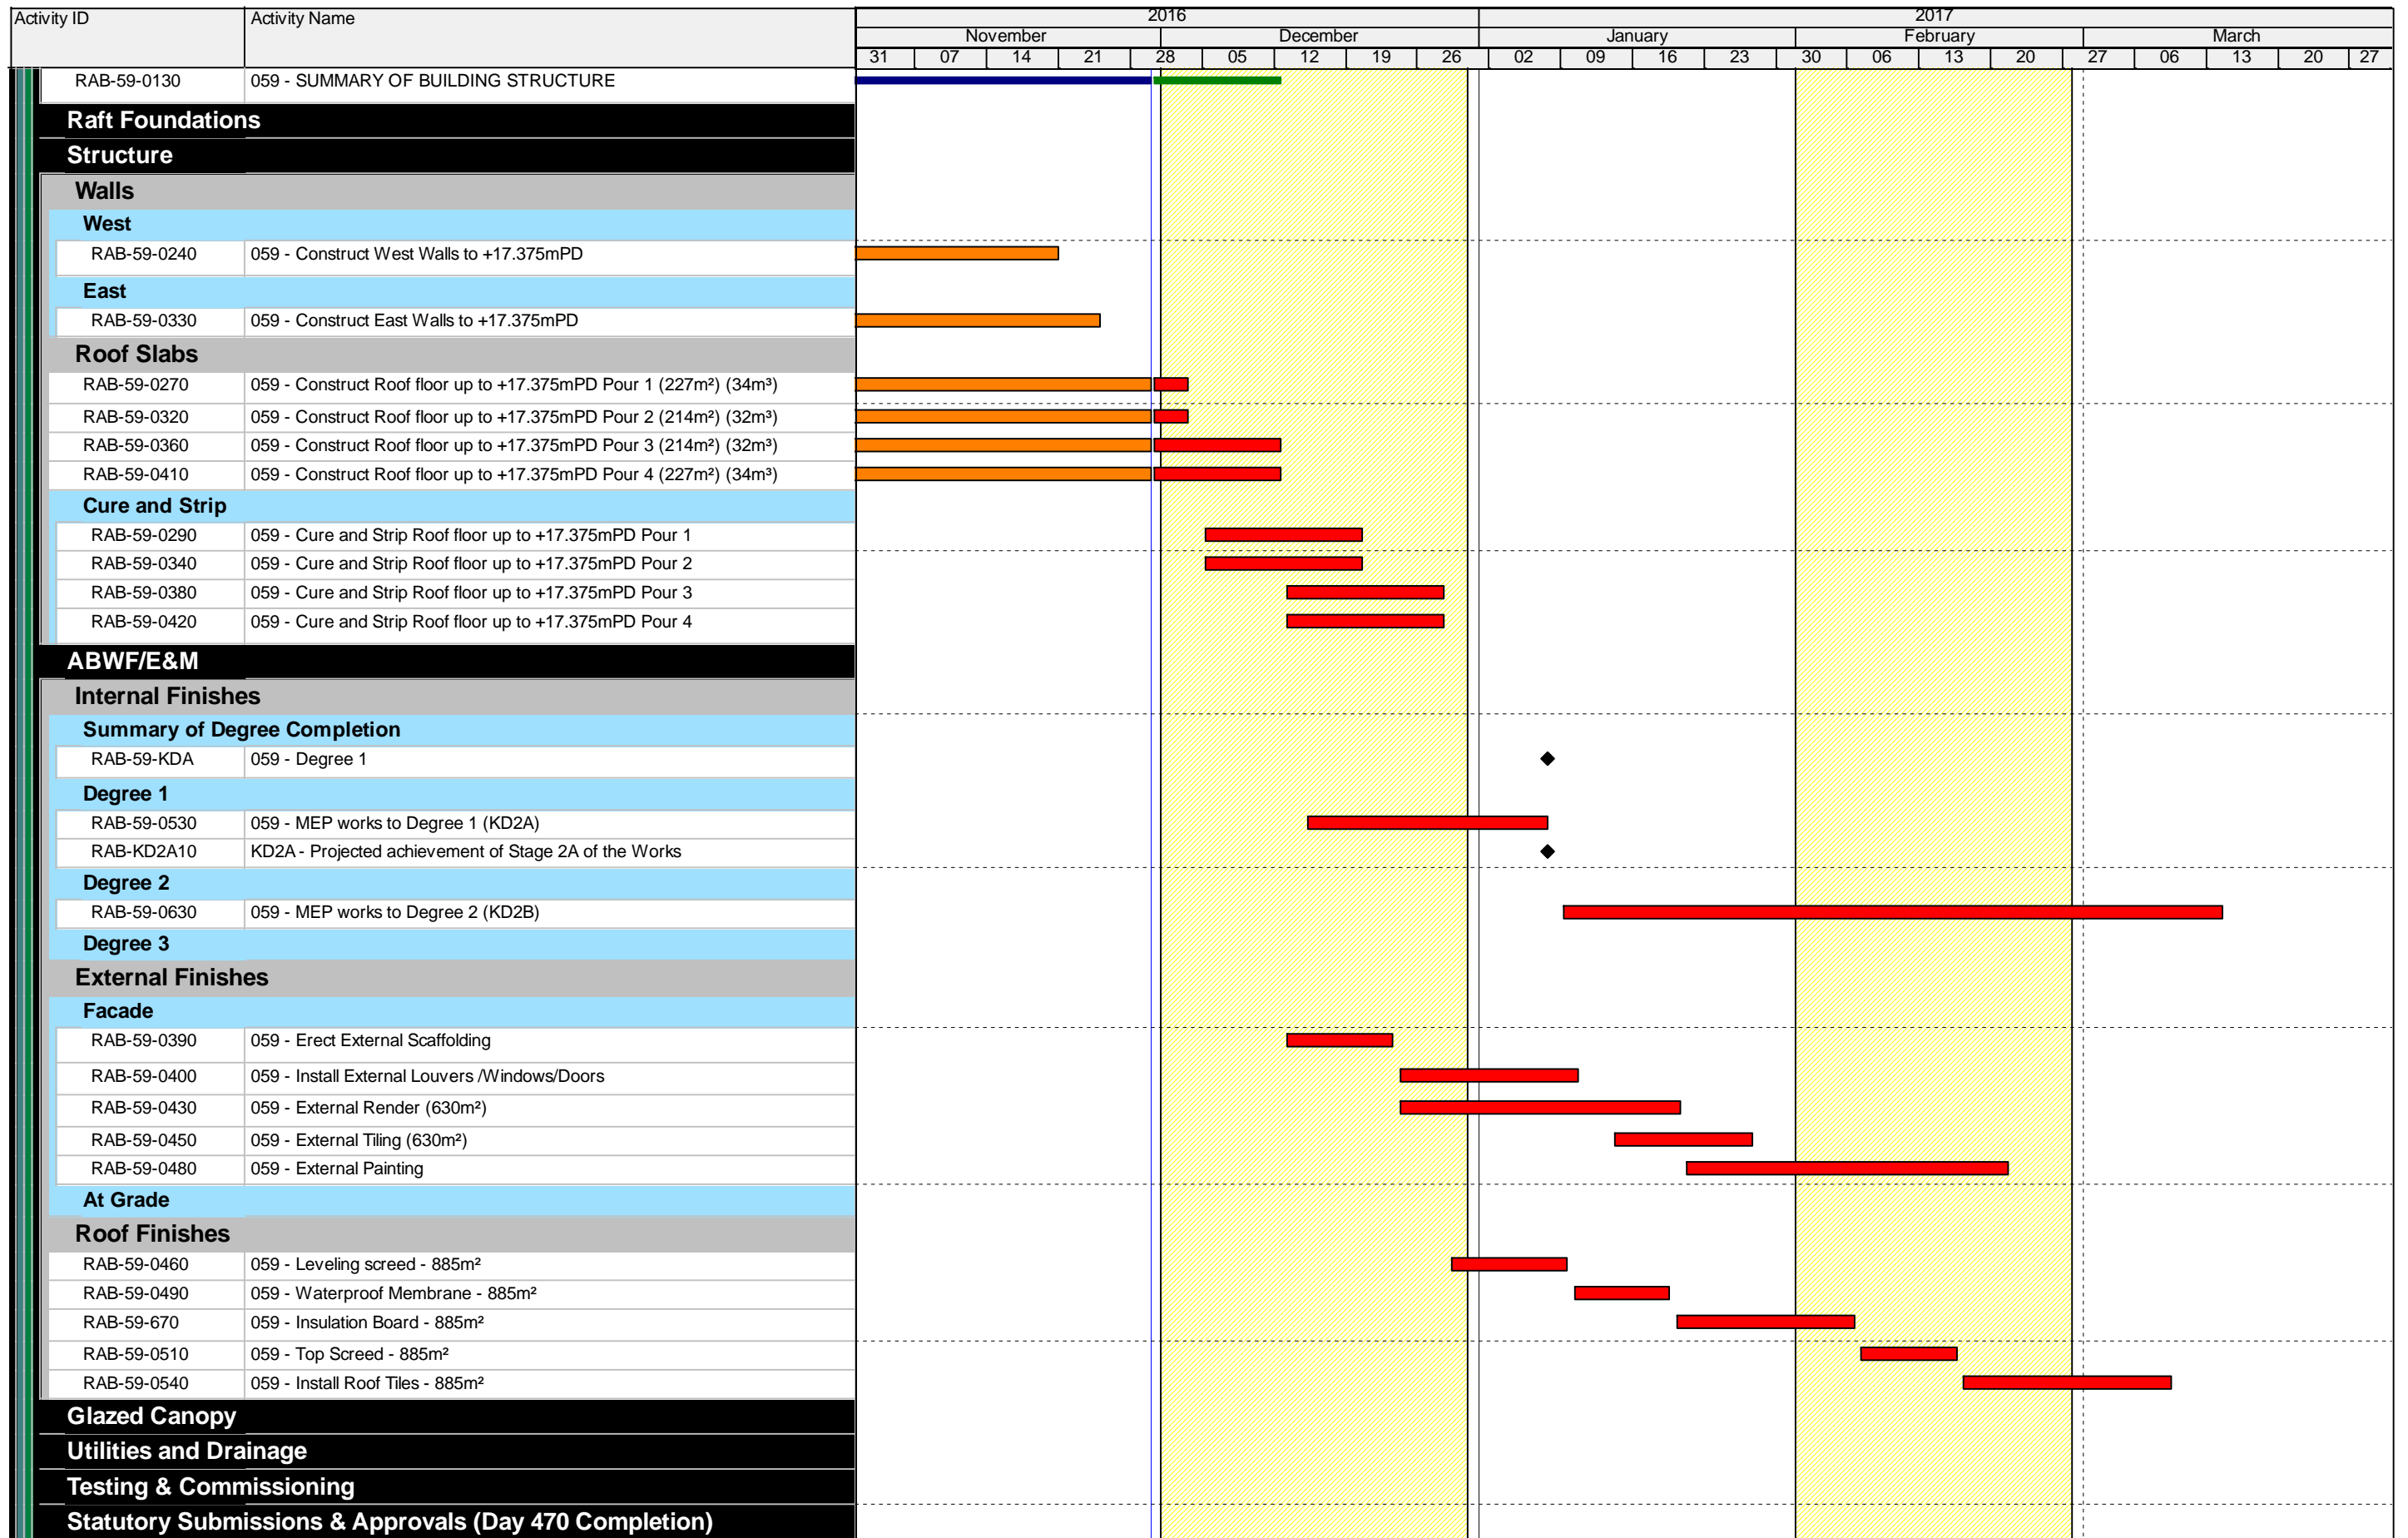

■ Remaining Level of Effort
■ Actual Work
■
■ Actual Level of Effort
■ Remaining Work
◆
◆

C8 - 3 MONTH ROLLING PROGRAMME, 01 DEC-16 UPDATE

Date	Revision	Checked	Appro...
01-Dec-16	Working Programme with RAB3 Baseline	SGJ	

Activity ID	Activity Name	2016									2017												
		November					December				January				February				March				
		31	07	14	21	28	05	12	19	26	02	09	16	23	30	06	13	20	27	06	13	20	27
	Fire Services Department (FSD) TPIDC																						



■ Remaining Level of Effort
■ Actual Work
■
■ Actual Level of Effort
■ Remaining Work ◆ ◆

C8 - 3 MONTH ROLLING PROGRAMME, 01 DEC-16 UPDATE

Date	Revision	Checked	Appro...
01-Dec-16	Working Programme with RAB3 Baseline	SGJ	
