


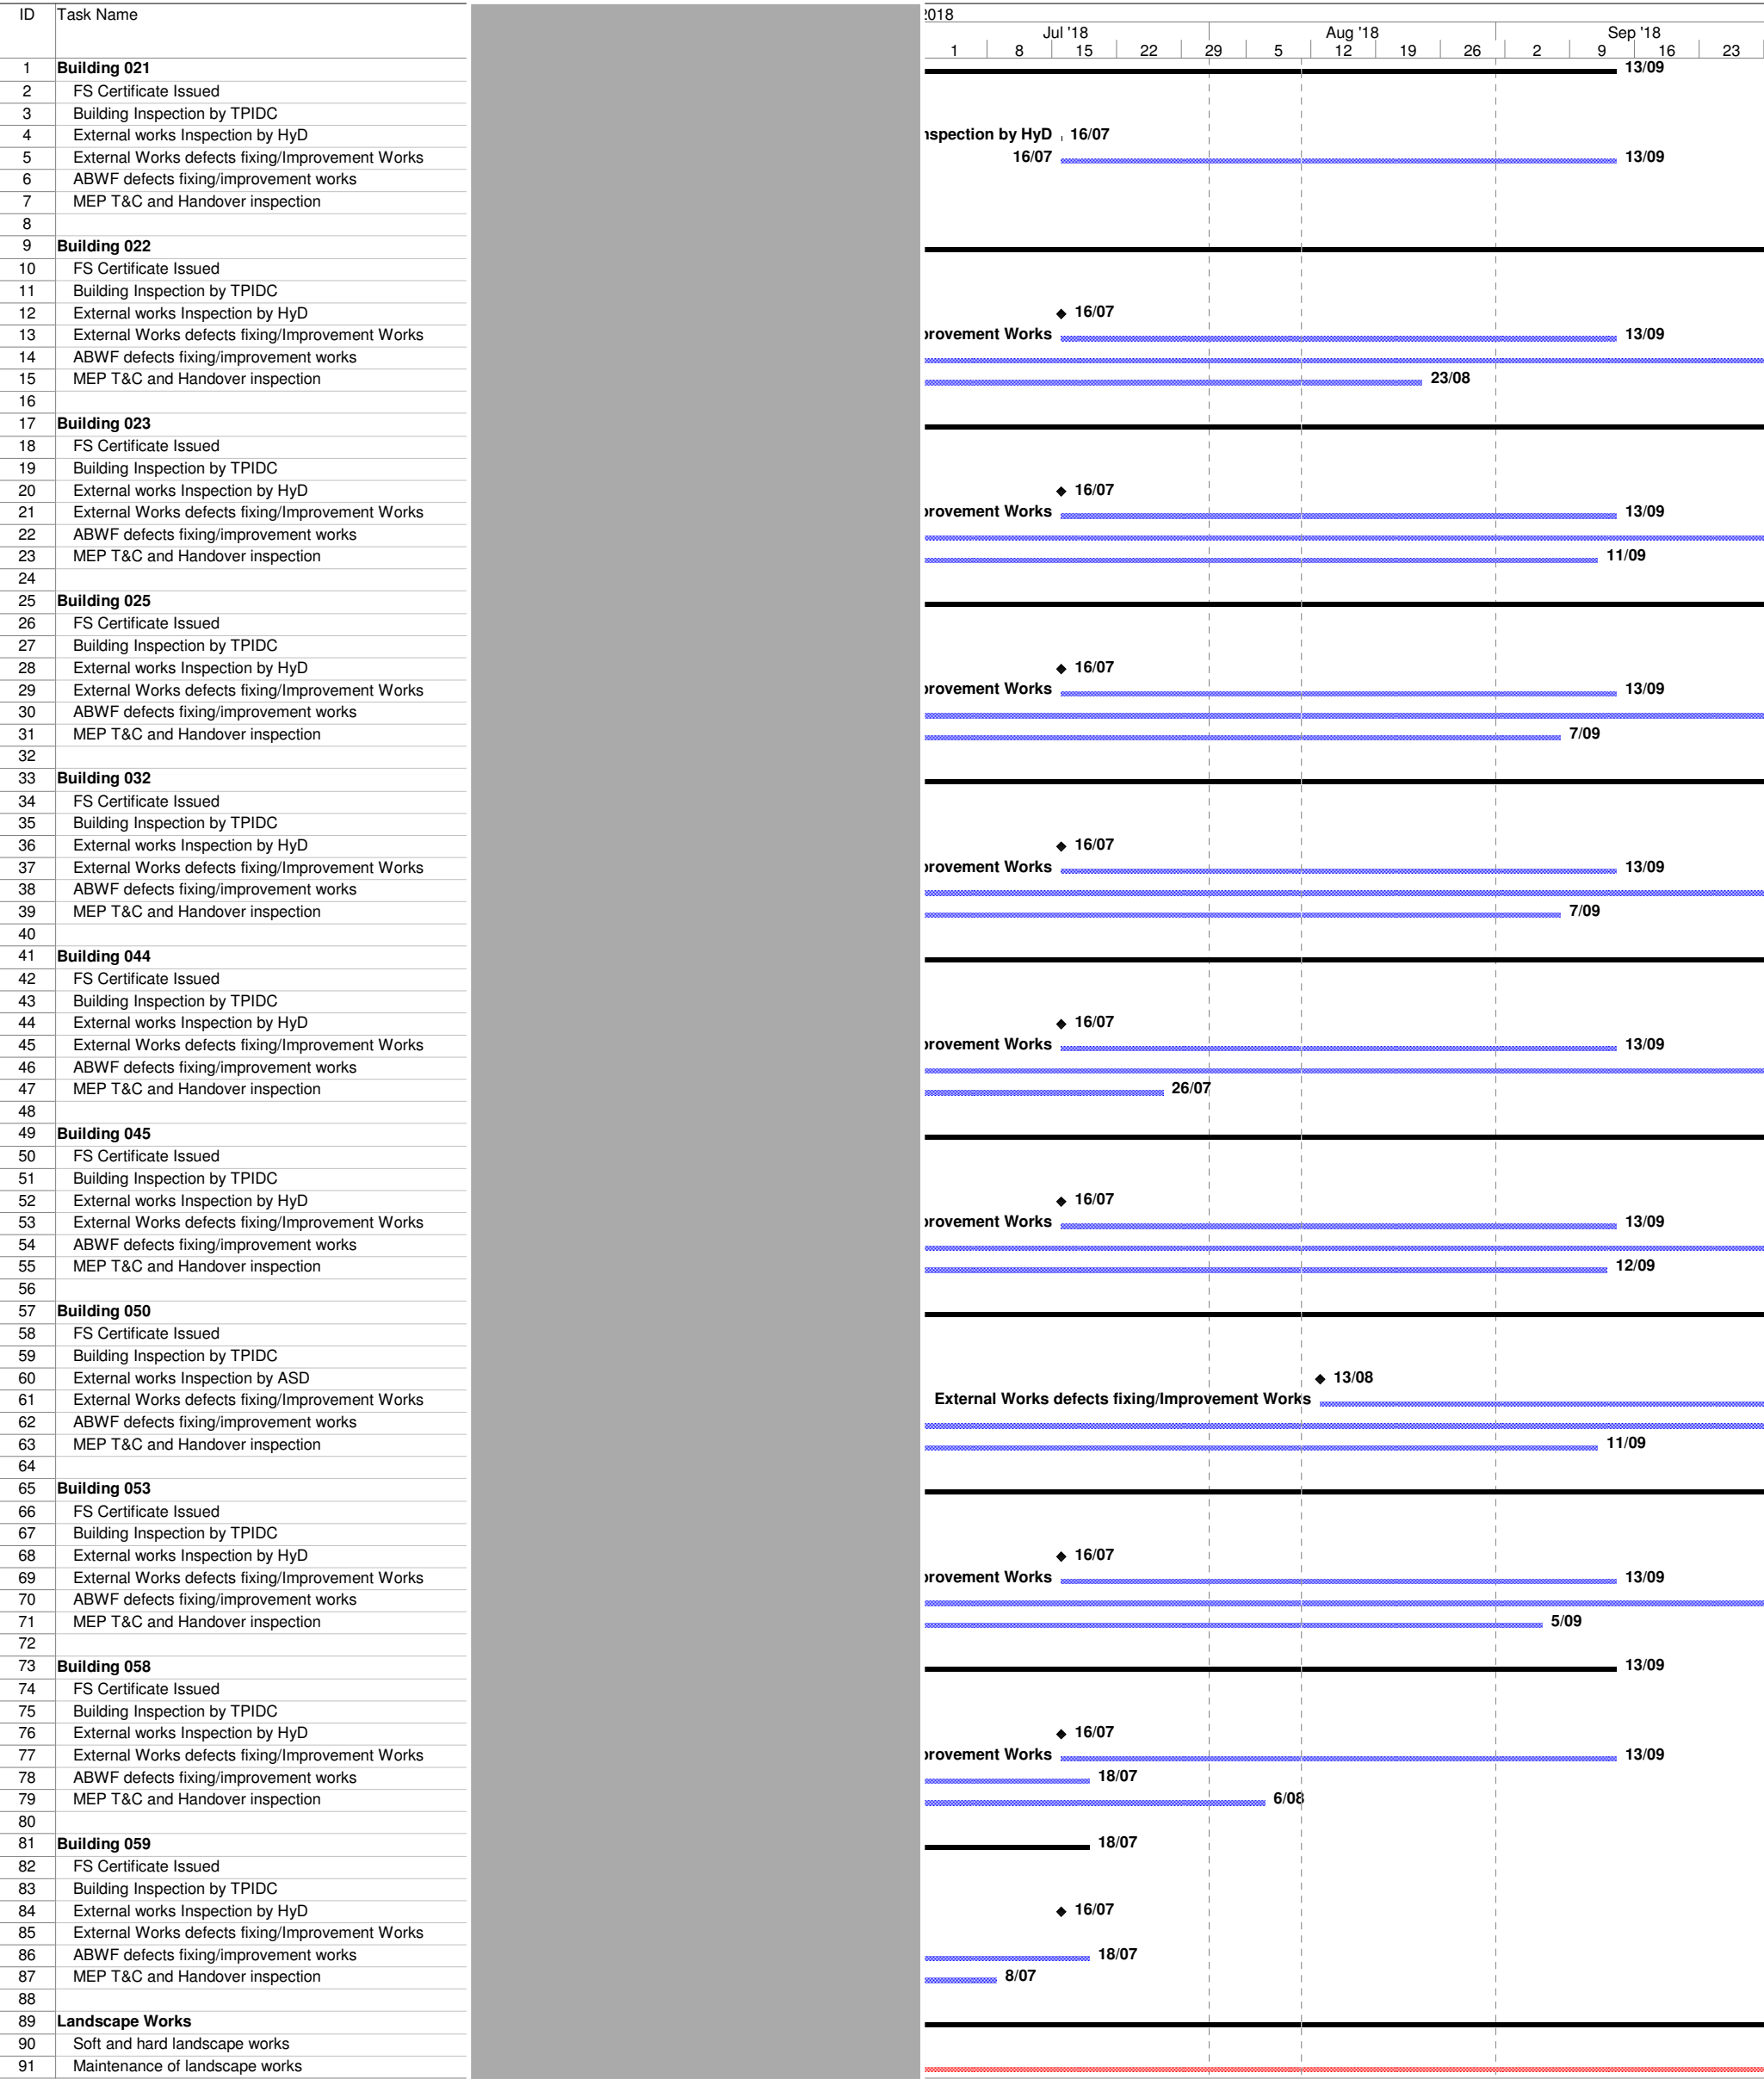

Remark: According to information from RSS, landscape works for Contract No. HY/2014/05 is considered substantially completed as of 23 April 2018. The related certificate (Ref.: BWLM: TTHK: wmy:60313494/C8/M15/905/M0531-2018010932T) dated 13 September 2018 was issued by RSS.

Contract No.: HY/2013/06		Detail Work Programme										Page 1 of 8																					
Activity ID		Activity Name										2015			2016				2017				2018				2019						
												Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3				
📁 Hong Kong-Zhuhai_Macao Bridge Hong Kong Boundary Crossing F																																	
📅 Key Dates																																	
📅 Interface Activities																																	
📅 Site and Facility Inspection																																	
📄 JS1200	Pre Site and Facility Inspection by Contractor at Location 4 - Deg2																																
📄 JS1210	Joint Site and Facility Inspection with Interface Contractor at Location 4 - Deg2																																
📄 JS1620	Pre Site and Facility Inspection by Contractor at Location 14 - Deg2																																
📄 JS1630	Joint Site and Facility Inspection with Interface Contractor at Location 14 - Deg2																																
📄 JS1760	Pre Site and Facility Inspection by Contractor at Location 18 - Deg1																																
📄 JS1770	Joint Site and Facility Inspection with Interface Contractor at Location 18 - Deg1																																
📄 JS1780	Pre Site and Facility Inspection by Contractor at Location 18 - Deg2																																
📄 JS1790	Joint Site and Facility Inspection with Interface Contractor at Location 18 - Deg2																																
📅 Access Dates																																	
📄 AD1000	Location 1(PCB (001) Basement)-Deg1 (270d)																																
📄 AD1010	Location 1(PCB (001) Basement)-Deg2 (380d)																																
📄 AD1020	Location 1(PCB (001) ELV Room (Grid Line E3))-Deg1 (270d)																																
📄 AD1030	Location 1(PCB (001) ELV Room (Grid Line E3))-Deg2 (380d)																																
📄 AD1040	Location 2(PCB (001) First Floor Main Server Room)-Deg1 (330d)																																
📄 AD1050	Location 2(PCB (001) First Floor Main Server Room)-Deg2 (380d)																																
📄 AD1060	Location 2(PCB (001) First Floor Main Server Room) - For Server Installation - Deg2 (330d)																																
📄 AD1070	Location 2(PCB (001) Ground Floor ELV Room (Grid Line E3)) - Deg1 (330d)																																
📄 AD1080	Location 2(PCB (001) Ground Floor DOH Port Health Control Room (Grid Line BD5)) - Deg1 (330d)																																
📄 AD1090	Location 2(PCB (001) Ground Floor DOH Port Health Control Room (Grid Line BD5)) - Deg2 (380d)																																
📄 AD1130	Location 3(Inbd Cargo Exam Bldg (037) Platform Control Room)-Deg2 (500d)																																
📄 AD1150	Location 3(Inbd Cargo Exam Bldg (037) Inspector Offices 128,129,130,131,128,129,140)-Deg2 (500d)																																
📄 AD1170	Location 3a(Inbd Cargo Exam Bldg (037) ROCARS Room)-Deg2 (480d)																																
📄 AD1190	Location 3a(Inbd Cargo Exam Bldg (037) Main Server Room)-Deg2 (480d)																																
📄 AD1200	Location 3a(Inbd Cargo Exam Bldg (037) Main Server Room) - For Server installation - Deg2 (480d)																																
📄 AD1220	Location 4(Outbd Cargo Exam Bldg (023))-Deg2 (680d)																																
📄 AD1240	Location 4a(Outbd Cargo Exam Bldg (023))-Deg2 (630d)																																
📄 AD1270	Location 6(Common Utility Enclosure & Staff Subway)-Deg1 (400d)																																
📄 AD1290	Location 7(Common Utility Enclosure & Staff Subway)-Deg1 (270d)																																
📄 AD1300	Location 8(Inbd Private Car Annex (025))-Deg1 (430d)																																
📄 AD1310	Location 8(Inbd Private Car Annex (025))-Deg2 (580d)																																
📄 AD1320	Location 8(Inbd Private Car Annex (025) Canopy)-Deg1 (430d)																																
📄 AD1330	Location 8(Inbd Private Car Annex (025) Canopy)-Deg2 (580d)																																
📄 AD1340	Location 9(Outbd Private Car Annex (032))-Deg1 (520d)																																
📄 AD1350	Location 9(Outbd Private Car Annex (032))-Deg2 (660d)																																
📄 AD1360	Location 9(Outbd Private Car Annex (032) Canopy)-Deg1 (520d)																																
📄 AD1370	Location 9(Outbd Private Car Annex (032) Canopy)-Deg2 (660d)																																
📄 AD1501	Location 12(Inbd Private Car Kiosks(027))-Deg1 (400d) Phase 2																																
📄 AD1510	Location 12(Inbd Private Car Kiosks(027))-Deg2 (480d) Phase 1																																
📄 AD1511	Location 12(Inbd Private Car Kiosks(027))-Deg2 (480d) Phase 2																																
📄 AD1521	Location 12(Inbd Private Car Kiosks(027) Canopy)-Deg1 (400d) Phase 2																																
Programme No.: HZMB-DWP		Actual Level of Effort Primary Baseline Actual Work Remaining Work Critical Remaining Work Baseline Milestone Milestone										Hong Kong-Zhuhai-Macao Bridge Hong Kong Boundary Crossing Facilities - Automatic Vehicle Clearance Support System (AVCSS)																					
Data Date: 14-Aug-15																																	
																						Date Revision Checked Approved											
																						14-Nov-16 Rev.: 0 WC LC											
																						10-Mar-17 Rev.: 1.0a WC LC											
																						5-May-17 Rev.: 1.0b WC LC											

Contract No.: HY/2013/06			Detail Work Programme			Page 3 of 8																
Activity ID		Activity Name		2015			2016				2017				2018				2019			
		Q2		Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3						
		Detailed Design Specification																				
		Contruction Design and Management																				
		Supply/Manufacture Mock-up items																				
		Supply/Manufacture prototypes																				
		Software Design, Coding and Testing																				
		Coding																				
		Software System Inetgration																				
		Prototype & Software Simulation Tests																				
		Procurement - Phase 1 / Section I																				
		Supply/Manufacture products for FAT																				
		Factory Acceptance Test (FAT)																				
		Supply/Manufacture Equipment																				
		Delivery and Bench Acceptance Test for Phase 1/ Section I																				
		Installation - Phase 1 / Section I																				
		Location 1(PCB (001) Basement)																				
		EM1920 L1(001)B/F - Cable Laying and termination at Location 1 and Location 2																				
		Location 1(PCB (001) ELV Room (Grid Line E3))																				
		EM1940 L1(001)ELV Rm - Cable Laying and termination at Location 1 and Location 2																				
		Location 2(PCB (001) Ground Floor ELV Room (Grid Line E3))																				
		EM1960 L2(001)ELV Rm - Cable Laying and termination at Location 1 and Location 2																				
		Location 2(PCB (001) Ground Floor DOH Port Health Control Room (Grid Line BD5))																				
		EM1080 L2(001)Heath Ctrl Rm - Cable Laying and termination at Location 1 and Location 2																				
		EM1100 L2(001)Heath Ctrl Rm - Cable Splicing and Testing and Labeling																				
		EM1120 L2(001)Health Ctrl Rm - Intercom and PA system Installation																				
		EM1140 L2(001)Heath Ctrl Rm - Intercom and PA system tuning																				
		Location 2(PCB (001) First Floor Main Server Room)																				
		EM1000 L2(001)Main Server Rm - Cable Laying and termination at Location 1 and Location 2																				
		EM1020 L2(001)Main Server Rm - Cable Splicing and Testing and Labeling																				
		EM1040 L2(001)Main Server Rm - AVCSS Network and Server Installation																				
		EM1060 L2(001)Main Server Rm - AVCSS Network and Server Tuning																				
		Location 3(Inbd Cargo Exam Bldg (037) MDF Room)																				
		Location 3(Inbd Cargo Exam Bldg (037) ELV Room)																				
		Location 3(Inbd Cargo Exam Bldg (037) Inspector Offices 128,129,130,131,128,129,141)																				
		EM2020 L3(037)Inspec Offices - Cable Laying and termination in Location 3 and Location 3a																				
		EM2040 L3(037)Inspec Offices - Cable Splicing and Testing and Labeling																				
		EM2060 L3(037)Inspec Offices - AVCSS SURCON WS and 55" LCD Installation																				
		EM2080 L3(037)Inspec Offices - VTS WS Installation																				
		EM2100 L3(037)Inspec Offices - SURCON and WS Tuning																				
		Location 3(Inbd Cargo Exam Bldg (037) Platform Control Room)																				
		EM1160 L3(037)PLF Ctrl Rm - Cable Laying and termination in Location 3 and Location 3a																				
		EM1180 L3(037)PLF Ctrl Rm - Cable Splicing and Testing and Labeling																				
		EM1200 L3(037)PLF Ctrl Rm - AVCSS SYSCON WS and 55" TV Wall Installation																				
		EM1220 L3(037)PLF Ctrl Rm - AVCSS SYSCON WS Tuning																				
Programme No.: HZMB-DWP		Actual Level of Effort	summary																Date	Revision	Checked	Approved
Data Date: 14-Aug-15		Primary Baseline																	14-Nov-16	Rev.: 0	WC	LC
		Actual Work																	10-Mar-17	Rev.: 1.0a	WC	LC
		Remaining Work																	5-May-17	Rev.: 1.0b	WC	LC
		Critical Remaining Work																				
		Baseline Milestone																				
		Milestone																				

Contract No.: HY/2013/06		Detail Work Programme										Page 8 of 8											
Activity ID	Activity Name		2015			2016				2017				2018				2019					
			Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3			
	 Site Acceptance Test (Phase 2 / Section III)																						
	 Operability Period Test (Phase 2 / Section III)																						
	 Completion (Phase 2 / Section III)																						
	 Operation (Phase 2 / Section III)																						
	 Defect Liability Period (DLP)																						
	 Document Submission (Phase 2 / Section III)																						
Programme No.: HZMB-DWP Data Date: 14-Aug-15		Actual Level of Effort Primary Baseline Actual Work Remaining Work Critical Remaining Work Baseline Milestone Milestone summary	Hong Kong-Zhuhai-Macao Bridge Hong Kong Boundary Crossing Facilities - Automatic Vehicle Clearance Support System (AVCSS)									Date 14-Nov-16 10-Mar-17 5-May-17	Revision Rev.: 0 Rev.: 1.0a Rev.: 1.0b	Checked WC WC WC	Approved LC LC LC								
