

Activity ID	Activity Name	Orig. Durn.	Act. Start / FC Early Start	Duration % Complete	Rem. Durn.	Act. Finish / FC Early Finish	Late Start	Late Finish	Total Float	Free Float	Physical % Complete	2015																					
												July				August				September				October									
												22	29	06	13	20	27	03	10	17	24	31	07	14	21	28	05	12	19				
HY/2012/07 - TM-CLK Link-SC [DWP rE1] - Status Update 21-07-2015																																	
Contract Key Dates																																	
Possession Dates / Access Period																																	
POS02	Portion A (Commencement of Works+499 days)	0	21-Jul-15*	0%	0		03-Jun-15		-48	0	0%																						
POS03	Portion B (Commencement of Works+619 days)	0	21-Jul-15*	0%	0		03-Jun-15		-48	0	0%																						
Section Completion Dates																																	
Vacate Works Area																																	
VAC05	Vacate Works Area WA5 (Zone 5C) (Commencement of Works+758 days)	0		0%	0	21-Jul-15*		19-Jul-15	-1	1227	0%																						
General Submissions																																	
General Requirements																																	
Temporary Works Design																																	
PR00130	Unloading Jetty at HKBCF - Working Platform design and approval	90	02-Jun-14 A	60%	36	31-Aug-15	14-May-15	26-Jun-15	-55	963	10%																						
Land Works																																	
PR00160	Propose/submit a performance review for piled fnds in accordance w/ ETW	101	26-May-14 A	80.2%	20	12-Aug-15	13-Jan-16	04-Feb-16	145	363	80%																						
Land GI Works																																	
PR02204	SQR Sampling & Testing and Approval	110	14-Aug-14 A	68.18%	35	29-Aug-15	24-Sep-14	05-Nov-14	-241	0	68%																						
PR03110	Trial Pits along Cheung Tung Road	20	21-Oct-13 A	90%	2	22-Jul-15	04-Nov-14	05-Nov-14	-208	33	85%																						
Design Submissions																																	
Detailed Design (v18.8 18-08-14)																																	
General Submissions																																	
ARDD0042-2	IC/SO Approval of O&M Facility Provisions DDA - BP11.01	75	14-Jan-15 A	40%	45	21-Sep-15	21-Aug-15	22-Oct-15	23	0	50%																						
ARDD0037-1	Preparation of Seismic Performance Report Viaduct A,B,C,D - AP12.01	20	21-Jul-15	0%	20	17-Aug-15	25-Sep-15	22-Oct-15	48	0	0%																						
ARDD0037-4	Preparation of Seismic Performance Report Viaduct E - AP12.02	20	21-Jul-15	0%	20	17-Aug-15	25-Sep-15	22-Oct-15	48	0	0%																						
ARDD0037-7	Preparation of Seismic Performance Report Viaduct F - AP12.03	20	21-Jul-15	0%	20	17-Aug-15	25-Sep-15	22-Oct-15	48	0	0%																						
ARDD0042-4	IC/SO Approval of O&M Facility Provisions DDA - BP11.01	0		0%	0	21-Sep-15		22-Oct-15	23	65	0%																						
ARDD0037-2	IC/SO Approval of Seismic Performance Report Viaduct A,B,C,D - AP12.01	75	18-Aug-15	0%	75	30-Nov-15	23-Oct-15	04-Feb-16	48	241	0%																						
ARDD0037-5	IC/SO Approval of Seismic Performance Report Viaduct E - AP12.02	75	18-Aug-15	0%	75	30-Nov-15	23-Oct-15	04-Feb-16	48	0	0%																						
ARDD0037-8	IC/SO Approval of Seismic Performance Report Viaduct F - AP12.03	75	18-Aug-15	0%	75	30-Nov-15	23-Oct-15	04-Feb-16	48	0	0%																						
Viaduct E5 and E6																																	
Viaduct Design																																	
Viaduct E5 E6 Superstructure Optimisation																																	
TGP0550	Viaduct E5 & E6 - Preparation of Optimised Movement Joint Schedule	15	03-Feb-15 A	70%	5	27-Jul-15	30-Nov-15	04-Dec-15	95	80	70%																						
Viaduct E7 & E8																																	
Viaduct Design																																	
Viaduct E7 E8 Superstructure Optimisation																																	
TGP0750	Viaduct E7 & E8 - Preparation of Optimised Movement Joint Schedule	15	03-Feb-15 A	70%	5	27-Jul-15	30-Nov-15	04-Dec-15	95	80	70%																						
Viaduct D																																	
Viaduct Design																																	
ARDD0333-8	Viaduct D - IC/SO Consent of Supplemental Working Drawings Viaduct D	10	28-Apr-15 A	80%	2	22-Jul-15	13-Nov-14	14-Nov-14	-178	0	80%																						
ARDD0333-9	Viaduct D - IC/SO Consent of Supplemental Working Drawings Viaduct D	0		0%	0	22-Jul-15		14-Nov-14	-178	0	0%																						
Viaduct C																																	
Viaduct Design																																	
ARDD0384-6	Viaduct C - Preparation and Coordination of Working Drawing Set	10	22-Apr-15 A	80%	2	22-Jul-15	26-Feb-15	27-Feb-15	-103	0	100%																						
ARDD0384-7	Viaduct C - Submission of Working DDA Drawings for Viaduct C DP13.03	0		0%	0	22-Jul-15		27-Mar-15	-83	38	0%																						
ARDD0384-8	Viaduct C - IC/SO Consent of Supplemental Working Drawings Viaduct C	10	15-Sep-15	0%	10	28-Sep-15	30-Mar-15	10-Apr-15	-121	0	0%																						
ARDD0384-9	Viaduct C - IC/SO Consent of Supplemental Working Drawings Viaduct C	0		0%	0	28-Sep-15		10-Apr-15	-121	1	0%																						
ARDD0384-3	Viaduct C - Coordination and Further Issue of Construction Method and Te	60	02-Mar-15 A	25%	45	21-Sep-15	27-Sep-18	28-Nov-18	832	0	0%																						
ARDD0384-5	Viaduct C - GCL/FRE Final Coordinated Construction Method/Temporary \	0		0%	0	21-Sep-15		28-Nov-18	832	832	0%																						
Associated Construction Milestones																																	
ARDD0414	Viaduct C - DDA approval ready for Initial Segment Casting	0	29-Sep-15	0%	0		10-Apr-15		-172	0	0%																						
ARDD0413	Viaduct C - DDA approval ready for Commencement of Pilecaps C1-C17	0	21-Jul-15	0%	0		28-Nov-18		1227	1227	0%																						

<ul style="list-style-type: none"> ■ Actual Work ■ Planned Bar ■ Critical Bar ◆ Milestone 	Project ID: J3518DWP rE1-M26 Layout: J3518-DWP-3MRP Submission - M26 Filter: TASK filters: 3-Month Lookahead, No CC Milestones, No Level of Effort.	Tuen Mun - Chek Lap Kok Link - Southern Connection 3-Month Rolling Programme (Page 1 of 40 Pages) (Progress as of 21-July-15)	<table border="1"> <thead> <tr> <th>Date</th> <th>Revision</th> <th>Checked</th> <th>Approved</th> </tr> </thead> <tbody> <tr> <td>29-May-...</td> <td></td> <td>WY</td> <td></td> </tr> <tr> <td>02-Jul-15</td> <td></td> <td>HF</td> <td>KWY</td> </tr> <tr> <td>28-Jul-15</td> <td></td> <td>PKN</td> <td>KWY</td> </tr> </tbody> </table>	Date	Revision	Checked	Approved	29-May-...		WY		02-Jul-15		HF	KWY	28-Jul-15		PKN	KWY	DWG. No.: J3518/GCL/PGM/3MRP-M26
Date	Revision	Checked	Approved																	
29-May-...		WY																		
02-Jul-15		HF	KWY																	
28-Jul-15		PKN	KWY																	

Activity ID	Activity Name	Orig. Durn.	Act. Start / FC Early Start	Duration % Complete	Rem. Durn.	Act. Finish / FC Early Finish	Late Start	Late Finish	Total Float	Free Float	Physical % Complete	2015																					
												July				August				September				October									
												22	29	06	13	20	27	03	10	17	24	31	07	14	21	28	05	12	19				
Viaduct A																																	
Viaduct Design																																	
ARDD0435-4	Viaduct A - Preparation of Draft DDA Working Drawing Set	60	01-Jun-15 A	20%	48	24-Sep-15	07-Dec-15	10-Feb-16	99	0	20%	[Gantt bar: 01-Jun-15 to 24-Sep-15]																					
ARDD0435-3	Viaduct A - Coordination and Further Issue of Construction Method and Ter	60	01-Jun-15 A	50%	30	31-Aug-15	31-Dec-15	10-Feb-16	117	18	50%	[Gantt bar: 01-Jun-15 to 31-Aug-15]																					
ARDD0435-5	Viaduct A - GCL/FRE Final Coordinated Construction Method/Temporary V	0		0%	0	24-Sep-15		10-Feb-16	99	0	0%	[Milestone: 24-Sep-15]																					
ARDD0435-6	Viaduct A - Preparation and Coordination of Working Drawing Set	10	25-Sep-15	0%	10	08-Oct-15	11-Feb-16	24-Feb-16	99	0	0%	[Gantt bar: 25-Sep-15 to 08-Oct-15]																					
ARDD0435	Viaduct A - IC/SO Approval of DDA DP11.03	75	23-Feb-15 A	80%	15	10-Sep-15	23-Feb-16	14-Mar-16	132	0	80%	[Gantt bar: 23-Feb-15 to 10-Sep-15]																					
ARDD0435-1	Viaduct A - IC/SO Approval of DDA DP11.03	0		0%	0	10-Sep-15		14-Mar-16	132	0	0%	[Milestone: 10-Sep-15]																					
ARDD0435-7	Viaduct A - Submission of Working Drawings for Viaduct A DP11.03	0		0%	0	08-Oct-15		13-Apr-16	134	0	0%	[Milestone: 08-Oct-15]																					
ARDD0435-8	Viaduct A - IC/SO Consent of Supplemental Working Drawings Viaduct A	10	09-Oct-15	0%	10	22-Oct-15	14-Apr-16	27-Apr-16	134	0	0%	[Gantt bar: 09-Oct-15 to 22-Oct-15]																					
ARDD0435-2	Viaduct A - GCL/FRE Issue of Construction Method/Temporary Work Data	0		0%	0	21-Jul-15		28-Nov-18	877	877	0%	[Milestone: 21-Jul-15]																					
ARDD0434-1	Viaduct A - Earliest IC Certificate for DDA DP11.02, DP11.03	0		100%	0	15-Jul-15 A					100%	[Milestone: 15-Jul-15]																					
ARDD0433-1	Viaduct A - Review and Update of Draft DDA Rev A1 - DP11.03	15	19-Feb-15 A	100%	0	15-Jul-15 A					100%	[Gantt bar: 19-Feb-15 to 15-Jul-15]																					
Viaduct F1 & F3																																	
Viaduct Design																																	
ARDD0486-2	Viaduct F1 & F3 - Coordination and Further Issue of Construction Method :	60	02-Mar-15 A	25%	45	21-Sep-15	03-Dec-14	03-Feb-15	-164	0	0%	[Gantt bar: 02-Mar-15 to 21-Sep-15]																					
ARDD0486-3	Viaduct F1 & F3 - Preparation of Draft Working Drawing Set	60	02-Mar-15 A	25%	45	21-Sep-15	03-Dec-14	03-Feb-15	-164	0	0%	[Gantt bar: 02-Mar-15 to 21-Sep-15]																					
ARDD0486-4	Viaduct F1 & F3 - GCL/FRE Final Coordinated Construction Method/Temp	0		0%	0	21-Sep-15		03-Feb-15	-164	0	0%	[Milestone: 21-Sep-15]																					
ARDD0486-5	Viaduct F1 & F3 - Preparation and Coordination of DDA/Working Drawing	10	22-Sep-15	0%	10	05-Oct-15	04-Feb-15	17-Feb-15	-164	0	0%	[Gantt bar: 22-Sep-15 to 05-Oct-15]																					
ARDD0486-6	Viaduct F1 & F3 - Submission of Working DDA Drawings Viaduct F1,F3 DF	0		0%	0	05-Oct-15		10-Jul-15	-61	0	0%	[Milestone: 05-Oct-15]																					
ARDD0486-	Viaduct F1 & F3 - IC/SO Consent of Supplemental Working Drawings Viad	10	06-Oct-15	0%	10	19-Oct-15	13-Jul-15	24-Jul-15	-61	5	0%	[Gantt bar: 06-Oct-15 to 19-Oct-15]																					
ARDD0485	Viaduct F1 & F3 - IC/SO Approval of DDA - DP16.02, (16.03, 16.08, 16.09	75	25-Nov-14 A	100%	0	15-Jul-15 A					100%	[Gantt bar: 25-Nov-14 to 15-Jul-15]																					
Viaduct F2, F4 and F5																																	
Viaduct Design																																	
ARDD0530-2	Viaduct F2, F4 & F5 - GCL/FRE Issue of Construction Method/Temporary	0		0%	0	21-Jul-15		11-Nov-14	-179	0	0%	[Milestone: 21-Jul-15]																					
ARDD0530-3	Viaduct F2, F4 & F5 - Coordination and Further Issue of Construction Meth	60	21-Jul-15	0%	60	12-Oct-15	12-Nov-14	03-Feb-15	-179	0	0%	[Gantt bar: 21-Jul-15 to 12-Oct-15]																					
ARDD0530-4	Viaduct F2, F4 & F5 - Preparation of Draft Working Drawing Set	60	21-Jul-15	0%	60	12-Oct-15	12-Nov-14	03-Feb-15	-179	0	0%	[Gantt bar: 21-Jul-15 to 12-Oct-15]																					
ARDD0530-5	Viaduct F2, F4 & F5 - GCL/FRE Final Coordination Construction Method/T	0		0%	0	12-Oct-15		03-Feb-15	-179	0	0%	[Milestone: 12-Oct-15]																					
ARDD0530-6	Viaduct F2, F4 & F5 - Preparation and Coordination of DDA/Working Draw	10	13-Oct-15	0%	10	26-Oct-15	04-Feb-15	17-Feb-15	-179	0	0%	[Gantt bar: 13-Oct-15 to 26-Oct-15]																					
ARDD0529	Viaduct F2, F4 & F5 - IC/SO Approval of DDA - DP(16.05, 06, 11, 12, 14, '	75	25-Nov-14 A	100%	0	15-Jul-15 A					100%	[Gantt bar: 25-Nov-14 to 15-Jul-15]																					
Parapet and Utility Trough																																	
ARDD0562-4	IC/SO Approval of DDA -DP30.01	75	31-Jul-14 A	90.67%	7	29-Jul-15	05-Feb-15	13-Feb-15	-118	0	90%	[Gantt bar: 31-Jul-14 to 29-Jul-15]																					
ARDD0562-5	IC/SO Approval of DDA -DP30.01	0		0%	0	29-Jul-15		13-Feb-15	-118	0	0%	[Milestone: 29-Jul-15]																					
ARDD0566	IC/SO Approval of DDA -DP31.01	75	24-Oct-14 A	80%	15	10-Aug-15	04-Sep-15	24-Sep-15	33	0	80%	[Gantt bar: 24-Oct-14 to 10-Aug-15]																					
ARDD0566-1	IC/SO Approval of DDA -DP31.01	0		0%	0	10-Aug-15		24-Sep-15	33	124	0%	[Milestone: 10-Aug-15]																					
Slopeworks for Viaduct B: 9SE- B/C8, B/C9, B/F9, B/F85+ 10SW-A/F52, A/F53																																	
ARDD0580-5	Preparation of Slope A/F52 Submission - CP12.03	20	10-Feb-15 A	50%	10	03-Aug-15	13-Apr-15	24-Apr-15	-71	0	50%	[Gantt bar: 10-Feb-15 to 03-Aug-15]																					
ARDD0580-6	IC/SO Approval of Slope - CP12.03	75	04-Aug-15	0%	75	16-Nov-15	27-Apr-15	07-Aug-15	-71	0	0%	[Gantt bar: 04-Aug-15 to 16-Nov-15]																					
Slopeworks for Viaduct C: 10NW -C/C22, C/C26, C/C27, C/F13, C/F14, C/F15																																	
ARDD0588-2	IC/SO Approval of Combined AIP/DDA -CP13.02	75	25-Feb-15 A	90%	8	30-Jul-15	08-Jul-16	19-Jul-16	254	0	90%	[Gantt bar: 25-Feb-15 to 30-Jul-15]																					
ARDD0588-3	IC/SO Approval of Combined AIP/DDA -CP13.02	0		0%	0	30-Jul-15		19-Jul-16	254	101	0%	[Milestone: 30-Jul-15]																					
Slopeworks for Viaduct D: 10NW -C/R4, C/F9, C/F10, C/F11, C/F17, C/F50																																	
ARDD0603	IC/SO Approval of Slope Combined AIP/DDA -CP14.01	75	16-Dec-14 A	90%	8	30-Jul-15	26-May-15	04-Jun-15	-40	0	90%	[Gantt bar: 16-Dec-14 to 30-Jul-15]																					
ARDD0603-1	IC/SO Approval of Slope Combined AIP/DDA -CP14.01	0		0%	0	30-Jul-15		04-Jun-15	-40	1	0%	[Milestone: 30-Jul-15]																					
ARDD0604-2	IC/SO Approval of Slope Combined AIP/DDA -CP14.02	75	18-May-15 A	50%	38	10-Sep-15	18-Aug-15	08-Oct-15	21	0	50%	[Gantt bar: 18-May-15 to 10-Sep-15]																					
ARDD0604-3	IC/SO Approval of Revised Slope Combined AIP/DDA -CP14.02	0		0%	0	10-Sep-15		08-Oct-15	21	61	0%	[Milestone: 10-Sep-15]																					
Waterworks, Drainage & Utility Diversions																																	
ARDD0629	IC/SO Approval of Waterworks, Drainage & Utility DDA - BP20.01	75	22-Jul-14 A	90%	8	30-Jul-15	16-Jun-15	25-Jun-15	-25	0	90%	[Gantt bar: 22-Jul-14 to 30-Jul-15]																					
ARDD0629-2	Gov't Approval of Submissions for Waterworks, Drainage & Utility Diversior	75	02-Jan-14 A	90.67%	7	29-Jul-15	17-Jun-15	25-Jun-15	-24	1	90%	[Gantt bar: 02-Jan-14 to 29-Jul-15]																					
ARDD0629-1	IC/SO Approval of Waterworks, Drainage & Utility DDA - BP20.01	0		0%	0	30-Jul-15		25-Jun-15	-25	0	0%	[Milestone: 30-Jul-15]																					
Viaduct Approach Ramp Retaining Walls																																	
Approach Ramp D																																	

<ul style="list-style-type: none"> █ Actual Work █ Planned Bar █ Critical Bar ◆ Milestone 	Project ID: J3518DWPRe1-M26 Layout: J3518-DWP-3MRP Submission - M26 Filter: TASK filters: 3-Month Lookahead, No CC Milestones, No Level of Effort.	Tuen Mun - Chek Lap Kok Link - Southern Connection 3-Month Rolling Programme (Page 2 of 40 Pages) (Progress as of 21-July-15)	<table border="1"> <tr> <th>Date</th> <th>Revision</th> <th>Checked</th> <th>Approved</th> </tr> <tr> <td>29-May-...</td> <td></td> <td>WY</td> <td></td> </tr> <tr> <td>02-Jul-15</td> <td></td> <td>HF</td> <td>KWY</td> </tr> <tr> <td>28-Jul-15</td> <td></td> <td>PKN</td> <td>KWY</td> </tr> </table>	Date	Revision	Checked	Approved	29-May-...		WY		02-Jul-15		HF	KWY	28-Jul-15		PKN	KWY	DWG. No.: J3518/GCL/PGM/3MRP-M26
Date	Revision	Checked	Approved																	
29-May-...		WY																		
02-Jul-15		HF	KWY																	
28-Jul-15		PKN	KWY																	

Activity ID	Activity Name	Orig. Durn.	Act. Start / FC Early Start	Duration % Complete	Rem. Durn.	Act. Finish / FC Early Finish	Late Start	Late Finish	Total Float	Free Float	Physical % Complete	2015																	
												July				August				September				October					
												22	29	06	13	20	27	03	10	17	24	31	07	14	21	28	05	12	19
ARDD0752	Viaduct F - Erection Sequence Analysis	30	21-Jul-15	0%	30	31-Aug-15	12-Nov-14	23-Dec-14	-179	0	0%	[Gantt Bar]																	
ARDD0753	Viaduct F - Target Geometry Analysis	30	01-Sep-15	0%	30	12-Oct-15	24-Dec-14	03-Feb-15	-179	0	0%	[Gantt Bar]																	
ARDD0754	Viaduct F - Segment Geometry Schedules	10	13-Oct-15	0%	10	26-Oct-15	04-Feb-15	17-Feb-15	-179	0	0%	[Gantt Bar]																	
Major Procurement																													
Marine Permanent Navigaion Aids																													
PR65011	Design & Approvals for Marine Navigation Aids	150	23-Oct-13 A	70%	45	10-Sep-15	10-Jun-15	03-Aug-15	-33	0	55%	[Gantt Bar]																	
PR65012	Procure & Deliver Marine Navigation Aids	240	11-Sep-15	0%	240	06-Jul-16	04-Aug-15	26-May-16	-33	0	0%	[Gantt Bar]																	
Tower Cranes																													
PR66011	Procure & Deliver Tower Cranes	236	03-Oct-14 A	21.61%	185	02-Mar-16	12-Jan-15	27-Aug-15	-152	814	0%	[Gantt Bar]																	
PR66013	Erect & Commission Tower Crane @ E4	12	21-Aug-15	0%	12	03-Sep-15	12-Jan-15	24-Jan-15	-165	0	0%	[Gantt Bar]																	
PR66018	Erect & Commission Tower Crane @ E9	12	03-Aug-15	0%	12	18-Aug-15	28-Mar-15	16-Apr-15	-90	0	0%	[Gantt Bar]																	
PR66023	Erect & Commission Tower Crane @ E13-Sth	12	10-Sep-15	0%	12	25-Sep-15	07-May-15	22-May-15	-92	122	0%	[Gantt Bar]																	
PR66019	Erect & Commission Tower Crane @ E10	12	02-Sep-15	0%	12	16-Sep-15	16-May-15	01-Jun-15	-79	0	0%	[Gantt Bar]																	
PR66014	Erect & Commission Tower Crane @ E5	12	18-Sep-15	0%	12	05-Oct-15	24-Jun-15	09-Jul-15	-67	8	0%	[Gantt Bar]																	
PR66021	Erect & Commission Tower Crane @ E12A	12	21-Jul-15	0%	12	04-Aug-15	19-Aug-15	02-Sep-15	23	177	0%	[Gantt Bar]																	
PR66024	Erect & Commission Tower Crane @ E13-Nth	12	03-Aug-15	0%	12	18-Aug-15	03-Dec-15	16-Dec-15	96	191	0%	[Gantt Bar]																	
PR66022	Erect & Commission Tower Crane @ E12B	12	21-Jul-15	0%	12	04-Aug-15	04-Dec-15	17-Dec-15	107	177	0%	[Gantt Bar]																	
Equipment Platforms for Tower Cranes																													
PR66026	Inst.Temp.Eqpt.Platform (piles & deck) @ E4	24	21-Jul-15	0%	24	19-Aug-15	11-Dec-14	10-Jan-15	-165	0	0%	[Gantt Bar]																	
Deck Segment Installation Equipment																													
Launching Gantry 2																													
PR67043	Launching Gantry 2 Fabrication	142	16-Jun-14 A	98.59%	2	22-Jul-15	19-Sep-14	20-Sep-14	-245	0	100%	[Gantt Bar]																	
PR67044	Launching Gantry 2 Delivery	12	23-Jul-15	0%	12	05-Aug-15	22-Sep-14	07-Oct-14	-245	0	0%	[Gantt Bar]																	
Lifting Frames																													
Lifting Frames 1 & 2																													
PR68013	Lifting Frame 1&2 Fabrication	85	24-Jan-15 A	52.94%	40	04-Sep-15	16-Feb-15	10-Apr-15	-122	0	0%	[Gantt Bar]																	
PR68014	Lifting Frame 1&2 Delivery	14	05-Sep-15	0%	14	21-Sep-15	11-Apr-15	27-Apr-15	-122	0	0%	[Gantt Bar]																	
Lifting Frames 3 & 4																													
PR68017	Lifting Frame 3&4 Fabrication	85	29-Sep-14 A	67.06%	28	21-Aug-15	11-Feb-15	18-Mar-15	-126	0	10%	[Gantt Bar]																	
PR68018	Lifting Frame 3&4 Delivery	30	22-Aug-15	0%	30	25-Sep-15	19-Mar-15	27-Apr-15	-126	53	0%	[Gantt Bar]																	
Lifting Frames 5 & 6																													
PR68019	Lifting Frame 5&6 Design	70	21-Jul-15	0%	70	12-Oct-15	15-Nov-14	07-Feb-15	-198	0	0%	[Gantt Bar]																	
PR68020	Lifting Frame 5&6 Approval	60	13-Oct-15	0%	60	22-Dec-15	09-Feb-15	27-Apr-15	-198	0	0%	[Gantt Bar]																	
Unloading Frames																													
Type 1 (at B6 and D6)																													
PR69110	Unloading Frame Type 1 Fabrication	80	23-Feb-15 A	28.75%	57	24-Sep-15	11-Apr-15	18-Jun-15	-82	0	0%	[Gantt Bar]																	
PR69120	Unloading Frame Type 1 Delivery (UF-1A & UF-1B)	24	25-Sep-15	0%	24	26-Oct-15	19-Jun-15	18-Jul-15	-82	0	0%	[Gantt Bar]																	
Type 2 (at Bridge E1)																													
PR69170	Unloading Frame Type 2 Design	50	21-Jul-15	0%	50	16-Sep-15	18-Aug-15	16-Oct-15	24	0	0%	[Gantt Bar]																	
PR69180	Unloading Frame Type 2 Fabrication	80	25-Aug-15	0%	80	28-Nov-15	22-Sep-15	29-Dec-15	24	0	0%	[Gantt Bar]																	
Deck Segments & Precast Pile Cap Shells																													
Preliminaries																													
MBBE0054	Precast Segment Mould Design (Viaduct F1 to F5)	42	21-Jul-15	0%	42	07-Sep-15	19-Jun-15	08-Aug-15	-25	0	0%	[Gantt Bar]																	
MBBE0056	Precast Segment Mould Fabrication & Erection (Viaduct F1 to F5)	52	01-Aug-15	0%	52	02-Oct-15	03-Jul-15	01-Sep-15	-25	63	0%	[Gantt Bar]																	
MBBE0050	Precast Segment Mould Fabrication & Erection (Viaduct A)	52	24-Dec-14 A	98.08%	1	21-Jul-15	03-Mar-16	03-Mar-16	185	0	100%	[Gantt Bar]																	
Viaduct B																													
Precast Deck Segments																													
MBBE130-1	B: Progressive Match Cast Segment Manufacture & Delivery remaining seq	598	24-Oct-14 A	23.91%	455	27-Jan-17	31-Oct-14	17-May-16	-211	1	10.48%	[Gantt Bar]																	
Viaduct E																													
Precast Pile Caps																													
Viaduct E2																													
PP7260	Production of Viaduct E2 Marine Precast Pile Cap Shells	80	12-Nov-14 A	0%	85	30-Oct-15	13-Jun-15	22-Sep-15	-30	914	33%	[Gantt Bar]																	

■ Actual Work
■ Planned Bar
■ Critical Bar
◆ Milestone

Project ID: J3518DWPrE1-M26
 Layout: J3518-DWP-3MRP Submission - M26
 Filter: TASK filters: 3-Month Lookahead, No CC Milestones, No Level of Effort.

Tuen Mun - Chek Lap Kok Link - Southern Connection
3-Month Rolling Programme (Page 4 of 40 Pages)
(Progress as of 21-July-15)

Date	Revision	Checked	Approved
29-May-...		WY	
02-Jul-15		HF	KWY
28-Jul-15		PKN	KWY

DWG. No.:
J3518/GCL/PGM/3MRP-M26

Activity ID	Activity Name	Orig. Durn.	Act. Start / FC Early Start	Duration % Complete	Rem. Durn.	Act. Finish / FC Early Finish	Late Start	Late Finish	Total Float	Free Float	Physical % Complete	2015																							
												July					August				September				October										
												22	29	06	13	20	27	03	10	17	24	31	07	14	21	28	05	12	19						
Pier B14 (B1f)																																			
Pier Head Segments																																			
SB1F0370	B14 (B1f) - Pier Head Segment - Temporary Platform	6	17-Jun-15 A	90%	1	21-Jul-15	06-May-15	06-May-15	-53	0	90%	[Gantt bar: 06-May-15 to 21-Jul-15, 90% complete]																							
SB1F0372	B14 (B1f) - Pier Head Segment Lift & Fix (1 seg)	2	21-Jul-15	0%	2	23-Jul-15	07-May-15	08-May-15	-53	0	0%	[Gantt bar: 21-Jul-15 to 23-Jul-15, 0% complete]																							
SB1F0374	B14 (B1f) - Pier Head Segment Diaphragm - Rebar	12	23-Jul-15	0%	12	07-Aug-15	09-May-15	26-May-15	-53	0	0%	[Gantt bar: 23-Jul-15 to 07-Aug-15, 0% complete]																							
SB1F0376	B14 (B1f) - Pier Head Segment Diaphragm - Formwork & Prep for Concre	8	07-Aug-15	0%	8	18-Aug-15	27-May-15	05-Jun-15	-53	0	0%	[Gantt bar: 07-Aug-15 to 18-Aug-15, 0% complete]																							
SB1F0378	B14 (B1f) - Pier Head Segment Diaphragm - Concreting	2	18-Aug-15	0%	2	21-Aug-15	06-Jun-15	08-Jun-15	-53	0	0%	[Gantt bar: 18-Aug-15 to 21-Aug-15, 0% complete]																							
SB1F0380	B14 (B1f) - Pier Head Segment Diaphragm - Curing & Striking of Forms	6	21-Aug-15	0%	6	28-Aug-15	10-Jun-15	18-Jun-15	-53	0	0%	[Gantt bar: 21-Aug-15 to 28-Aug-15, 0% complete]																							
Pier B15 (B1e)																																			
Pier Head Segments																																			
SB1E0374	B15 (B1e) - Pier Head Segment Diaphragm - Rebar	12	21-Jul-15	0%	12	04-Aug-15	01-Jun-15	18-Jun-15	-34	0	0%	[Gantt bar: 21-Jul-15 to 04-Aug-15, 0% complete]																							
SB1E0376	B15 (B1e) - Pier Head Segment Diaphragm - Formwork & Prep for Concre	8	05-Aug-15	0%	8	14-Aug-15	19-Jun-15	02-Jul-15	-34	0	0%	[Gantt bar: 05-Aug-15 to 14-Aug-15, 0% complete]																							
SB1E0378	B15 (B1e) - Pier Head Segment Diaphragm - Concreting	2	15-Aug-15	0%	2	17-Aug-15	03-Jul-15	04-Jul-15	-34	0	0%	[Gantt bar: 15-Aug-15 to 17-Aug-15, 0% complete]																							
SB1E0380	B15 (B1e) - Pier Head Segment Diaphragm - Curing & Striking of Forms	6	18-Aug-15	0%	6	25-Aug-15	06-Jul-15	13-Jul-15	-33	0	0%	[Gantt bar: 18-Aug-15 to 25-Aug-15, 0% complete]																							
SB1E0370	B15 (B1e) - Pier Head Segment - Temporary Platform	6	15-Jun-15 A	100%	0	25-Jun-15 A					100%	[Gantt bar: 15-Jun-15 A to 25-Jun-15 A, 100% complete]																							
SB1E0372	B15 (B1e) - Pier Head Segment Lift & Fix (1 seg)	2	14-Jul-15 A	100%	0	14-Jul-15 A					100%	[Gantt bar: 14-Jul-15 A to 14-Jul-15 A, 100% complete]																							
Viaduct C																																			
Milestones - Marine Foundation																																			
GFXX197-1	C6 (C3f) - Completion of piling works	0		0%	0	21-Jul-15		28-Nov-18	999	999	0%	[Milestone: 21-Jul-15]																							
GFXX212-1	C3 (C4c) - Completion of piling works	0		0%	0	21-Jul-15		28-Nov-18	999	999	0%	[Milestone: 21-Jul-15]																							
GFXX202-1	C5 (C4a) - Completion of piling works	0		0%	0	21-Jul-15		28-Nov-18	999	999	0%	[Milestone: 21-Jul-15]																							
Milestones - Land Foundation																																			
ZC00051	C17 (C2a) - Completion of piling works	0		0%	0	21-Jul-15		28-Nov-18	999	999	0%	[Milestone: 21-Jul-15]																							
ZC00061	C16 (C2b) - Completion of piling works	0		0%	0	21-Jul-15		28-Nov-18	999	999	0%	[Milestone: 21-Jul-15]																							
ZC00091-1	C12 (C2f) - Completion of piling works	0		0%	0	21-Jul-15		28-Nov-18	999	999	0%	[Milestone: 21-Jul-15]																							
ZC00092-1	C11 (C3a) - Completion of piling works	0		0%	0	21-Jul-15		28-Nov-18	999	999	0%	[Milestone: 21-Jul-15]																							
ZC00096-1	C7 (C3e) - Completion of piling works	0		0%	0	21-Jul-15		28-Nov-18	999	999	0%	[Milestone: 21-Jul-15]																							
Bridge C4																																			
Pier C1 (C4e)																																			
Pier Works																																			
SC4E0310	C1 (C4e) - Type 4B-MJ Pier Head Rebarwork, Formwork & Prep	10	29-May-15 A	90%	1	21-Jul-15	23-Mar-15	23-Mar-15	-84	0	90%	[Gantt bar: 29-May-15 A to 21-Jul-15, 90% complete]																							
SC4E0330	C1 (C4e) - Type 4B-MJ Pier Head Concreting	1	22-Jul-15	0%	1	22-Jul-15	24-Mar-15	24-Mar-15	-84	0	0%	[Gantt bar: 22-Jul-15 to 22-Jul-15, 0% complete]																							
SC4E0340	C1 (C4e) - Type 4B-MJ Pier Head Curing/Striking of Forms/Remove Scaff	6	23-Jul-15	0%	6	30-Jul-15	25-Mar-15	31-Mar-15	-84	0	0%	[Gantt bar: 23-Jul-15 to 30-Jul-15, 0% complete]																							
SC4E0360	C1 (C4e) - Type 4B-Bearing Plinth	6	23-Jul-15	0%	6	30-Jul-15	25-Mar-15	31-Mar-15	-84	0	0%	[Gantt bar: 23-Jul-15 to 30-Jul-15, 0% complete]																							
Pier Head Segments																																			
SC4E0370	C1 (C4e) - Pier Head Segment - Temporary Platform	6	31-Jul-15	0%	6	06-Aug-15	01-Apr-15	11-Apr-15	-84	159	0%	[Gantt bar: 31-Jul-15 to 06-Aug-15, 0% complete]																							
Pier C2 (C4d)																																			
Pier Works																																			
SC4D0310	C2 (C4d) - Type 4B Pier Head Rebarwork, Formwork & Prep	10	30-Jun-15 A	70%	3	23-Jul-15	29-Sep-15	02-Oct-15	54	0	70%	[Gantt bar: 30-Jun-15 A to 23-Jul-15, 70% complete]																							
SC4D0330	C2 (C4d) - Type 4B Pier Head Concreting	1	24-Jul-15	0%	1	24-Jul-15	03-Oct-15	03-Oct-15	54	0	0%	[Gantt bar: 24-Jul-15 to 24-Jul-15, 0% complete]																							
SC4D0340	C2 (C4d) - Type 4B Pier Head Curing/Striking of Forms/Remove Scaffoldir	6	25-Jul-15	0%	6	01-Aug-15	05-Oct-15	10-Oct-15	54	0	0%	[Gantt bar: 25-Jul-15 to 01-Aug-15, 0% complete]																							
SC4D0300	C2 (C4d) - Type 4B Pier Head Scaffolding	4	24-Jun-15 A	100%	0	29-Jun-15 A					100%	[Gantt bar: 24-Jun-15 A to 29-Jun-15 A, 100% complete]																							
SC4D0240	C2 (C4d) - Type 4B Pier Concreting, Curing & Striking, CJ prep (2nd Lift)	3	17-Jun-15 A	100%	0	22-Jun-15 A					100%	[Gantt bar: 17-Jun-15 A to 22-Jun-15 A, 100% complete]																							
Pier Head Segments																																			
SC4D0370	C2 (C4d) - Pier Head Segment - Temporary Platform	6	03-Aug-15	0%	6	08-Aug-15	12-Oct-15	19-Oct-15	54	39	0%	[Gantt bar: 03-Aug-15 to 08-Aug-15, 0% complete]																							
SC4D0372	C2 (C4d) - Pier Head Segment Lift & Fix (1 seg)	2	30-Sep-15	0%	2	02-Oct-15	20-Oct-15	22-Oct-15	15	0	0%	[Gantt bar: 30-Sep-15 to 02-Oct-15, 0% complete]																							
SC4D0374	C2 (C4d) - Pier Head Segment Diaphragm - Rebar	12	03-Oct-15	0%	12	17-Oct-15	23-Oct-15	06-Nov-15	15	0	0%	[Gantt bar: 03-Oct-15 to 17-Oct-15, 0% complete]																							
SC4D0376	C2 (C4d) - Pier Head Segment Diaphragm - Formwork & Prep for Concre	8	19-Oct-15	0%	8	28-Oct-15	07-Nov-15	16-Nov-15	15	0	0%	[Gantt bar: 19-Oct-15 to 28-Oct-15, 0% complete]																							
Pier C3 (C4c)																																			
Pile Cap Works																																			
SC4C0140	C3 (C4c) - Marine Pile Cap M2b - Rebar fixing, inst.inserts etc	10	21-Jul-15	0%	10	01-Aug-15	08-Aug-15	21-Aug-15	15	0	0%	[Gantt bar: 21-Jul-15 to 01-Aug-15, 0% complete]																							
SC4C0150	C3 (C4c) - Marine Pile Cap M2b - Concreting	1	03-Aug-15	0%	1	03-Aug-15	22-Aug-15	22-Aug-15	15	0	0%	[Gantt bar: 03-Aug-15 to 03-Aug-15, 0% complete]																							
SC4C0160	C3 (C4c) - Marine Pile Cap M2b - Curing incl. CJ Preparation	6	04-Aug-15	0%	6	10-Aug-15	24-Aug-15	29-Aug-15	15	0	0%	[Gantt bar: 04-Aug-15 to 10-Aug-15, 0% complete]																							
SC4C0100	C3 (C4c) - Marine Pile Cap M2b - Weld Fin plates/Plug Rebar & Concrete	8	19-Jun-15 A	100%	0	28-Jun-15 A					100%	[Gantt bar: 19-Jun-15 A to 28-Jun-15 A, 100% complete]																							

■ Actual Work
■ Planned Bar
■ Critical Bar
◆ Milestone

Project ID: J3518DWPRe1-M26
 Layout: J3518-DWP-3MRP Submission - M26
 Filter: TASK filters: 3-Month Lookahead, No CC Milestones, No Level of Effort.

Tuen Mun - Chek Lap Kok Link - Southern Connection
3-Month Rolling Programme (Page 11 of 40 Pages)
(Progress as of 21-July-15)

Date	Revision	Checked	Approved
29-May-...		WY	
02-Jul-15		HF	KWY
28-Jul-15		PKN	KWY

DWG. No.:
J3518/GCL/PGM/3MRP-M26

Activity ID	Activity Name	Orig. Durn.	Act. Start / FC Early Start	Duration % Complete	Rem. Durn.	Act. Finish / FC Early Finish	Late Start	Late Finish	Total Float	Free Float	Physical % Complete	2015																			
												July					August					September					October				
												22	29	06	13	20	27	03	10	17	24	31	07	14	21	28	05	12	19		
Pier D8 (D3d)																															
Pier Works																															
SD3D0190	D8 (D3d) - Type 5B Pier Scaffolding (2nd Lift)	2	21-Jul-15	0%	2	22-Jul-15	25-Mar-15	26-Mar-15	-82	0	0%																				
SD3D0200	D8 (D3d) - Type 5B Pier Rebarwork (2nd Lift)	2	23-Jul-15	0%	2	24-Jul-15	27-Mar-15	28-Mar-15	-82	0	0%																				
SD3D0210	D8 (D3d) - Type 5B Pier Formwork & Prep for Concreting (2nd Lift)	2	25-Jul-15	0%	2	27-Jul-15	30-Mar-15	31-Mar-15	-82	0	0%																				
SD3D0220	D8 (D3d) - Type 5B Pier Concreting (2nd Lift)	1	28-Jul-15	0%	1	28-Jul-15	01-Apr-15	01-Apr-15	-82	0	0%																				
SD3D0222	D8 (D3d) - Type 5B Pier Curing & Striking of Forms incl. CJ prep (2nd Lift)	2	30-Jul-15	0%	2	31-Jul-15	02-Apr-15	08-Apr-15	-82	0	0%																				
SD3D0230	D8 (D3d) - Type 5B Pier Scaffolding (3rd Lift)	2	01-Aug-15	0%	2	03-Aug-15	09-Apr-15	10-Apr-15	-82	0	0%																				
SD3D0240	D8 (D3d) - Type 5B Pier Rebarwork (3rd Lift)	3	04-Aug-15	0%	3	06-Aug-15	11-Apr-15	14-Apr-15	-82	0	0%																				
SD3D0250	D8 (D3d) - Type 5B Pier Formwork & Prep for Concreting (3rd Lift)	3	07-Aug-15	0%	3	10-Aug-15	16-Apr-15	18-Apr-15	-82	0	0%																				
SD3D0260	D8 (D3d) - Type 5B Pier Concreting (3rd Lift)	1	12-Aug-15	0%	1	12-Aug-15	20-Apr-15	20-Apr-15	-82	0	0%																				
SD3D0262	D8 (D3d) - Type 5B Pier Curing & Striking of Forms incl. CJ prep (3rd Lift)	2	13-Aug-15	0%	2	14-Aug-15	21-Apr-15	22-Apr-15	-82	0	0%																				
SD3D0270	D8 (D3d) - Type 5B Pier Head Scaffolding	3	15-Aug-15	0%	3	18-Aug-15	24-Apr-15	27-Apr-15	-82	0	0%																				
SD3D0280	D8 (D3d) - Type 5B Pier Head Rebarwork	4	19-Aug-15	0%	4	24-Aug-15	28-Apr-15	02-May-15	-82	0	0%																				
SD3D0290	D8 (D3d) - Type 5B Pier Head Formwork & Prep for Concreting	4	25-Aug-15	0%	4	28-Aug-15	04-May-15	07-May-15	-82	0	0%																				
SD3D0300	D8 (D3d) - Type 5B Pier Head Concreting	1	29-Aug-15	0%	1	29-Aug-15	08-May-15	08-May-15	-82	0	0%																				
SD3D0310	D8 (D3d) - Type 5B Pier Head Curing/Striking of Forms/Remove Scaffoldir	6	31-Aug-15	0%	6	05-Sep-15	09-May-15	16-May-15	-82	0	0%																				
SD3D0320	D8 (D3d) - Type 5B Pier Backfilling Works	4	16-Jun-15 A	60%	2	22-Jul-15	15-May-15	16-May-15	-46	36	0%																				
Pier Head Segments																															
SD3D0370	D8 (D3d) - Pier Head Segment - Temporary Platform	6	07-Sep-15	0%	6	14-Sep-15	18-May-15	26-May-15	-82	2	0%																				
SD3D0372	D8 (D3d) - Pier Head Segment Lift & Fix (1 seg)	2	18-Sep-15	0%	2	19-Sep-15	27-May-15	28-May-15	-84	0	0%																				
SD3D0374	D8 (D3d) - Pier Head Segment Diaphragm - Rebar	13	21-Sep-15	0%	13	07-Oct-15	29-May-15	16-Jun-15	-84	0	0%																				
SD3D0376	D8 (D3d) - Pier Head Segment Diaphragm - Formwork	8	08-Oct-15	0%	8	17-Oct-15	18-Jun-15	30-Jun-15	-84	0	0%																				
SD3D0378	D8 (D3d) - Pier Head Segment Diaphragm - Concreting	2	19-Oct-15	0%	2	20-Oct-15	02-Jul-15	03-Jul-15	-84	0	0%																				
Pier D9 (D3c)																															
Pile Cap Works																															
SD3C0140	D9 (D3c) - Pile cap Curing & Striking of Forms incl. CJ prep	6	21-Jul-15	0%	6	27-Jul-15	22-Nov-18	28-Nov-18	955	955	0%																				
SD3C0122	D9 (D3c) - Pile cap Kicker Formwork	2	21-Jul-15	0%	2	22-Jul-15	27-Nov-18	28-Nov-18	959	959	0%																				
Pier Works																															
SD3C0190	D9 (D3c) - Type 5B Pier Scaffolding (2nd Lift)	2	21-Jul-15	0%	2	22-Jul-15	13-May-15	14-May-15	-48	0	0%																				
SD3C0200	D9 (D3c) - Type 5B Pier Rebarwork (2nd Lift)	3	23-Jul-15	0%	3	25-Jul-15	15-May-15	18-May-15	-48	0	0%																				
SD3C0210	D9 (D3c) - Type 5B Pier Formwork & Prep for Concreting (2nd Lift)	3	27-Jul-15	0%	3	30-Jul-15	19-May-15	22-May-15	-48	0	0%																				
SD3C0220	D9 (D3c) - Type 5B Pier Concreting (2nd Lift)	1	31-Jul-15	0%	1	31-Jul-15	23-May-15	23-May-15	-48	0	0%																				
SD3C0222	D9 (D3c) - Type 5B Pier Curing & Striking of Forms incl. CJ prep (2nd Lift)	2	01-Aug-15	0%	2	03-Aug-15	26-May-15	27-May-15	-48	0	0%																				
SD3C0230	D9 (D3c) - Type 5B Pier head Scaffolding	3	04-Aug-15	0%	3	06-Aug-15	28-May-15	30-May-15	-48	0	0%																				
SD3C0240	D9 (D3c) - Type 5B Pier Head Rebarwork	4	07-Aug-15	0%	4	12-Aug-15	01-Jun-15	05-Jun-15	-48	0	0%																				
SD3C0250	D9 (D3c) - Type 5B Pier Head Formwork & Prep for Concreting	4	13-Aug-15	0%	4	17-Aug-15	06-Jun-15	12-Jun-15	-48	0	0%																				
SD3C0260	D9 (D3c) - Type 5B Pier Head Concreting	1	18-Aug-15	0%	1	18-Aug-15	13-Jun-15	13-Jun-15	-48	0	0%																				
SD3C0262	D9 (D3c) - Type 5B Pier Head Curing & Striking of Forms incl. CJ prep	2	19-Aug-15	0%	2	21-Aug-15	15-Jun-15	16-Jun-15	-48	0	0%																				
SD3C0160	D9 (D3c) - Type 5B Pier Rebarwork (1st Lift)	3	15-Jun-15 A	100%	0	19-Jul-15 A					100%																				
SD3C0170	D9 (D3c) - Type 5B Pier Formwork & Prep for Concreting (1st Lift)	2	24-Jun-15 A	100%	0	27-Jun-15 A					100%																				
SD3C0180	D9 (D3c) - Type 5B Pier Concreting (1st Lift)	1	30-Jun-15 A	100%	0	30-Jun-15 A					100%																				
SD3C0182	D9 (D3c) - Type 5B Pier Curing & Striking of Forms incl. CJ prep (1st Lift)	2	30-Jun-15 A	100%	0	02-Jul-15 A					100%																				
Pier Head Segments																															
SD3C0370	D9 (D3c) - Pier Head Segment - Temporary Platform	6	22-Aug-15	0%	6	28-Aug-15	18-Jun-15	27-Jun-15	-48	15	0%																				
SD3C0372	D9 (D3c) - Pier Head Segment Lift & Fix (1 seg)	2	18-Sep-15	0%	2	19-Sep-15	29-Jun-15	30-Jun-15	-63	0	0%																				
SD3C0374	D9 (D3c) - Pier Head Segment Diaphragm - Rebar	12	21-Sep-15	0%	12	06-Oct-15	02-Jul-15	15-Jul-15	-63	0	0%																				
SD3C0376	D9 (D3c) - Pier Head Segment Diaphragm - Formwork	8	07-Oct-15	0%	8	16-Oct-15	17-Jul-15	25-Jul-15	-63	0	0%																				
SD3C0378	D9 (D3c) - Pier Head Segment Diaphragm - Concreting	2	17-Oct-15	0%	2	19-Oct-15	27-Jul-15	28-Jul-15	-63	0	0%																				
SD3C0380	D9 (D3c) - Pier Head Segment Diaphragm - Curing & Striking of Forms	6	20-Oct-15	0%	6	27-Oct-15	30-Jul-15	05-Aug-15	-63	0	0%																				
Pier D10 (D3b)																															
Pile Cap Works																															
SD3BR090	D10B (D3b-R) - Pile cap Excavation / ELS (incl. sheet piling)	12	21-Jul-15	0%	12	04-Aug-15	23-Mar-15	09-Apr-15	-84	0	0%																				
SD3BR092	D10B (D3b-R) - Pile cap Pile breakdown to cut-off etc	3	05-Aug-15	0%	3	07-Aug-15	10-Apr-15	13-Apr-15	-84	0	0%																				

■ Actual Work
■ Planned Bar
■ Critical Bar
◆ Milestone

Project ID: J3518DWPRe1-M26
 Layout: J3518-DWP-3MRP Submission - M26
 Filter: TASK filters: 3-Month Lookahead, No CC
 Milestones, No Level of Effort.

Tuen Mun - Chek Lap Kok Link - Southern Connection
3-Month Rolling Programme (Page 22 of 40 Pages)
(Progress as of 21-July-15)

Date	Revision	Checked	Approved
29-May-...		WY	
02-Jul-15		HF	KWY
28-Jul-15		PKN	KWY

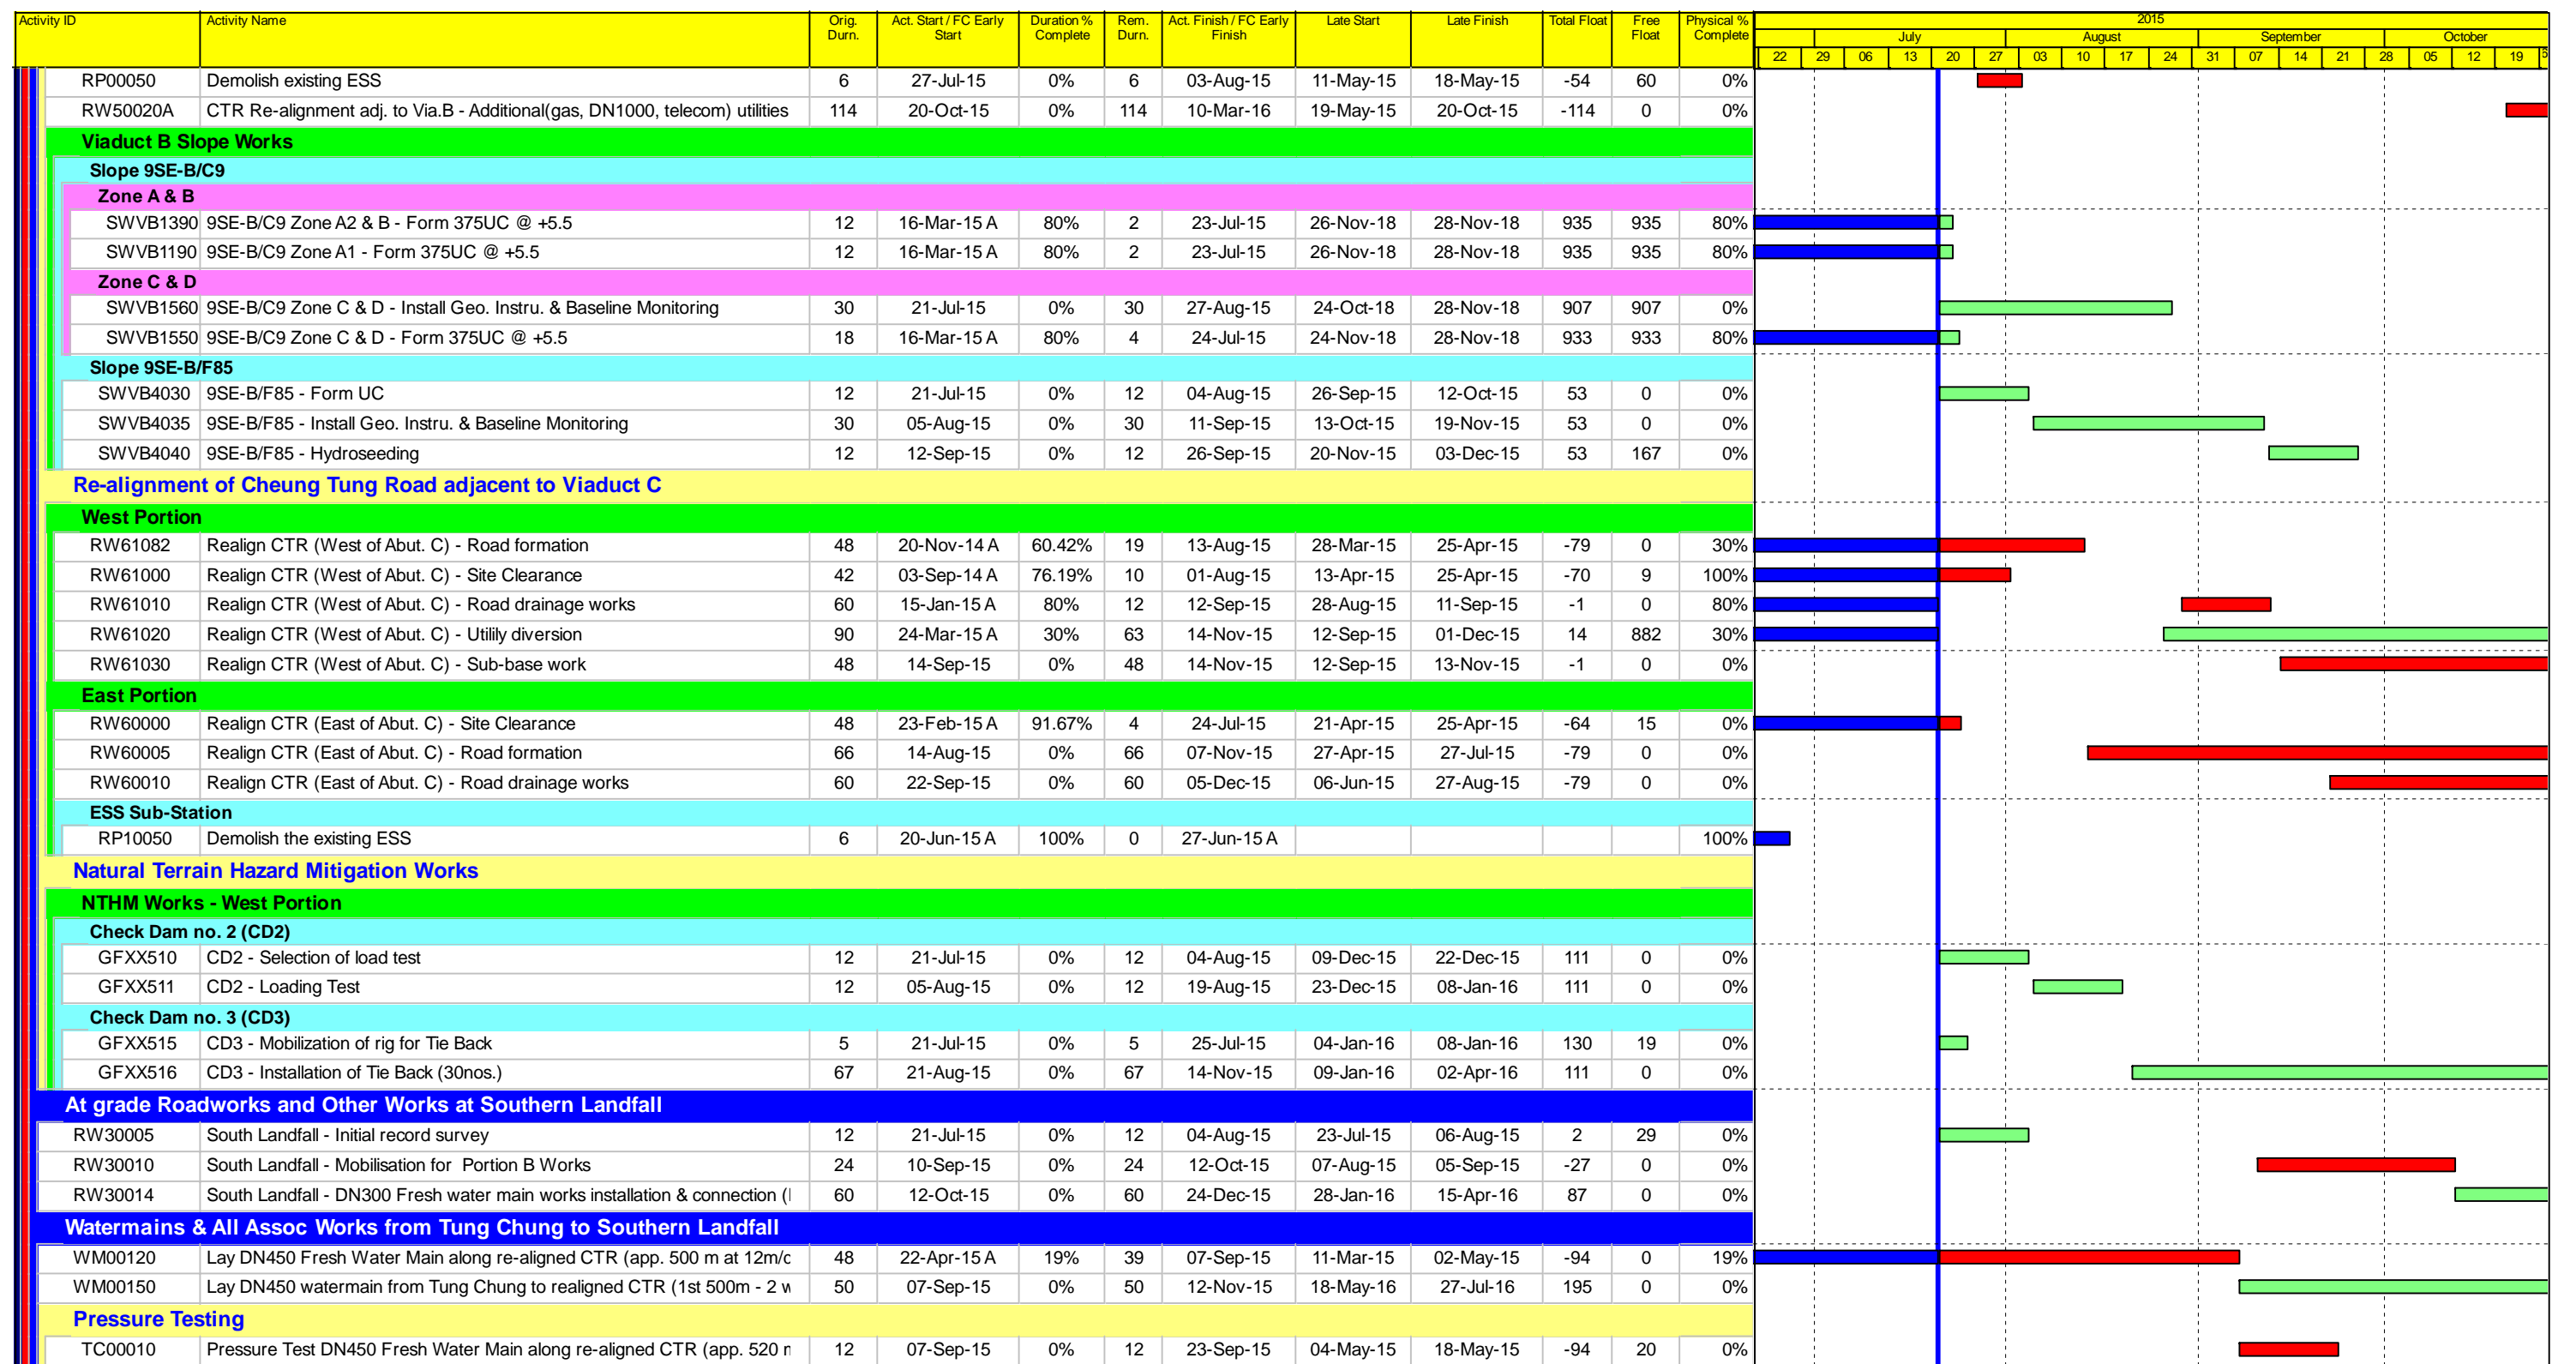
DWG. No.:
J3518/GCL/PGM/3MRP-M26





Activity ID	Activity Name	Orig. Durn.	Act. Start / FC Early Start	Duration % Complete	Rem. Durn.	Act. Finish / FC Early Finish	Late Start	Late Finish	Total Float	Free Float	Physical % Complete	2015															
												July				August				September				October			
												22	29	06	13	20	27	03	10	17	24	31	07	14	21	28	05
C400030-1	Pier C4 (C4b) ready for Viaduct C4 PH segment erection	0		0%	0	21-Sep-15		31-Mar-15	-125	0	0%																
C400060-1	Pier C1 (C4e) ready for Viaduct C4 PH segment erection	0		0%	0	30-Jul-15		31-Mar-15	-84	0	0%																
C400010-1	Pier C6 (C3f) ready for Viaduct C4 PH segment erection	0		0%	0	20-Oct-15		02-May-15	-125	0	0%																
C400050-1	Pier C2 (C4d) ready for Viaduct C4 PH segment erection	0		0%	0	01-Aug-15		10-Oct-15	54	0	0%																
C400040-1	Pier C3 (C4c) ready for Viaduct C4 PH segment erection	0		0%	0	02-Oct-15		22-Oct-15	15	0	0%																
Bridge C3 Superstructure																											
Milestones																											
Milestones Ready for PH Segment Erection																											
C300060-1	Pier C6 (C3f) ready for Viaduct C3 PH segment erection	0		0%	0	20-Oct-15		02-May-15	-125	0	0%																
C300050-1	Pier C7 (C3e) ready for Viaduct C3 PH segment erection	0		0%	0	07-Oct-15		19-Nov-15	34	0	0%																
C300040-1	Pier C8 (C3d) ready for Viaduct C3 PH segment erection	0		0%	0	24-Aug-15		24-Dec-15	98	0	0%																
C300030-1	Pier C9 (C3c) ready for Viaduct C3 PH segment erection	0		0%	0	03-Aug-15		22-Jan-16	136	0	0%																
C300020-1	Pier C10 (C3b) ready for Viaduct C3 PH segment erection	0		0%	0	15-Sep-15		19-Feb-16	123	0	0%																
C300010-1	Pier C11 (C3a) ready for Viaduct C3 PH segment erection	0		0%	0	30-Sep-15		24-Mar-16	141	0	0%																
Bridge C2 Superstructure																											
Milestones																											
Milestones Ready for PH Segment Erection																											
C200050-1	Pier C12 (C2f) ready for Viaduct C2 PH segment erection	0		0%	0	11-Sep-15		03-Mar-16	137	0	0%																
C200030-1	Pier C14 (C2d) ready for Viaduct C2 PH segment erection	0		0%	0	28-Aug-15		19-Mar-16	162	0	0%																
C200060-1	Pier C11 (C3a) ready for Viaduct C2 PH segment erection	0		0%	0	30-Sep-15		24-Mar-16	141	0	0%																
C200020-1	Pier C15 (C2c) ready for Viaduct C2 PH segment erection	0		0%	0	27-Jul-15		30-Mar-16	193	0	0%																
C200010-1	Pier C16 (C2b) ready for Viaduct C2 PH segment erection	0		0%	0	15-Sep-15		04-May-16	180	0	0%																
Bridge C1 Superstructure																											
Milestones																											
Milestones Ready for PH Segment Erection																											
C100020-1	Pier C19 (C1d) ready for Viaduct C1 PH segment erection	0		0%	0	27-Jul-15		30-Dec-15	122	0	0%																
C100010-1	Pier C20 (C1c) ready for Viaduct C1 PH segment erection	0		0%	0	21-Jul-15		05-Mar-16	181	0	0%																
C100040-1	Pier C17 (C2a) ready for Viaduct C1 PH segment erection	0		0%	0	15-Sep-15		10-Mar-16	140	0	0%																
C100050-1	Pier C16 (C2b) ready for Viaduct C1 PH segment erection	0		0%	0	15-Sep-15		04-May-16	180	0	0%																
Viaduct D Superstructure																											
Bridge D3 Superstructure																											
Milestones																											
Milestones Ready for PH Segment Erection																											
D300030-1	Pier D4 (D4c) ready for Viaduct D3 PH segment erection	0		0%	0	07-Sep-15		24-Mar-15	-121	0	0%																
D300020-1	Pier D5 (D4b) ready for Viaduct D3 PH segment erection	0		0%	0	24-Sep-15		02-Apr-15	-125	0	0%																
D300060-1	Pier D1 (D4f) ready for Viaduct D3 PH segment erection	0		0%	0	27-Jul-15		22-Apr-15	-68	0	0%																
D300010-1	Pier D6 (D4a) ready for Viaduct D3 PH segment erection	0		0%	0	12-Oct-15		08-Jun-15	-93	0	0%																
D300040-1	Pier D3 (D4d) ready for Viaduct D3 PH segment erection	0		0%	0	07-Aug-15		12-Nov-15	74	0	0%																
D300050-1	Pier D2 (D4e) ready for Viaduct D3 PH segment erection	0		0%	0	12-Aug-15		27-Nov-15	84	129	0%																
Bridge D2 Superstructure																											
Milestones																											
Milestones Ready for PH Segment Erection																											
D200070-1	Pier D7 (D3e) ready for Viaduct D2 PH segment erection	0		0%	0	10-Oct-15		30-Apr-15	-120	0	0%																
D200060-1	Pier D8 (D3d) ready for Viaduct D2 PH segment erection	0		0%	0	05-Sep-15		16-May-15	-82	0	0%																
D200080-1	Pier D6 (D4a) ready for Viaduct D2 PH segment erection	0		0%	0	12-Oct-15		08-Jun-15	-93	0	0%																
D200050-1	Pier D9 (D3c) ready for Viaduct D2 PH segment erection	0		0%	0	21-Aug-15		16-Jun-15	-48	0	0%																
D200010-1	Pier D13 (D2d) ready for Viaduct D2 PH segment erection	0		0%	0	21-Sep-15		15-Oct-15	18	0	0%																
Bridge D1 Superstructure																											
Milestones																											
Milestones Ready for PH Segment Erection																											
D100030-1	Pier D17 (D1d) ready for Viaduct D1 PH segment erection	0		0%	0	23-Jul-15		15-Aug-15	18	0	0%																
D100040-1	Pier D16 (D2a) ready for Viaduct D1 PH segment erection	0		0%	0	15-Oct-15		15-Aug-15	-46	0	0%																
D100050-1	Pier D15 (D2b) ready for Viaduct D1 PH segment erection	0		0%	0	05-Sep-15		03-Oct-15	20	0	0%																
D100010-1	Pier D19 (D1b) ready for Viaduct D1 PH segment erection	0		0%	0	31-Jul-15		12-Oct-15	56	0	0%																

<ul style="list-style-type: none"> ■ Actual Work ■ Planned Bar ■ Critical Bar ◆ Milestone 	Project ID: J3518DWPRe1-M26 Layout: J3518-DWP-3MRP Submission - M26 Filter: TASK filters: 3-Month Lookahead, No CC Milestones, No Level of Effort.	Tuen Mun - Chek Lap Kok Link - Southern Connection 3-Month Rolling Programme (Page 38 of 40 Pages) (Progress as of 21-July-15)	Date	Revision	Checked	Approved	DWG. No.: J3518/GCL/PGM/3MRP-M26
			29-May-...		WY		
			02-Jul-15		HF	KWY	
			28-Jul-15		PKN	KWY	

Activity ID	Activity Name	Orig. Durn.	Act. Start / FC Early Start	Duration % Complete	Rem. Durn.	Act. Finish / FC Early Finish	Late Start	Late Finish	Total Float	Free Float	Physical % Complete	2015																
												July					August					September				October		
												22	29	06	13	20	27	03	10	17	24	31	07	14	21	28	05	12
D100070-1	Pier D13 (D2d) ready for Viaduct D1 PH segment erection	0		0%	0	21-Sep-15		15-Oct-15	18	0	0%																	
D100020-1	Pier D18 (D1c) ready for Viaduct D1 PH segment erection	0		0%	0	27-Jul-15		12-Nov-15	83	4	0%																	
Viaduct E																												
Bridge E1 Superstructure																												
Milestones																												
Milestones Ready for PH Segment Erection																												
E100160-1	Pier E3A (E2a4) ready for Viaduct E1 PH segment erection	0		0%	0	22-Aug-15		07-Jan-15	-169	0	0%																	
E100110-1	Pier E2B (E1b3) ready for Viaduct E1 PH segment erection	0		0%	0	28-Aug-15		08-Jan-15	-175	0	0%																	
E100150-1	Pier E3B (E2a3) ready for Viaduct E1 PH segment erection	0		0%	0	18-Aug-15		30-Jan-15	-147	92	0%																	
E100140-1	Pier E3C (E2a2) ready for Viaduct E1 PH segment erection	0		0%	0	24-Aug-15		24-Feb-15	-133	98	0%																	
E100060-1	Pier E1C (E1a2) ready for Viaduct E1 PH segment erection	0		0%	0	14-Sep-15		02-Mar-15	-146	0	0%																	
E100100-1	Pier E2C (E1b2) ready for Viaduct E1 PH segment erection	0		0%	0	19-Aug-15		16-Mar-15	-113	132	0%																	
E100020-1	Pier C1 (C4e) ready for Viaduct E1 PH segment erection	0		0%	0	30-Jul-15		31-Mar-15	-84	0	0%																	
E100030-1	Pier D1 (D4f) ready for Viaduct E1 PH segment erection	0		0%	0	27-Jul-15		22-Apr-15	-68	0	0%																	
E100050-1	Pier E1D (E1a1) ready for Viaduct E1 PH segment erection	0		0%	0	17-Aug-15		17-Feb-16	143	0	0%																	
E100090-1	Pier E2D (E1b1) ready for Viaduct E1 PH segment erection	0		0%	0	19-Aug-15		22-Feb-16	146	0	0%																	
E100130-1	Pier E3D (E2a1) ready for Viaduct E1 PH segment erection	0		0%	0	26-Aug-15		27-Feb-16	146	107	0%																	
E100010-1	Pier A1 (A2e) ready for Viaduct E1 PH segment erection	0		0%	0	05-Oct-15		16-Apr-16	153	0	0%																	
E100120-1	Pier E2A (E1b4) ready for Viaduct E1 PH segment erection	0		0%	0	21-Jul-15		28-Nov-18	937	937	0%																	
E100070-1	Pier E1B (E1a3) ready for Viaduct E1 PH segment erection	0		0%	0	21-Jul-15		28-Nov-18	937	937	0%																	
E100080-1	Pier E1A (E1a4) ready for Viaduct E1 PH segment erection	0		0%	0	21-Jul-15		28-Nov-18	937	937	0%																	
Milestones Ready for Deck Segment Erection																												
E100080	Pier E1A (E1a4) ready for Viaduct E1 deck segment erection	0		0%	0	28-Aug-15		02-Jan-15	-179	50	0%																	
E100120	Pier E2A (E1b4) ready for Viaduct E1 deck segment erection	0		0%	0	27-Aug-15		23-Jan-15	-160	69	0%																	
E100110	Pier E2B (E1b3) ready for Viaduct E1 deck segment erection	0		0%	0	10-Oct-15		17-Feb-15	-173	72	0%																	
E100070	Pier E1B (E1a3) ready for Viaduct E1 deck segment erection	0		0%	0	28-Aug-15		04-May-15	-85	160	0%																	
E100090	Pier E2D (E1b1) ready for Viaduct E1 deck segment erection	0		0%	0	30-Sep-15		05-Apr-16	147	387	0%																	
Bridge E2 Superstructure																												
Milestones																												
Milestones Ready for PH Segment Erection																												
E200040-1	Pier E3A (E2a4) ready for Viaduct E2 PH segment erection	0		0%	0	22-Aug-15		07-Jan-15	-169	0	0%																	
E200030-1	Pier E3B (E2a3) ready for Viaduct E2 PH segment erection	0		0%	0	18-Aug-15		30-Jan-15	-147	92	0%																	
E200060-1	Pier E4A (E2b2) ready for Viaduct E2 PH segment erection	0		0%	0	11-Sep-15		04-Feb-15	-162	2	0%																	
E200020-1	Pier E3C (E2a2) ready for Viaduct E2 PH segment erection	0		0%	0	24-Aug-15		24-Feb-15	-133	98	0%																	
E200010-1	Pier E3D (E2a1) ready for Viaduct E2 PH segment erection	0		0%	0	26-Aug-15		27-Feb-16	146	107	0%																	
At-Grade Roadworks & Other Works along NLH																												
Viaduct A Slope Works																												
Slope 9SE-B/FR8																												
GFXX485	9SE-B/FR8 - Protective Fencing	46	21-Jul-15	0%	46	16-Sep-15	10-Sep-15	09-Nov-15	40	0	0%																	
GFXX490	9SE-B/FR8 - Mobilization for Mini Pile	3	18-Sep-15	0%	3	21-Sep-15	10-Nov-15	12-Nov-15	40	0	0%																	
GFXX491	9SE-B/FR8 - Installation of Mini Pile (118 No.)	148	22-Sep-15	0%	148	24-Mar-16	13-Nov-15	20-May-16	40	0	0%																	
At-Grade Roadworks along NLH Westbound																												
RW10003	NLH W/B (Viaduct C) - Gantry Footing (GT326, GT327, GT328) - Verge (54	05-May-15 A	40%	32	31-Aug-15	29-Jun-15	08-Aug-15	-16	0	0%																	
RW10005	NLH W/B (Viaduct C) - Implement TTM - Verge for Gantry Footings (GT3:	2	31-Aug-15*	0%	2	02-Sep-15	10-Aug-15	12-Aug-15	-16	0	0%																	
RW10007	NLH W/B (Viaduct C) - Gantry Footing (GT324, GT325) - Verge (KD3)	36	02-Sep-15	0%	36	20-Oct-15	13-Aug-15	26-Sep-15	-16	0	0%																	
RW10009	NLH W/B (Viaduct C) - Implement TTM - Median for Gantry Footings (GT:	2	20-Oct-15	0%	2	23-Oct-15	29-Sep-15	30-Sep-15	-16	0	0%																	
At-Grade Roadworks along NLH Eastbound																												
RW21000	NLH E/B (Viaduct A) - Implement TTM - Verge for Slope Works & Gantry F	2	18-Sep-15	0%	2	19-Sep-15	12-Mar-16	14-Mar-16	140	0	0%																	
RW21001	NLH E/B (Viaduct A) - Gantry Footing (GT319, GT320) - Verge (KD5)	36	21-Sep-15	0%	36	06-Nov-15	15-Mar-16	03-May-16	140	0	0%																	
At-Grade Roadworks and Other Works along Cheung Tung Road																												
Re-alignment of Cheung Tung Road adjacent to Viaduct B																												
RW50020	CTR Re-alignment adj. to Via.B - Diversion of utilities (Gas, DN1000, powe	177	12-Jan-15 A	60%	71	20-Oct-15	12-Feb-15	18-May-15	-114	0	60%																	
RP00040	Remove equipment in existing ESS	10	11-Jul-15 A	50%	5	25-Jul-15	05-May-15	09-May-15	-54	0	50%																	

<ul style="list-style-type: none"> Actual Work Planned Bar Critical Bar Milestone 	Project ID: J3518DWPPrE1-M26 Layout: J3518-DWP-3MRP Submission - M26 Filter: TASK filters: 3-Month Lookahead, No CC Milestones, No Level of Effort.	Tuen Mun - Chek Lap Kok Link - Southern Connection 3-Month Rolling Programme (Page 39 of 40 Pages) (Progress as of 21-July-15)			Date: 29-May-15 Revision: 02-Jul-15 28-Jul-15	Checked: WY HF PKN	Approved: KWY KWY	DWG. No.: J3518/GCL/PGM/3MRP-M26
---	---	--	--	--	---	--------------------------	----------------------	---



-  Actual Work
-  Planned Bar
-  Critical Bar
-  Milestone

Project ID: J3518DWPre1-M26
 Layout: J3518-DWP-3MRP Submission - M26
 Filter: TASK filters: 3-Month Lookahead, No CC Milestones, No Level of Effort.

Tuen Mun - Chek Lap Kok Link - Southern Connection
3-Month Rolling Programme (Page 40 of 40 Pages)
(Progress as of 21-July-15)

Date	Revision	Checked	Approved
29-May-15		WY	
02-Jul-15		HF	KWY
28-Jul-15		PKN	KWY

DWG. No.: **J3518/GCL/PGM/3MRP-M26**
