

Activity ID	Activity Name	Orig. Durn.	Act. Start / FC Early Start	Rem. Durn.	Act. Finish / FC Early Finish	Late Start	Late Finish	Total Float	Physical % Complete	2016												2017												
										January						February						March						April						
										19	26	02	09	16	23	30	06	13	20	27	03	10	17	24										
Contract Milestones																																		
Key Dates for Completion																																		
Stage of the Works																																		
Completion Date																																		
General																																		
KD03	KD3 - Stage 3: TCSS Along NLH Near Viaduct C, D (EoT 5-Apr-16)		0		0	21-Jan-17*		05-Apr-16	-290	0%																								
Portion Handover Dates																																		
Possession of the Works Area																																		
Access Dates																																		
General																																		
POS02-6B	Portion A - Area 6B (To be confirmed)		0		0	21-Jan-17*		15-Dec-15	-403	0%																								
Design																																		
Detailed Design																																		
General Submissions																																		
Reports & Manuals																																		
General																																		
ARDD0037-7	Preparation of Seismic Performance Report Viaduct F - AP12.03		160	21-Aug-15 A	0	11-Jan-17 A				100%																								
ARDD0037-8	IC/SO Approval of Seismic Performance Report Viaduct F - AP12.03		75	12-Jan-17 A	75	26-Apr-17	08-Apr-16	08-Jul-16	-237	0%																								
ARDD0040-2	IC/SO Approval of Operation and Maintenance Manual - AP08.00		75	20-Oct-15 A	16	11-Feb-17	20-Jun-16	08-Jul-16	-178	0%																								
ARDD0042-2	IC/SO Approval of O&M Facility Provisions DDA - BP11.01		75	14-Jan-15 A	16	11-Feb-17	20-Jun-16	08-Jul-16	-178	50%																								
Slope Works Near Viaduct A																																		
Feature 9SE-B/FR8, B/R1, B/R2																																		
Slope Works Design																																		
ARDD0596	Preparation of remaining portion of Slope FR8 Combined AIP/DDA - CP11.		35	21-Dec-16 A	11	06-Feb-17	19-Jan-16	30-Jan-16	-299	50%																								
ARDD0596-1	IC/SO Approval of Slope Combined AIP/DDA - CP11.01		60	07-Feb-17	60	21-Apr-17	01-Feb-16	18-Apr-16	-299	0%																								
Slope Works Near Viaduct C																																		
Feature 10NW-C/C22, C/C26, C/C27, C/F13, C/F14, C/F15																																		
Slope Works Design																																		
ARDD0589-1	Preparation of Slope Combined AIP/DDA - CP13.01		60	21-Jan-17*	60	04-Apr-17	19-Jul-16	27-Sep-16	-154	0%																								
ARDD0589-2	IC/SO Approval of Combined AIP/DDA - CP13.01		28	04-Apr-17	28	02-May-17	28-Sep-16	25-Oct-16	-189	0%																								
ARDD0590	Newfill slopes PF1 & PF2 Preparation of Combined AIP/DDA - CP13.01		60	21-Jan-17	60	04-Apr-17	05-Jul-16	12-Sep-16	-166	0%																								
ARDD0590-1	New fill slopes PF1 & PF2 IC/SO Approval of combined AIP/DDA - CP13.0		28	06-Apr-17	28	13-May-17	13-Sep-16	18-Oct-16	-166	0%																								
Slope Works Near Viaduct D																																		
Feature 10NW-C/R4, C/F9, C/F10, C/F11, C/F17, C/F50																																		
Slope Works Design																																		
ARDD0603	IC/SO Approval of Slope Combined AIP/DDA -CP14.01		75	16-Dec-14 A	7	01-Feb-17	17-Feb-16	24-Feb-16	-277	75%																								
ARDD0603-1	IC/SO Approval of Slope Combined AIP/DDA -CP14.01		0		0	01-Feb-17		24-Feb-16	-277	0%																								
Watermain, Drainage & Utility Diversions																																		
General																																		
Design																																		
ARDD0629	IC/SO Approval of Waterworks, Drainage & Utility DDA - BP20.01		75	22-Jul-14 A	22	18-Feb-17	01-Mar-16	29-Mar-16	-266	95%																								
ARDD0629-1	IC/SO Approval of Waterworks, Drainage & Utility DDA - BP20.01		0		0	18-Feb-17		29-Mar-16	-266	0%																								
ARDD0629-2	Gov't Approval of Submissions for Waterworks, Drainage & Utility Diversior		75	02-Jan-14 A	22	18-Feb-17	01-Mar-16	29-Mar-16	-266	95%																								
Viaduct Approach Ramp Retaining Walls																																		
Abutment & Approach Ramp B																																		
Design																																		
ARDD0664	Approach B - IC/SO Approval of Approach Ramp B DDA -DP21.01		75	14-Oct-14 A	4	25-Jan-17	09-Mar-16	12-Mar-16	-259	95%																								
ARDD0664-1	Approach B - IC/SO Approval of Approach Ramp B DDA -DP21.01		0		0	25-Jan-17		12-Mar-16	-259	0%																								
Abutment & Approach Ramp F																																		
Design																																		
ARDD0676	Approach F - IC/SO Approval of Approach Ramp F DDA -DP24.01		75	23-Dec-14 A	34	04-Mar-17	13-May-16	23-Jun-16	-208	70%																								
ARDD0676-1	Approach F - IC/SO Approval of Approach Ramp F DDA -DP24.01		0		0	04-Mar-17		23-Jun-16	-208	0%																								
Segment Target Geometry & Erection Engineering																																		
Viaduct A																																		


■ Actual Work
■ Planned Bar
■ Critical Bar
◆ Milestone

Project ID: TMCLK-DWPH-M44
 Layout: J3518-DWP-3MRP Submission - M44
 Filter: TASK filters: 3-Month Lookahead, No CC
 Milestones, No Level of Effort.

Tuen Mun - Chek Lap Kok Link - Southern Connection
3-Month Rolling Programme (Page 1 of 13 Pages)
(Progress as of 21-Jan-17)

Date	Revision	Checked	Approved
30-Nov-...		PKN	GL
03-Jan-17		PKN	GL
26-Jan-17		PKN	GL

DWG. No.:
J3518/GCL/PGM/3MRP-M44

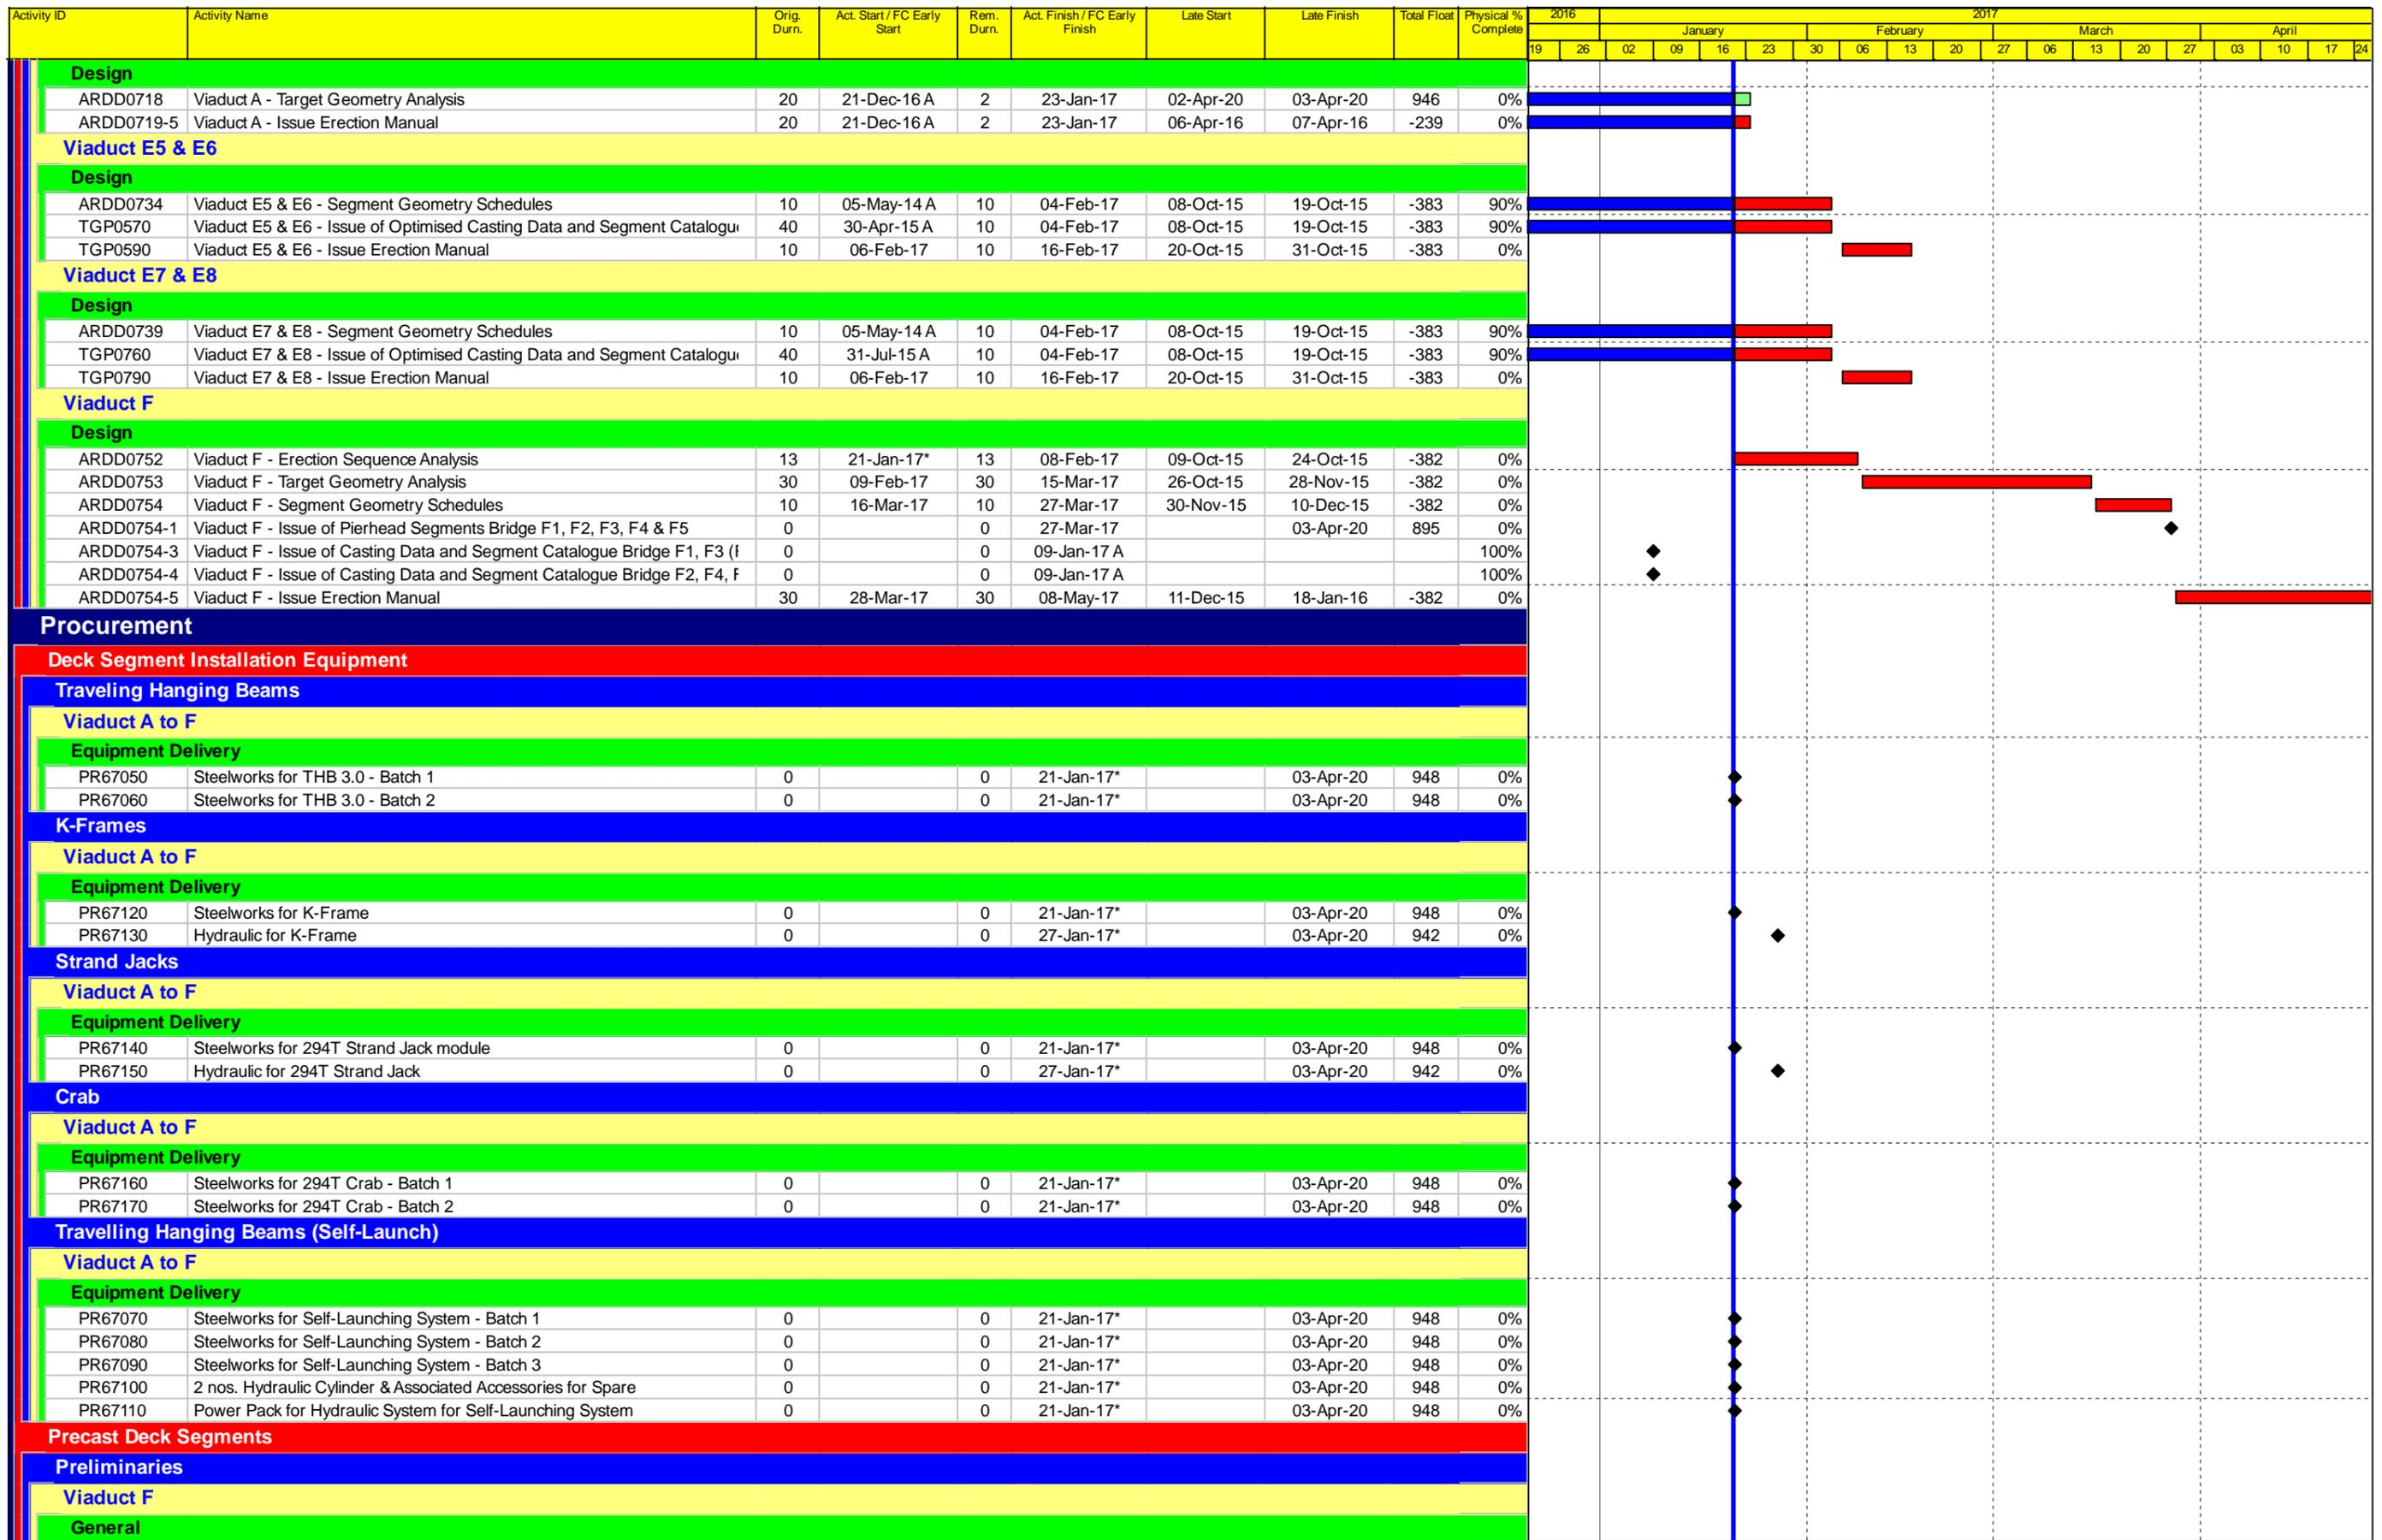


■ Actual Work
■ Planned Bar
■ Critical Bar
◆ Milestone

Project ID: TMCLK-DWPH-M44
 Layout: J3518-DWP-3MRP Submission - M44
 Filter: TASK filters: 3-Month Lookahead, No CC
 Milestones, No Level of Effort.

Tuen Mun - Chek Lap Kok Link - Southern Connection
3-Month Rolling Programme (Page 2 of 13 Pages)
(Progress as of 21-Jan-17)

Date	Revision	Checked	Approved
30-Nov-...		PKN	GL
03-Jan-17		PKN	GL
26-Jan-17		PKN	GL

DWG. No.:
J3518/GCL/PGM/3MRP-M44

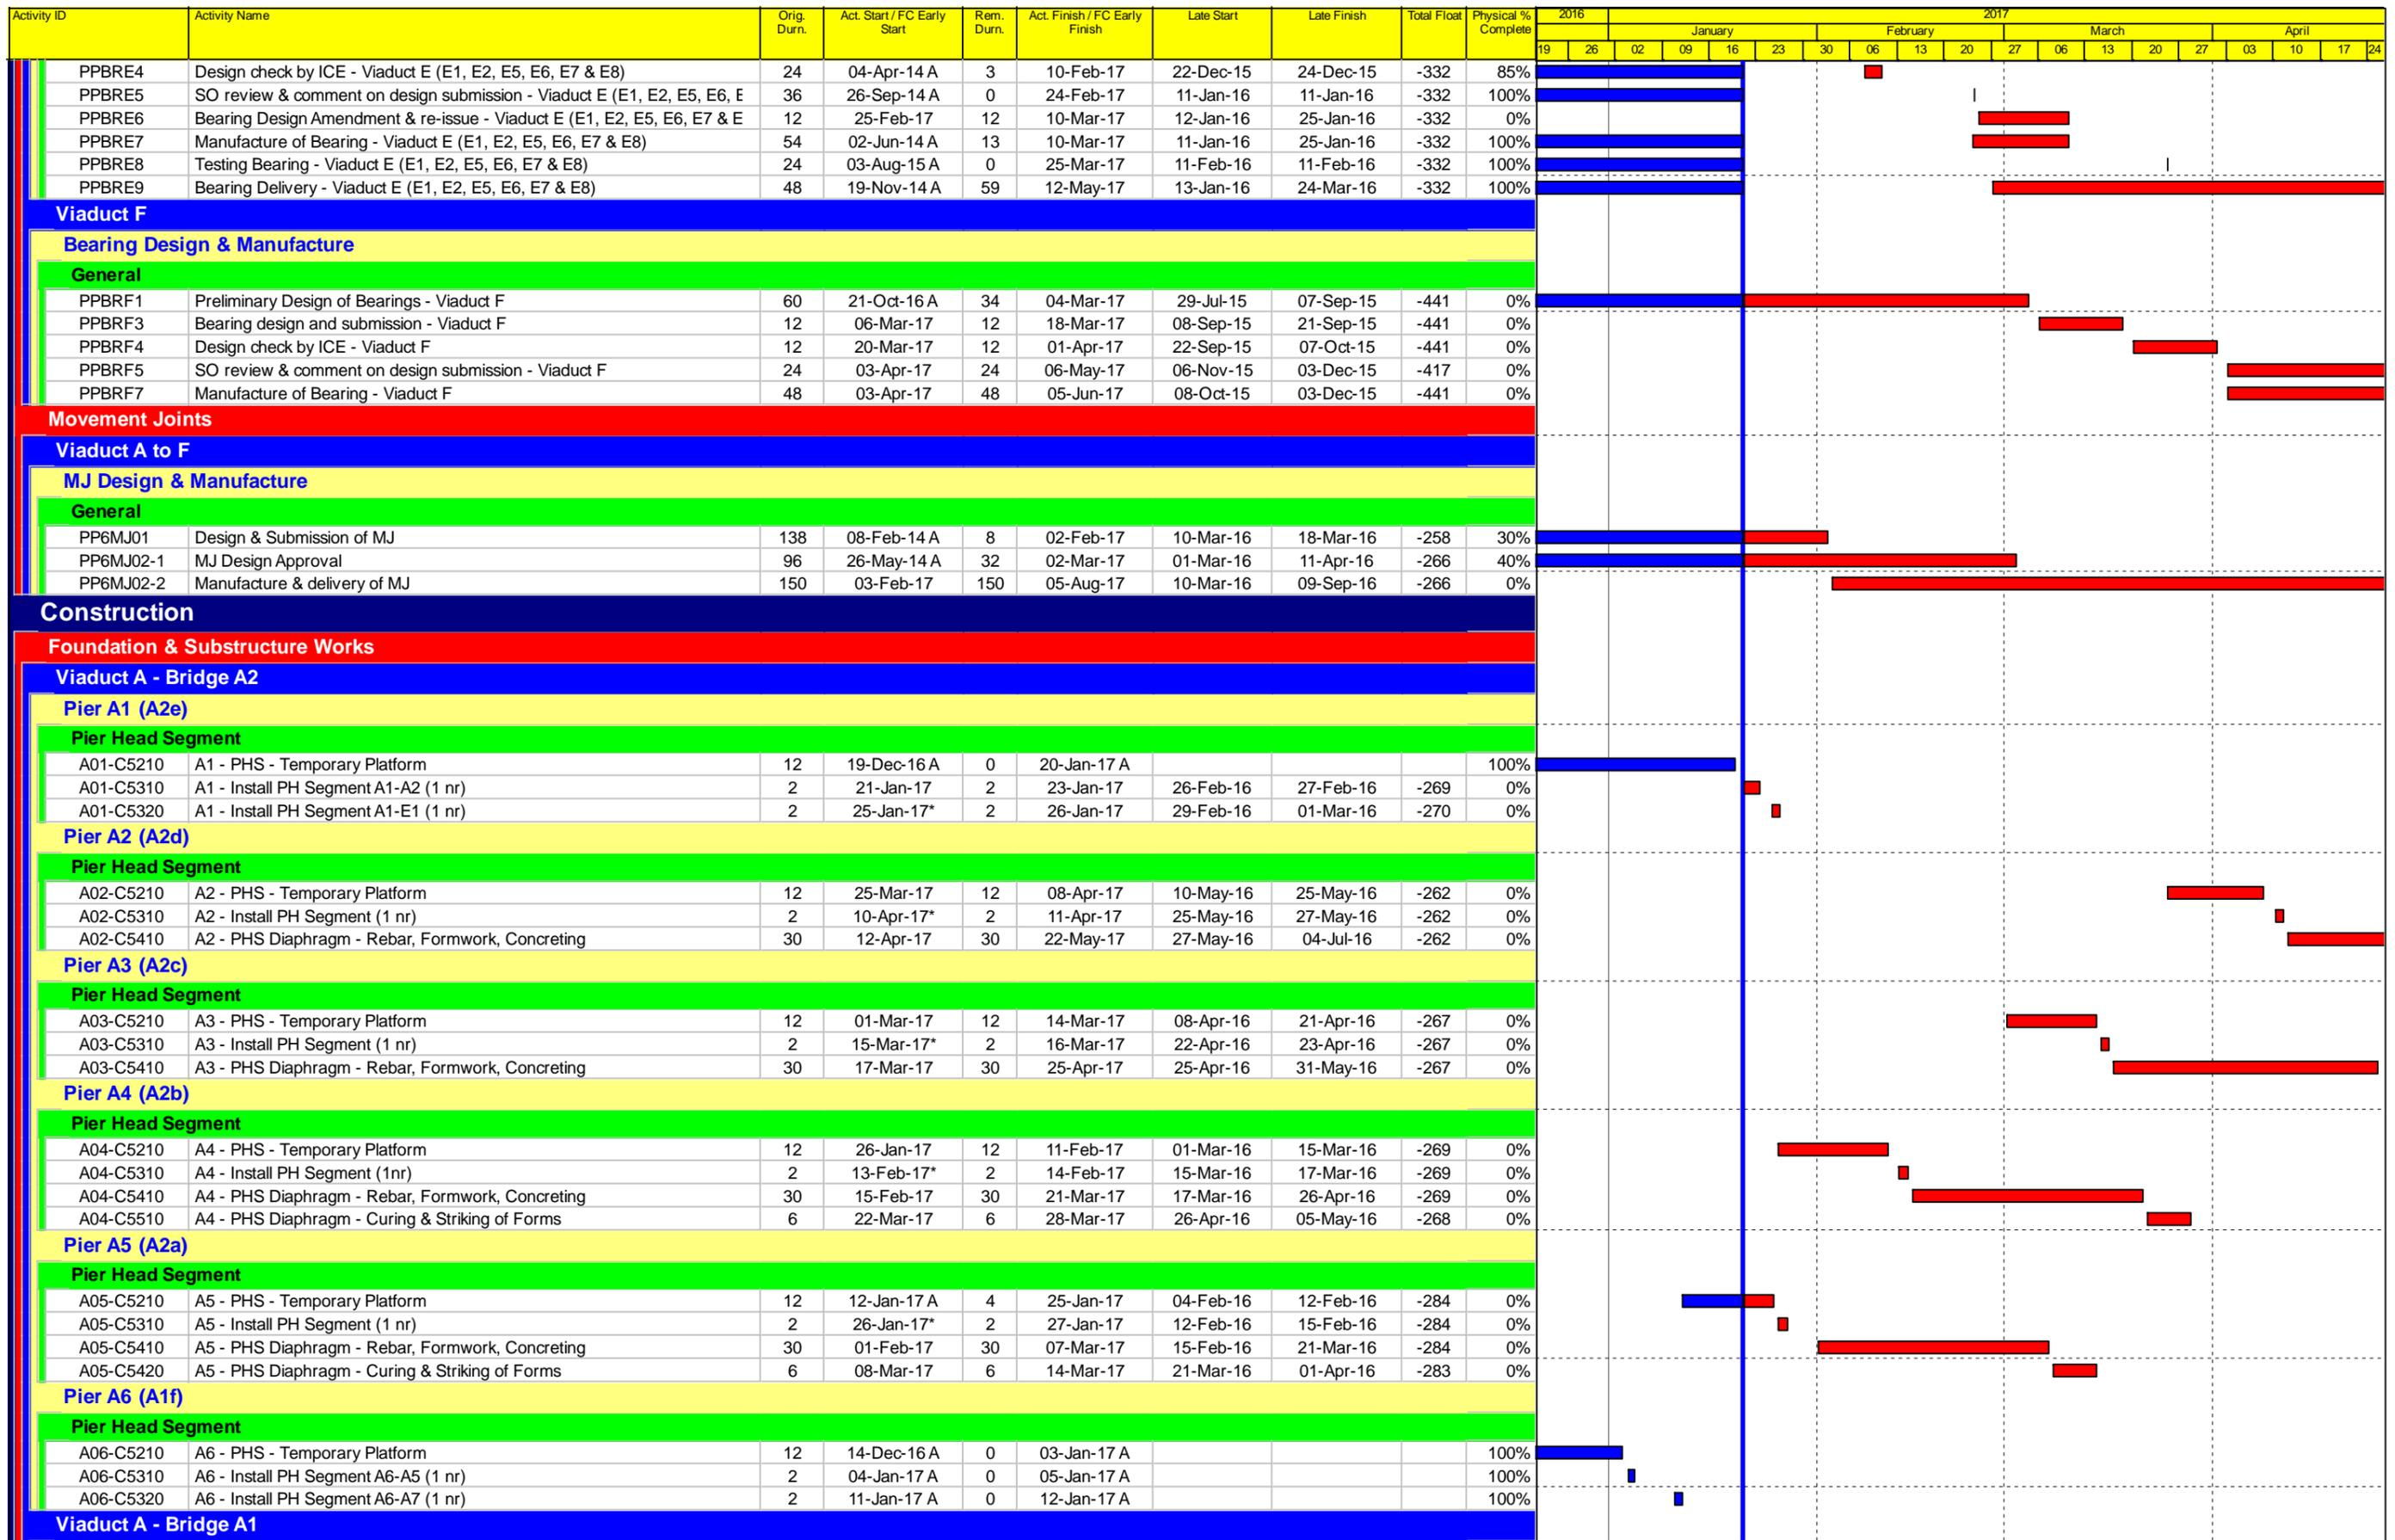

■ Actual Work
■ Planned Bar
■ Critical Bar
◆ Milestone

Project ID: TMCLK-DWPH-M44
 Layout: J3518-DWP-3MRP Submission - M44
 Filter: TASK filters: 3-Month Lookahead, No CC
 Milestones, No Level of Effort.

Tuen Mun - Chek Lap Kok Link - Southern Connection
3-Month Rolling Programme (Page 4 of 13 Pages)
(Progress as of 21-Jan-17)

Date	Revision	Checked	Approved
30-Nov-...		PKN	GL
03-Jan-17		PKN	GL
26-Jan-17		PKN	GL

DWG. No.:
J3518/GCL/PGM/3MRP-M44

Activity ID	Activity Name	Orig. Durn.	Act. Start / FC Early Start	Rem. Durn.	Act. Finish / FC Early Finish	Late Start	Late Finish	Total Float	Physical % Complete	2016												2017											
										2016						2017						2017						2017					
										19	26	02	09	16	23	30	06	13	20	27	03	10	17	24	31	07	14	21	28	04	11	18	25
Pier A8 (A1d)																																	
Pier Head Segment																																	
A08-C5410	A8 - PHS Diaphragm - Rebar, Formwork, Concreting	36	02-Dec-16 A	6	27-Jan-17	12-Jan-16	18-Jan-16	-305	50%																								
A08-C5420	A8 - PHS Diaphragm - Curing & Striking of Forms	12	01-Feb-17	12	14-Feb-17	19-Jan-16	01-Feb-16	-305	0%																								
Pier A9 (A1c)																																	
Pier Head Segment																																	
A09-C5210	A9 - PHS - Temporary Platform	12	13-Feb-17	12	25-Feb-17	26-Jan-16	11-Feb-16	-309	0%																								
A09-C5310	A9 - Install PH Segment (1 nr)	2	27-Feb-17*	2	28-Feb-17	12-Feb-16	13-Feb-16	-309	0%																								
A09-C5410	A9 - PHS Diaphragm - Rebar, Formwork, Concreting	36	01-Mar-17	36	12-Apr-17	15-Feb-16	30-Mar-16	-309	0%																								
A09-C5420	A9 - PHS Diaphragm - Curing & Striking of Forms	6	13-Apr-17	6	22-Apr-17	31-Mar-16	07-Apr-16	-309	0%																								
Pier A10 (A1b)																																	
Pier Head Segment																																	
A10-C5210	A10 - PHS - Temporary Platform	12	03-Apr-17	12	20-Apr-17	16-Apr-16	29-Apr-16	-288	0%																								
Pier A11 (A1a)																																	
Pier Head Segment																																	
A11-C5210	A11 - PHS - Temporary Platform	12	28-Mar-17	12	11-Apr-17	18-Jul-16	30-Jul-16	-208	0%																								
A11-C5310	A11 - Install PH Segment (1nr)	2	12-Apr-17*	2	13-Apr-17	01-Aug-16	02-Aug-16	-208	0%																								
Ramp A																																	
Abutment & Approach Ramp A																																	
Ramp Structure																																	
ARA-C6140	Ramp A - Remaining RE & RC Walls	48	21-Jan-17*	48	21-Mar-17	21-Jan-16	19-Mar-16	-297	0%																								
ARA-C6150	Ramp A - Backfill to Walls	18	15-Mar-17	18	04-Apr-17	14-Mar-16	07-Apr-16	-297	0%																								
Ramp Finishes, E&M & Roadworks																																	
ARA-C7710	Ramp A - Parapet Panels	42	06-Apr-17	42	31-May-17	08-Apr-16	28-May-16	-297	0%																								
Viaduct B - Bridge B1																																	
Pier B17 (B1c)																																	
Foundation - Socketed H-Piles																																	
B17-C2110	B17 - Install SH Pile (10 nr) (incl. proof drilling)	36	01-Dec-16 A	0	10-Jan-17 A				100%																								
Pile Cap																																	
B17-C3110	B17 - Pile Cap Excavation / ELS & Break Pile	24	16-Jan-17 A	19	15-Feb-17	22-Dec-15	15-Jan-16	-320	0%																								
B17-C3210	B17 - Pile Cap Blinding, Rebar, Formwork, Concrete	15	16-Feb-17	15	04-Mar-17	16-Jan-16	02-Feb-16	-320	0%																								
B17-C3310	B17 - Pile Cap Curing, Strike Formwork, CJ Prep, Backfill	6	06-Mar-17	6	11-Mar-17	03-Feb-16	12-Feb-16	-320	0%																								
Pier																																	
B17-C4110	B17 - Pier Scaffold, Rebar, Formwork, Concrete (1st Lift)	12	13-Mar-17	12	25-Mar-17	13-Feb-16	26-Feb-16	-320	0%																								
B17-C4210	B17 - Pier Scaffold, Rebar, Formwork, Concrete (2nd Lift)	15	27-Mar-17	15	13-Apr-17	27-Feb-16	15-Mar-16	-320	0%																								
B17-C4310	B17 - Pier Curing, Remove Formwork	6	18-Apr-17	6	24-Apr-17	16-Mar-16	22-Mar-16	-320	0%																								
Pier B18 (B1b)																																	
Foundation - Socketed H-Piles																																	
B18-C2110	B18 - Install SH Pile (6 nr) (incl. proof drilling)	27	09-Dec-16 A	0	14-Jan-17 A				100%																								
Pile Cap																																	
B18-C3110	B18 - Pile Cap Excavation / ELS & Break Pile	24	06-Feb-17*	24	04-Mar-17	14-Apr-16	12-May-16	-242	0%																								
B18-C3210	B18 - Pile Cap Blinding, Rebar, Formwork, Concrete	15	06-Mar-17	15	22-Mar-17	13-May-16	31-May-16	-242	0%																								
B18-C3310	B18 - Pile Cap Curing, Strike Formwork, CJ Prep, Backfill	6	23-Mar-17	6	29-Mar-17	01-Jun-16	07-Jun-16	-242	0%																								
Pier																																	
B18-C4110	B18 - Pier Scaffold, Rebar, Formwork, Concrete	18	30-Mar-17	18	24-Apr-17	08-Jun-16	29-Jun-16	-242	0%																								
Ramp B																																	
Abutment & Approach Ramp B																																	
Ramp Structure																																	
ARB-C6110	Ramp B - Erect Fence / Enabling Works	12	16-Jan-17 A	11	06-Feb-17	01-Mar-16	12-Mar-16	-266	20%																								
ARB-C6120	Ramp B - RE Wall - Excavation & Bottom Layer to Grnd Level	36	07-Feb-17	36	20-Mar-17	14-Mar-16	28-Apr-16	-266	0%																								
ARB-C6130	Ramp B - RE Wall - Upper Layer With Backfill in Stages	48	21-Mar-17	48	22-May-17	29-Apr-16	27-Jun-16	-266	0%																								
Viaduct C - Bridge C2																																	
Pier C16 (C2b)																																	
Pier Head Segment																																	
C16-C5410	C16 - PHS Diaphragm - Rebar, Formwork, Concreting	36	15-Nov-16 A	0	24-Dec-16 A				100%																								
C16-C5420	C16 - PHS Diaphragm - Curing & Striking of Forms	6	28-Dec-16 A	0	04-Jan-17 A				100%																								
Ramp C																																	

Actual Work
 Planned Bar
 Critical Bar
 Milestone

Project ID: TMCLK-DWPH-M44
 Layout: J3518-DWP-3MRP Submission - M44
 Filter: TASK filters: 3-Month Lookahead, No CC
 Milestones, No Level of Effort.

Tuen Mun - Chek Lap Kok Link - Southern Connection
3-Month Rolling Programme (Page 5 of 13 Pages)
(Progress as of 21-Jan-17)

Date	Revision	Checked	Approved
30-Nov-...		PKN	GL
03-Jan-17		PKN	GL
26-Jan-17		PKN	GL

DWG. No.:
J3518/GCL/PGM/3MRP-M44

Activity ID	Activity Name	Orig. Durn.	Act. Start / FC Early Start	Rem. Durn.	Act. Finish / FC Early Finish	Late Start	Late Finish	Total Float	Physical % Complete	2016												2017																							
										2016						2017						2017						2017																	
										19	26	02	09	16	23	30	06	13	20	27	03	10	17	24	31	07	14	21	28	04	11	18	25	01	08	15	22	29	05	12	19	26	02	09	16
Abutment & Approach Ramp C																																													
Ramp Structure																																													
ARC-C6140	Ramp C - RC Wall - Backfill	12	16-May-16 A	22	18-Feb-17	15-Jan-16	12-Feb-16	-302	90%																																				
ARC-C6150	Ramp C - Utility - Termination of 800 Tee	72	21-Sep-16 A	22	18-Feb-17	15-Jan-16	12-Feb-16	-302	0%																																				
ARC-C6160	Ramp C - Utility - Remove 800 Tee & Backfill	12	20-Feb-17	12	04-Mar-17	13-Feb-16	26-Feb-16	-302	0%																																				
ARC-C6170	Ramp C - RE Wall - Remaining Bays at 800 Tee	36	06-Mar-17	36	20-Apr-17	27-Feb-16	13-Apr-16	-302	0%																																				
Ramp Finishes, E&M & Roadworks																																													
ARC-C7710	Ramp C - Parapet Panels (Initial)	24	26-Sep-16 A	30	28-Feb-17	21-Apr-16	27-May-16	-226	10%																																				
Viaduct D - Bridge D2																																													
Pier D13 (D2d)																																													
Pier Head Segment																																													
D13-C5410	D13 - PHS Diaphragm - Rebar, Formwork, Concreting	42	12-Sep-16 A	6	27-Jan-17	11-Feb-16	17-Feb-16	-282	60%																																				
D13-C5420	D13 - PHS Diaphragm - Curing, Striking of Forms, Remove Scaffold	12	01-Feb-17	12	14-Feb-17	18-Feb-16	02-Mar-16	-282	0%																																				
Ramp D																																													
Abutment & Approach Ramp D																																													
Ramp Structure																																													
ARD-C6140	Ramp D - Box Structure Bay 1 & Bay 8	55	07-Mar-16 A	9	03-Feb-17	16-Mar-16	29-Mar-16	-253	80%																																				
ARD-C6150	Ramp D - Backfill Embankment	90	02-Nov-15 A	22	18-Feb-17	16-Mar-16	14-Apr-16	-253	70%																																				
Ramp Finishes, E&M & Roadworks																																													
ARD-C7710	Ramp D - Parapet Panels	42	15-Oct-16 A	46	18-Mar-17	16-Mar-16	13-May-16	-253	50%																																				
ARD-C7720	Ramp D - Ducting, Gantry & TCSS Provisions (KD4)	36	06-Mar-17	36	20-Apr-17	29-Apr-16	13-Jun-16	-253	0%																																				
ARD-C7810	Ramp D - Drainage, Fire Main & E&M Services	54	27-Mar-17	54	05-Jun-17	23-May-16	26-Jul-16	-253	0%																																				
Viaduct E - Bridge E2																																													
Pier E4A (E2b2)																																													
Pier Head Segment																																													
E04A-C5140	E4A - Remove Rail Beams, Megashore Towers. Crane	17	13-Oct-16 A	0	24-Dec-16 A				100%																																				
E04A-C5145	E4A - Install Infill Segments (4 nr) - THB	26	14-Nov-16 A	0	12-Jan-17 A				100%																																				
E04A-C5150	E4A - IFS Stitch & Remove Equipment	9	13-Jan-17 A	12	07-Feb-17	04-Jul-16	16-Jul-16	-167	35%																																				
Pier E4B (E2b1)																																													
Pier Head Segment																																													
E04B-C5130	E4B - Diaphragm of PHS - Formwork, Rebar, Concreting	125	14-Sep-16 A	0	19-Jan-17 A				100%																																				
E04B-C5140	E4B - Remove Rail Beams, Megashore Towers	8	20-Jan-17 A	13	08-Feb-17	07-Jul-16	21-Jul-16	-164	5%																																				
E04B-C5145	E4B - Install Infill Segments (4 nr) - THB	21	09-Feb-17	21	04-Mar-17	22-Jul-16	15-Aug-16	-164	0%																																				
E04B-C5150	E4B - IFS Stitch & Remove Equipment	10	06-Mar-17	10	16-Mar-17	16-Aug-16	26-Aug-16	-164	0%																																				
Pier E5A (E2c2)																																													
Pier Head Segment																																													
E05A-C5145	E5A - Install Infill Segments (4 nr) - THB	23	12-Nov-16 A	0	31-Dec-16 A				100%																																				
E05A-C5150	E5A - IFS Stitch & Remove Equipment	12	03-Jan-17 A	7	01-Feb-17	05-Jan-16	12-Jan-16	-311	70%																																				
Pier E5B (E2c1)																																													
Pier Head Segment																																													
E05B-C5145	E5B - Install Infill Segments (4 nr) - THB	15	08-Dec-16 A	0	04-Jan-17 A				100%																																				
E05B-C5150	E5B - IFS Stitch & Remove Equipment	12	05-Jan-17 A	5	26-Jan-17	03-Feb-16	11-Feb-16	-286	70%																																				
Pier E6A (E2d2)																																													
Pier Head Segment																																													
E06A-C5145	E6A - Install Infill Segments (4 nr) - THB	16	29-Nov-16 A	0	18-Jan-17 A				100%																																				
E06A-C5150	E6A - IFS Stitch & Remove Equipment	11	19-Jan-17 A	10	04-Feb-17	18-Feb-16	29-Feb-16	-276	15%																																				
Pier E6B (E2d1)																																													
Pier Head Segment																																													
E06B-C5140	E6B - Remove Rail Beams	9	06-Dec-16 A	0	04-Jan-17 A				100%																																				
E06B-C5145	E6B - Install Infill Segments (4 nr) - THB	17	16-Dec-16 A	11	06-Feb-17	08-Mar-16	19-Mar-16	-260	50%																																				
E06B-C5150	E6B - IFS Stitch & Remove Equipment	10	07-Feb-17	10	17-Feb-17	21-Mar-16	05-Apr-16	-260	0%																																				
Pier E7A (E2e2)																																													
Pier Head Segment																																													
E07A-C5140	E7A - Remove Rail Beams, Crane	14	15-Dec-16 A	0	06-Jan-17 A				100%																																				
E07A-C5145	E7A - Install Infill Segments (4 nr) - THB	18	07-Jan-17 A	21	17-Feb-17	13-Feb-16	08-Mar-16	-280	40%																																				
E07A-C5150	E7A - IFS Stitch & Remove Equipment	10	18-Feb-17	10	01-Mar-17	09-Mar-16	19-Mar-16	-280	0%																																				
Pier E7B (E2e1)																																													

Actual Work
 Planned Bar
 Critical Bar
 Milestone

Project ID: TMCLK-DWPH-M44
 Layout: J3518-DWP-3MRP Submission - M44
 Filter: TASK filters: 3-Month Lookahead, No CC
 Milestones, No Level of Effort.

Tuen Mun - Chek Lap Kok Link - Southern Connection
3-Month Rolling Programme (Page 6 of 13 Pages)
(Progress as of 21-Jan-17)

Date	Revision	Checked	Approved
30-Nov-...		PKN	GL
03-Jan-17		PKN	GL
26-Jan-17		PKN	GL

DWG. No.:
J3518/GCL/PGM/3MRP-M44

Activity ID	Activity Name	Orig. Durn.	Act. Start / FC Early Start	Rem. Durn.	Act. Finish / FC Early Finish	Late Start	Late Finish	Total Float	Physical % Complete	2016												2017											
										January						February						March						April					
										19	26	02	09	16	23	30	06	13	20	27	06	13	20	27	03	10	17	24					
Pier Head Segment																																	
E07B-C5130	E7B - Diaphragm of PHS - Formwork, Rebar, Concreting	76	14-Oct-16 A	0	20-Jan-17 A				100%																								
E07B-C5140	E7B - Remove Rail Beams	15	21-Jan-17	15	10-Feb-17	03-Dec-15	19-Dec-15	-336	0%																								
E07B-C5145	E7B - Install Infill Segments (4 nr) - THB	18	06-Mar-17*	18	25-Mar-17	21-Dec-15	13-Jan-16	-355	0%																								
E07B-C5150	E7B - IFS Stitch & Remove Equipment	10	27-Mar-17	10	07-Apr-17	14-Jan-16	25-Jan-16	-355	0%																								
Pier E8A (E2f2)																																	
Pier Head Segment																																	
E08A-C5130	E8A - Diaphragm of PHS - Formwork, Rebar, Concreting	82	28-Sep-16 A	0	30-Dec-16 A				100%																								
E08A-C5140	E8A - Remove Rail Beams, Crane	8	31-Dec-16 A	0	17-Jan-17 A				100%																								
E08A-C5145	E8A - Install Infill Segments (4 nr) - THB	18	18-Jan-17 A	18	14-Feb-17	14-Nov-15	04-Dec-15	-352	50%																								
E08A-C5150	E8A - IFS Stitch & Remove Equipment	10	15-Feb-17	10	25-Feb-17	05-Dec-15	16-Dec-15	-352	0%																								
Pier E8B (E2f1)																																	
Pier Head Segment																																	
E08B-C5130	E8B - Diaphragm of PHS - Formwork, Rebar, Concreting	61	26-Oct-16 A	0	18-Jan-17 A				100%																								
E08B-C5140	E8B - Remove Rail Beams	8	11-Jan-17 A	10	04-Feb-17	07-Apr-16	18-Apr-16	-238	50%																								
E08B-C5145	E8B - Install Infill Segments (4 nr) - THB	18	06-Feb-17	18	25-Feb-17	19-Apr-16	10-May-16	-238	0%																								
E08B-C5150	E8B - IFS Stitch & Remove Equipment	10	27-Feb-17	10	09-Mar-17	11-May-16	23-May-16	-238	0%																								
Pier E9A (E2g2)																																	
Pier Head Segment																																	
E09A-C5130	E9A - Diaphragm of PHS - Formwork, Rebar, Concreting	86	23-Sep-16 A	0	17-Jan-17 A				100%																								
E09A-C5140	E9A - Remove Rail Beams, Crane	14	18-Jan-17 A	15	10-Feb-17	04-Jan-16	20-Jan-16	-312	15%																								
E09A-C5145	E9A - Install Infill Segments (4 nr) - THB	18	11-Feb-17	18	03-Mar-17	21-Jan-16	13-Feb-16	-312	0%																								
E09A-C5150	E9A - IFS Stitch & Remove Equipment	10	04-Mar-17	10	15-Mar-17	15-Feb-16	25-Feb-16	-312	0%																								
Pier E9B (E2g1)																																	
Pier Head Segment																																	
E09B-C5130	E9B - Diaphragm of PHS - Formwork, Rebar, Concreting	33	17-Oct-16 A	4	25-Jan-17	01-Feb-16	04-Feb-16	-288	50%																								
E09B-C5140	E9B - Remove Rail Beams	36	26-Jan-17	36	11-Mar-17	05-Feb-16	21-Mar-16	-288	0%																								
E09B-C5145	E9B - Install Infill Segments (4 nr) - THB	19	27-Mar-17	19	21-Apr-17	22-Mar-16	16-Apr-16	-300	0%																								
Pier E10A (E2h2)																																	
Pier Head Segment																																	
E10A-C5130	E10A - Diaphragm of PHS - Formwork, Rebar, Concreting	56	15-Oct-16 A	0	19-Jan-17 A				100%																								
E10A-C5140	E10A - Remove Rail Beams, Crane	13	20-Jan-17 A	19	15-Feb-17	03-May-16	25-May-16	-217	5%																								
E10A-C5145	E10A - Install Infill Segments (4 nr) - THB	17	01-Mar-17*	17	20-Mar-17	26-May-16	15-Jun-16	-228	0%																								
E10A-C5150	E10A - IFS Stitch & Remove Equipment	12	21-Mar-17	12	03-Apr-17	16-Jun-16	29-Jun-16	-228	0%																								
Pier E10B (E2h1)																																	
Pier Head Segment																																	
E10B-C5130	E10B - Diaphragm of PHS - Formwork, Rebar, Concreting	51	19-Nov-16 A	3	24-Jan-17	28-Apr-16	30-Apr-16	-220	95%																								
E10B-C5140	E10B - Remove Rail Beams	18	25-Jan-17	18	17-Feb-17	03-May-16	24-May-16	-220	0%																								
E10B-C5145	E10B - Install Infill Segments (4 nr) - THB	18	18-Feb-17	18	10-Mar-17	25-May-16	15-Jun-16	-220	0%																								
E10B-C5150	E10B - IFS Stitch & Remove Equipment	12	11-Mar-17	12	24-Mar-17	16-Jun-16	29-Jun-16	-220	0%																								
Viaduct E - Bridge E5, E6, E7, E8																																	
Pier E11A (E7E8a)																																	
Pier Head Segment																																	
E11A-C5130	E11A - Diaphragm of PHS - Formwork, Rebar, Concreting	80	10-Dec-16 A	58	01-Apr-17	05-Nov-15	14-Jan-16	-360	35%																								
E11A-C5140	E11A - Remove Rail Beams, Spreader Beams, Crane	14	03-Apr-17	14	22-Apr-17	15-Jan-16	30-Jan-16	-360	0%																								
Pier E11B (E5e6a)																																	
Pier Head Segment																																	
E11B-C5130	E11B - Diaphragm of PHS - Formwork, Rebar, Concreting	81	19-Dec-16 A	59	03-Apr-17	04-Jun-15	13-Aug-15	-486	30%																								
E11B-C5140	E11B - Remove Rail Beams, Spreader Beams	14	04-Apr-17	14	24-Apr-17	14-Aug-15	29-Aug-15	-486	0%																								
Pier E12A (E8b)																																	
Pile Cap Dolphin																																	
E12A-C3130	E12A - Dolphin - Marine Pile Cap - Fixings, Dewatering & Trim Pile	11	20-Feb-17*	11	03-Mar-17	07-Nov-16	18-Nov-16	-84	0%																								
E12A-C3150	E12A - Dolphin - Marine Pile Cap - Rebar, Concreting	5	04-Mar-17	5	09-Mar-17	19-Nov-16	24-Nov-16	-84	0%																								
E12A-C3160	E12A - Dolphin - Marine Pile Cap - CJ preparation & Curing	3	10-Mar-17	3	13-Mar-17	25-Nov-16	28-Nov-16	-84	0%																								
Pier Head Segment / Infill Segment																																	
E12A-C5110	E12A - Temp. Work, Grillages, Megashore Towers, Rail Beams	28	17-Dec-16 A	16	11-Feb-17	02-Jun-15	19-Jun-15	-488	60%																								
E12A-C5120	E12A - Install PH Segment (4 nr)	10	13-Feb-17	10	23-Feb-17	22-Jun-15	03-Jul-15	-488	0%																								
E12A-C5130	E12A - Diaphragm of PHS - Formwork, Rebar, Concreting	78	24-Feb-17	78	02-Jun-17	04-Jul-15	06-Oct-15	-488	0%																								

■ Actual Work
■ Planned Bar
■ Critical Bar
◆ Milestone

Project ID: TMCLK-DWPH-M44
 Layout: J3518-DWP-3MRP Submission - M44
 Filter: TASK filters: 3-Month Lookahead, No CC
 Milestones, No Level of Effort.

Tuen Mun - Chek Lap Kok Link - Southern Connection
3-Month Rolling Programme (Page 7 of 13 Pages)
(Progress as of 21-Jan-17)

Date	Revision	Checked	Approved
30-Nov-...		PKN	GL
03-Jan-17		PKN	GL
26-Jan-17		PKN	GL

DWG. No.:
J3518/GCL/PGM/3MRP-M44

Activity ID	Activity Name	Orig. Durn.	Act. Start / FC Early Start	Rem. Durn.	Act. Finish / FC Early Finish	Late Start	Late Finish	Total Float	Physical % Complete	2016												2017																			
										January				February				March				April				January				February				March				April			
										19	26	02	09	16	23	30	06	13	20	27	06	13	20	27	03	10	17	24	19	26	02	09	16	23	30	06	13	20	27	03	10
Pier E12B (E7b)																																									
Pier Head Segment / Infill Segment																																									
E12B-C5110	E12B - Temp. Work, Grillages, Megashore Towers, Rail Beams	29	02-Dec-16 A	0	07-Jan-17 A				100%	[Gantt bar: 02-Dec-16 to 07-Jan-17, 100% complete]																															
E12B-C5120	E12B - Install PH Segment (4 nr)	8	08-Jan-17 A	14	09-Feb-17	07-Dec-15	22-Dec-15	-333	75%	[Gantt bar: 08-Jan-17 to 09-Feb-17, 75% complete]																															
E12B-C5130	E12B - Diaphragm of PHS - Formwork, Rebar, Concreting	81	10-Feb-17	81	22-May-17	23-Dec-15	06-Apr-16	-333	0%	[Gantt bar: 10-Feb-17 to 22-May-17, 0% complete]																															
Pier E12C (E6b)																																									
Pier Head Segment / Infill Segment																																									
E12C-C5110	E12C - Temp. Work, Grillages, Megashore Towers, Rail Beams	28	29-Nov-16 A	0	11-Jan-17 A				100%	[Gantt bar: 29-Nov-16 to 11-Jan-17, 100% complete]																															
E12C-C5120	E12C - Install PH Segment (4 nr)	10	12-Jan-17 A	2	23-Jan-17	17-Dec-15	18-Dec-15	-324	0%	[Gantt bar: 12-Jan-17 to 23-Jan-17, 0% complete]																															
E12C-C5130	E12C - Diaphragm of PHS - Formwork, Rebar, Concreting	79	24-Jan-17	79	05-May-17	19-Dec-15	30-Mar-16	-324	0%	[Gantt bar: 24-Jan-17 to 05-May-17, 0% complete]																															
Pier E12D (E5b)																																									
Pier																																									
E12D-C4050	E12D Pier - Curing, CJ, Remove Formwork & Falsework	12	16-Dec-16 A	0	11-Jan-17 A				100%	[Gantt bar: 16-Dec-16 to 11-Jan-17, 100% complete]																															
Pier Head Segment / Infill Segment																																									
E12D-C5110	E12D - Temp. Work, Grillages, Megashore Towers, Rail Beams	28	12-Jan-17 A	20	16-Feb-17	26-May-15	17-Jun-15	-494	40%	[Gantt bar: 12-Jan-17 to 16-Feb-17, 40% complete]																															
E12D-C5120	E12D - Install PH Segment (4 nr)	10	17-Feb-17	10	28-Feb-17	18-Jun-15	30-Jun-15	-494	0%	[Gantt bar: 17-Feb-17 to 28-Feb-17, 0% complete]																															
E12D-C5130	E12D - Diaphragm of PHS - Formwork, Rebar, Concreting	77	01-Mar-17	77	06-Jun-17	02-Jul-15	02-Oct-15	-494	0%	[Gantt bar: 01-Mar-17 to 06-Jun-17, 0% complete]																															
Pier E13A (E8c)																																									
Pier																																									
E13A-C4050	E13A Pier - Curing, CJ, Remove Formwork & Falsework	12	17-Dec-16 A	0	11-Jan-17 A				100%	[Gantt bar: 17-Dec-16 to 11-Jan-17, 100% complete]																															
Pier Head Segment / Infill Segment																																									
E13A-C5110	E13A - Temp. Work, Grillages, Megashore Towers, Rail Beams	29	12-Jan-17 A	21	17-Feb-17	22-May-15	16-Jun-15	-496	25%	[Gantt bar: 12-Jan-17 to 17-Feb-17, 25% complete]																															
E13A-C5120	E13A - Install PH Segment (4 nr)	8	18-Feb-17	8	27-Feb-17	17-Jun-15	26-Jun-15	-496	0%	[Gantt bar: 18-Feb-17 to 27-Feb-17, 0% complete]																															
E13A-C5130	E13A - Diaphragm of PHS - Formwork, Rebar, Concreting	77	28-Feb-17	77	05-Jun-17	27-Jun-15	26-Sep-15	-496	0%	[Gantt bar: 28-Feb-17 to 05-Jun-17, 0% complete]																															
Pier E13B (E7c)																																									
Pier																																									
E13B-C4030	E13B Pier - TW, Rebar, Formwork, Concreting - Upper Arm (Solid)	52	31-Oct-16 A	0	29-Dec-16 A				100%	[Gantt bar: 31-Oct-16 to 29-Dec-16, 100% complete]																															
E13B-C4040	E13B Pier - Curing, CJ, Remove Formwork & Falsework	12	30-Dec-16 A	0	16-Jan-17 A				100%	[Gantt bar: 30-Dec-16 to 16-Jan-17, 100% complete]																															
Pier Head Segment / Infill Segment																																									
E13B-C5110	E13B - Temp. Work, Grillages, Megashore Towers, Rail Beams	29	17-Jan-17 A	25	22-Feb-17	27-May-15	25-Jun-15	-493	15%	[Gantt bar: 17-Jan-17 to 22-Feb-17, 15% complete]																															
E13B-C5120	E13B - Install PH Segment (4 nr)	8	23-Feb-17	8	03-Mar-17	26-Jun-15	06-Jul-15	-493	0%	[Gantt bar: 23-Feb-17 to 03-Mar-17, 0% complete]																															
E13B-C5130	E13B - Diaphragm of PHS - Formwork, Rebar, Concreting	77	04-Mar-17	77	09-Jun-17	07-Jul-15	07-Oct-15	-493	0%	[Gantt bar: 04-Mar-17 to 09-Jun-17, 0% complete]																															
Pier E13C (E6c)																																									
Pier																																									
E13C-C4030	E13C Pier - TW, Rebar, Formwork, Concreting - Upper Arm (Solid)	36	15-Nov-16 A	0	27-Dec-16 A				100%	[Gantt bar: 15-Nov-16 to 27-Dec-16, 100% complete]																															
E13C-C4040	E13C Pier - Curing, CJ, Remove Formwork & Falsework	12	28-Dec-16 A	0	20-Jan-17 A				100%	[Gantt bar: 28-Dec-16 to 20-Jan-17, 100% complete]																															
Pier Head Segment / Infill Segment																																									
E13C-C5110	E13C - Temp. Work, Grillages, Megashore Towers, Rail Beams	29	21-Jan-17	29	27-Feb-17	04-Sep-15	09-Oct-15	-410	0%	[Gantt bar: 21-Jan-17 to 27-Feb-17, 0% complete]																															
E13C-C5120	E13C - Install PH Segment (4 nr)	12	28-Feb-17	12	13-Mar-17	10-Oct-15	24-Oct-15	-410	0%	[Gantt bar: 28-Feb-17 to 13-Mar-17, 0% complete]																															
E13C-C5130	E13C - Diaphragm of PHS - Formwork, Rebar, Concreting	76	14-Mar-17	76	17-Jun-17	26-Oct-15	25-Jan-16	-410	0%	[Gantt bar: 14-Mar-17 to 17-Jun-17, 0% complete]																															
Pier E13D (E5c)																																									
Pier																																									
E13D-C4030	E13D Pier - TW, Rebar, Formwork, Concreting - Upper Arm (Solid)	36	21-Nov-16 A	0	30-Dec-16 A				100%	[Gantt bar: 21-Nov-16 to 30-Dec-16, 100% complete]																															
E13D-C4040	E13D Pier - Curing, CJ, Remove Formwork & Falsework	12	31-Dec-16 A	3	24-Jan-17	12-Aug-15	14-Aug-15	-429	0%	[Gantt bar: 31-Dec-16 to 24-Jan-17, 0% complete]																															
Pier Head Segment / Infill Segment																																									
E13D-C5110	E13D - Temp. Work, Grillages, Megashore Towers, Rail Beams	29	25-Jan-17	29	02-Mar-17	15-Aug-15	18-Sep-15	-429	0%	[Gantt bar: 25-Jan-17 to 02-Mar-17, 0% complete]																															
E13D-C5120	E13D - Install PH Segment (4 nr)	8	03-Mar-17	8	11-Mar-17	19-Sep-15	29-Sep-15	-429	0%	[Gantt bar: 03-Mar-17 to 11-Mar-17, 0% complete]																															
E13D-C5130	E13D - Diaphragm of PHS - Formwork, Rebar, Concreting	77	13-Mar-17	77	17-Jun-17	30-Sep-15	02-Jan-16	-429	0%	[Gantt bar: 13-Mar-17 to 17-Jun-17, 0% complete]																															
Pier E14A (E8d)																																									
Foundation - Bored Piles																																									
E14A-C2140	E14A EB Pile - Excavate, Rebar, Concrete (2nd) P3 - Resume	9	20-Dec-16 A	0	16-Jan-17 A				100%	[Gantt bar: 20-Dec-16 to 16-Jan-17, 100% complete]																															
E14A-C2210	E14A EB Pile - Curing & Sonic Test	18	17-Jan-17 A	14	09-Feb-17	10-Jul-15	25-Jul-15	-457	0%	[Gantt bar: 17-Jan-17 to 09-Feb-17, 0% complete]																															
E14A-C2220	E14A EB Pile - Full Depth Core & Test	12	10-Feb-17	12	23-Feb-17	27-Jul-15	08-Aug-15	-457	0%	[Gantt bar: 10-Feb-17 to 23-Feb-17, 0% complete]																															
Pile Cap																																									
E14A-C3110	E14A Pile Cap - Excavate, Break Pile Head	15	24-Feb-17*	15	13-Mar-17	10-Aug-15	26-Aug-15	-457	0%	[Gantt bar: 24-Feb-17 to 13-Mar-17, 0% complete]																															
E14A-C3210	E14A Pile Cap - Blinding, Formwork, Rebar, Concrete	19	14-Mar-17	19	04-Apr-17	27-Aug-15	18-Sep-15	-457	0%	[Gantt bar: 14-Mar-17 to 04-Apr-17, 0% complete]																															
E14A-C3310	E14A Pile Cap - Curing, Remove Formwork, Backfill	12	06-Apr-17	12	22-Apr-17	19-Sep-15	05-Oct-15	-457	0%	[Gantt bar: 06-Apr-17 to 22-Apr-17, 0% complete]																															
Pier E14B (E7d)																																									

■ Actual Work
■ Planned Bar
■ Critical Bar
◆ Milestone

Project ID: TMCLK-DWPH-M44
 Layout: J3518-DWP-3MRP Submission - M44
 Filter: TASK filters: 3-Month Lookahead, No CC
 Milestones, No Level of Effort.

Tuen Mun - Chek Lap Kok Link - Southern Connection
3-Month Rolling Programme (Page 8 of 13 Pages)
(Progress as of 21-Jan-17)

Date	Revision	Checked	Approved
30-Nov-...		PKN	GL
03-Jan-17		PKN	GL
26-Jan-17		PKN	GL

DWG. No.:
J3518/GCL/PGM/3MRP-M44

Activity ID	Activity Name	Orig. Durn.	Act. Start / FC Early Start	Rem. Durn.	Act. Finish / FC Early Finish	Late Start	Late Finish	Total Float	Physical % Complete	2016												2017															
										January						February						March						April									
										19	26	02	09	16	23	30	06	13	20	27	03	10	17	24													
Foundation - Bored Piles																																					
E14B-C2140	E14B EB Pile - Excavate, Rebar, Concrete (3rd) P1	19	19-Dec-16 A	1	21-Jan-17	26-Jun-15	26-Jun-15	-468	0%	[Gantt bar: 21-Jan-17 to 26-Jun-15]																											
E14B-C2210	E14B EB Pile - Curing & Sonic Test	18	23-Jan-17	18	15-Feb-17	27-Jun-15	18-Jul-15	-468	0%	[Gantt bar: 15-Feb-17 to 18-Jul-15]																											
E14B-C2220	E14B EB Pile - Full Depth Core & Test	12	16-Feb-17	12	01-Mar-17	20-Jul-15	01-Aug-15	-468	0%	[Gantt bar: 01-Mar-17 to 01-Aug-15]																											
Pile Cap																																					
E14B-C3110	E14B Pile Cap - Excavate, Break Pile Head	15	17-Mar-17*	15	03-Apr-17	03-Aug-15	19-Aug-15	-481	0%	[Gantt bar: 03-Apr-17 to 19-Aug-15]																											
E14B-C3210	E14B Pile Cap - Blinding, Formwork, Rebar, Concrete	19	04-Apr-17	19	29-Apr-17	20-Aug-15	11-Sep-15	-481	0%	[Gantt bar: 29-Apr-17 to 11-Sep-15]																											
Pier E14C (E6d)																																					
Foundation - Bored Piles																																					
E14C-C2140	E14C EB Pile - Excavate, Rebar, Concrete (3rd) P2	18	07-Dec-16 A	0	17-Jan-17 A				100%	[Gantt bar: 17-Jan-17 to 17-Jan-17]																											
E14C-C2210	E14C EB Pile - Curing & Sonic Test	18	18-Jan-17 A	15	10-Feb-17	08-Oct-15	26-Oct-15	-383	0%	[Gantt bar: 10-Feb-17 to 26-Oct-15]																											
Pile Cap																																					
E14C-C3110	E14C Pile Cap - Excavate, Break Pile Head	15	11-Feb-17	15	28-Feb-17	27-Oct-15	12-Nov-15	-383	0%	[Gantt bar: 28-Feb-17 to 12-Nov-15]																											
E14C-C3210	E14C Pile Cap - Blinding, Formwork, Rebar, Concrete	19	01-Mar-17	19	22-Mar-17	13-Nov-15	04-Dec-15	-383	0%	[Gantt bar: 22-Mar-17 to 04-Dec-15]																											
E14C-C3310	E14C Pile Cap - Curing, Remove Formwork, Backfill	12	23-Mar-17	12	06-Apr-17	05-Dec-15	18-Dec-15	-383	0%	[Gantt bar: 06-Apr-17 to 18-Dec-15]																											
Pier																																					
E14C-C4110	E14C Pier - Scaffold, Rebar, Formwork, Concrete (1st Lift)	13	07-Apr-17	13	25-Apr-17	19-Dec-15	06-Jan-16	-383	0%	[Gantt bar: 25-Apr-17 to 06-Jan-16]																											
Pier E14D (E5d)																																					
Foundation - Bored Piles																																					
E14D-C2130	E14D EB Pile - Excavate, Rebar, Concrete (2nd) P4	18	29-Nov-16 A	0	12-Jan-17 A				100%	[Gantt bar: 12-Jan-17 to 12-Jan-17]																											
E14D-C2140	E14D EB Pile - Excavate, Rebar, Concrete (3rd) P1	18	13-Jan-17 A	12	07-Feb-17	13-Apr-15	25-Apr-15	-529	0%	[Gantt bar: 07-Feb-17 to 25-Apr-15]																											
E14D-C2150	E14D EB Pile - Excavate, Rebar, Concrete (4th) P3	18	14-Feb-17*	18	06-Mar-17	27-Apr-15	18-May-15	-534	0%	[Gantt bar: 06-Mar-17 to 18-May-15]																											
E14D-C2210	E14D EB Pile - Curing & Sonic Test	18	07-Mar-17	18	27-Mar-17	19-May-15	09-Jun-15	-534	0%	[Gantt bar: 27-Mar-17 to 09-Jun-15]																											
Pile Cap																																					
E14D-C3110	E14D Pile Cap - Excavate, Break Pile Head	15	28-Mar-17	15	18-Apr-17	10-Jun-15	27-Jun-15	-534	0%	[Gantt bar: 18-Apr-17 to 27-Jun-15]																											
E14D-C3210	E14D Pile Cap - Blinding, Formwork, Rebar, Concrete	19	19-Apr-17	19	12-May-17	29-Jun-15	21-Jul-15	-534	0%	[Gantt bar: 12-May-17 to 21-Jul-15]																											
Viaduct F - Bridge F1																																					
Pier F1 (F1b)																																					
Foundation - Bored Piles																																					
F01-C2210	F1 EB Pile - Curing & Sonic Test	18	12-Dec-16 A	3	24-Jan-17	01-Aug-15	04-Aug-15	-438	100%	[Gantt bar: 24-Jan-17 to 24-Jan-17]																											
Pile Cap																																					
F01-C3110	F1 Pile Cap - Excavate, Break Pile Head	15	25-Jan-17	15	14-Feb-17	05-Aug-15	21-Aug-15	-438	0%	[Gantt bar: 14-Feb-17 to 21-Aug-15]																											
F01-C3210	F1 Pile Cap - Blinding, Formwork, Rebar, Concrete	19	15-Feb-17	19	08-Mar-17	22-Aug-15	14-Sep-15	-438	0%	[Gantt bar: 08-Mar-17 to 14-Sep-15]																											
F01-C3310	F1 Pile Cap - Curing, Remove Formwork, Backfill	12	09-Mar-17	12	22-Mar-17	15-Sep-15	29-Sep-15	-438	0%	[Gantt bar: 22-Mar-17 to 29-Sep-15]																											
Pier																																					
F01-C4110	F1 Pier - Scaffold, Rebar, Formwork, Concrete (1st Lift)	13	23-Mar-17	13	07-Apr-17	30-Sep-15	15-Oct-15	-438	0%	[Gantt bar: 07-Apr-17 to 15-Oct-15]																											
F01-C4210	F1 Pier - Scaffold, Rebar, Formwork, Concrete (2nd Lift)	18	08-Apr-17	18	04-May-17	16-Oct-15	06-Nov-15	-438	0%	[Gantt bar: 04-May-17 to 06-Nov-15]																											
Pier F2 (F1c)																																					
Foundation - Bored Piles																																					
F02-C2110	F2 Fr Pile - Set-up Plant & Install Sleeve	6	01-Feb-17*	6	07-Feb-17	01-Jun-15	06-Jun-15	-495	0%	[Gantt bar: 07-Feb-17 to 06-Jun-15]																											
F02-C2120	F2 Fr Pile - Excavate, Rebar, Concrete (1st) P1	12	08-Feb-17	12	21-Feb-17	08-Jun-15	22-Jun-15	-495	0%	[Gantt bar: 21-Feb-17 to 22-Jun-15]																											
F02-C2130	F2 Fr Pile - Excavate, Rebar, Concrete (2nd) P2	12	25-Feb-17*	12	10-Mar-17	23-Jun-15	07-Jul-15	-498	0%	[Gantt bar: 10-Mar-17 to 07-Jul-15]																											
F02-C2140	F2 Fr Pile - Excavate, Rebar, Concrete (3rd) P3	12	28-Mar-17*	12	11-Apr-17	08-Jul-15	21-Jul-15	-512	0%	[Gantt bar: 11-Apr-17 to 21-Jul-15]																											
F02-C2210	F2 Fr Pile - Curing & Sonic Test	18	12-Apr-17	18	08-May-17	22-Jul-15	11-Aug-15	-512	0%	[Gantt bar: 08-May-17 to 11-Aug-15]																											
Pier F3 (F1d)																																					
Foundation - Bored Piles																																					
F03-C2130	F3 Fr Pile - Excavate, Rebar, Concrete (1st) P2	15	07-Feb-17*	15	23-Feb-17	26-Jun-15	14-Jul-15	-479	0%	[Gantt bar: 23-Feb-17 to 14-Jul-15]																											
F03-C2180	F3 Fr Pile - Excavate, Rebar, Concrete (2nd) P1 -Replacement	15	02-Mar-17*	15	18-Mar-17	15-Jul-15	31-Jul-15	-484	0%	[Gantt bar: 18-Mar-17 to 31-Jul-15]																											
F03-C2190	F3 Fr Pile - Excavate, Rebar, Concrete (3rd) P3	15	08-Apr-17*	15	28-Apr-17	01-Aug-15	18-Aug-15	-500	0%	[Gantt bar: 28-Apr-17 to 18-Aug-15]																											
Viaduct F - Bridge F2																																					
Pier F4 (F2b)																																					
Foundation - Bored Piles																																					
F04-C2110	F4 Fr Pile - Set-up Plant & Install Sleeve	6	14-Mar-17*	6	20-Mar-17	04-Sep-15	10-Sep-15	-451	0%	[Gantt bar: 20-Mar-17 to 10-Sep-15]																											
F04-C2120	F4 Fr Pile - Excavate, Rebar, Concrete (1st) P1	18	21-Mar-17	18	11-Apr-17	11-Sep-15	03-Oct-15	-451	0%	[Gantt bar: 11-Apr-17 to 03-Oct-15]																											
Pier F5 (F2c)																																					
Foundation - Bored Piles																																					
F05-C2140	F5 EB Pile - Excavate, Rebar, Concrete (3rd) P2	18	21-Dec-16 A	6	27-Jan-17	16-Oct-15	23-Oct-15	-376	100%	[Gantt bar: 27-Jan-17 to 27-Jan-17]																											
F05-C2210	F5 EB Pile - Curing & Sonic Test	18	01-Feb-17	18	21-Feb-17	24-Oct-15	13-Nov-15	-376	0%	[Gantt bar: 21-Feb-17 to 13-Nov-15]																											

■ Actual Work
■ Planned Bar
■ Critical Bar
◆ Milestone

Project ID: TMCLK-DWPH-M44
 Layout: J3518-DWP-3MRP Submission - M44
 Filter: TASK filters: 3-Month Lookahead, No CC
 Milestones, No Level of Effort.

Tuen Mun - Chek Lap Kok Link - Southern Connection
3-Month Rolling Programme (Page 9 of 13 Pages)
(Progress as of 21-Jan-17)

Date	Revision	Checked	Approved
30-Nov-...		PKN	GL
03-Jan-17		PKN	GL
26-Jan-17		PKN	GL

DWG. No.:
J3518/GCL/PGM/3MRP-M44

