


■ Planned Bar
■ Planned Bar - Critical
◆ Planned Milestone
■ Progress bar
◆ Progress Milestone

Date	Revision	Checked	Approved
12-Feb-14	TMCLKDJGENPRG08507	WYu	SPs
08-Apr-14	TMCLKDJGENPRG08507	SPs	WYu
28-Aug-14	TMCLKDJGENPRG08507	CLs	WYu
30-Oct-15	TMCLKDJGENPRG08507	WYu	

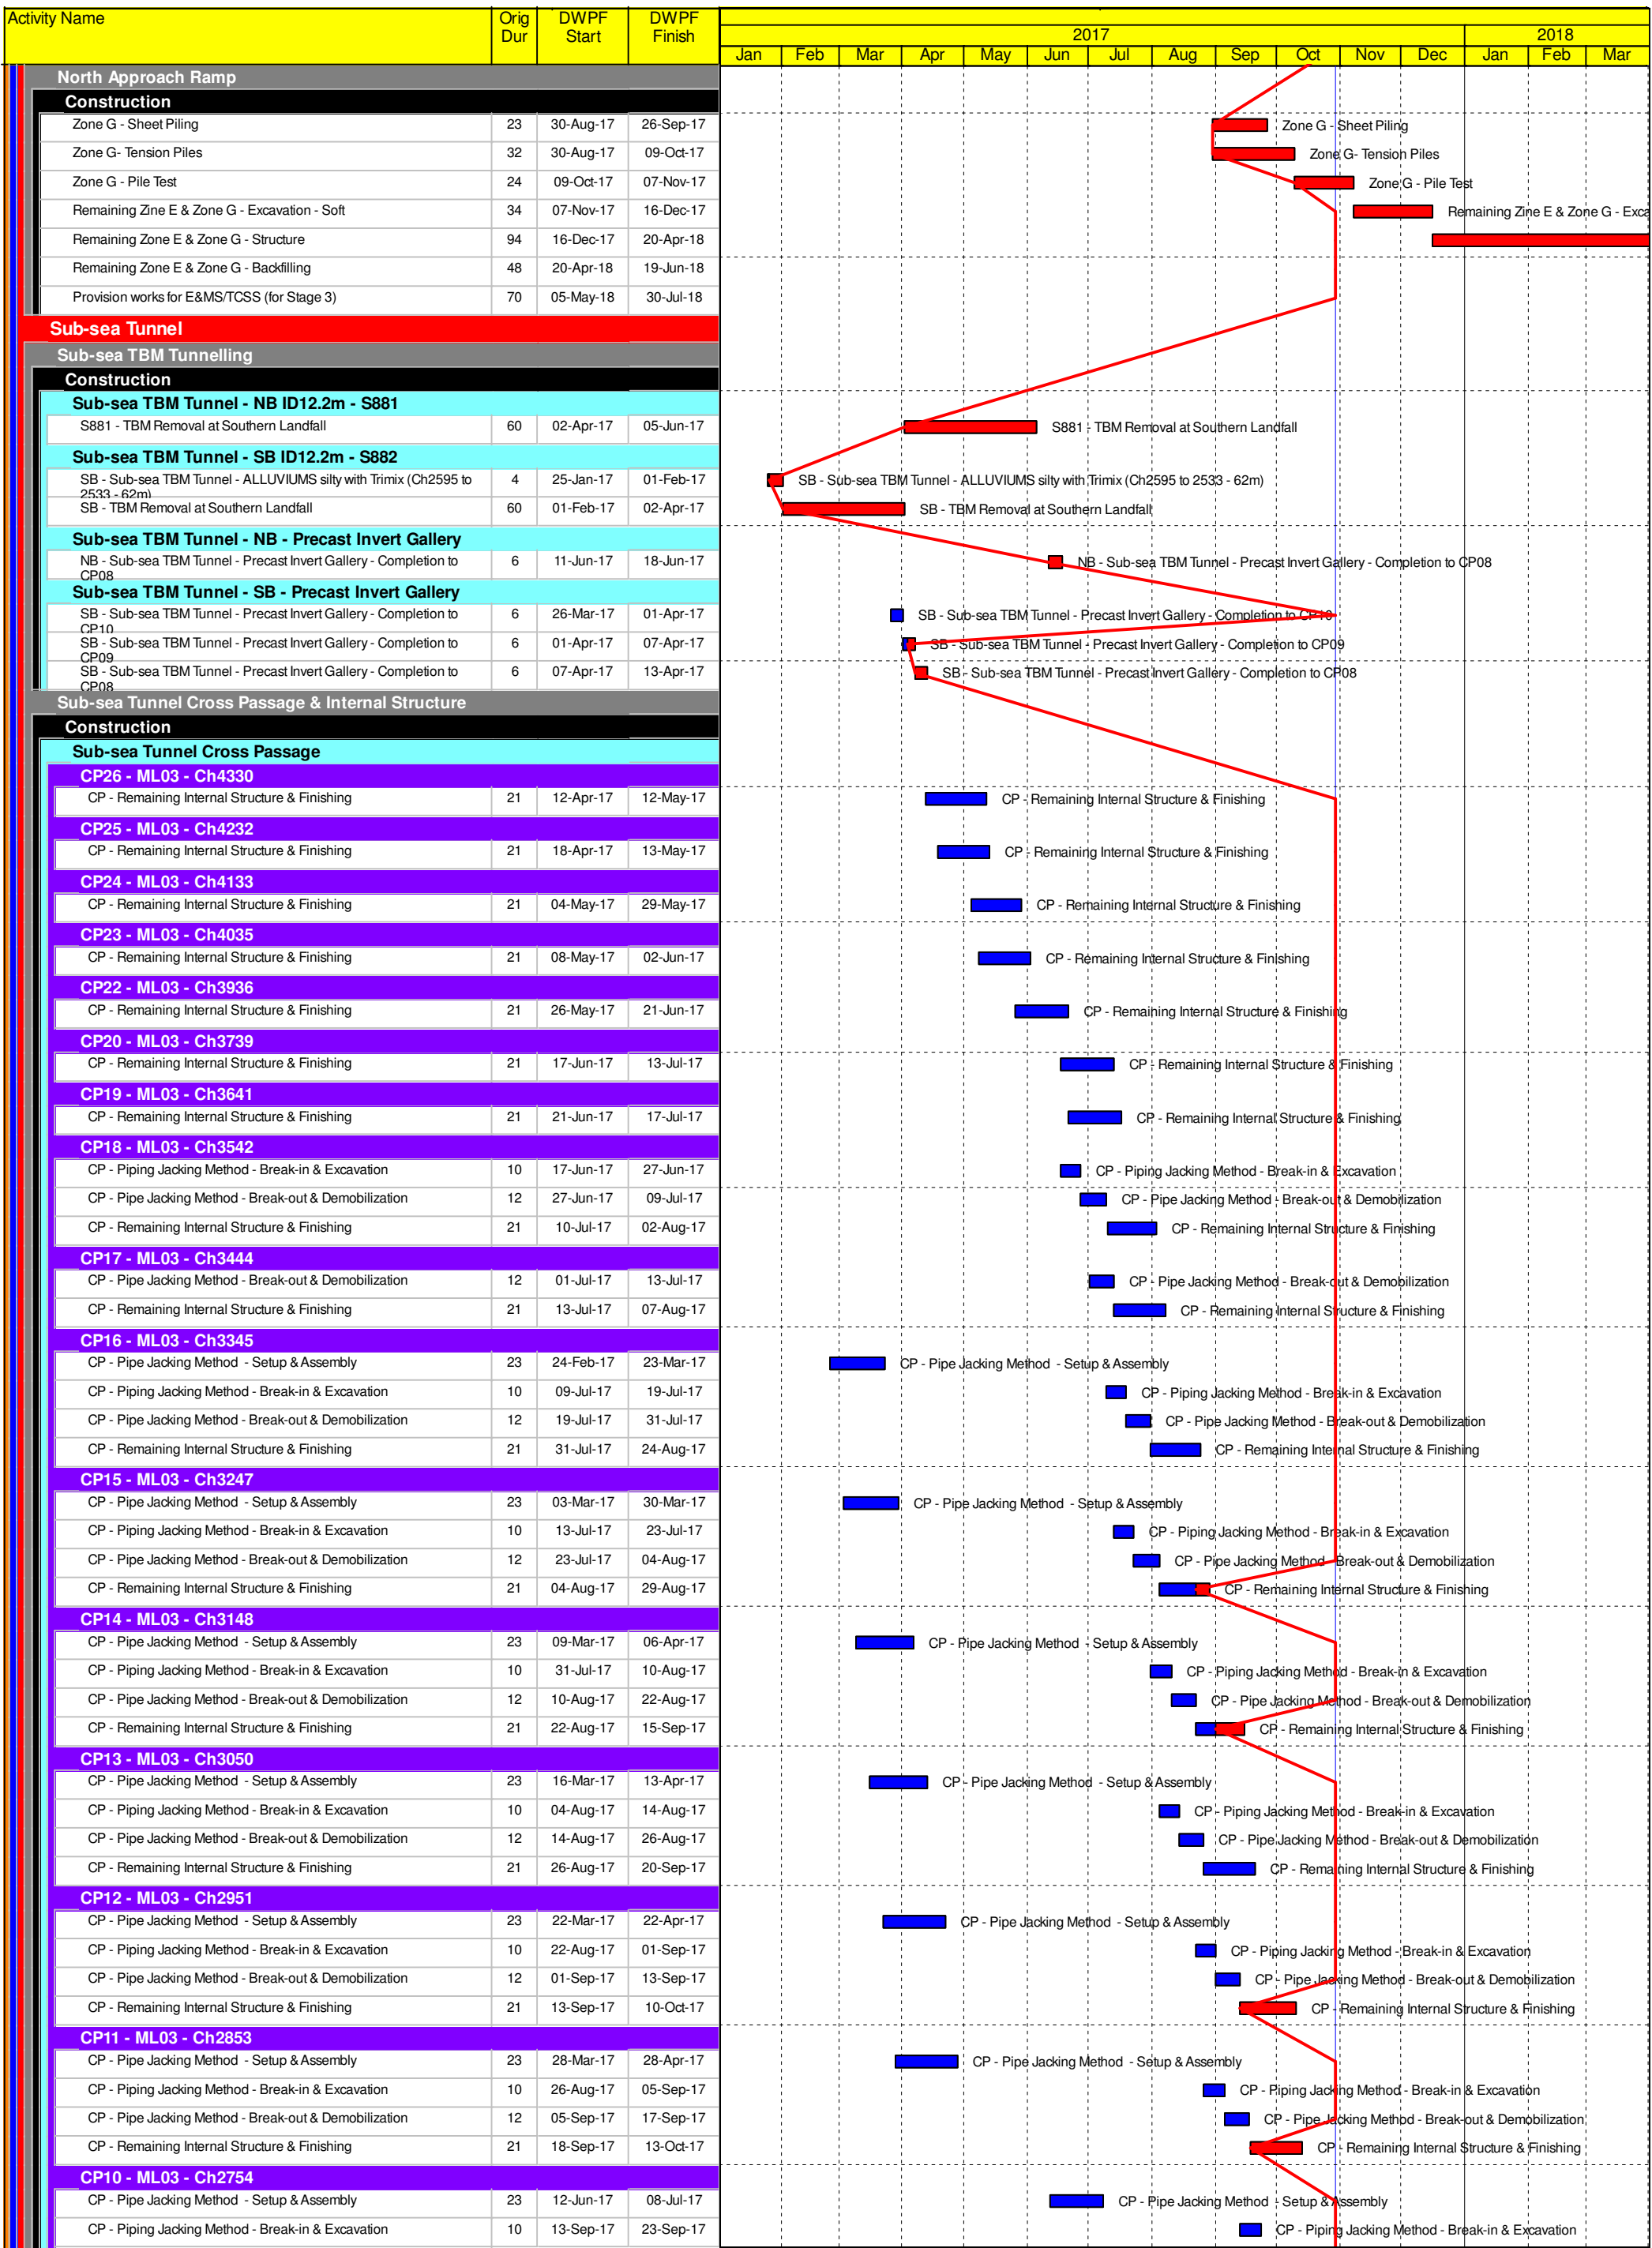


■ Planned Bar
■ Planned Bar - Critical
◆ Planned Milestone
■ Progress bar
◆ Progress Milestone

Date	Revision	Checked	Approved
12-Feb-14	TMCLK0BJENPRG08507	WYu	SPs
08-Apr-14	TMCLK0BJENPRG08507	SPs	WYu
28-Aug-14	TMCLK0BJENPRG08507	CLs	WYu
30-Oct-15	TMCLK0BJENPRG08507	WYu	



- Planned Bar
- Planned Bar - Critical
- Planned Milestone
- Progress bar
- Progress Milestone

Date	Revision	Checked	Approved
12-Feb-14	TMCLKDJGENPRG08507	WYu	SPa
08-Apr-14	TMCLKDJGENPRG08507	SPa	WYu
28-Aug-14	TMCLKDJGENPRG08507	CLa	WYu
30-Oct-15	TMCLKDJGENPRG08507	WYu	

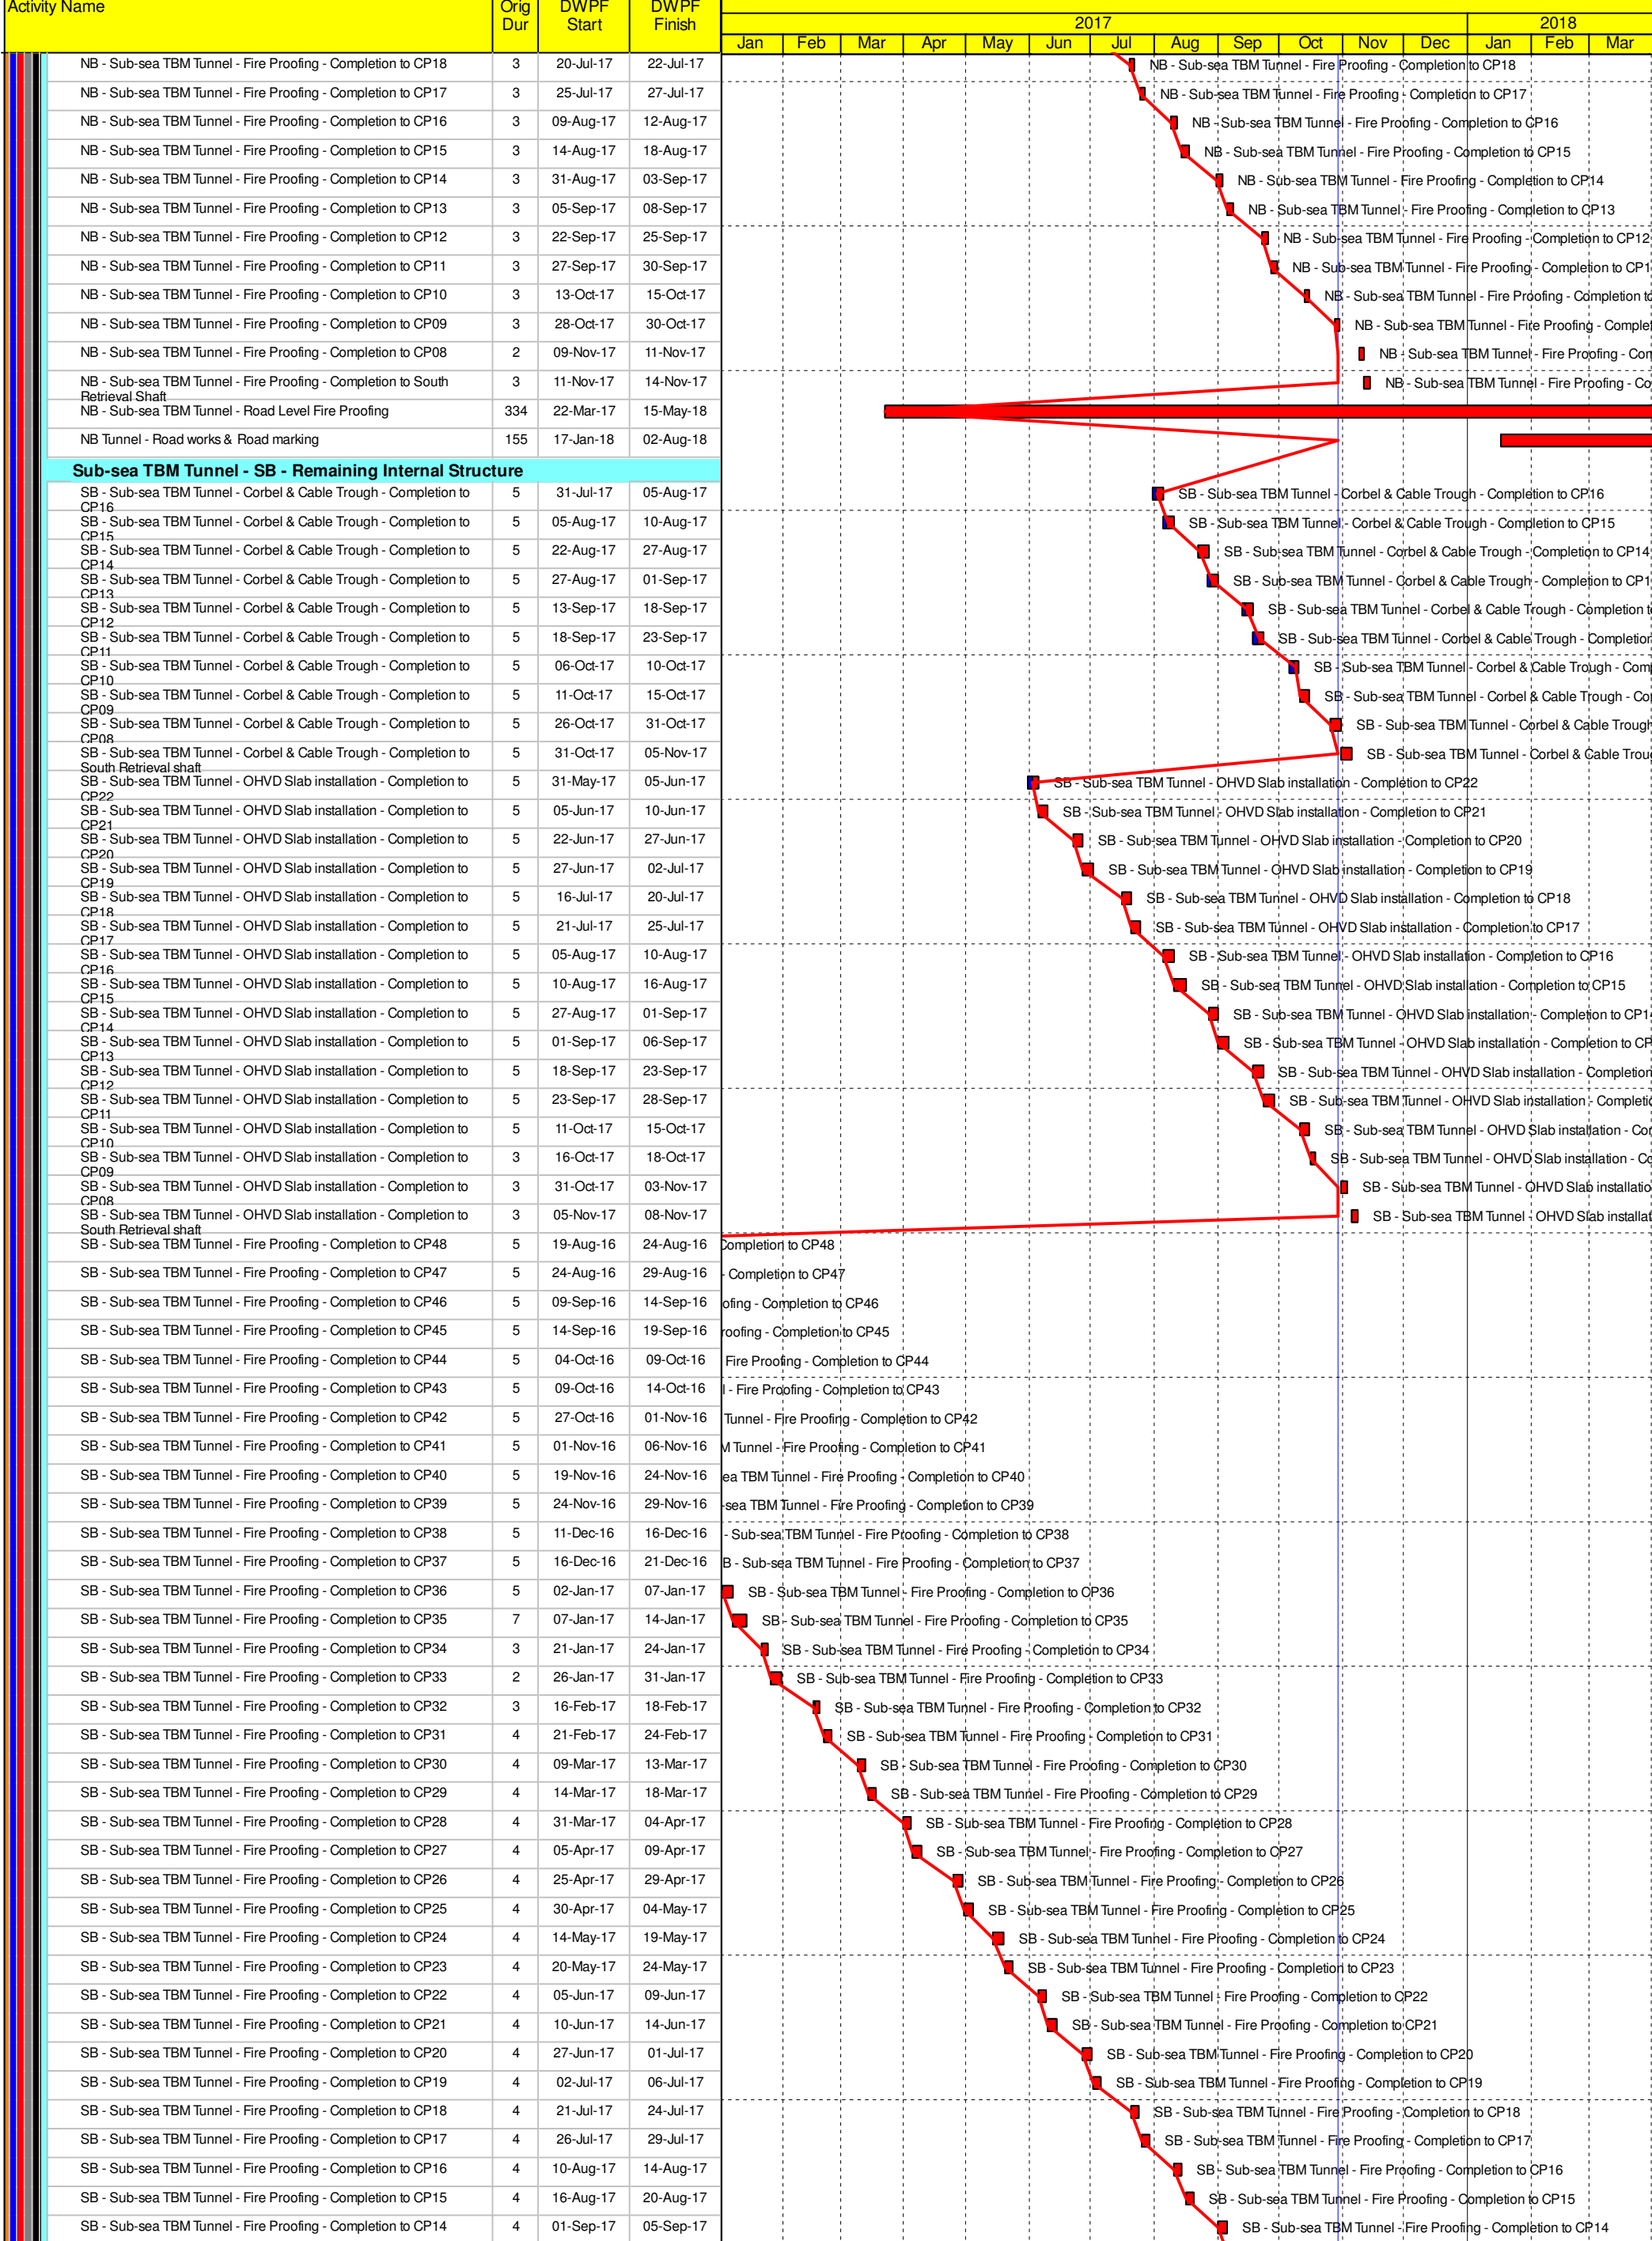

- █ Planned Bar
- █ Planned Bar - Critical
- ◆ Planned Milestone
- █ Progress bar
- ◆ Progress Milestone

Date	Revision	Checked	Approved
12-Feb-14	TMCLKDJENPRG08507	WYu	SPs
08-Apr-14	TMCLKDJENPRG08507	SPs	WYu
28-Aug-14	TMCLKDJENPRG08507	CLs	WYu
30-Oct-15	TMCLKDJENPRG08507	WYu	

Activity Name	Orig Dur	DWPF Start	DWPF Finish	2017												2018						
				Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar				
				SB - Sub-sea TBM Tunnel - Fire Proofing - Completion to CP13	4	06-Sep-17	10-Sep-17															
SB - Sub-sea TBM Tunnel - Fire Proofing - Completion to CP12	4	23-Sep-17	27-Sep-17																			
SB - Sub-sea TBM Tunnel - Fire Proofing - Completion to CP11	4	28-Sep-17	02-Oct-17																			
SB - Sub-sea TBM Tunnel - Fire Proofing - Completion to CP10	3	16-Oct-17	18-Oct-17																			
SB - Sub-sea TBM Tunnel - Fire Proofing - Completion to CP09	3	19-Oct-17	21-Oct-17																			
SB - Sub-sea TBM Tunnel - Fire Proofing - Completion to CP08	8	03-Nov-17	11-Nov-17																			
SB - Sub-sea TBM Tunnel - Fire Proofing - Completion to South Retrieval Shaft	3	11-Nov-17	14-Nov-17																			
SB - Remaining Fire Proofing in Tunnel	334	04-Feb-17	23-Mar-18																			
SB Tunnel - Road works & Road Marking	155	17-Jan-18	02-Aug-18																			

Southern Landfall

South Cut & Cover Tunnel

Construction			
South C&C Tunnel - Diaphragm Wall	120	03-Oct-15	02-Mar-16
C&C Tunnel - 1st 85m - Excavation by ramp	23	03-Mar-16	01-Apr-16
C&C Tunnel - 1st 85m - Excavation by vertical mean	11	02-Apr-16	15-Apr-16
C&C Tunnel - 1st 85m - Tunnel Structure	95	16-Apr-16	09-Aug-16
C&C Tunnel - 1st 85m - Backfilling	4	10-Aug-16	13-Aug-16
C&C Tunnel - 2nd 85m - Excavation by ramp	17	30-Apr-16	21-May-16
C&C Tunnel - 2nd 85m - Excavation by vertical mean	18	23-May-16	13-Jun-16
C&C Tunnel - 2nd 85m - Tunnel Structure	83	14-Jun-16	20-Sep-16
C&C Tunnel - 2nd 85m - Backfilling	9	21-Sep-16	30-Sep-16
C&C Tunnel - 3rd 85m - Excavation by ramp	18	23-May-16	13-Jun-16
C&C Tunnel - 3rd 85m - Excavation by vertical mean	25	14-Jun-16	13-Jul-16
C&C Tunnel - 3rd 85m - Tunnel Structure	83	26-Jul-16	02-Nov-16
C&C Tunnel - 3rd 85m - Backfilling	15	03-Nov-16	19-Nov-16
C&C Tunnel - 4th 85m - Excavation by ramp	21	30-Jun-16	25-Jul-16
C&C Tunnel - 4th 85m - Excavation by vertical mean	35	26-Jul-16	03-Sep-16
C&C Tunnel - 4th 85m - Tunnel Structure	83	05-Sep-16	13-Dec-16
C&C Tunnel - 5th 85m - Excavation by ramp	23	26-Jul-16	20-Aug-16
C&C Tunnel - 5th 85m - Excavation by vertical mean	44	22-Aug-16	14-Oct-16
C&C Tunnel - 6th 85m - Excavation by ramp	27	22-Aug-16	22-Sep-16
C&C Tunnel - 6th 85m - Excavation by vertical mean	52	23-Sep-16	24-Nov-16
C&C Tunnel - 7th 152m - Excavation by ramp	15	03-Nov-16	19-Nov-16

South Retrieval Shaft

Construction			
Retrieval Shaft - Temp. Slab/Prepare for TBM Breakthrough	48	03-Oct-16	28-Nov-16
Retrieval Shaft - Mobilization for Retrieval Shaft Tunnel Structure	30	05-Jun-17	11-Jul-17
Retrieval Shaft - Tunnel Structure	180	11-Jul-17	13-Feb-18
Retrieval Shaft - Tunnel Structure - Provision for TCSS/E&MS works for KD-3	24	13-Feb-18	20-Mar-18
Retrieval Shaft - Vent duct Structure & Backfilling	48	13-Feb-18	21-Apr-18

South Ventilation Building

Construction			
S - Piling (Socket H-piles)	132	23-Oct-15	08-Apr-16
S - Pile Test	24	09-Apr-16	07-May-16
S - Sheet Piling	48	23-Oct-15	17-Dec-15
S - Excavation	100	09-May-16	05-Sep-16
Substructure	95	06-Sep-16	30-Dec-16
Superstructure	65	31-Dec-16	21-Mar-17
Finishing Works	155	25-Mar-17	30-Sep-17
E&MS & Equipments Installation (by Others)	72	27-May-17	21-Aug-17
Remaining Finishing Works	96	11-Jul-17	02-Nov-17
Handover Portion N10	0		02-Nov-17

South Surface Roadworks, Utility & Drainage works

Construction			
South Landfall - Seawall Modification	144	18-Oct-17	19-Apr-18
South Landfall - Road Furniture	72	13-Mar-18	12-Jun-18

Testing & Commissioning/Inspection & Handover

Final Inspection & Handover			
Construction			
Statutory Inspection	48	04-Aug-18	02-Oct-18
Final Inspection & Handover	63	02-Oct-18	15-Dec-18

- Planned Bar
- Planned Bar - Critical
- Planned Milestone
- Progress bar
- Progress Milestone

Date	Revision	Checked	Approved
12-Feb-14	TMCLK0BJGENPRG08507	WYu	SPa
08-Apr-14	TMCLK0BJGENPRG08507	SPa	WYu
28-Aug-14	TMCLK0BJGENPRG08507	CLa	WYu
30-Oct-15	TMCLK0BJGENPRG08507	WYu	
