




Activity Name	
TMCLK - Northern Connection Sub-Sea Tunnel Section	
Construction	
Northern Landfall	
Box Culvert Extension	
Construction	
CH100-150 Land Section	
ELS & Structure	
Pile A41/A39 CJ to Pile A39/A37 CJ (Bay 7)	
Box Culvert Structure	
Removal of strut S2 & Backfilling up to required level	
Pile A39/A37 CJ to Pile A37/A35 CJ (Bay 8)	
Box Culvert Structure	
Removal of strut S2 & Backfilling up to required level	
Pile A37/A35 CJ to Pile A35/A33 CJ (Bay 9)	
Box Culvert Structure	
Removal of strut S2 & Backfilling up to required level	
Pile A35/A33 CJ to Pile A33/P117 CJ (Bay 10)	
Box Culvert Structure	
Removal of strut S2 & Backfilling up to required level	
Ch150-250 Marine Section	
ELS & Structure	
Pile A33/P117 CJ to Pile P113/P109 CJ (Bay 11)	
Box Culvert Structure	
Removal of strut S2 & Backfilling up to required level	
Pile P113/P109 CJ to Pile P105/P101 CJ (Bay 12)	
Box Culvert Structure	
Removal of strut S2 & Backfilling up to required level	
Pile P105/P101 CJ to Pile P97/P93 CJ (Bay 13)	
Box Culvert Structure	
Removal of strut S2 & Backfilling up to required level	
Pile P97/P93 CJ to Pile P89/P85 CJ (Bay 14)	
Box Culvert Structure	
Removal of strut S2 & Backfilling up to required level	
Pile P89/P85 CJ to Pile P81/P77 CJ (Bay 15)	
Box Culvert Structure	
Removal of strut S2 & Backfilling up to required level	
Pile P81/P77 CJ to Pile P73/P69 CJ (Bay 16)	
Box Culvert Structure	
Removal of strut S2 & Backfilling up to required level	
Ch250-380 Marine Section	
ELS & Structure	
Pile P73/P69 CJ to Pile P65/P61 CJ (Bay 17)	
Box Culvert Structure	
System Formwork Assembly & Setup	
Walls & top slab construction	
Removal of strut S2 & Backfilling up to required level	
Pile P65/P61 CJ to Pile P57/P53 CJ (Bay 18)	
Box Culvert Structure	
Removal of strut S2 & Backfilling up to required level	
Pile P57/P53 CJ to Pile P49/P45 CJ (Bay 19)	
Box Culvert Structure	
Removal of strut S2 & Backfilling up to required level	
Pile P49/P45 CJ to Pile P41/P37 CJ (Bay 20)	
Box Culvert Structure	
Removal of strut S2 & Backfilling up to required level	
Pile P41/P37 CJ to Pile P33/P29 CJ (Bay 21)	
Box Culvert Structure	
Removal of strut S2 & Backfilling up to required level	
Pile P33/P29 CJ to Pile P25/P21 CJ (Bay 22)	
Box Culvert Structure	
Walls & top slab construction	
Removal of strut S2 & Backfilling up to required level	
Pile P25/P21 CJ to Pile P17/P13 CJ (Bay 23)	
Box Culvert Structure	
Base slab construction including kicker	
Removal of strut S1	
Walls & top slab construction	
Removal of strut S2 & Backfilling up to required level	
Pile P17/P13 CJ to Pile P09/P05 CJ (Bay 24)	
Box Culvert Structure	
Base slab construction including kicker	
Removal of strut S1	
Walls & top slab construction	
Removal of strut S2 & Backfilling up to required level	
Pile P09/P05 CJ to End Wall CJ (Bay 25)	
Box Culvert Structure	

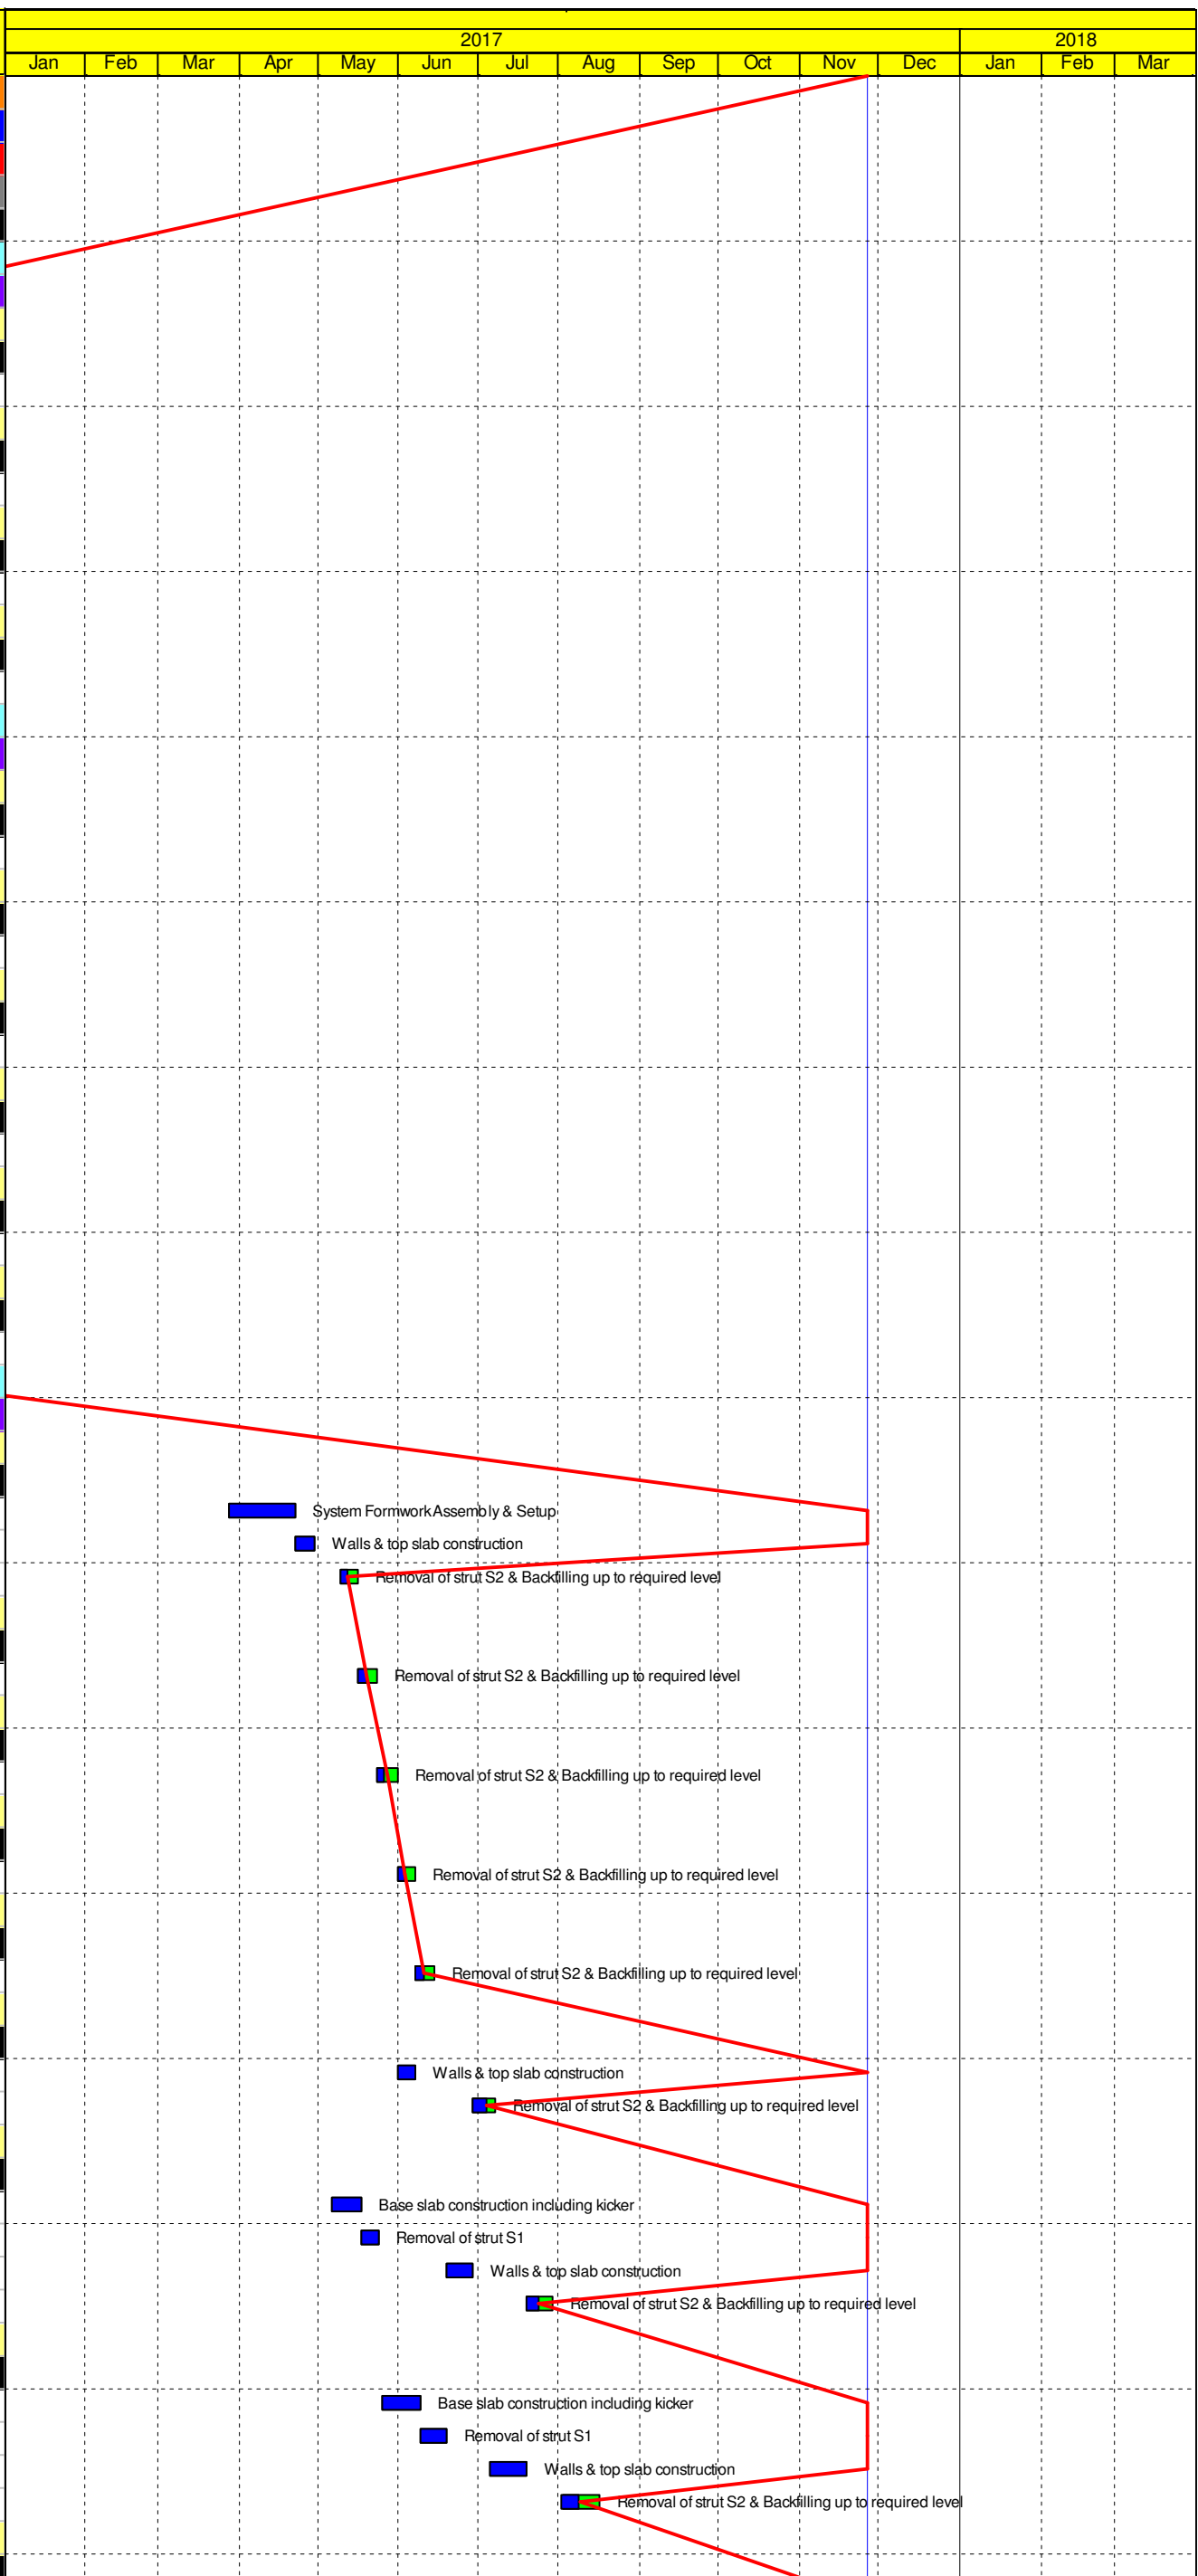

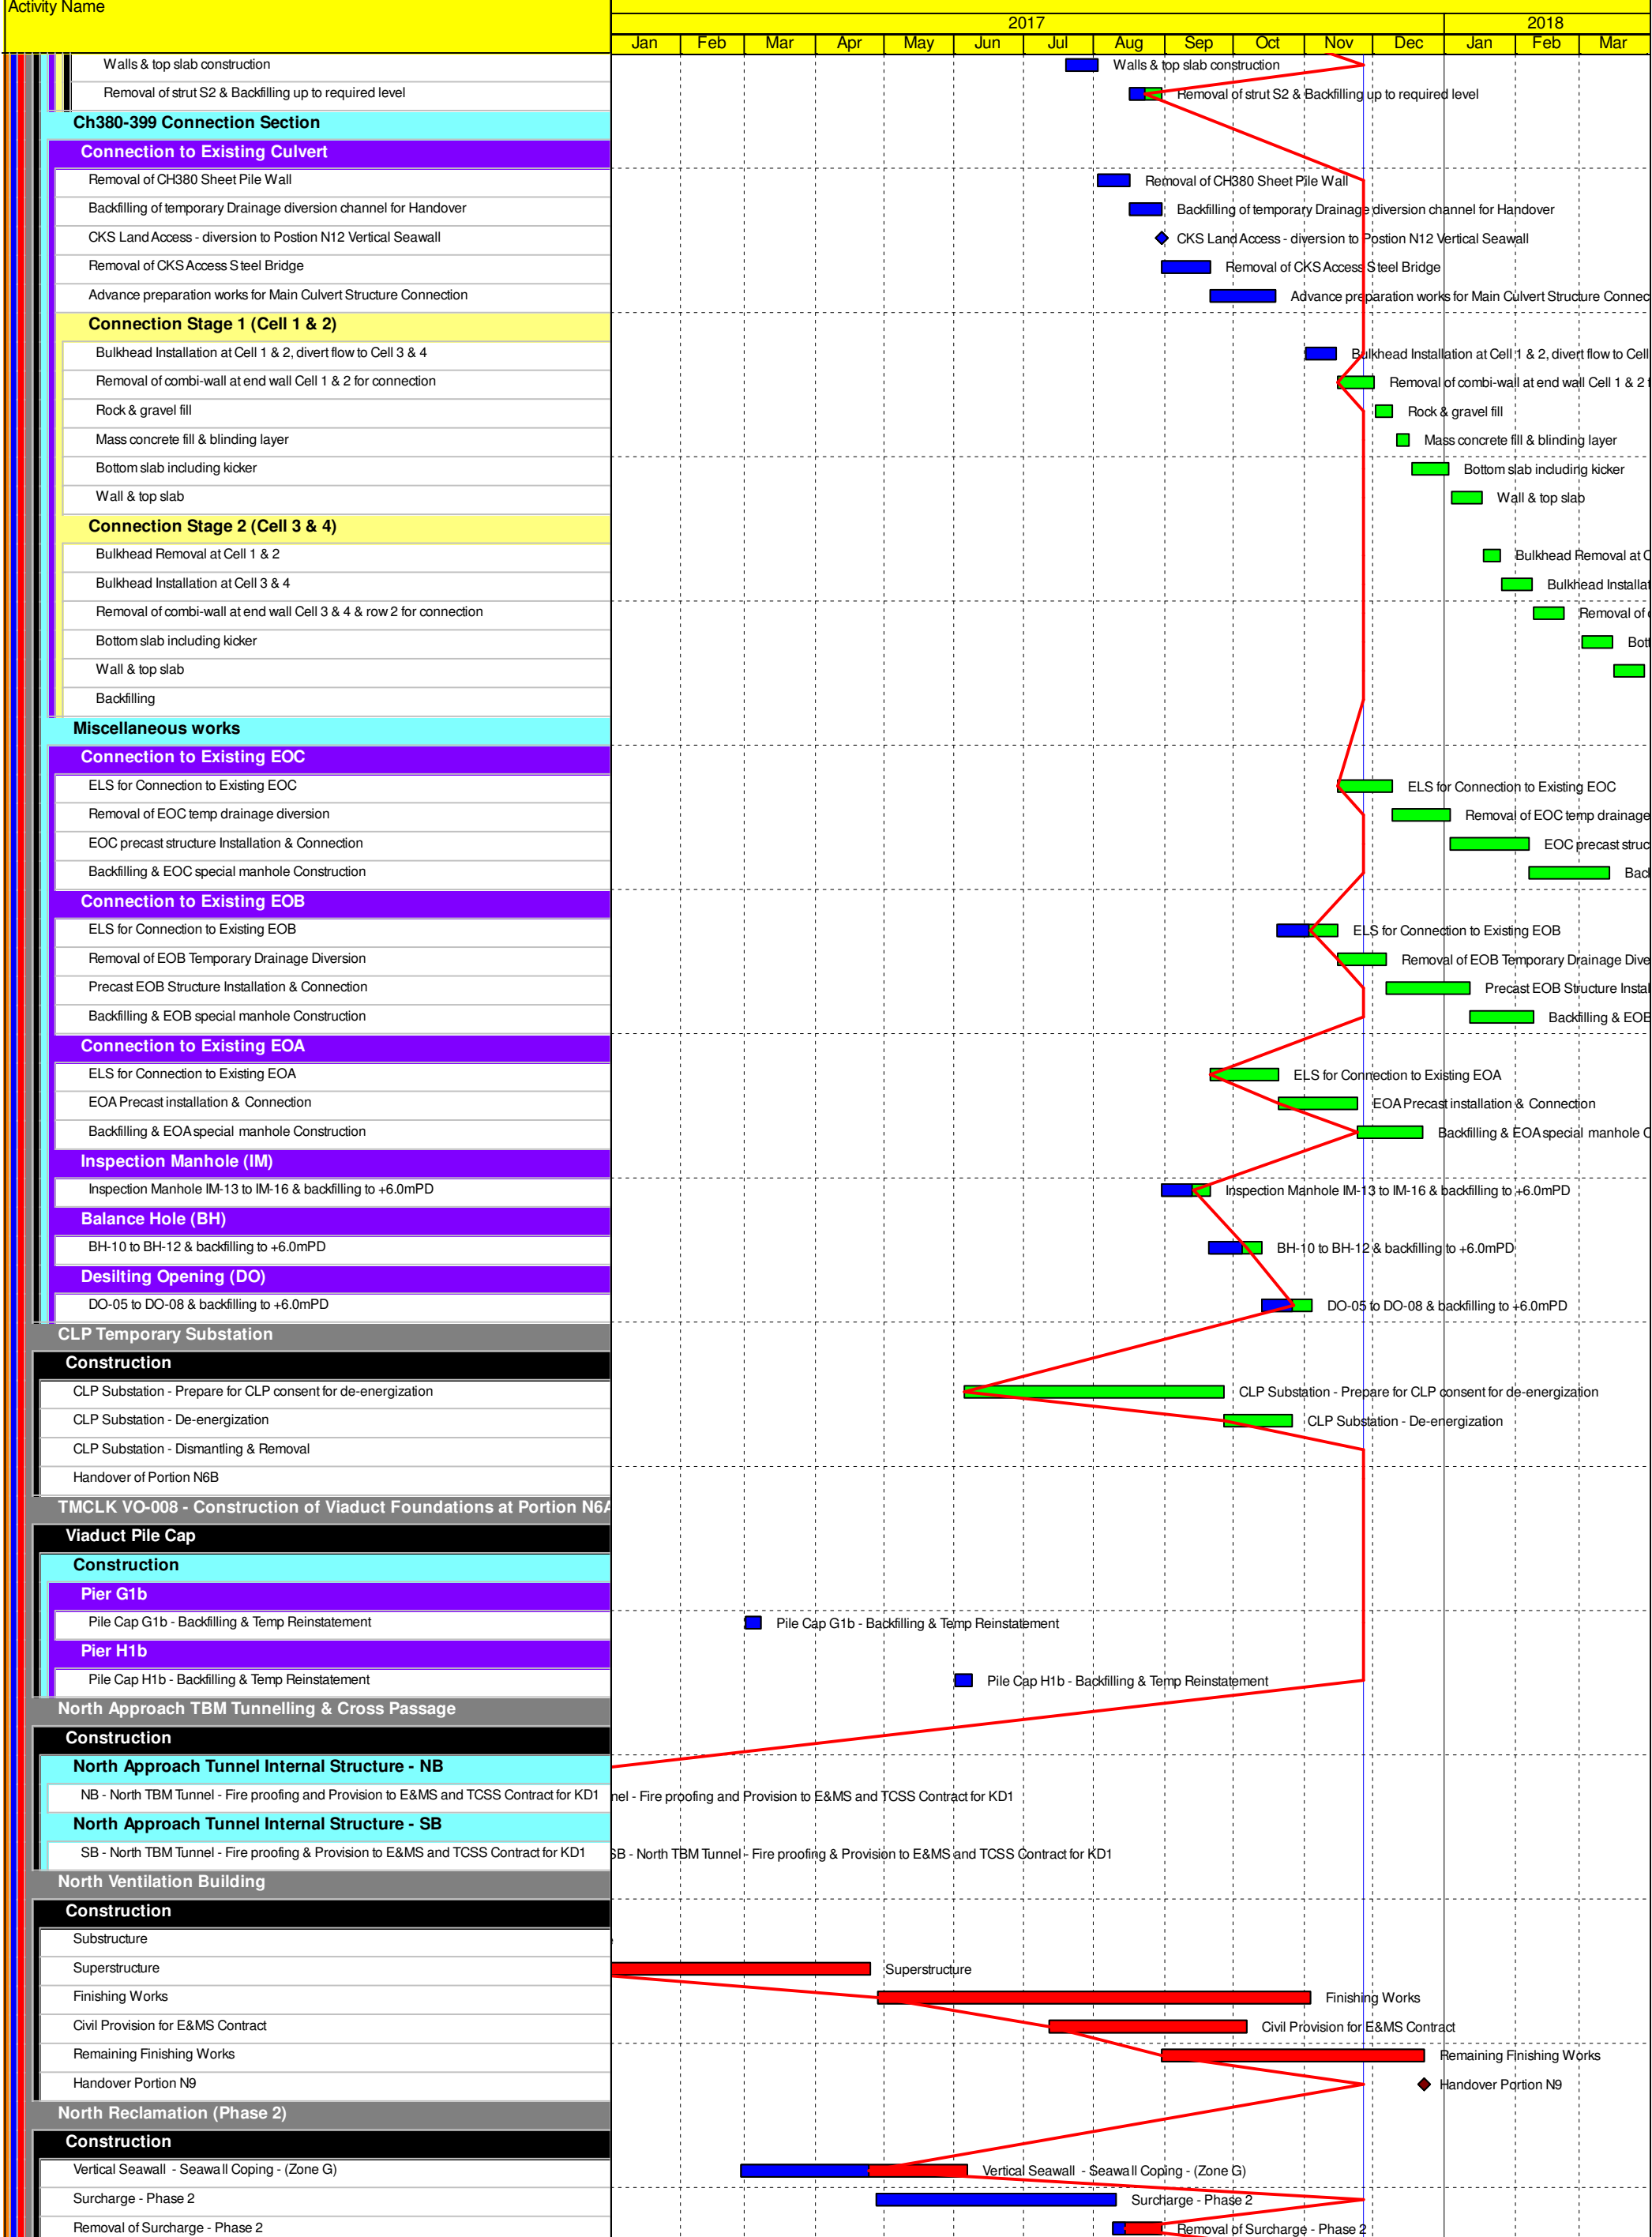


■ Planned Bar
■ Planned Bar - Critical
◆ Planned Milestone
■ Progress bar
◆ Progress Milestone

Date	Revision	Checked	Approved
12-Feb-14	TMCLKDBJGENPRG98507	WYu	SPc
08-Apr-14	TMCLKDBJGENPRG98507	SPc	WYu
28-Aug-14	TMCLKDBJGENPRG98507	CLa	WYu
30-Oct-15	TMCLKDBJGENPRG98507	WYu	

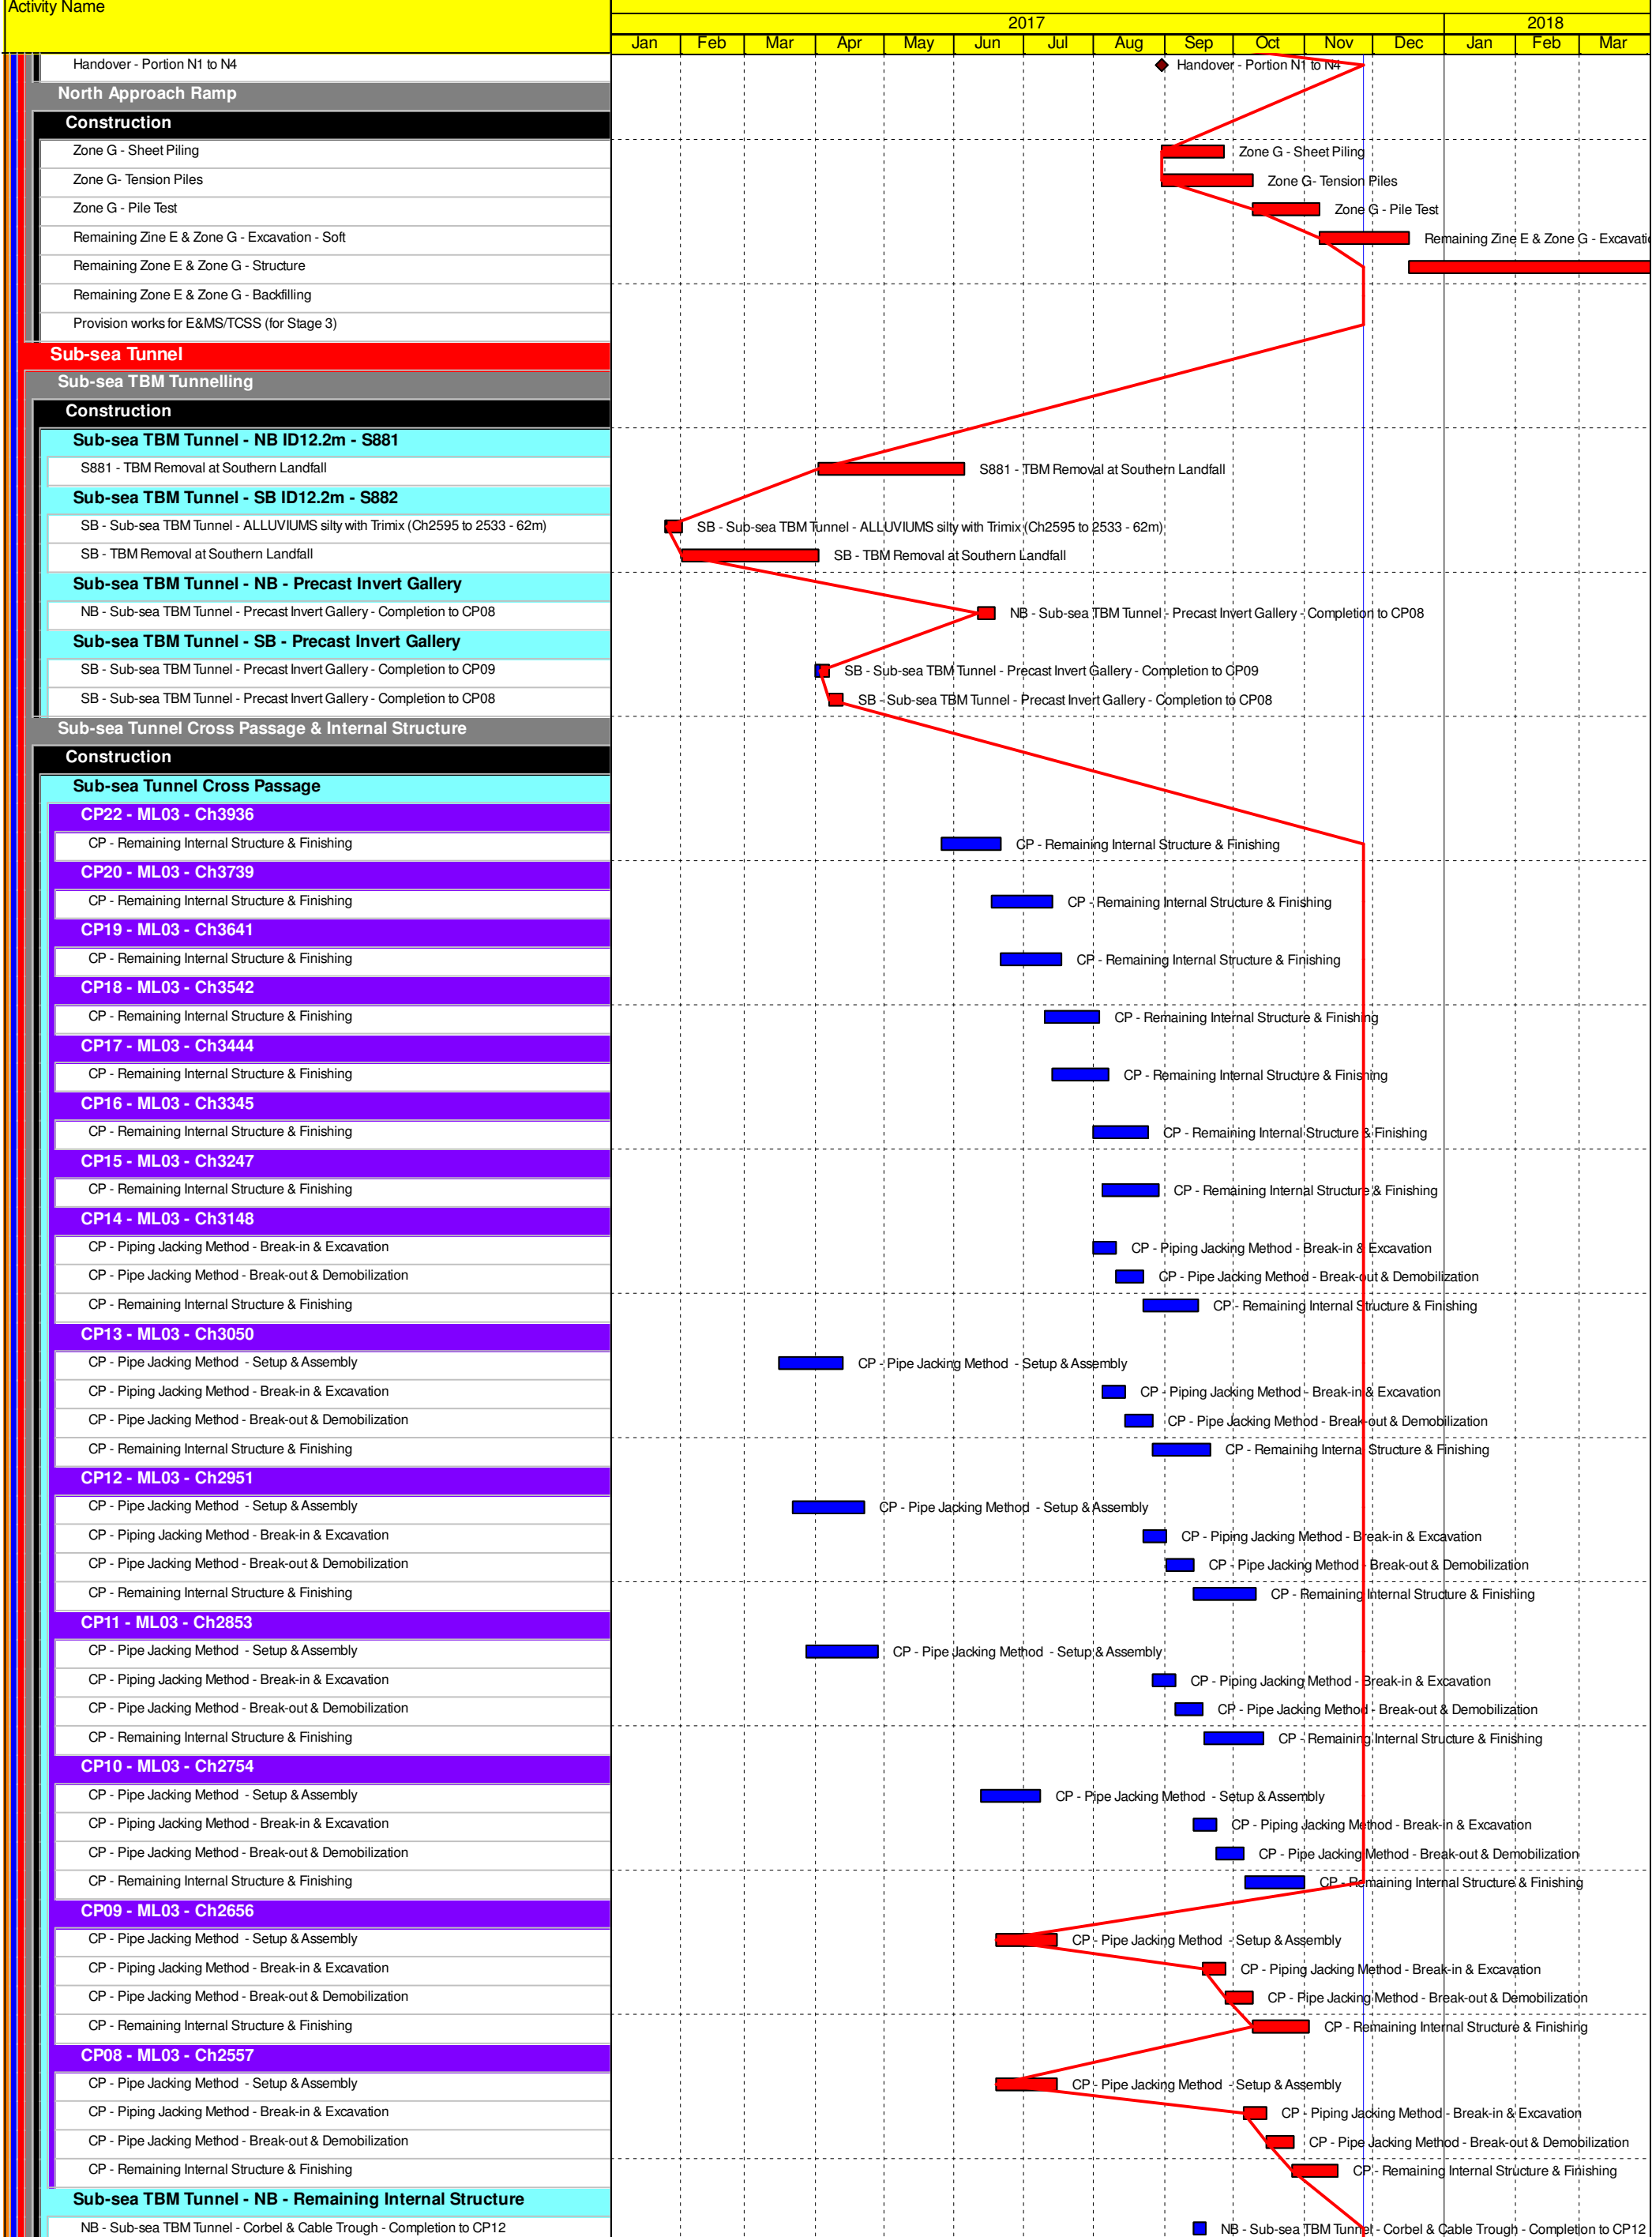

- Planned Bar
- Planned Bar - Critical
- Progress bar
- ◆ Planned Milestone
- ◆ Progress Milestone

Date	Revision	Checked	Approved
12-Feb-14	TMCLKDBJGENPRG98507	WYu	SP
08-Apr-14	TMCLKDBJGENPRG98507	SP	WYu
28-Aug-14	TMCLKDBJGENPRG98507	CLa	WYu
30-Oct-15	TMCLKDBJGENPRG98507	WYu	

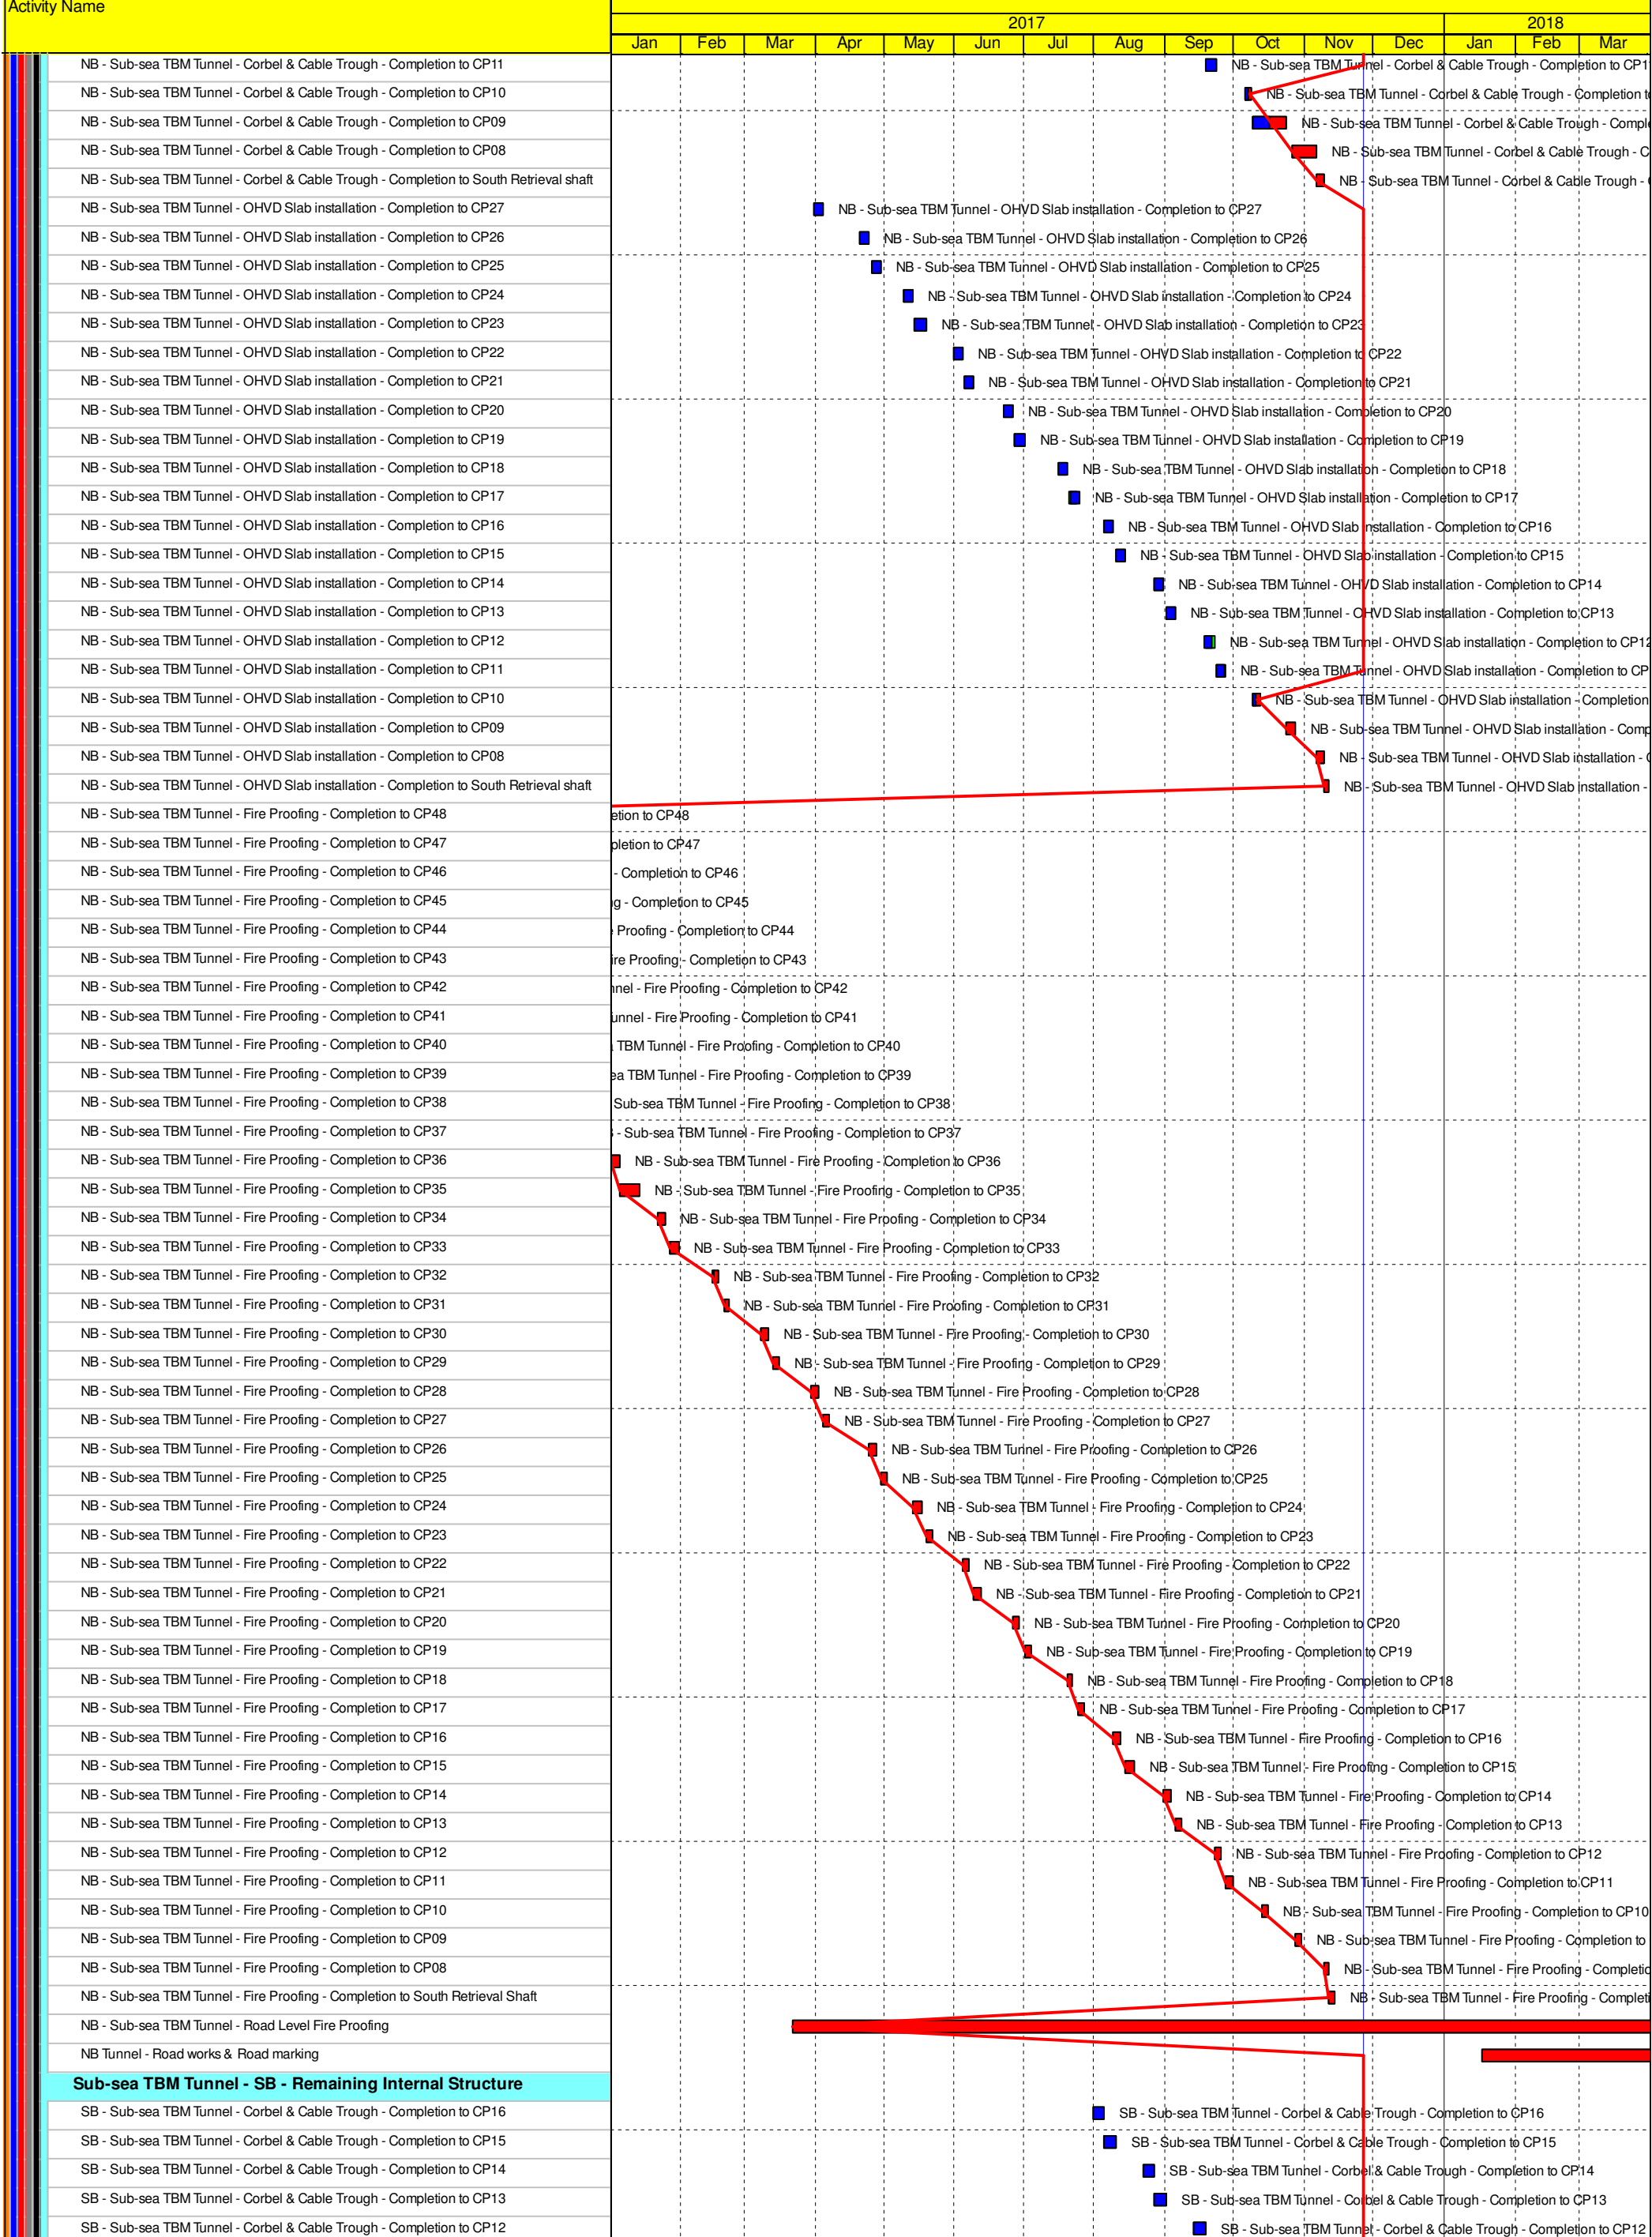


■ Planned Bar
■ Planned Bar - Critical
◆ Planned Milestone
■ Progress bar
◆ Progress Milestone

Date	Revision	Checked	Approved
12-Feb-14	TMCLKDBJGENPRG98507	WYu	SPc
08-Apr-14	TMCLKDBJGENPRG98507	SPc	WYu
28-Aug-14	TMCLKDBJGENPRG98507	CLa	WYu
30-Oct-15	TMCLKDBJGENPRG98507	WYu	



- Planned Bar
- Planned Bar - Critical
- ◆ Planned Milestone
- Progress bar
- ◆ Progress Milestone

Date	Revision	Checked	Approved
12-Feb-14	TMCLKDBJGENPRG98507	WYu	SPe
08-Apr-14	TMCLKDBJGENPRG98507	SPe	WYu
28-Aug-14	TMCLKDBJGENPRG98507	CLa	WYu
30-Oct-15	TMCLKDBJGENPRG98507	WYu	

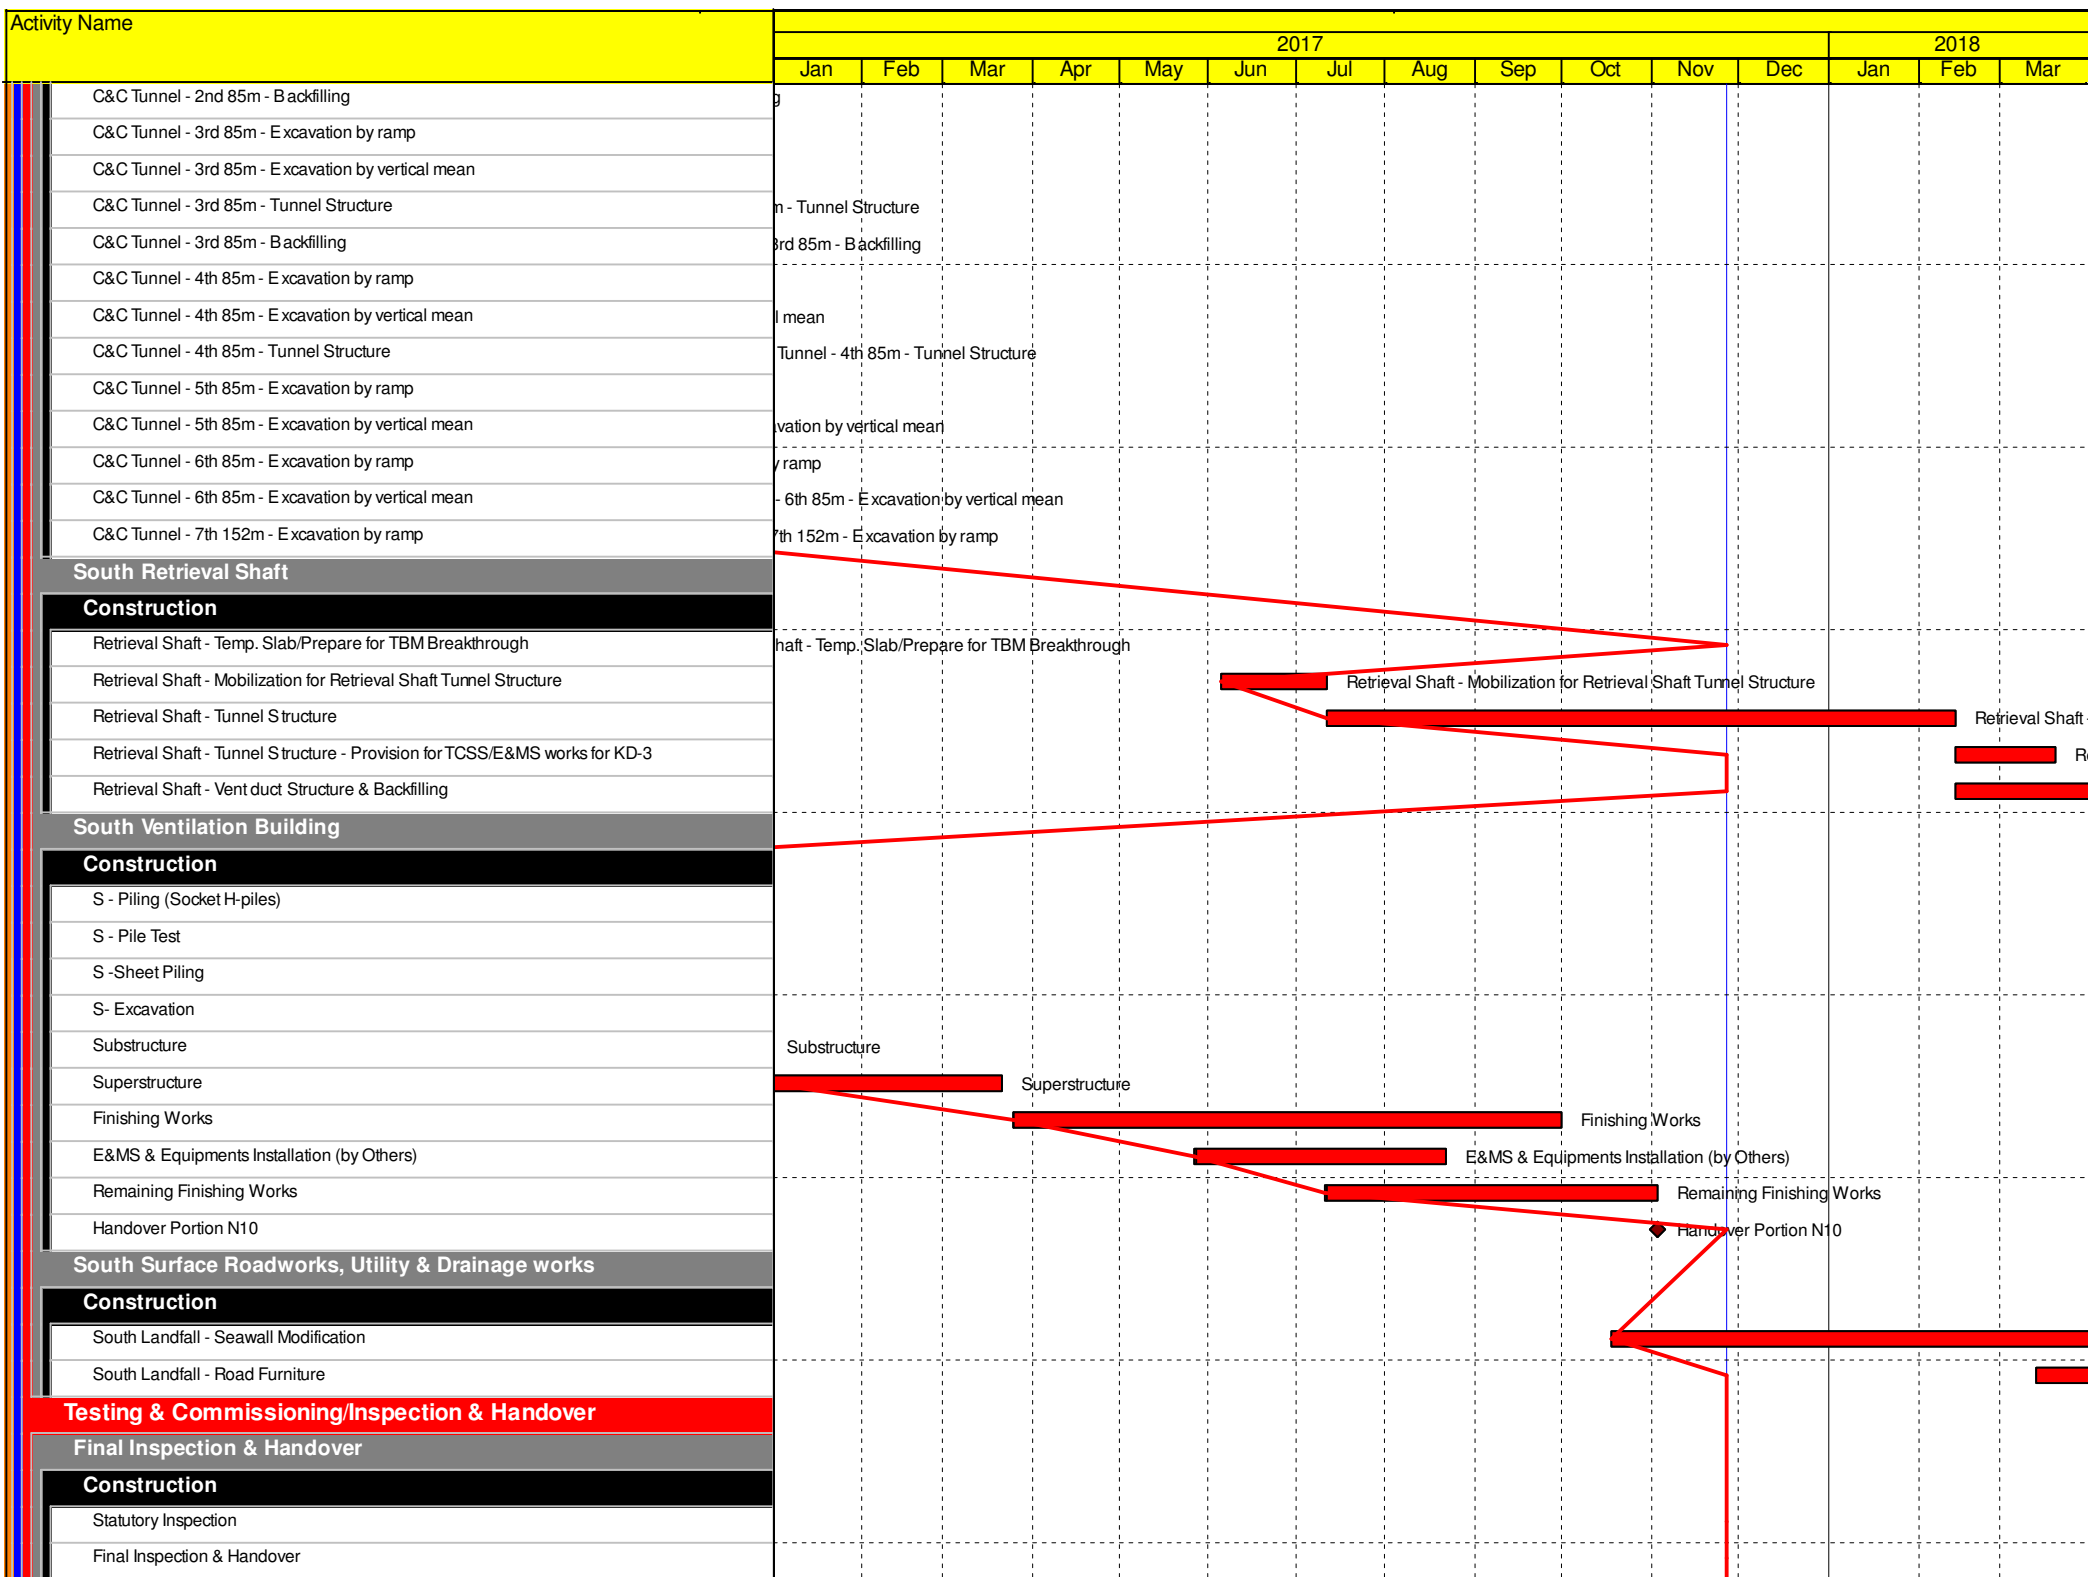

- Planned Bar
- Planned Bar - Critical
- Planned Milestone
- Progress bar
- Progress Milestone

Date	Revision	Checked	Approved
12-Feb-14	TMCLKDBJGENPRG.98507	WYu	SPa
08-Apr-14	TMCLKDBJGENPRG.98507	SPa	WYu
28-Aug-14	TMCLKDBJGENPRG.98507	CLa	WYu
30-Oct-15	TMCLKDBJGENPRG.98507	WYu	
