


■ Planned Bar
■ Planned Bar - Critical
◆ Planned Milestone
■ Progress bar
◆ Progress Milestone


TMCLK - Northern Connection Sub-Sea Tunnel Section
Detailed Works Programme (Rev. F)
Three Months Rolling Programme
 Progress as of 27-Aug-17

Date	Revision	Checked	Approved
12-Feb-14	TMCLKDBJGN-FRG98507	WYu	SPa
08-Apr-14	TMCLKDBJGN-FRG98507 Rev B	SPa	WYu
28-Aug-14	TMCLKDBJGN-FRG98507 Rev C	CLa	WYu
30-Oct-15	TMCLKDBJGN-FRG98507 Rev F	WYu	

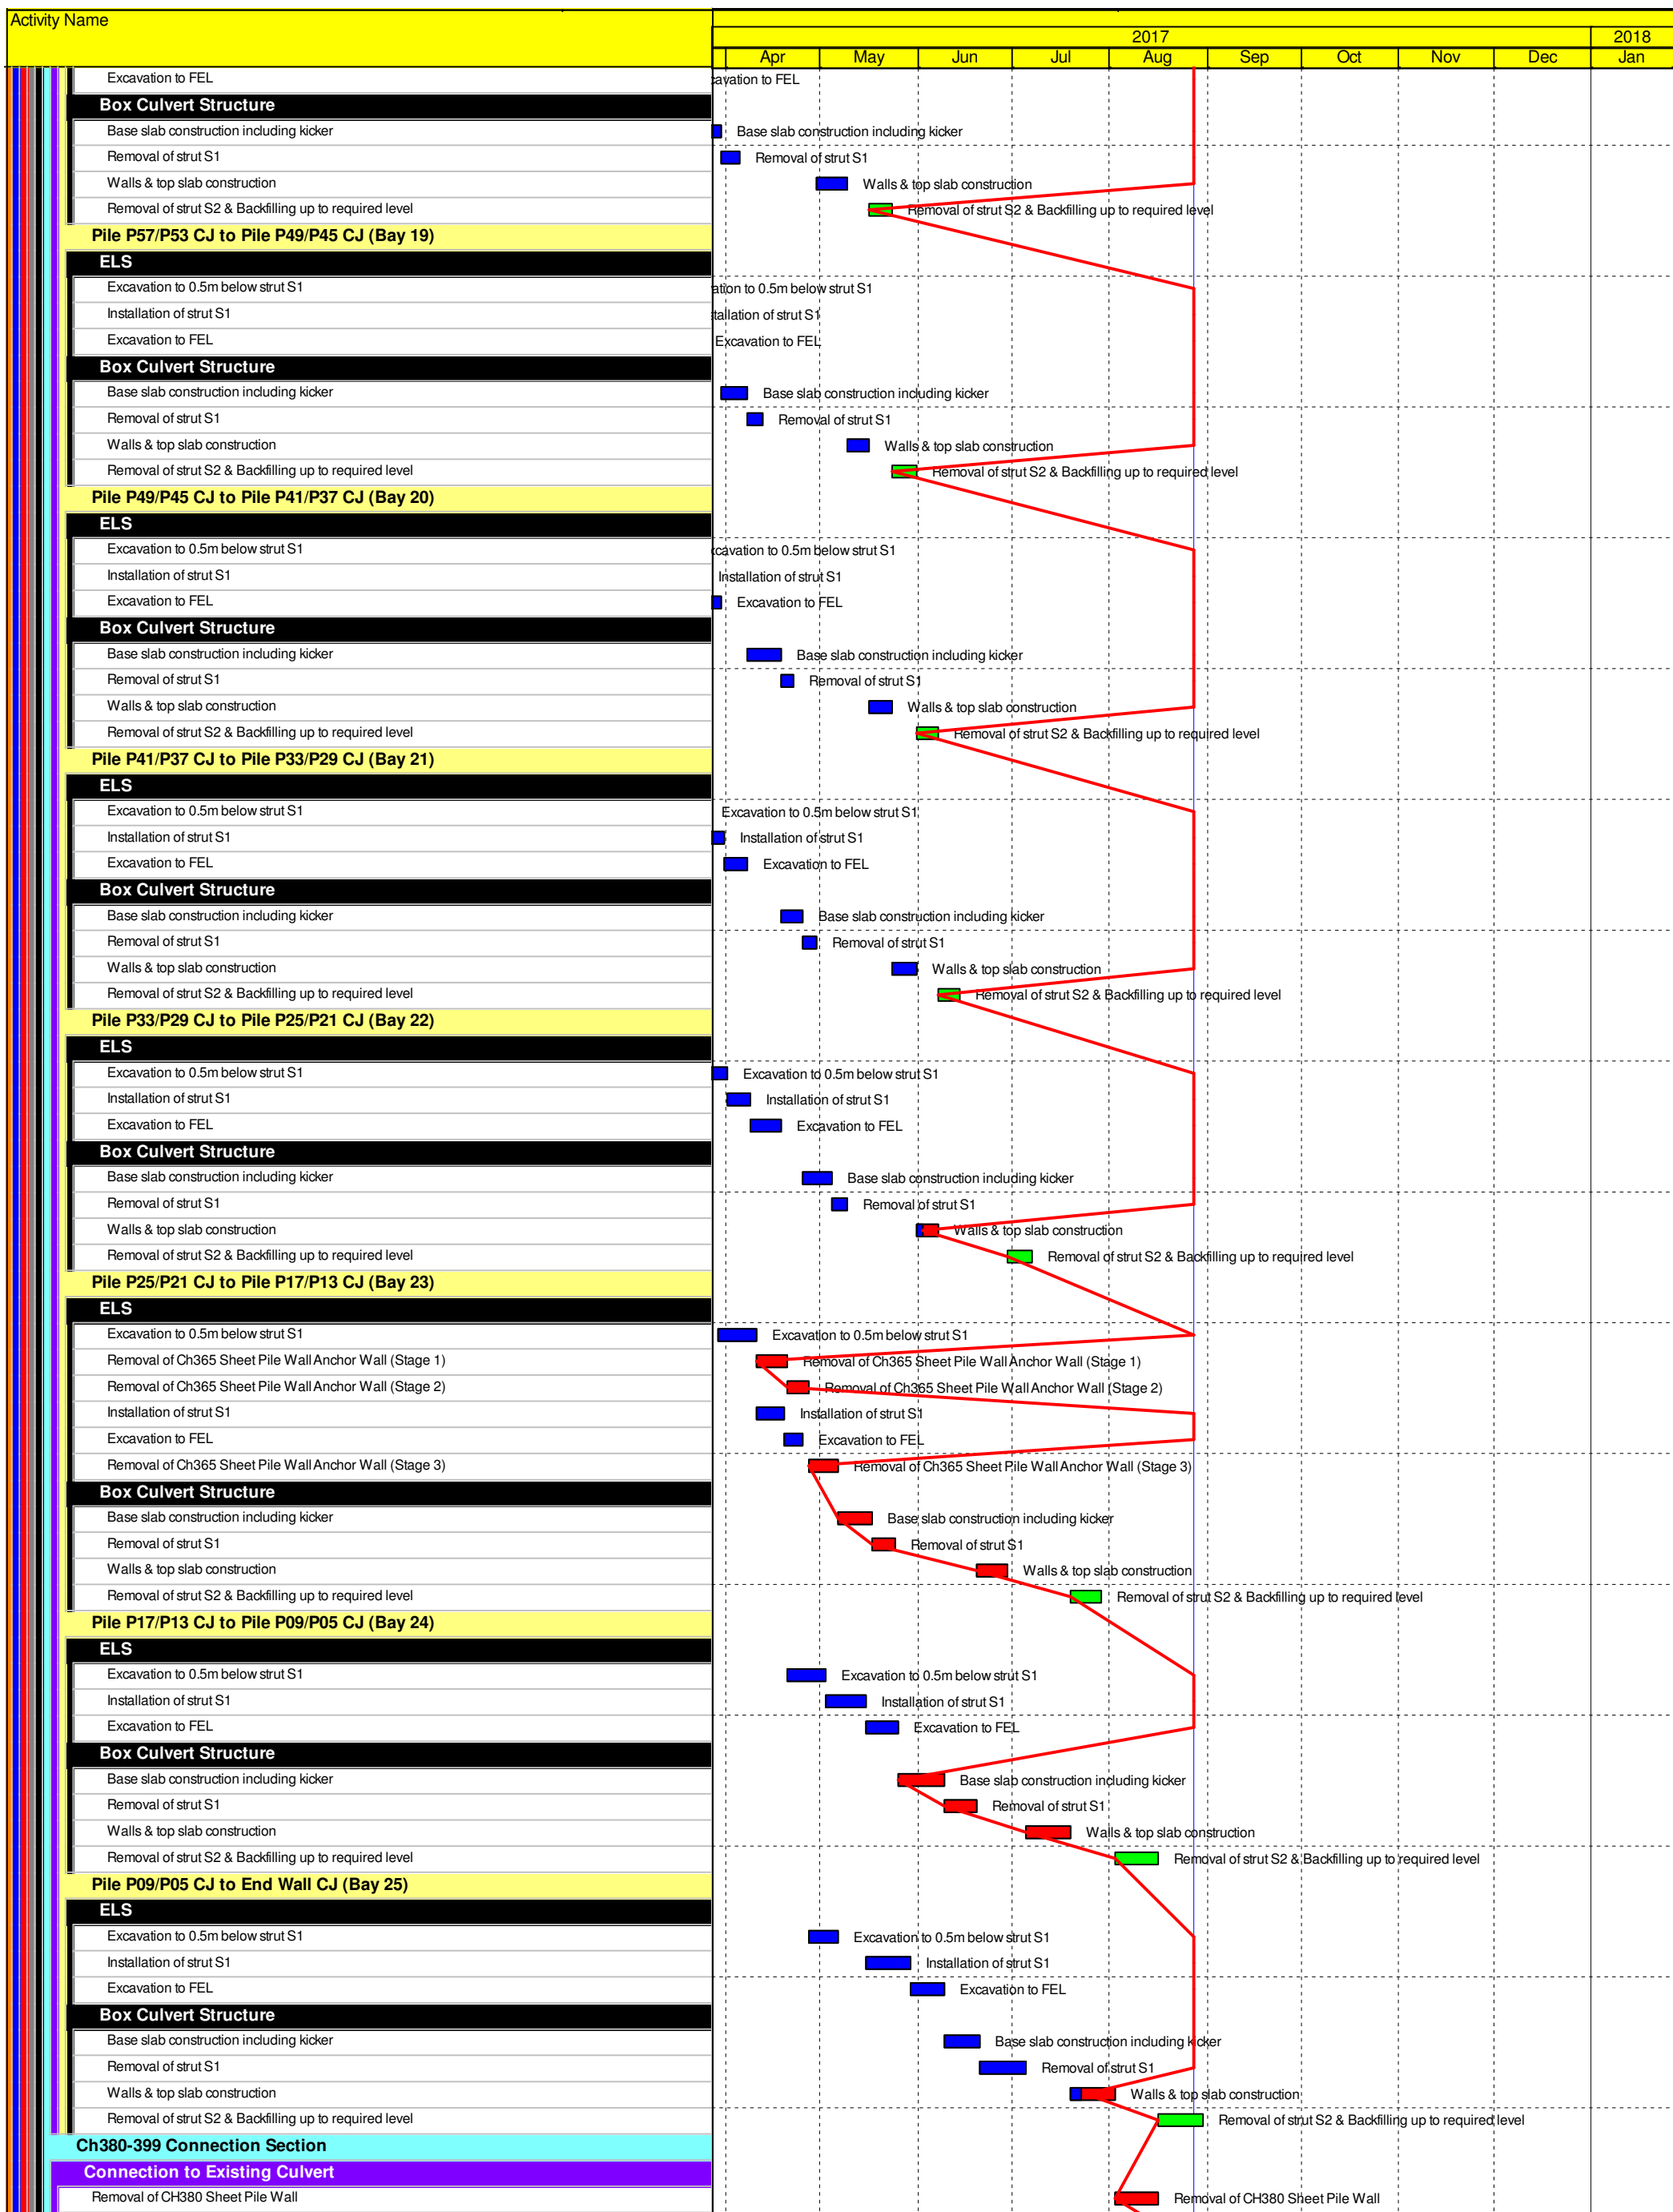


- Planned Bar
- Planned Bar - Critical
- Progress bar
- ◆ Planned Milestone
- ◆ Progress Milestone

Date	Revision	Checked	Approved
12-Feb-14	TMCLKDBJGN-PRG08507	WYu	SPa
08-Apr-14	TMCLKDBJGN-PRG08507 Rev B	SPa	WYu
28-Aug-14	TMCLKDBJGN-PRG08507 Rev C	CLa	WYu
30-Oct-15	TMCLKDBJGN-PRG08507 Rev F	WYu	

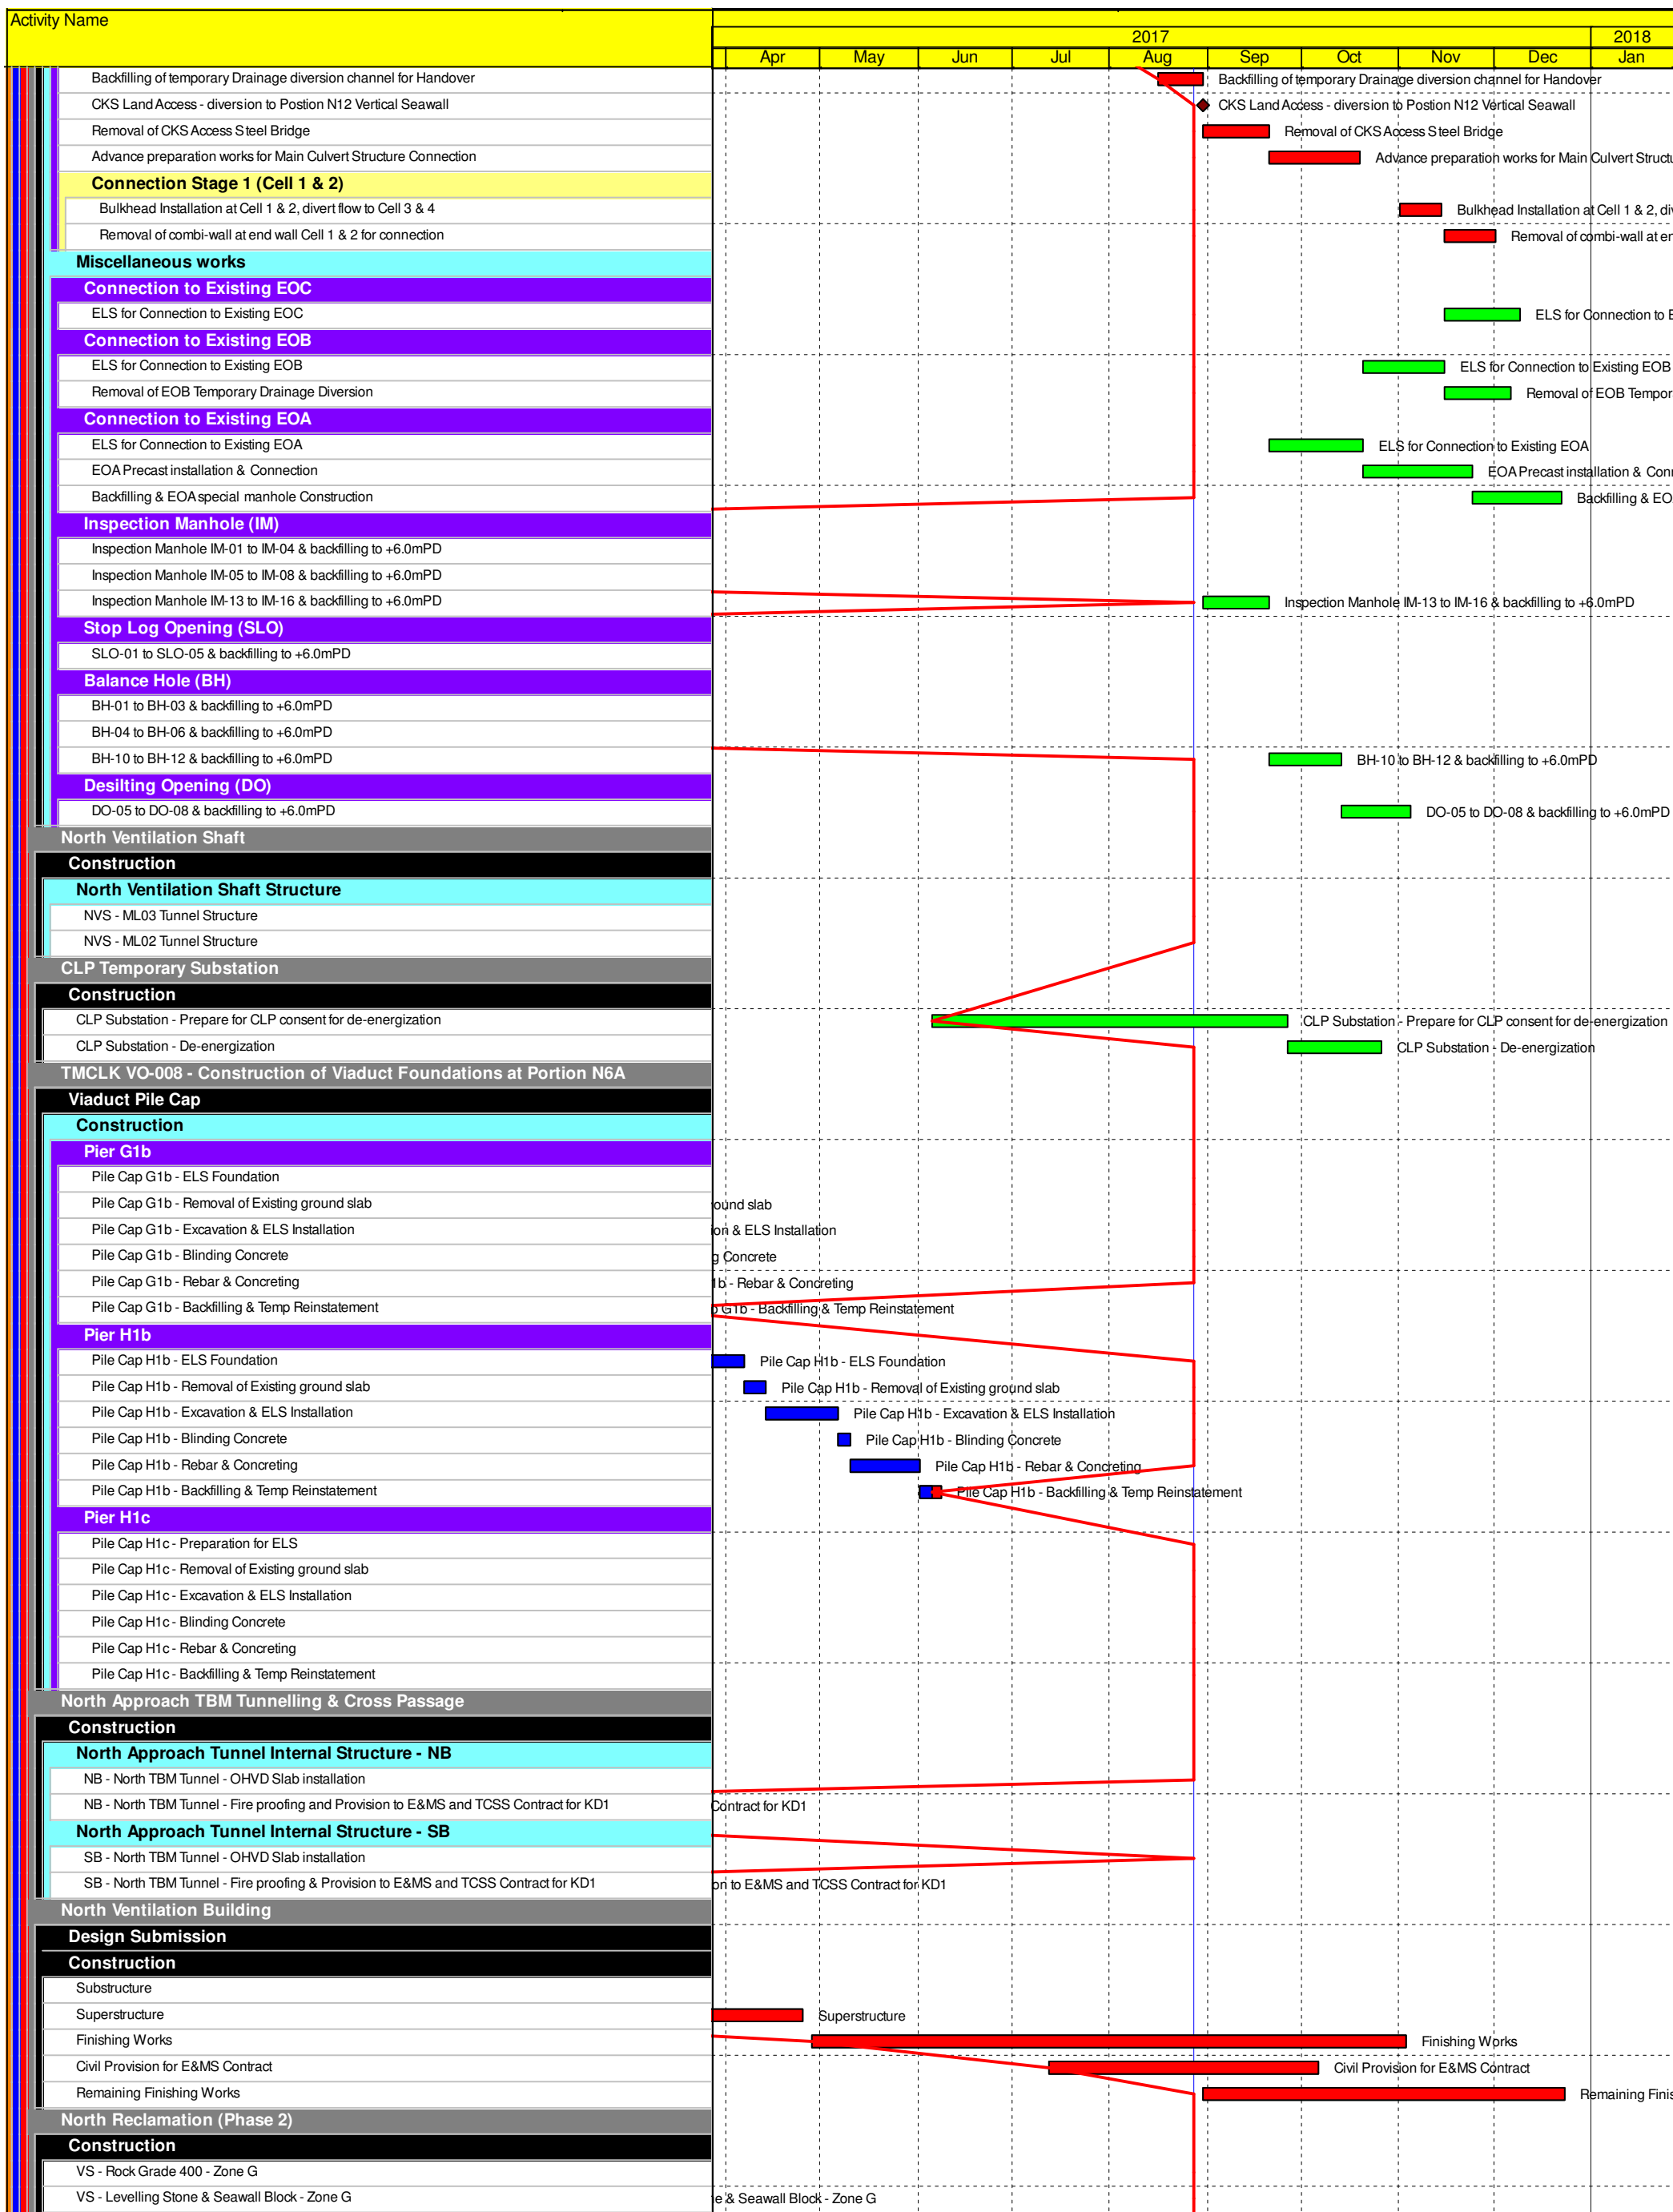

■ Planned Bar
■ Planned Bar - Critical
◆ Progress bar
◆ Progress Milestone

Date	Revision	Checked	Approved
12-Feb-14	TMCLKDBJGEN-PRG98507	WYu	SPa
08-Apr-14	TMCLKDBJGEN-PRG98507 Rev B	SPa	WYu
28-Aug-14	TMCLKDBJGEN-PRG98507 Rev C	CLa	WYu
30-Oct-15	TMCLKDBJGEN-PRG98507 Rev F	WYu	

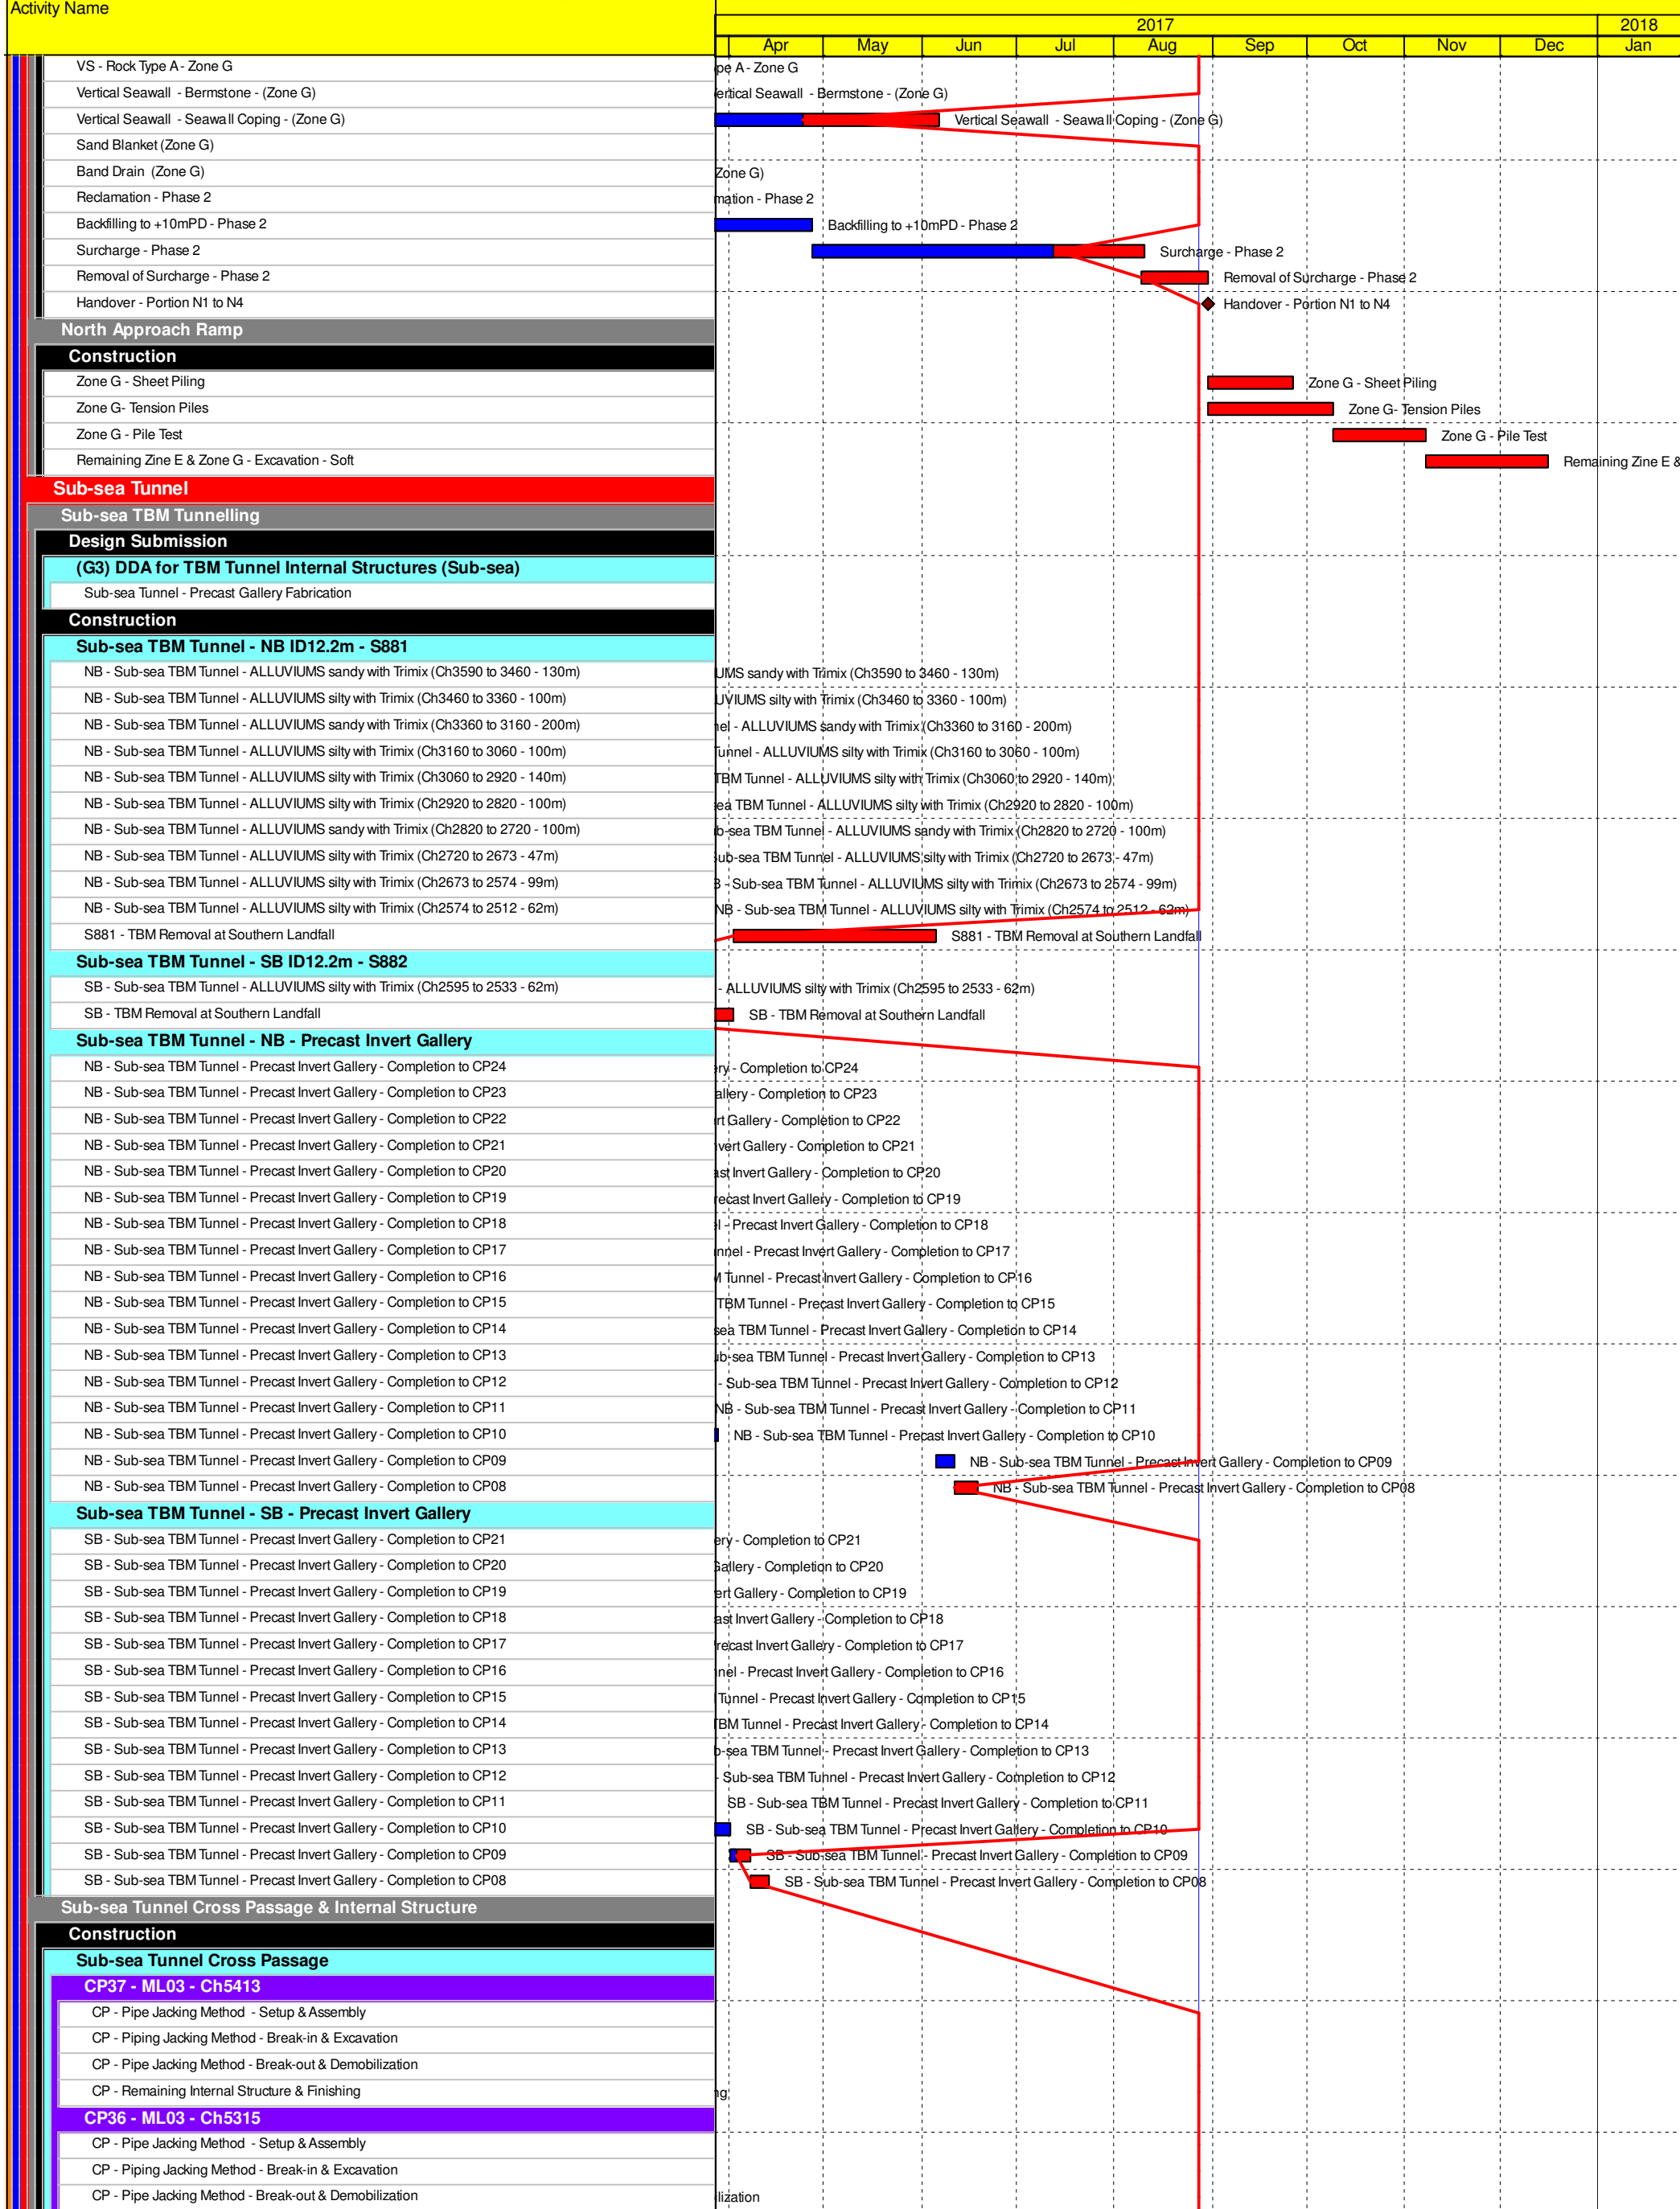

■ Planned Bar
■ Planned Bar - Critical
◆ Planned Milestone
■ Progress bar
◆ Progress Milestone

TMCLK - Northern Connection Sub-Sea Tunnel Section
 Detailed Works Programme (Rev. F)
 Three Months Rolling Programme
 Progress as of 27-Aug-17


Date	Revision	Checked	Approved
12-Feb-14	TMCLKDBJGN-FRG98507	WYu	SPa
08-Apr-14	TMCLKDBJGN-FRG98507 Rev B	SPa	WYu
28-Aug-14	TMCLKDBJGN-FRG98507 Rev C	CLa	WYu
30-Oct-15	TMCLKDBJGN-FRG98507 Rev F	WYu	

Activity Name	2017										2018
	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	
CP - Remaining Internal Structure & Finishing											
CP35 - ML03 - Ch5217											
CP - Pipe Jacking Method - Setup & Assembly											
CP - Piping Jacking Method - Break-in & Excavation											
CP - Pipe Jacking Method - Break-out & Demobilization											
CP - Remaining Internal Structure & Finishing											
CP34 - ML03 - Ch5118											
CP - Pipe Jacking Method - Setup & Assembly											
CP - Piping Jacking Method - Break-in & Excavation											
CP - Pipe Jacking Method - Break-out & Demobilization											
CP - Remaining Internal Structure & Finishing											
CP33 - ML03 - Ch5020											
CP - Pipe Jacking Method - Setup & Assembly											
CP - Piping Jacking Method - Break-in & Excavation											
CP - Pipe Jacking Method - Break-out & Demobilization											
CP - Remaining Internal Structure & Finishing											
CP32 - ML03 - Ch4921											
CP - Pipe Jacking Method - Setup & Assembly											
CP - Piping Jacking Method - Break-in & Excavation											
CP - Pipe Jacking Method - Break-out & Demobilization											
CP - Remaining Internal Structure & Finishing											
CP31 - ML03 - Ch4823											
CP - Pipe Jacking Method - Setup & Assembly											
CP - Piping Jacking Method - Break-in & Excavation											
CP - Pipe Jacking Method - Break-out & Demobilization											
CP - Remaining Internal Structure & Finishing											
CP30 - ML03 - Ch4724											
CP - Pipe Jacking Method - Setup & Assembly											
CP - Piping Jacking Method - Break-in & Excavation											
CP - Pipe Jacking Method - Break-out & Demobilization											
CP - Remaining Internal Structure & Finishing											
CP29 - ML03 - Ch4626											
CP - Pipe Jacking Method - Setup & Assembly											
CP - Piping Jacking Method - Break-in & Excavation											
CP - Pipe Jacking Method - Break-out & Demobilization											
CP - Remaining Internal Structure & Finishing											
CP28 - ML03 - Ch4527											
CP - Pipe Jacking Method - Setup & Assembly											
CP - Piping Jacking Method - Break-in & Excavation											
CP - Pipe Jacking Method - Break-out & Demobilization											
CP - Remaining Internal Structure & Finishing											
CP27 - ML03 - Ch4429											
CP - Pipe Jacking Method - Setup & Assembly											
CP - Piping Jacking Method - Break-in & Excavation											
CP - Pipe Jacking Method - Break-out & Demobilization											
CP - Remaining Internal Structure & Finishing											
CP26 - ML03 - Ch4330											
CP - Pipe Jacking Method - Setup & Assembly											
CP - Piping Jacking Method - Break-in & Excavation											
CP - Pipe Jacking Method - Break-out & Demobilization											
CP - Remaining Internal Structure & Finishing											
CP25 - ML03 - Ch4232											
CP - Pipe Jacking Method - Setup & Assembly											
CP - Piping Jacking Method - Break-in & Excavation											
CP - Pipe Jacking Method - Break-out & Demobilization											
CP - Remaining Internal Structure & Finishing											
CP24 - ML03 - Ch4133											
CP - Pipe Jacking Method - Setup & Assembly											
CP - Piping Jacking Method - Break-in & Excavation											
CP - Pipe Jacking Method - Break-out & Demobilization											
CP - Remaining Internal Structure & Finishing											
CP23 - ML03 - Ch4035											
CP - Pipe Jacking Method - Setup & Assembly											
CP - Piping Jacking Method - Break-in & Excavation											
CP - Pipe Jacking Method - Break-out & Demobilization											
CP - Remaining Internal Structure & Finishing											
CP22 - ML03 - Ch3936											
CP - Pipe Jacking Method - Setup & Assembly											
CP - Piping Jacking Method - Break-in & Excavation											
CP - Pipe Jacking Method - Break-out & Demobilization											
CP - Remaining Internal Structure & Finishing											
CP21 - ML03 - Ch3838											
CP - Pipe Jacking Method - Setup & Assembly											
CP - Piping Jacking Method - Break-in & Excavation											
CP - Pipe Jacking Method - Break-out & Demobilization											
CP - Remaining Internal Structure & Finishing											
CP20 - ML03 - Ch3739											
CP - Pipe Jacking Method - Setup & Assembly											
CP - Piping Jacking Method - Break-in & Excavation											
CP - Pipe Jacking Method - Break-out & Demobilization											
CP - Remaining Internal Structure & Finishing											
CP19 - ML03 - Ch3641											

■ Planned Bar
■ Planned Bar - Critical
■ Progress bar
◆ Planned Milestone
◆ Progress Milestone

TMCLK - Northern Connection Sub-Sea Tunnel Section
Detailed Works Programme (Rev. F)
Three Months Rolling Programme
 Progress as of 27-Aug-17


Date	Revision	Checked	Approved
12-Feb-14	TMCLKDBJGEN-PRG08507	WYu	SPa
08-Apr-14	TMCLKDBJGEN-PRG08507 Rev B	SPa	WYu
28-Aug-14	TMCLKDBJGEN-PRG08507 Rev C	CLa	WYu
30-Oct-15	TMCLKDBJGEN-PRG08507 Rev F	WYu	

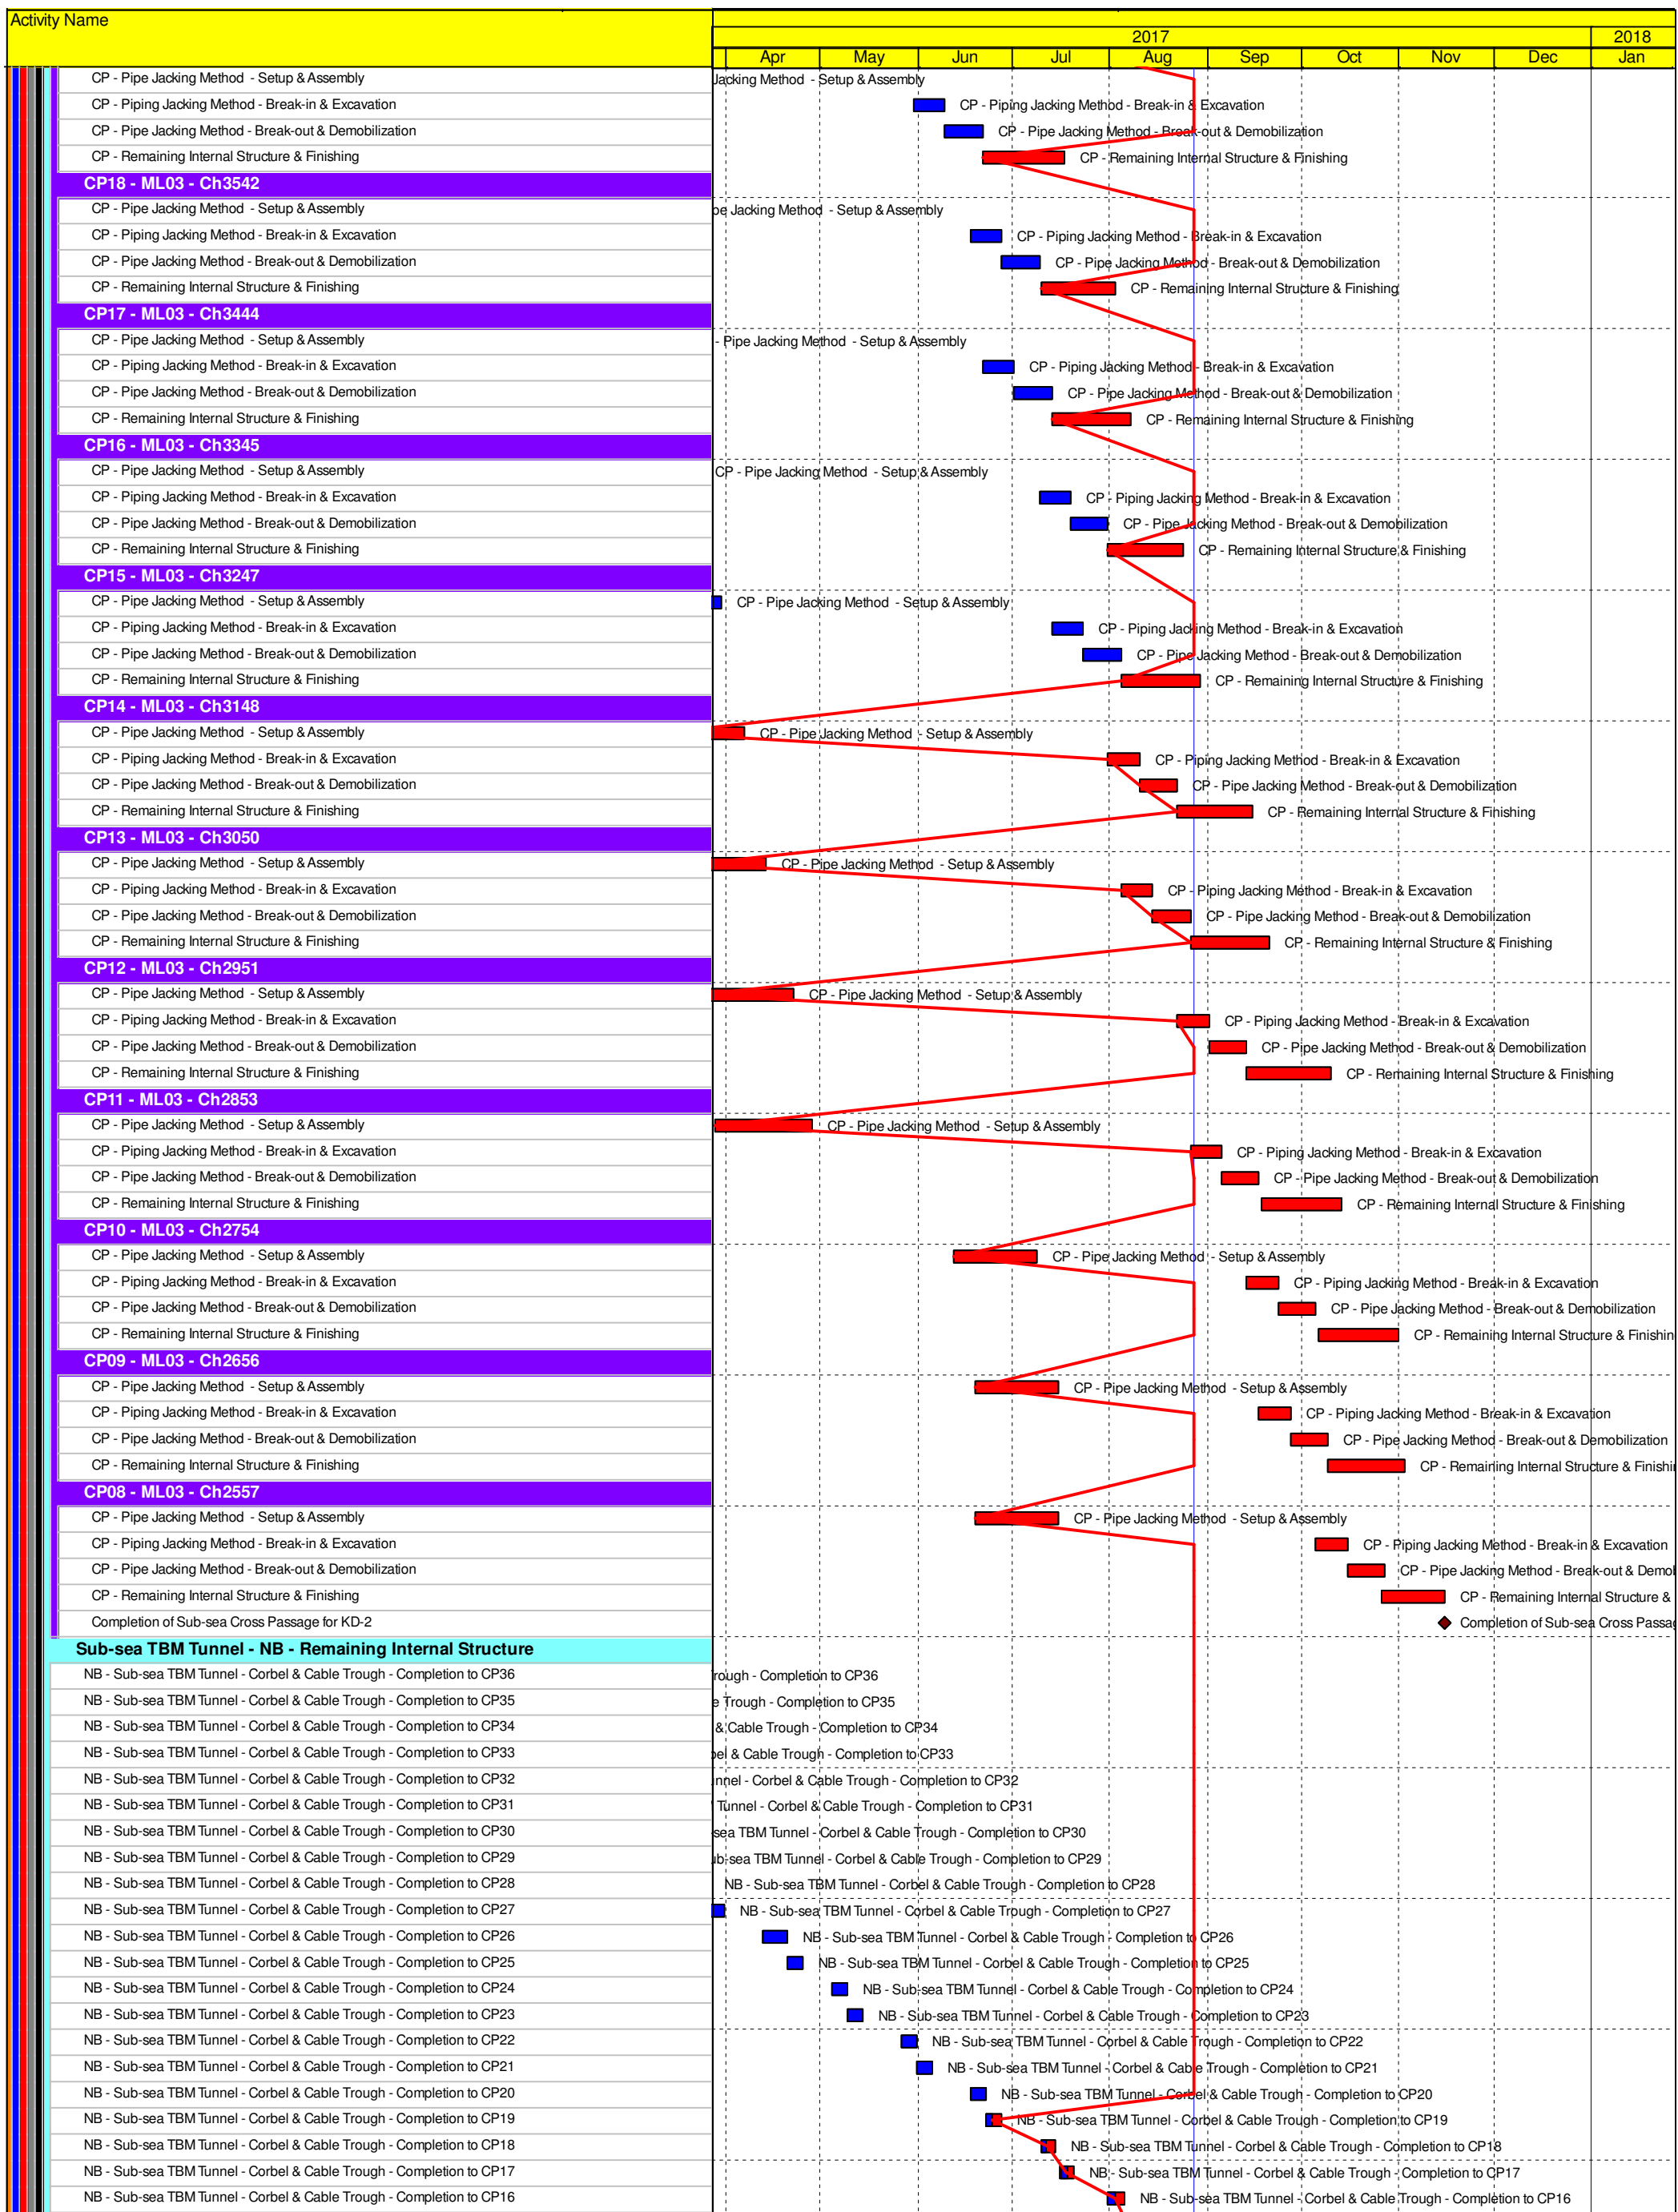

■ Planned Bar
■ Planned Bar - Critical
■ Progress bar
◆ Planned Milestone
◆ Progress Milestone

TMCLK - Northern Connection Sub-Sea Tunnel Section
Detailed Works Programme (Rev. F)
Three Months Rolling Programme
 Progress as of 27-Aug-17

Date	Revision	Checked	Approved
12-Feb-14	TMCLKDBJGEN-FRG98507	WYu	SPa
08-Apr-14	TMCLKDBJGEN-FRG98507 Rev B	SPa	WYu
28-Aug-14	TMCLKDBJGEN-FRG98507 Rev C	CLa	WYu
30-Oct-15	TMCLKDBJGEN-FRG98507 Rev F	WYu	

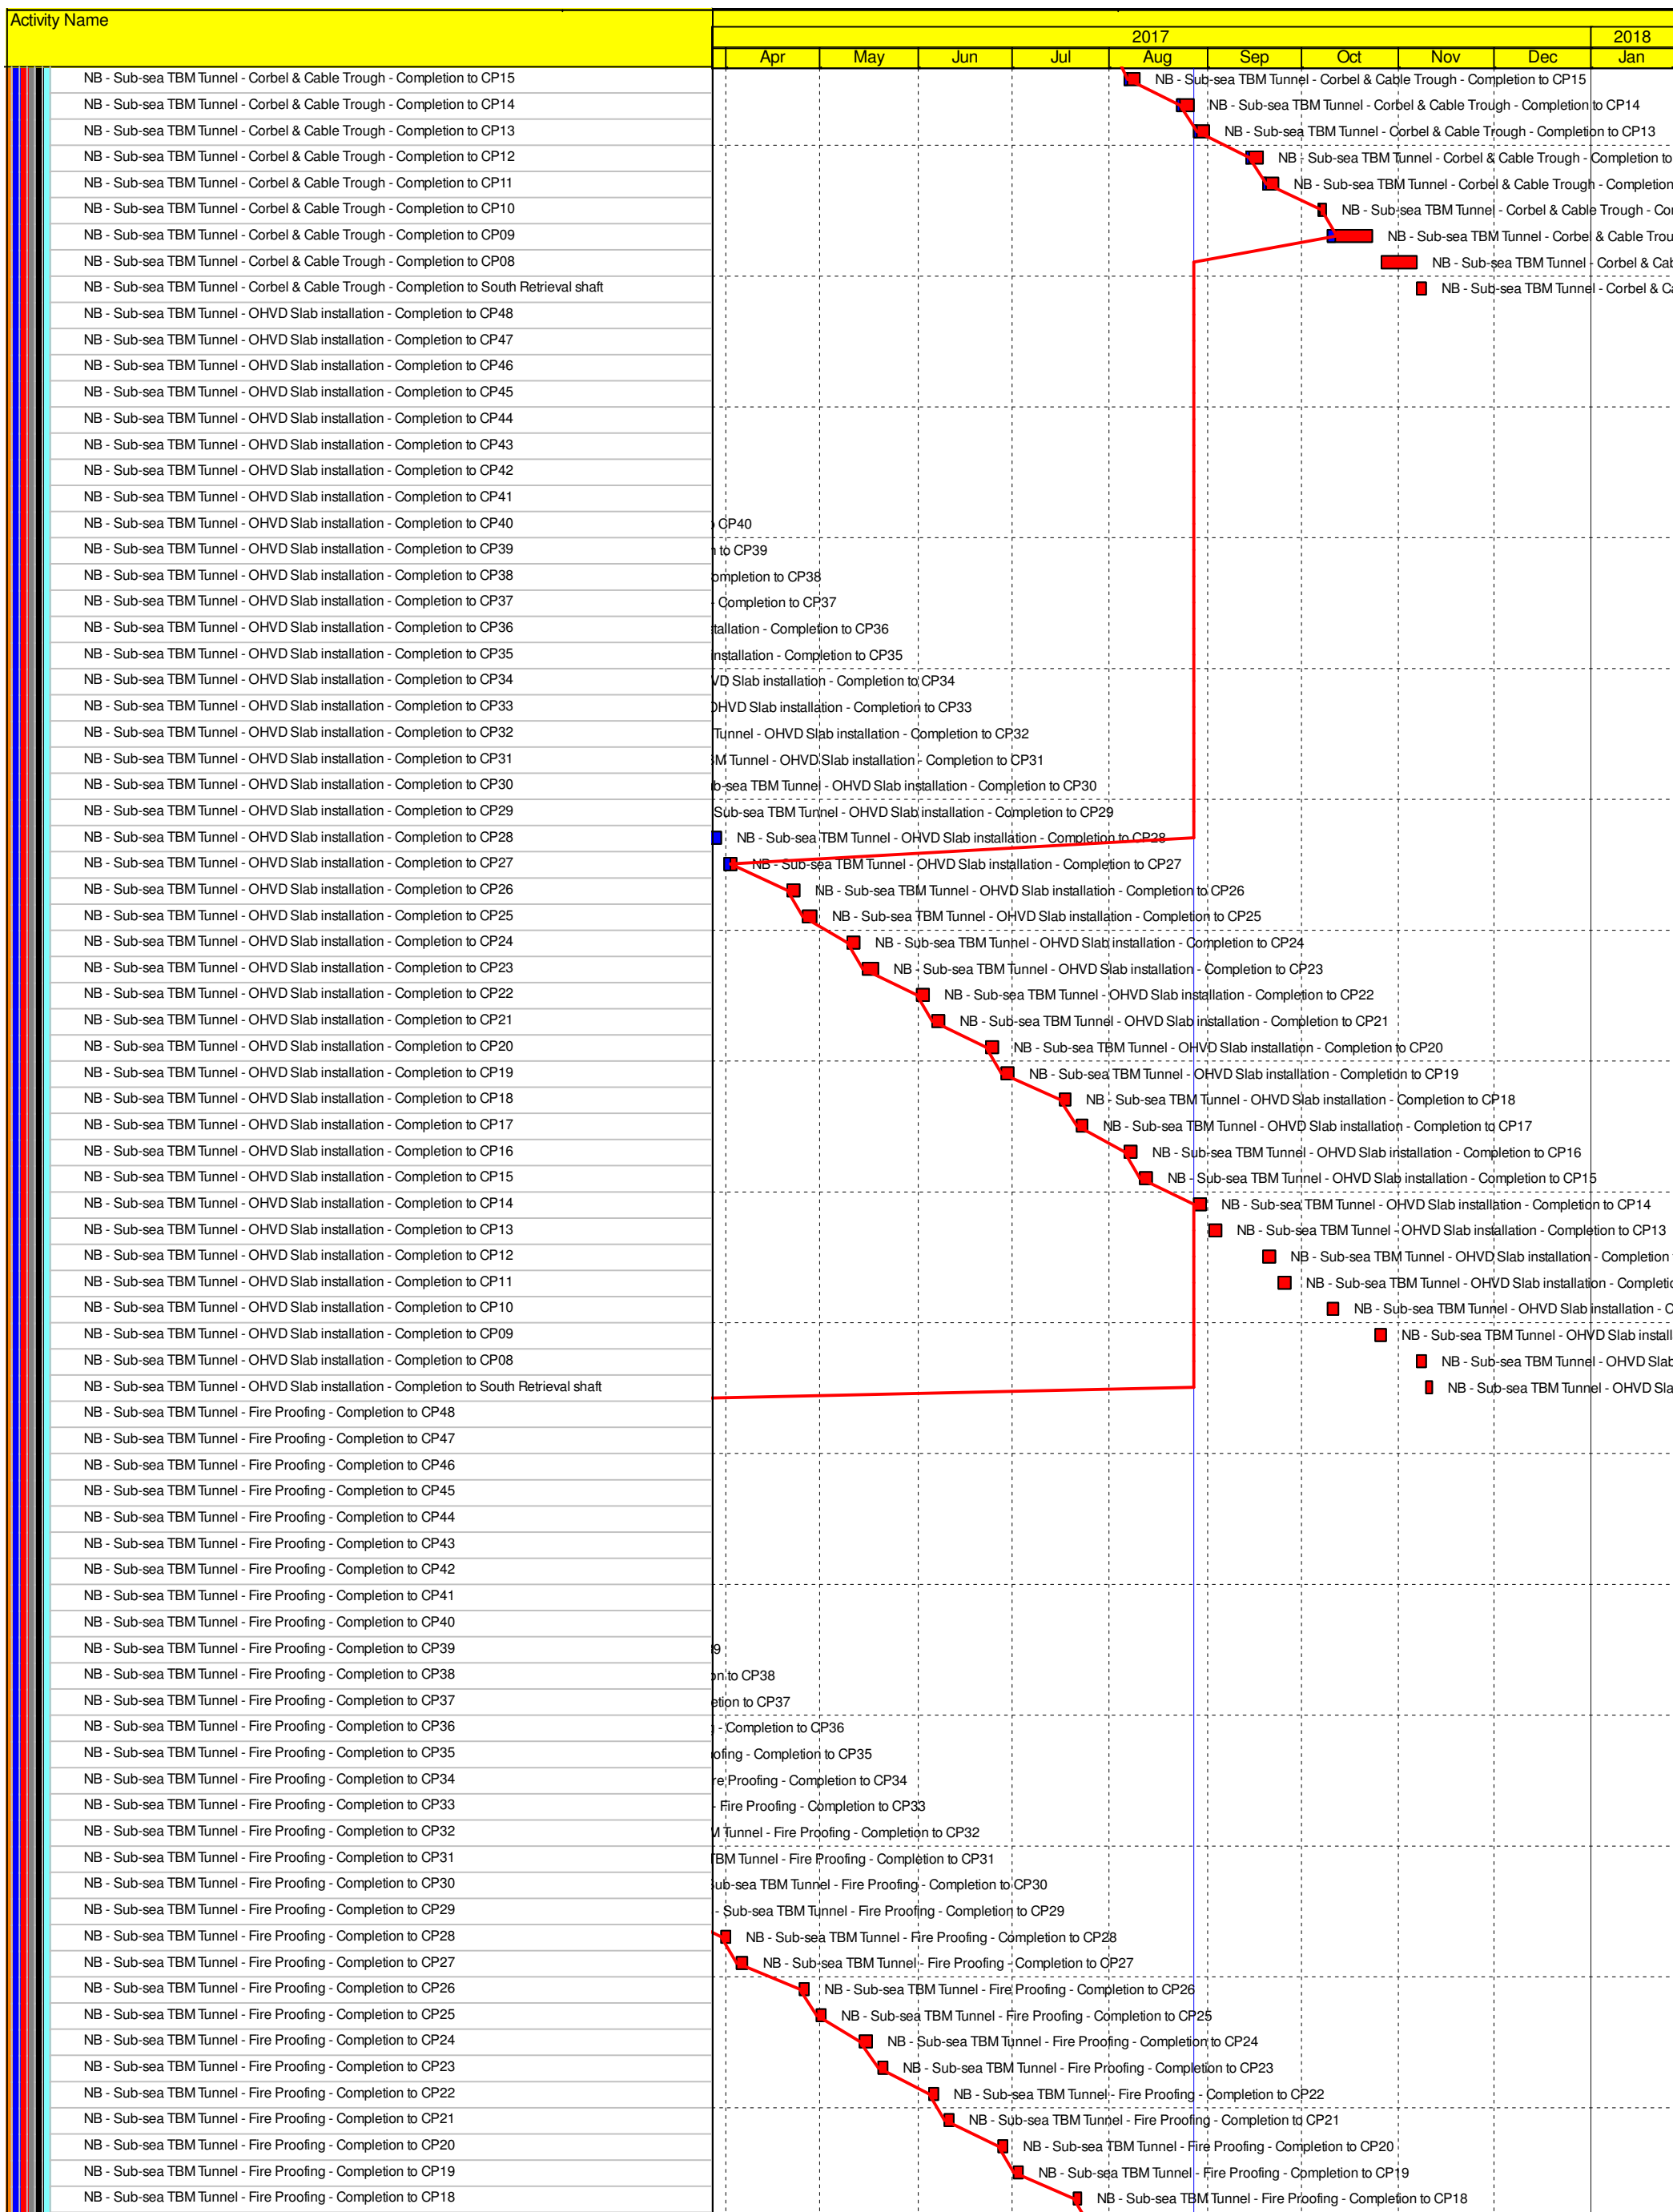


	Planned Bar
	Planned Bar - Critical
	Planned Milestone
	Progress bar
	Progress Milestone






TMCLK - Northern Connection Sub-Sea Tunnel Section
 Detailed Works Programme (Rev. F)
 Three Months Rolling Programme
 Progress as of 27-Aug-17

Date	Revision	Checked	Approved
12-Feb-14	TMCLKDBJGN-FRG98507	WYu	SPa
08-Apr-14	TMCLKDBJGN-FRG98507 Rev B	SPa	WYu
28-Aug-14	TMCLKDBJGN-FRG98507 Rev C	CLa	WYu
30-Oct-15	TMCLKDBJGN-FRG98507 Rev F	WYu	

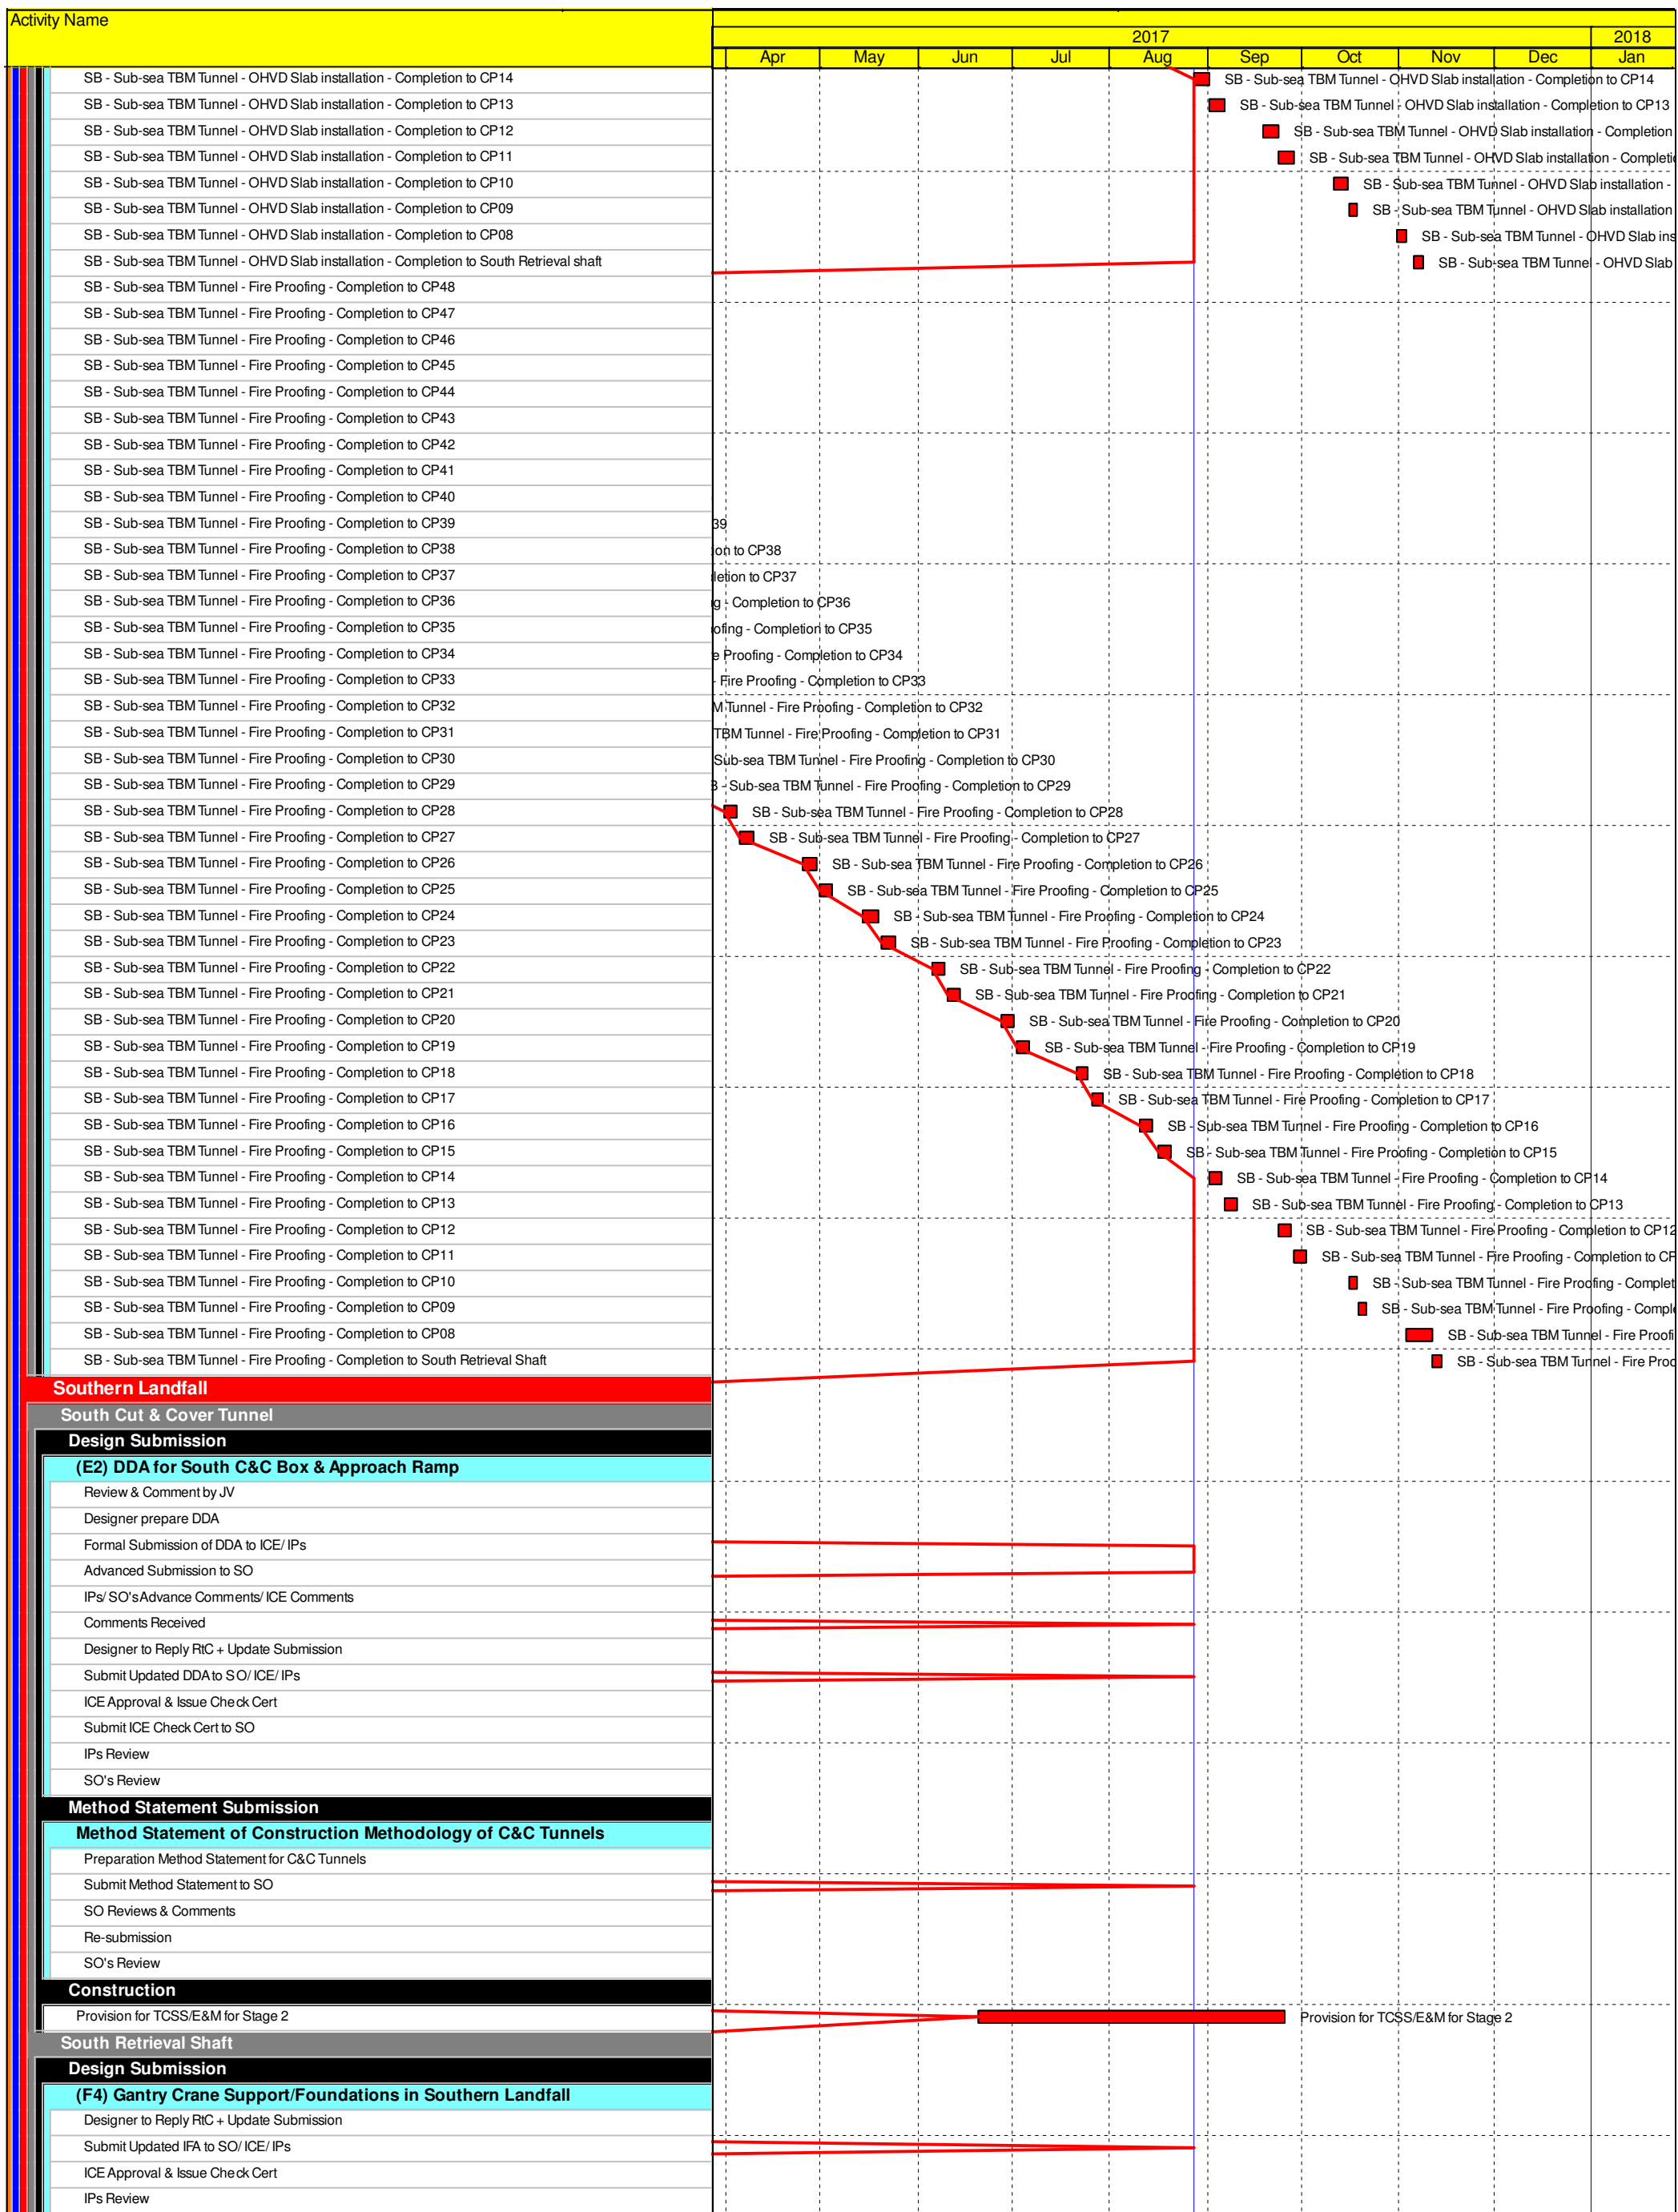Activity Name	2017											2018
	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan		
	NB - Sub-sea TBM Tunnel - Fire Proofing - Completion to CP17											
NB - Sub-sea TBM Tunnel - Fire Proofing - Completion to CP16												
NB - Sub-sea TBM Tunnel - Fire Proofing - Completion to CP15												
NB - Sub-sea TBM Tunnel - Fire Proofing - Completion to CP14												
NB - Sub-sea TBM Tunnel - Fire Proofing - Completion to CP13												
NB - Sub-sea TBM Tunnel - Fire Proofing - Completion to CP12												
NB - Sub-sea TBM Tunnel - Fire Proofing - Completion to CP11												
NB - Sub-sea TBM Tunnel - Fire Proofing - Completion to CP10												
NB - Sub-sea TBM Tunnel - Fire Proofing - Completion to CP09												
NB - Sub-sea TBM Tunnel - Fire Proofing - Completion to CP08												
NB - Sub-sea TBM Tunnel - Fire Proofing - Completion to South Retrieval Shaft												
NB - Sub-sea TBM Tunnel - Road Level Fire Proofing												






	Planned Bar
	Planned Bar - Critical
	Planned Milestone
	Progress bar
	Progress Milestone


TMCLK - Northern Connection Sub-Sea Tunnel Section
 Detailed Works Programme (Rev. F)
 Three Months Rolling Programme
 Progress as of 27-Aug-17

Date	Revision	Checked	Approved
12-Feb-14	TMCLKDBJGN-FRG98507	WYu	SPu
08-Apr-14	TMCLKDBJGN-FRG98507 Rev B	SPu	WYu
28-Aug-14	TMCLKDBJGN-FRG98507 Rev C	CLa	WYu
30-Oct-15	TMCLKDBJGN-FRG98507 Rev F	WYu	

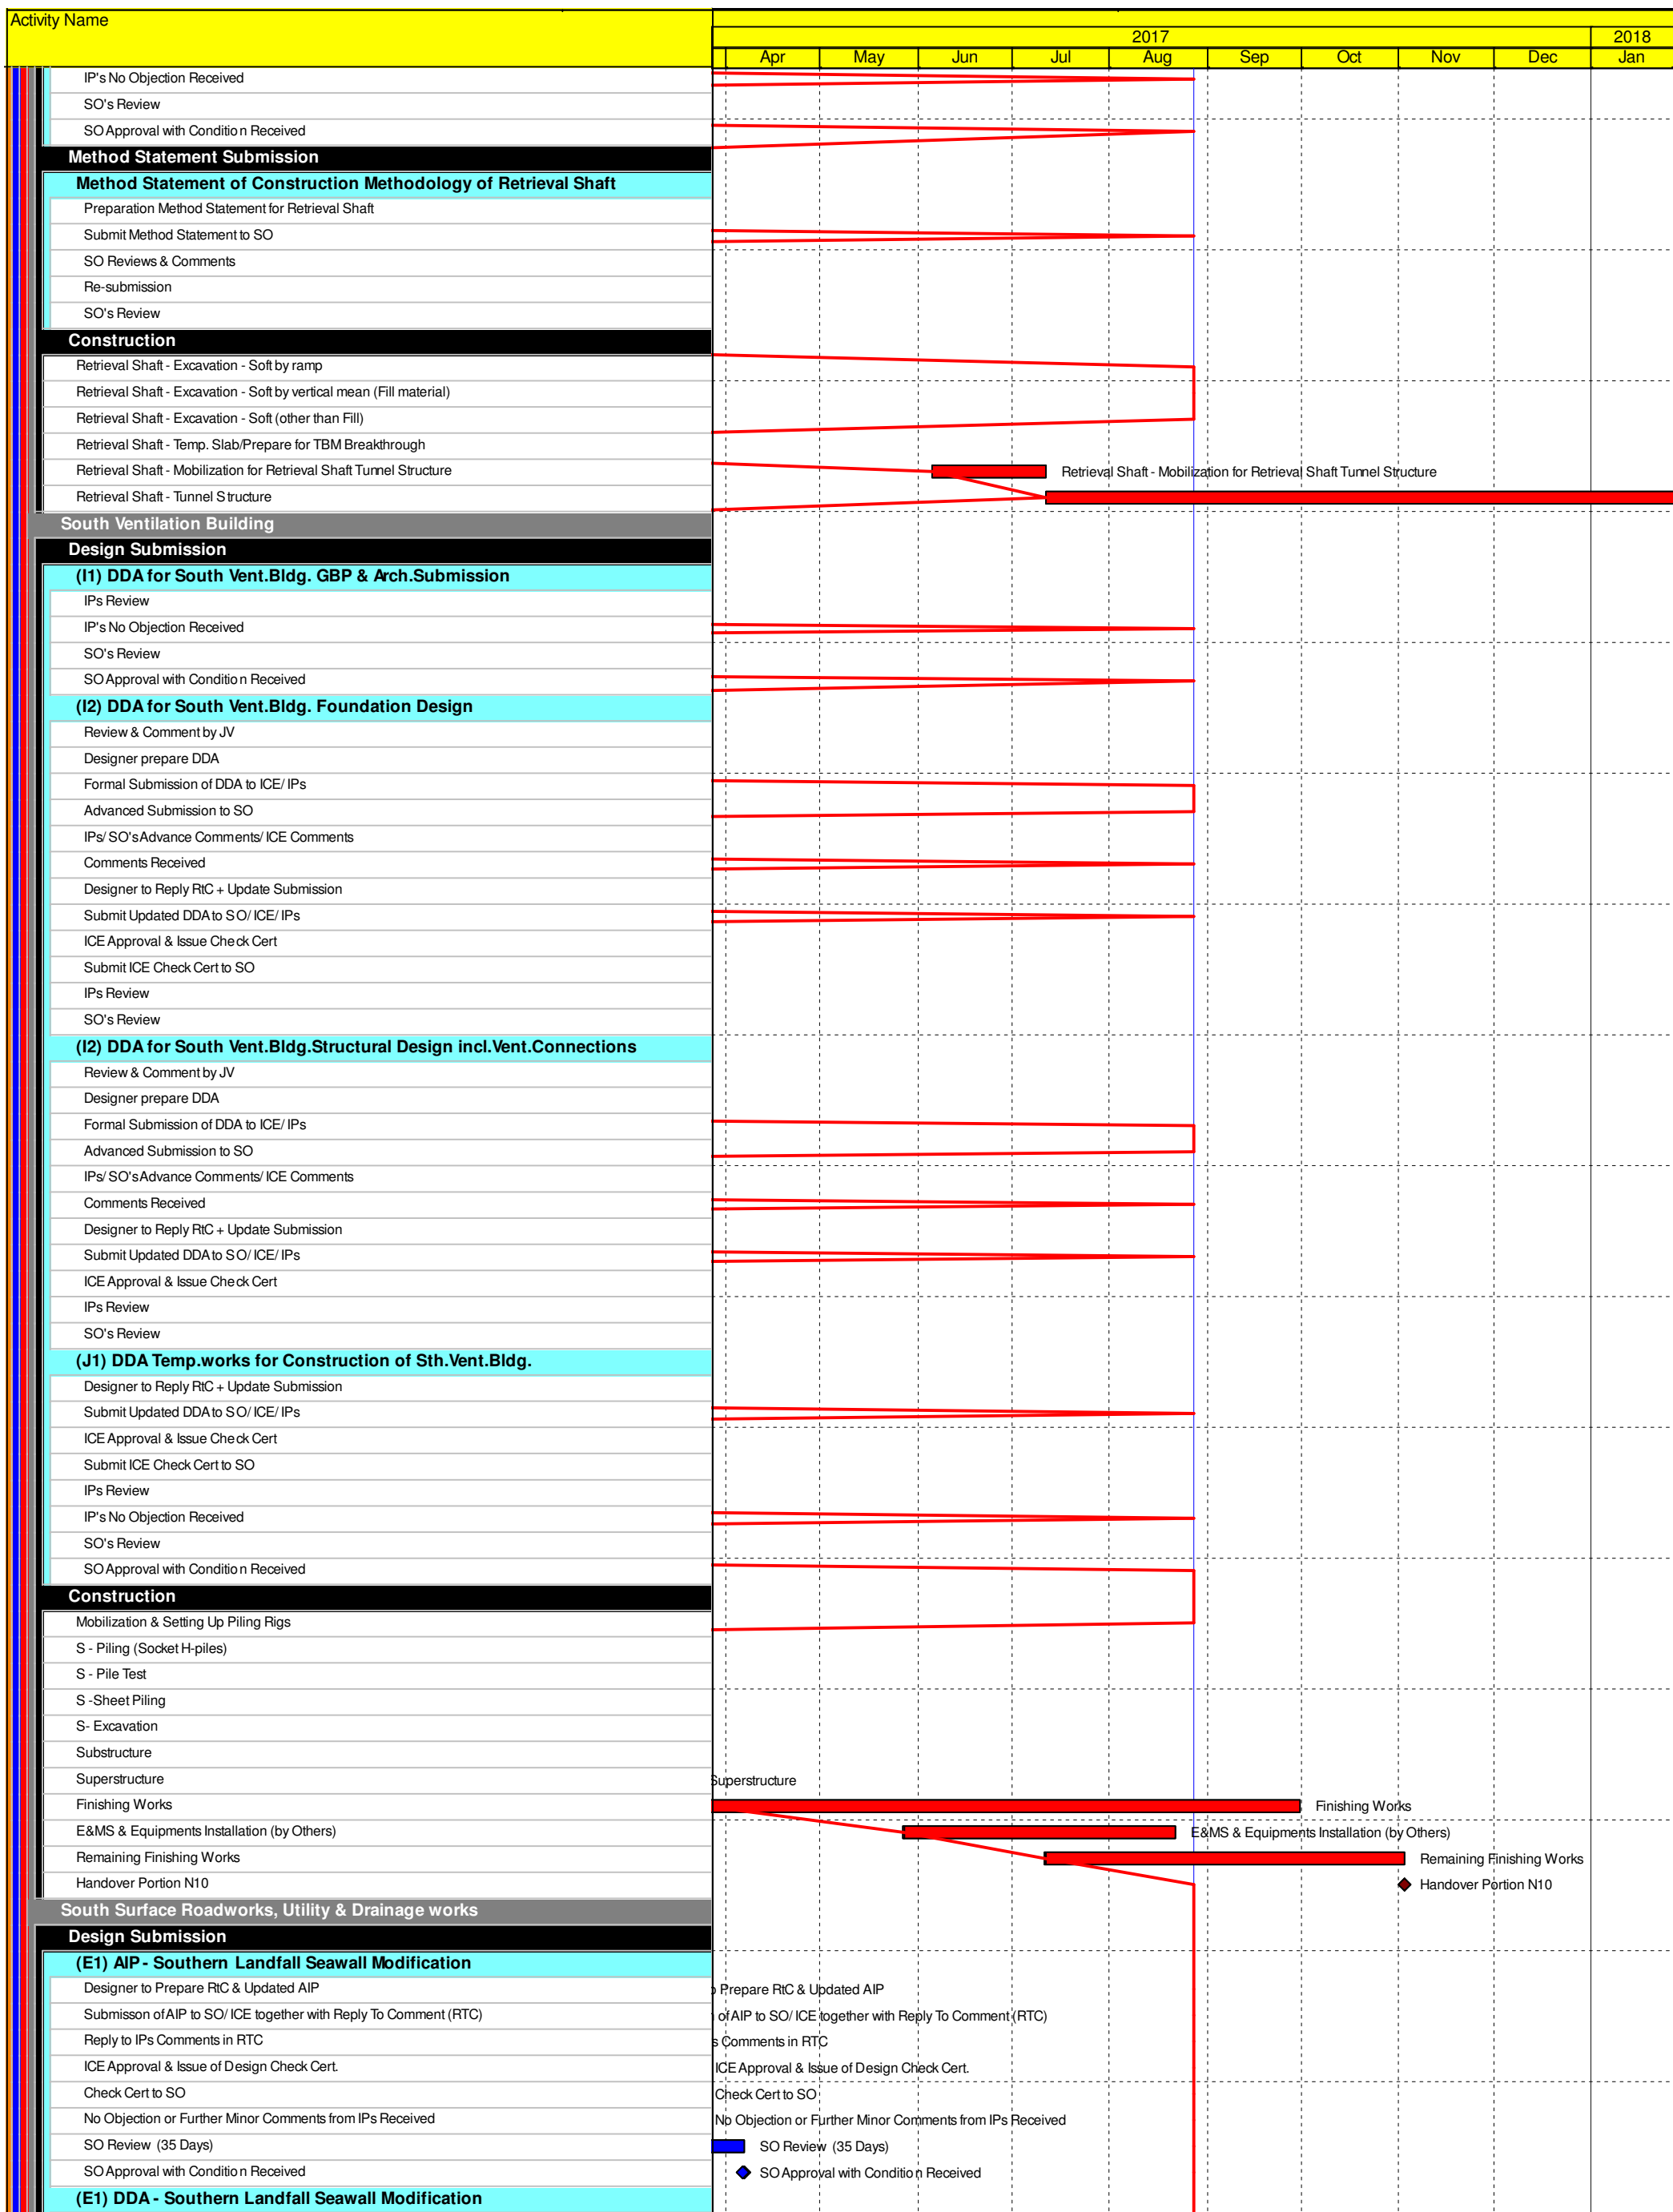

■ Planned Bar
■ Planned Bar - Critical
◆ Planned Milestone
■ Progress bar
◆ Progress Milestone

Date	Revision	Checked	Approved
12-Feb-14	TMCLKDBJGEN-PRG08507	WYu	SPa
08-Apr-14	TMCLKDBJGEN-PRG08507 Rev B	SPa	WYu
28-Aug-14	TMCLKDBJGEN-PRG08507 Rev C	CLa	WYu
30-Oct-15	TMCLKDBJGEN-PRG08507 Rev F	WYu	

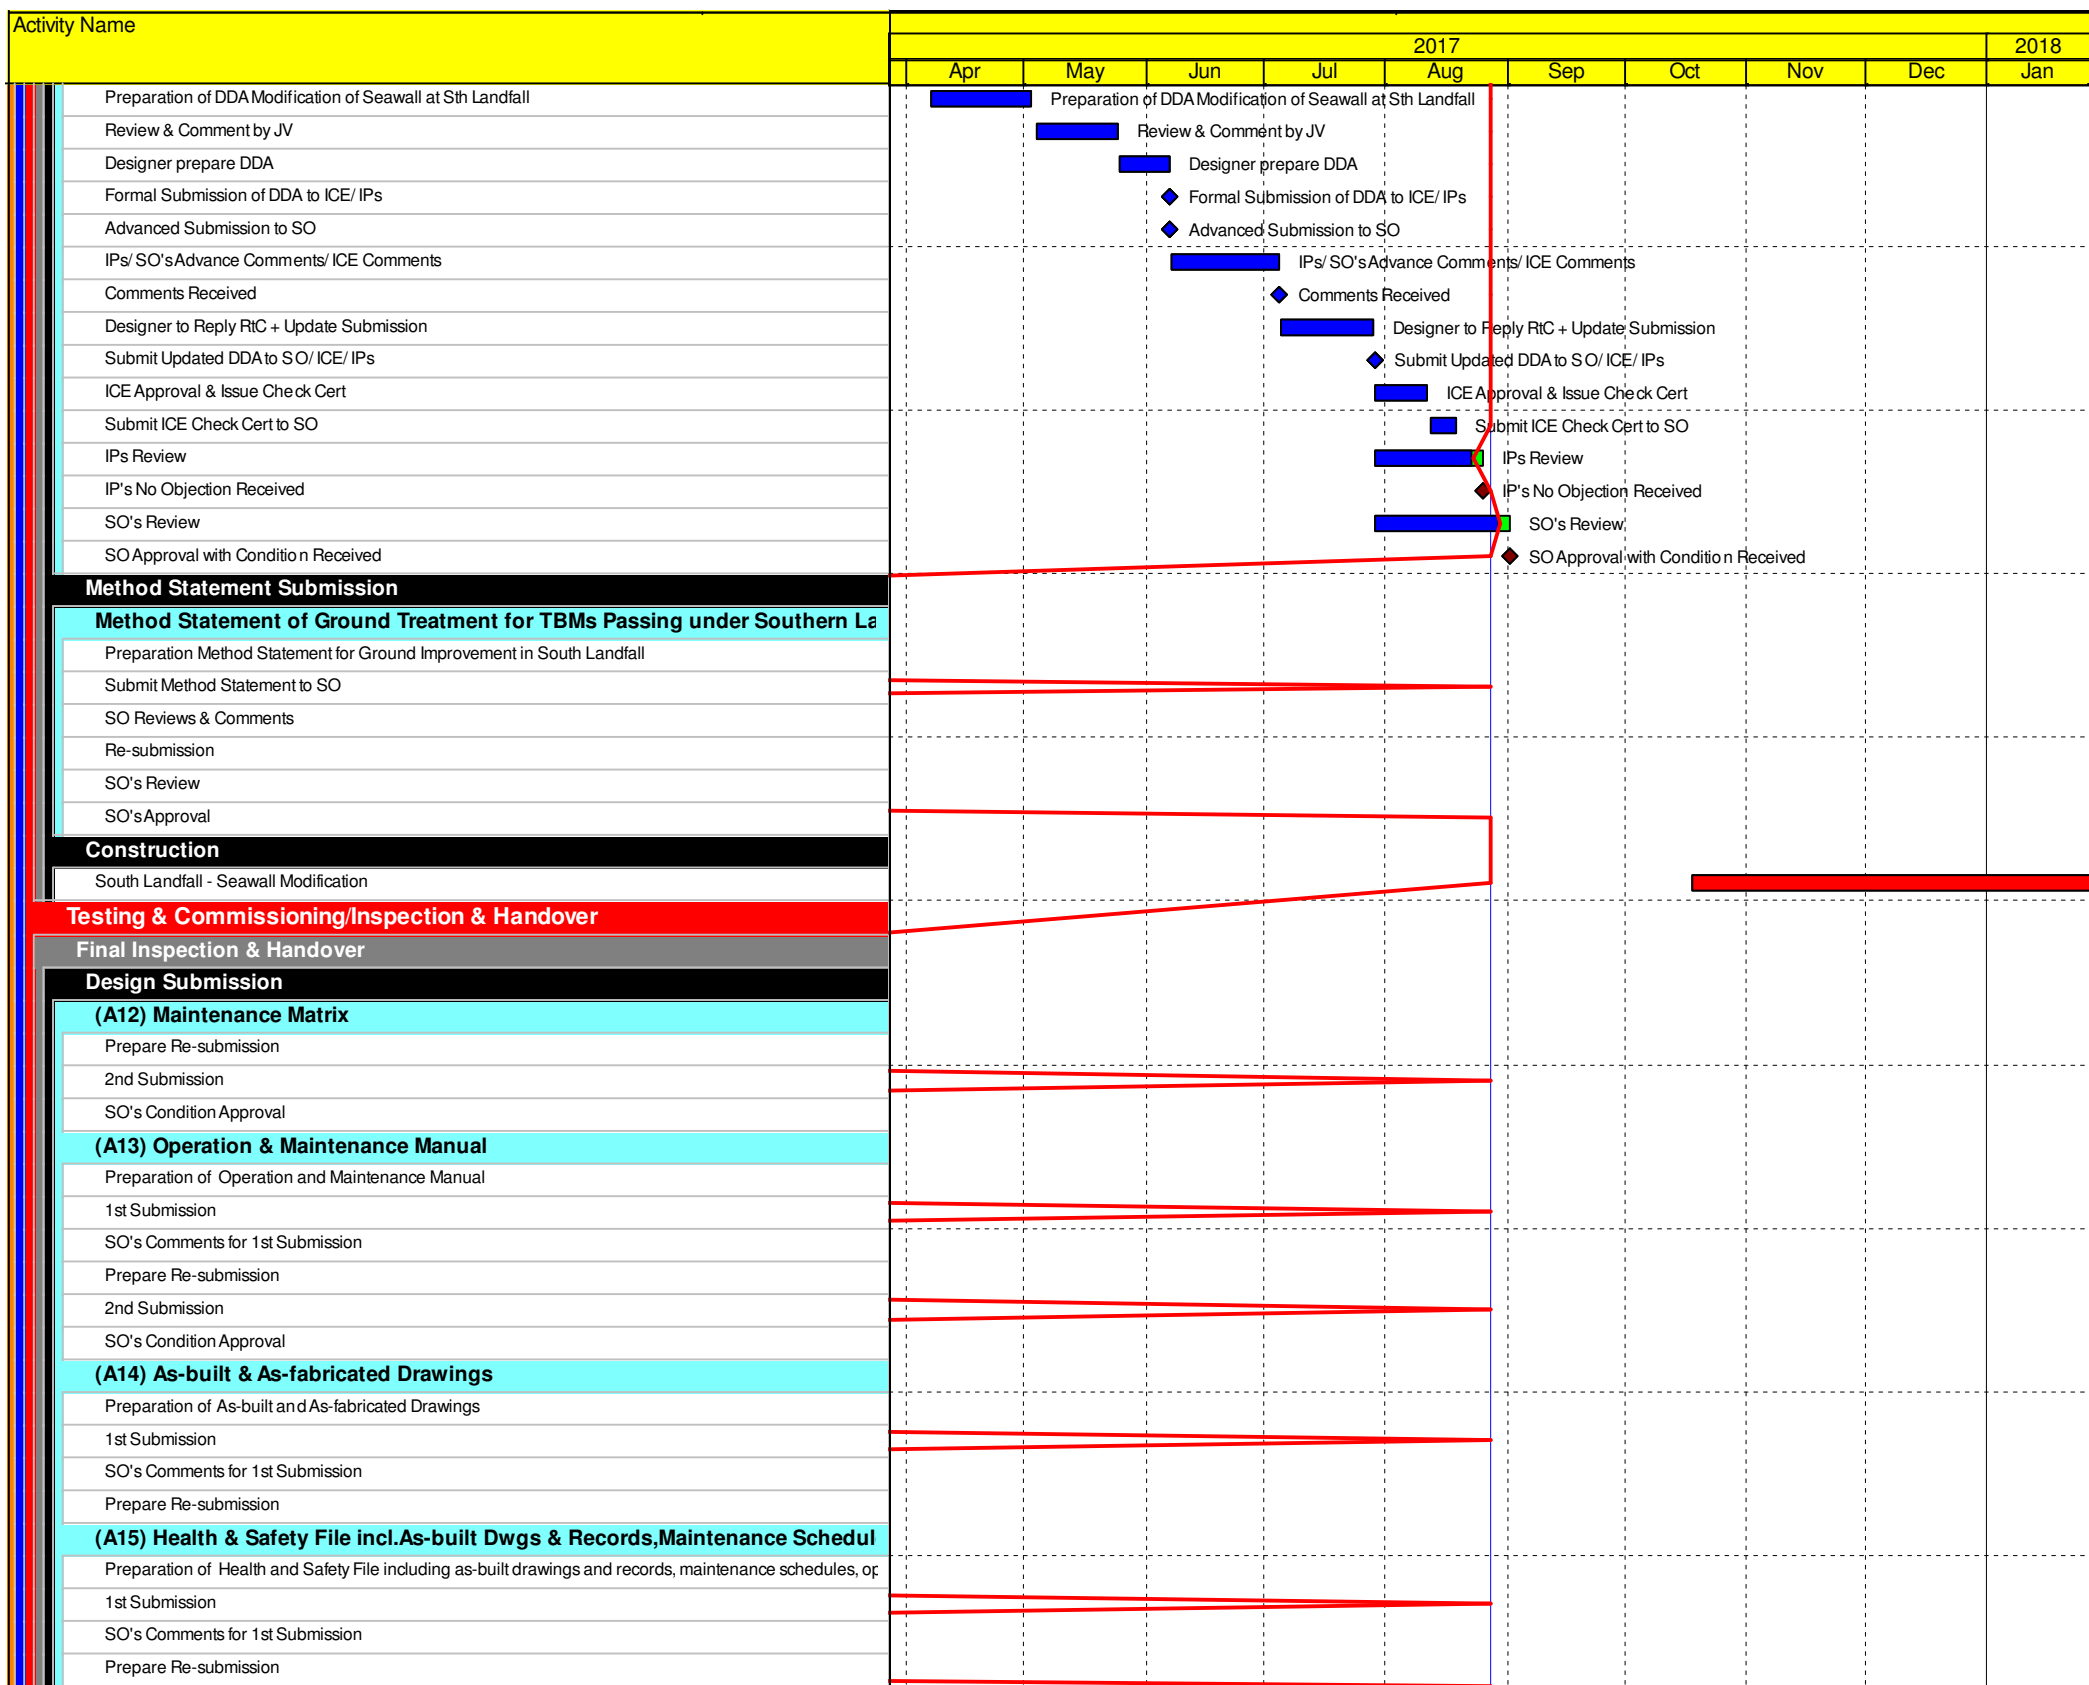

- Planned Bar
- Planned Bar - Critical
- Planned Milestone
- Progress bar
- Progress Milestone

Date	Revision	Checked	Approved
12-Feb-14	TMCLKDBJGEN-PRG08507	WYu	SPa
08-Apr-14	TMCLKDBJGEN-PRG08507 Rev B	SPa	WYu
28-Aug-14	TMCLKDBJGEN-PRG08507 Rev C	CLa	WYu
30-Oct-15	TMCLKDBJGEN-PRG08507 Rev F	WYu	
