


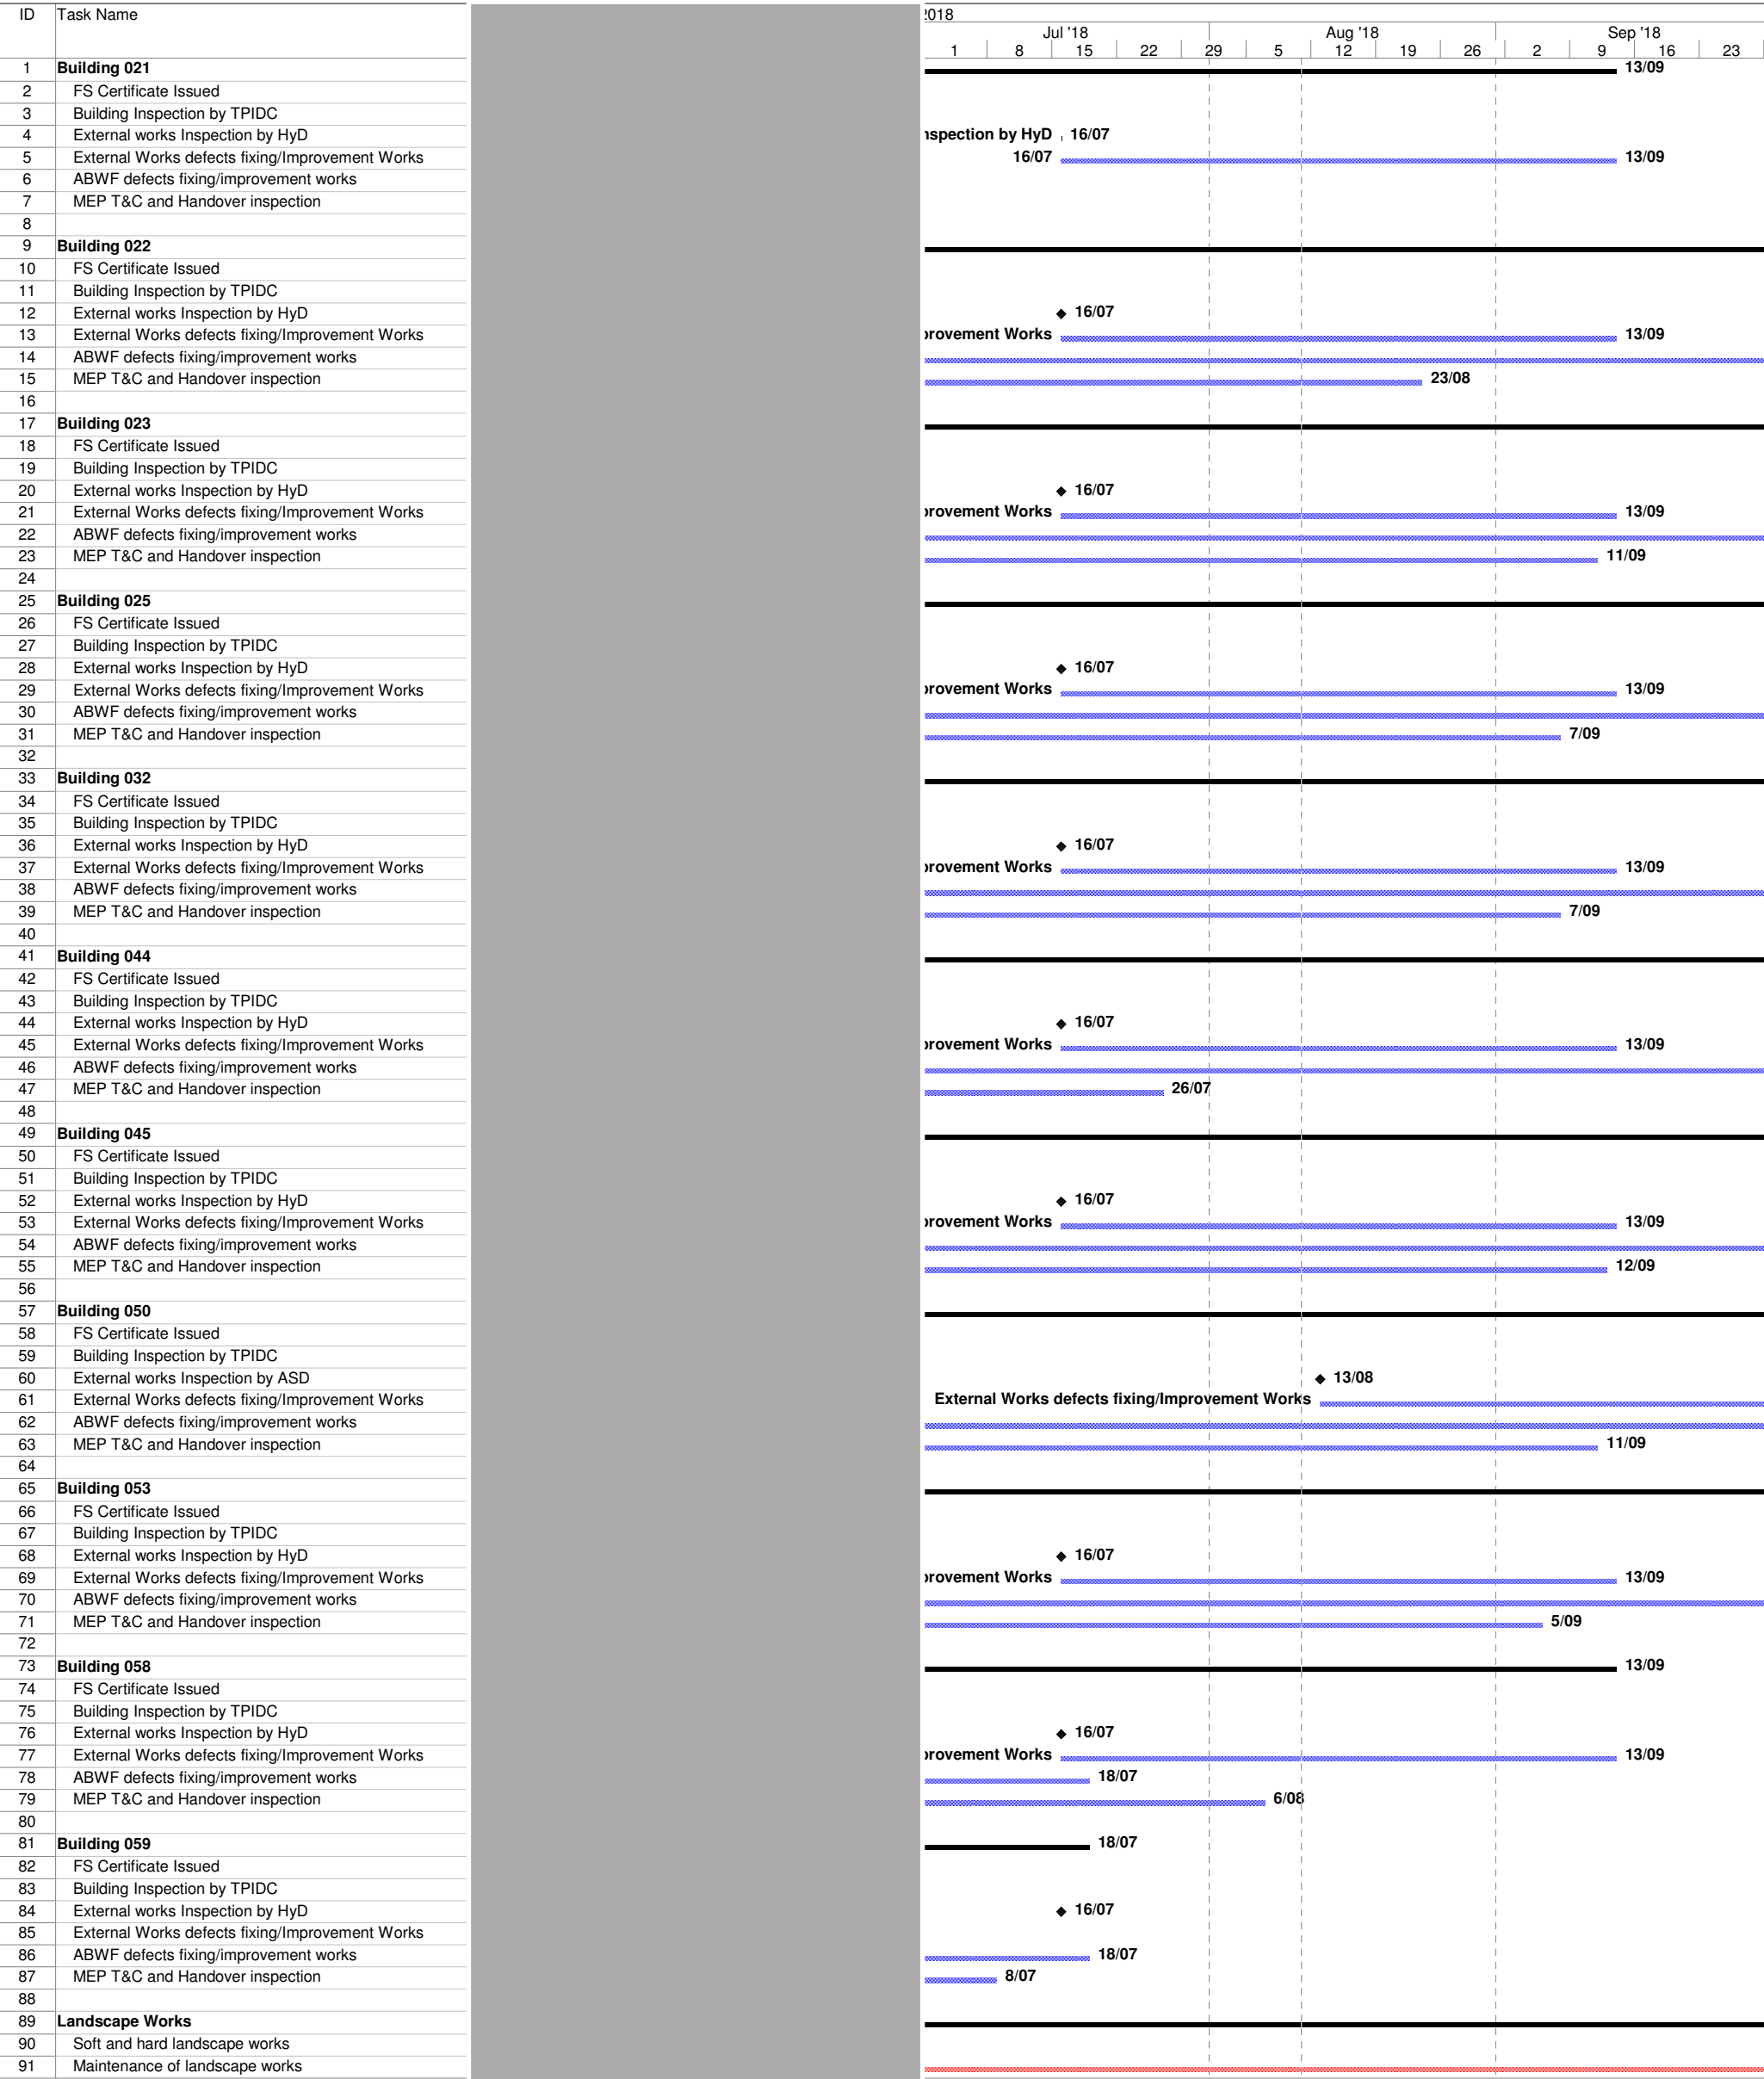

Remark: As confirmed by Contractor, work conducted in July 2018 were Defect Rectification work, landscape works at Building 022, 023, 025, 032, 044 and 045 and Testing and Commissioning.

Task		Rolled Up Task		Split		Inactive Task		Manual Task		Start-only	
Critical Task		Rolled Up Critical Task		External Tasks		Inactive Task		Duration-only		Finish-only	
Milestone		Rolled Up Milestone		Project Summary		Inactive Milestone		Manual Summary Rollup		Progress	
Summary		Rolled Up Progress		Group By Summary		Inactive Summary		Manual Summary		Deadline	

Contract No.: HY/2013/06		Detail Work Programme										Page 1 of 8																																													
Activity ID	Activity Name											2015			2016				2017				2018				2019																														
												Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3																												
📁 Hong Kong-Zhuhai_Macao Bridge Hong Kong Boundary Crossing F																																																									
📅 Key Dates																																																									
📅 Interface Activities																																																									
📅 Site and Facility Inspection																																																									
📄 JS1200	Pre Site and Facility Inspection by Contractor at Location 4 - Deg2																																																								
📄 JS1210	Joint Site and Facility Inspection with Interface Contractor at Location 4 - Deg2																																																								
📄 JS1620	Pre Site and Facility Inspection by Contractor at Location 14 - Deg2																																																								
📄 JS1630	Joint Site and Facility Inspection with Interface Contractor at Location 14 - Deg2																																																								
📄 JS1760	Pre Site and Facility Inspection by Contractor at Location 18 - Deg1																																																								
📄 JS1770	Joint Site and Facility Inspection with Interface Contractor at Location 18 - Deg1																																																								
📄 JS1780	Pre Site and Facility Inspection by Contractor at Location 18 - Deg2																																																								
📄 JS1790	Joint Site and Facility Inspection with Interface Contractor at Location 18 - Deg2																																																								
📅 Access Dates																																																									
📄 AD1000	Location 1(PCB (001) Basement)-Deg1 (270d)																																																								
📄 AD1010	Location 1(PCB (001) Basement)-Deg2 (380d)																																																								
📄 AD1020	Location 1(PCB (001) ELV Room (Grid Line E3))-Deg1 (270d)																																																								
📄 AD1030	Location 1(PCB (001) ELV Room (Grid Line E3))-Deg2 (380d)																																																								
📄 AD1040	Location 2(PCB (001) First Floor Main Server Room)-Deg1 (330d)																																																								
📄 AD1050	Location 2(PCB (001) First Floor Main Server Room)-Deg2 (380d)																																																								
📄 AD1060	Location 2(PCB (001) First Floor Main Server Room) - For Server Installation - Deg2 (330d)																																																								
📄 AD1070	Location 2(PCB (001) Ground Floor ELV Room (Grid Line E3)) - Deg1 (330d)																																																								
📄 AD1080	Location 2(PCB (001) Ground Floor DOH Port Health Control Room (Grid Line BD5)) - Deg1 (330d)																																																								
📄 AD1090	Location 2(PCB (001) Ground Floor DOH Port Health Control Room (Grid Line BD5)) - Deg2 (380d)																																																								
📄 AD1130	Location 3(Inbd Cargo Exam Bldg (037) Platform Control Room)-Deg2 (500d)																																																								
📄 AD1150	Location 3(Inbd Cargo Exam Bldg (037) Inspector Offices 128,129,130,131,128,129,140)-Deg2 (500d)																																																								
📄 AD1170	Location 3a(Inbd Cargo Exam Bldg (037) ROCARS Room)-Deg2 (480d)																																																								
📄 AD1190	Location 3a(Inbd Cargo Exam Bldg (037) Main Server Room)-Deg2 (480d)																																																								
📄 AD1200	Location 3a(Inbd Cargo Exam Bldg (037) Main Server Room) - For Server installation - Deg2 (480d)																																																								
📄 AD1220	Location 4(Outbd Cargo Exam Bldg (023))-Deg2 (680d)																																																								
📄 AD1240	Location 4a(Outbd Cargo Exam Bldg (023))-Deg2 (630d)																																																								
📄 AD1270	Location 6(Common Utility Enclosure & Staff Subway)-Deg1 (400d)																																																								
📄 AD1290	Location 7(Common Utility Enclosure & Staff Subway)-Deg1 (270d)																																																								
📄 AD1300	Location 8(Inbd Private Car Annex (025))-Deg1 (430d)																																																								
📄 AD1310	Location 8(Inbd Private Car Annex (025))-Deg2 (580d)																																																								
📄 AD1320	Location 8(Inbd Private Car Annex (025) Canopy)-Deg1 (430d)																																																								
📄 AD1330	Location 8(Inbd Private Car Annex (025) Canopy)-Deg2 (580d)																																																								
📄 AD1340	Location 9(Outbd Private Car Annex (032))-Deg1 (520d)																																																								
📄 AD1350	Location 9(Outbd Private Car Annex (032))-Deg2 (660d)																																																								
📄 AD1360	Location 9(Outbd Private Car Annex (032) Canopy)-Deg1 (520d)																																																								
📄 AD1370	Location 9(Outbd Private Car Annex (032) Canopy)-Deg2 (660d)																																																								
📄 AD1501	Location 12(Inbd Private Car Kiosks(027))-Deg1 (400d) Phase 2																																																								
📄 AD1510	Location 12(Inbd Private Car Kiosks(027))-Deg2 (480d) Phase 1																																																								
📄 AD1511	Location 12(Inbd Private Car Kiosks(027))-Deg2 (480d) Phase 2																																																								
📄 AD1521	Location 12(Inbd Private Car Kiosks(027) Canopy)-Deg1 (400d) Phase 2																																																								
Programme No.: HZMB-DWP		Actual Level of Effort Primary Baseline Actual Work Remaining Work Critical Remaining Work Baseline Milestone Milestone										Hong Kong-Zhuhai-Macao Bridge Hong Kong Boundary Crossing Facilities - Automatic Vehicle Clearance Support System (AVCSS)										Date				Revision				Checked				Approved																							
Data Date: 14-Aug-15																						14-Nov-16				Rev.: 0				WC				LC																							
																						10-Mar-17				Rev.: 1.0a				WC				LC																							
																						5-May-17				Rev.: 1.0b				WC				LC																							

Contract No.: HY/2013/06			Detail Work Programme																	Page 3 of 8																	
Activity ID		Activity Name																		2015			2016				2017				2018				2019		
																				Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3

Contract No.: HY/2013/06			Detail Work Programme										Page 4 of 8																		
Activity ID	Activity Name		2015			2016				2017				2018				2019													
			Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3											
			 Location 3a(Inbnd Cargo Exam Bldg (037) ROCARS Room)																 07-Aug-17, Location 3a(Inbnd Cargo Exam Bldg (037) ROCARS Room)												
			 EM1240 L3a(037) ROCARS Rm - Cable Laying and termination in Location 3 and Location 3a																 L3a(037) ROCARS Rm - Cable Laying and termination in Location 3 and Location 3a												
			 EM1260 L3a(037) ROCARS Rm - Cable Splicing and Testing and Labeling																 L3a(037) ROCARS Rm - Cable Splicing and Testing and Labeling												
			 EM1280 L3a(037) ROCARS Rm - AVCSS SYSCON and SURCON and Intercom Installation																 L3a(037) ROCARS Rm - AVCSS SYSCON and SURCON and Intercom Installation												
			 EM1300 L3a(037) ROCARS Rm - VTS WS Installation																 L3a(037) ROCARS Rm - VTS WS Installation												
			 EM1320 L3a(037) ROCARS Rm - VID WS Installation																 L3a(037) ROCARS Rm - VID WS Installation												
			 EM1340 L3a(037) ROCARS Rm - SURCON and SYSCON and WS Tuning																 L3a(037) ROCARS Rm - SURCON and SYSCON and WS Tuning												
			 Location 3a(Inbnd Cargo Exam Bldg (037) Main Server Room)																 07-Aug-17, Location 3a(Inbnd Cargo Exam Bldg (037) Main Server Room)												
			 EM2120 L3a(037)Main Server Rm - Cable Laying and termination in Location 3 and Location 3a																 L3a(037)Main Server Rm - Cable Laying and termination in Location 3 and Location 3a												
			 EM2140 L3a(037)Main Server Rm - Cable Splicing and Testing and Labeling																 L3a(037)Main Server Rm - Cable Splicing and Testing and Labeling												
			 EM2160 L3a(037)Main Server Rm - AVCSS Server Installation																 L3a(037)Main Server Rm - AVCSS Server Installation												
			 EM2180 L3a(037)Main Server Rm - VTS Server Installation																 L3a(037)Main Server Rm - VTS Server Installation												
			 EM2200 L3a(037)Main Server Rm - Servers Tuning																 L3a(037)Main Server Rm - Servers Tuning												
			 Location 4(Outbnd Cargo Exam Bldg (023) MDF Room)																												
			 Location 4a(Outbnd Cargo Exam Bldg (023) ROCARS Room)																 04-Aug-17, Location 4a(Outbnd Cargo Exam Bldg (023) ROCARS Room)												
			 EM2240 L4a(023)ROCARS Rm - Cable Splicing and Testing and Labeling																 L4a(023)ROCARS Rm - Cable Splicing and Testing and Labeling												
			 EM2260 L4a(023)ROCARS Rm - AVCSS SYSCON and SURCON and Intercom Installation																 L4a(023)ROCARS Rm - AVCSS SYSCON and SURCON and Intercom Installation												
			 EM2280 L4a(023)ROCARS Rm - VTS WS Installation																 L4a(023)ROCARS Rm - VTS WS Installation												
			 EM2300 L4a(023)ROCARS Rm - SYSCON and SURCON and WS Tuning																 L4a(023)ROCARS Rm - SYSCON and SURCON and WS Tuning												
			 Location 5(Common Utility Enclosure & Staff Subway)																 01-Sep-17, Location 5(Common Utility Enclosure & Staff Subway)												
			 EM2341 L5(CUE) - Cable Laying between Location 5 and Location 6																 L5(CUE) - Cable Laying between Location 5 and Location 6												
			 EM2361 L5(CUE) - Cable Laying between Location 5 and Location 7																 L5(CUE) - Cable Laying between Location 5 and Location 7												
			 EM2380 L5(CUE) - Cable Splicing and Testing and Labeling																 L5(CUE) - Cable Splicing and Testing and Labeling												
			 Location 6(Common Utility Enclosure & Staff Subway)																 26-Aug-17, Location 6(Common Utility Enclosure & Staff Subway)												
			 EM2400 L6(CUE) - Cable Laying between Location 5 and Location 6																 L6(CUE) - Cable Laying between Location 5 and Location 6												
			 EM2420 L6(CUE) - Cable Splicing and Testing and Labeling																 L6(CUE) - Cable Splicing and Testing and Labeling												
			 Location 7(Common Utility Enclosure & Staff Subway)																 01-Sep-17, Location 7(Common Utility Enclosure & Staff Subway)												
			 EM2440 L7(CUE) - Cable Laying between Location 5 and Location 7																 L7(CUE) - Cable Laying between Location 5 and Location 7												
			 EM2460 L7(CUE) - Cable Splicing and Testing and Labeling																 L7(CUE) - Cable Splicing and Testing and Labeling												
			 Location 12(Inbnd Private Car Kiosks,GV Kiosks (027,028,029))																 30-Aug-17, Location 12(Inbnd Private Car Kiosks,GV Kiosks (027,028,029))												
			 Inbnd Private Car Kiosks(027) - 9 nos (Phase 1)																 24-Aug-17, Inbnd Private Car Kiosks(027) - 9 nos (Phase 1)												
			 EM1500 L12(027)(9nos P1) - Cable Splicing and Testing and Labeling																 L12(027)(9nos P1) - Cable Splicing and Testing and Labeling												
			 EM1520 L12(027)(9nos P1) - AVCSS/MOM Kiosk Equipment Installation (9 nos)																 L12(027)(9nos P1) - AVCSS/MOM Kiosk Equipment Installation (9 nos)												
			 EM1541 L12(027)(9nos P1) - XDB installation (18 nos)																 L12(027)(9nos P1) - XDB installation (18 nos)												
			 EM1542 L12(027)(9nos P1) - ODB installation (5 nos)																 L12(027)(9nos P1) - ODB installation (5 nos)												
			 EM1543 L12(027)(9nos P1) - ODB installation (2 nos)																 L12(027)(9nos P1) - ODB installation (2 nos)												
			 EM1544 L12(027)(9nos P1) - ODB installation (2 nos)																 L12(027)(9nos P1) - ODB installation (2 nos)												
			 EM1560 L12(027)(9nos P1) - Loop installation (45 nos)																 L12(027)(9nos P1) - Loop installation (45 nos)												
			 Inbnd Goods Vehicle Kiosks(028) - 5 nos (Phase 1)																 30-Aug-17, Inbnd Goods Vehicle Kiosks(028) - 5 nos (Phase 1)												
			 EM1620 L12(028)(5nos P1) - Cable Laying and termination																 L12(028)(5nos P1) - Cable Laying and termination												
 EM1640 L12(028)(5nos P1) - Cable Splicing and Testing and Labeling																 L12(028)(5nos P1) - Cable Splicing and Testing and Labeling															
 EM1660 L12(028)(5nos P1) - AVCSS/MOM Kiosk Equipment Installation (5 nos)																 L12(028)(5nos P1) - AVCSS/MOM Kiosk Equipment Installation (5 nos)															
 EM1681 L12(028)(5nos P1) - XDB installation (10 nos)																 L12(028)(5nos P1) - XDB installation (10 nos)															
 EM1682 L12(028)(5nos P1) - ODB installation (3 nos)																 L12(028)(5nos P1) - ODB installation (3 nos)															
 EM1683 L12(028)(5nos P1) - ODB installation (2 nos)																 L12(028)(5nos P1) - ODB installation (2 nos)															
Programme No.: HZMB-DWP		 Actual Level of Effort  summary		Hong Kong-Zhuhai-Macao Bridge Hong Kong Boundary Crossing Facilities - Automatic Vehicle Clearance Support System (AVCSS)										Date		Revision		Checked		Approved											
Data Date: 14-Aug-15		 Primary Baseline												14-Nov-16		Rev.: 0		WC		LC											
		 Actual Work												10-Mar-17		Rev.: 1.0a		WC		LC											
		 Remaining Work												5-May-17		Rev.: 1.0b		WC		LC											
		 Critical Remaining Work																													
		 Baseline Milestone																													
		 Milestone																													

Contract No.: HY/2013/06			Detail Work Programme										Page 5 of 8																																																													
Activity ID		Activity Name													2015			2016				2017				2018				2019																																												
															Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3																																										
		EM1700	L12(028)(5nos P1) - AIOP Installation (5 nos)																																																																							
		EM1720	L12(028)(5nos P1) - Loop installation (25 nos)																																																																							
		Outbd Goods Vehicle Kiosks(029) - 5 nos (Phase 1)																																																																								
		EM1740	L12(029)(5nos P1) - Cable Containment in Kiosks																																																																							
		EM1760	L12(029)(5nos P1) - Cable Laying and termination																																																																							
		EM1780	L12(029)(5nos P1) - Cable Splicing and Testing and Labeling																																																																							
		EM1800	L12(029)(5nos P1) - AVCSS/MOM Kiosk Equipment Installation (5 nos)																																																																							
		EM1821	L12(029)(5nos P1) - XDB installation (5 nos)																																																																							
		EM1822	L12(029)(5nos P1) - ODB installation (4 nos)																																																																							
		EM1823	L12(029)(5nos P1) - ODB installation (1 nos)																																																																							
		EM1840	L12(029)(5nos P1) - AIOP Installation (5 nos)																																																																							
		Location 13(Outbd Private Car Kiosks (030)) - 9 nos (Phase 1)																																																																								
		EM2520	L13(030)(9nos P1) - Cable Containment in Kiosks																																																																							
		EM2540	L13(030)(9nos P1) - Cable Laying and termination																																																																							
		EM2560	L13(030)(9nos P1) - Cable Splicing and Testing and Labeling																																																																							
		EM2580	L13(030)(9nos P1) - AVCSS/MOM Kiosk Equipment Installation (9 nos)																																																																							
		EM2601	L13(030)(9nos P1) - XDB installation (9 nos)																																																																							
		EM2602	L13(030)(9nos P1) - ODB installation (7 nos)																																																																							
		Location 14(Future-Outbd/Inbd Private Car Kiosks) - 6+6 nos																																																																								
		EM1440	L14 - Cable Laying and termination at ELV Room in CUE																																																																							
		Location 15(Inbd Traffic Control Kiosk (100))																																																																								
		Location 16(Outbd Traffic Control Kiosk (101))																																																																								
		EM2760	L16(101) - Cable Laying and termination																																																																							
		EM2780	L16(101) - Cable Splicing and Testing and Labeling																																																																							
		EM2800	L16(101) - AVCSS SYSCON and SURCON Installation																																																																							
		EM2820	L16(101) - VTS WS and 55" LCD Installation																																																																							
		Location 17(Inbd Private Car Exam Bldg(033) Operational Office)																																																																								
		Location 18 (Outbd Private Car Exam Bldg(024) Operational Office)																																																																								
		EM2940	L18(024) - Cable Laying and termination																																																																							
		EM2960	L18(024) - Cable Splicing and Testing and Labeling																																																																							
		EM2980	L18(024) - AVCSS SURCON and 55" LCD Installation																																																																							
		EM3000	L18(024) - SURCON Tuning																																																																							
		Location 19 (DOH Cargo Clearance Bldg(043))																																																																								
		EM1360	L19(043) - Cable Laying and termination																																																																							
		EM1380	L19(043) - Cable Splicing and Testing and Labeling																																																																							
		EM1400	L19(043) - PA and Intercom Installation																																																																							
		EM1420	L19(043) - PA and Intercom Tuning																																																																							
		Inbd Vehicle Clearance Plaza - 8 nos VID, 7 nos VTS, 4 nos TLS																																																																								
		EM3020	Inbound VID cabling from pillar box to VID field equipment																																																																							
		EM3040	Inbound VTS cabling from pillar box to VTS field equipment																																																																							
		EM3060	Inbound TLS cabling from pillar box to TLS field equipment																																																																							
		EM3080	Inbound VID field equipment installation (8 VID)																																																																							
		EM3100	Inbound VTS field equipment installation (4 RFID + 3 Cameras)																																																																							
		EM3120	Inbound TLS field equipment installation (4 TLS)																																																																							
		EM3140	Inbound VID and VTS and TLS field equipment tuning																																																																							
Programme No.: HZMB-DWP		Actual Level of Effort Primary Baseline Actual Work Remaining Work Critical Remaining Work Baseline Milestone Milestone													Hong Kong-Zhuhai-Macao Bridge Hong Kong Boundary Crossing Facilities - Automatic Vehicle Clearance Support System (AVCSS)																				Date	Revision	Checked	Approved																																				
Data Date: 14-Aug-15																																			14-Nov-16	Rev.: 0	WC	LC																																				
																																													10-Mar-17	Rev.: 1.0a	WC	LC																										
																																																							5-May-17	Rev.: 1.0b	WC	LC																

Contract No.: HY/2013/06		Detail Work Programme										Page 8 of 8											
Activity ID	Activity Name		2015			2016				2017				2018				2019					
			Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3			
	 Site Acceptance Test (Phase 2 / Section III)																						
	 Operability Period Test (Phase 2 / Section III)																						
	 Completion (Phase 2 / Section III)																						
	 Operation (Phase 2 / Section III)																						
	 Defect Liability Period (DLP)																						
	 Document Submission (Phase 2 / Section III)																						
Programme No.: HZMB-DWP Data Date: 14-Aug-15		Actual Level of Effort Primary Baseline Actual Work Remaining Work Critical Remaining Work Baseline Milestone Milestone summary	Hong Kong-Zhuhai-Macao Bridge Hong Kong Boundary Crossing Facilities - Automatic Vehicle Clearance Support System (AVCSS)									Date 14-Nov-16 10-Mar-17 5-May-17	Revision Rev.: 0 Rev.: 1.0a Rev.: 1.0b	Checked WC WC WC	Approved LC LC LC								
