

Activity Name	Orig Dur	Planned Start	Planned Finish	Current Start	Current Finish	2014				
						Jun	Jul	Aug	Sep	Oct
TMCLK - Northern Connection Sub-Sea Tunnel Section										
Construction										
Northern Landfall										
North Reclamation (Phase 1)										
Construction										
Ground Investigation										
Ground Investigation (Phase 2) - Northern Landfall & Sub-sea Tunnel	148	25-Oct-13	30-Apr-14	25-Oct-13 A	14-Jun-14 A					
Milestones										
200m Leading Seawall for Reclamation: 400-450 (Zone D2)	0	24-Mar-14		02-Jun-14 A						
200m Leading Seawall for Reclamation: 450-500 (Zone C1)	0	29-Mar-14		18-Jun-14 A						
200m Leading Seawall for Reclamation: 500-550 (Zone C1)	0	04-Apr-14		12-Jul-14						
200m Leading Seawall for Reclamation: 550-600 (Zone C2)	0	11-Apr-14		24-Jul-14						
200m Leading Seawall for Reclamation: 600-650 (Zone B)	0	28-Apr-14		30-Jul-14						
200m Leading Seawall for Reclamation: 650-700 (Zone B)	0	08-May-14		07-Aug-14						
200m Leading Seawall for Reclamation: 700-956 (Zone B, A1 & A2)	0	16-May-14		21-Aug-14						
Completion of Zone E Reclamation up to +6mPD	0		30-Apr-14		19-Jun-14 A					
Completion of Zone D1 Reclamation up to +5.0mPD	0		16-May-14		10-Jul-14					
Completion of Zone D2 Reclamation up to +5.0mPD	0		06-Jun-14		09-Aug-14					
Completion of Zone C1 Reclamation up to +5.0mPD	0		27-Jun-14		29-Aug-14					
Completion Zone C2 Reclamation up to +6mPD	0		02-Jul-14		02-Sep-14					
Zone E										
Vertical Seawall										
VS - Berm Stone - Zone E - (CH0 to 50)	2	06-Jun-14	07-Jun-14	16-Jun-14 A	26-Jun-14 A					
VS - Berm Stone - Zone E - (CH50 to 100)	2	09-Jun-14	10-Jun-14	27-Jun-14 A	30-Jun-14					
VS - Berm Stone - Zone E - (CH100 to 150)	3	11-Jun-14	13-Jun-14	02-Jul-14	04-Jul-14					
VS - Berm Stone - Zone E - (CH150 to 205)	5	14-Jun-14	19-Jun-14	05-Jul-14	10-Jul-14					
VS - Mass Concrete Coping - Zone E - (CH0 to 50)	8	07-May-14	15-May-14	07-Jul-14*	15-Jul-14					
VS - Mass Concrete Coping - Zone E - (CH50 to 100)	8	16-May-14	24-May-14	16-Jul-14	24-Jul-14					
VS - Mass Concrete Coping - Zone E - (CH100 to 150)	8	26-May-14	04-Jun-14	25-Jul-14	02-Aug-14					
VS - Mass Concrete Coping - Zone E - (CH150 to 205)	11	05-Jun-14	17-Jun-14	04-Aug-14	15-Aug-14					
Reclamation										
Public Fill - Zone E - (CH150 to 205) to -2.5mPD	4	28-Mar-14	01-Apr-14	06-May-14 A	09-Jun-14 A					
Public Fill - Zone E - (CH100 to 150) to +2.5mPD	7	20-Mar-14	27-Mar-14	18-Apr-14 A	06-Jun-14 A					
Public Fill - Zone E - (CH150 to 205) to +2.5mPD	7	02-Apr-14	10-Apr-14	20-May-14 A	10-Jun-14 A					
Public Fill - Zone E - (CH100 to 150) to +6.0mPD	7	11-Apr-14	22-Apr-14	09-May-14 A	06-Jun-14 A					
Public Fill - Zone E - (CH150 to 205) to +6.0mPD	7	23-Apr-14	30-Apr-14	14-May-14 A	19-Jun-14 A					
Zone D1										
Vertical Seawall										
VS - Granular Filter - Zone D1 - (CH255 to 305)	4	20-Feb-14	24-Feb-14	20-May-14 A	05-Jun-14 A					
VS - Granular Filter - Zone D1 - (CH305 to 355)	4	25-Feb-14	28-Feb-14	30-Jun-14	02-Jul-14					
VS - Berm Stone - Zone D1 - (CH205 to 255)	6	20-Jun-14	26-Jun-14	11-Jul-14	17-Jul-14					
VS - Berm Stone - Zone D1 - (CH255 to 305)	3	27-Jun-14	30-Jun-14	18-Jul-14	21-Jul-14					
VS - Berm Stone - Zone D1 - (CH305 to 355)	3	02-Jul-14	04-Jul-14	22-Jul-14	24-Jul-14					
VS - Mass Concrete Coping - Zone D1 - (CH205 to 255)	15	18-Jun-14	05-Jul-14	30-Jun-14*	17-Jul-14					
VS - Mass Concrete Coping - Zone D1 - (CH255 to 305)	8	07-Jul-14	15-Jul-14	18-Jul-14	26-Jul-14					
VS - Mass Concrete Coping - Zone D1 - (CH305 to 355)	8	16-Jul-14	24-Jul-14	28-Jul-14	05-Aug-14					
Sloping Seawall										
VS - Berm Stone - Zone D1 - RTT	2	20-Jun-14	21-Jun-14	11-Jul-14	12-Jul-14					
VS - Mass Concrete Coping - Zone D1 - RTT	4	07-May-14	10-May-14	30-Jun-14	04-Jul-14					
SS - Armour Rock Underlayer - Zone D1 - (CH255 to 305)	5	27-Dec-13	02-Jan-14	30-Jun-14	05-Jul-14					
SS - Armour Rock Underlayer - Zone D1 - (CH305 to 355)	5	03-Jan-14	08-Jan-14	07-Jul-14	11-Jul-14					
SS - Armour Rock - Zone D1 - (CH255 to 305)	4	03-Jan-14	07-Jan-14	07-Jul-14	10-Jul-14					
SS - Armour Rock - Zone D1 - (CH305 to 355)	4	08-Jan-14	11-Jan-14	11-Jul-14	15-Jul-14					
SS - Mass Concrete Coping - Zone D1 - (CH255 to 305)	7	12-May-14	19-May-14	11-Jul-14	18-Jul-14					
SS - Mass Concrete Coping - Zone D1 - (CH305 to 355)	7	20-May-14	27-May-14	19-Jul-14	26-Jul-14					
Reclamation - Band Drain - Zone D1 - (CH255 to 305)	5	17-Mar-14	21-Mar-14	12-May-14 A	19-Jun-14 A					
Reclamation - Band Drain - Zone D1 - (CH305 to 355)	5	24-Mar-14	28-Mar-14	20-May-14 A	19-Jun-14 A					
Reclamation										
Compacted Sandfill - Zone D1 - (CH255 to 305) to -2.5mPD	3	07-Apr-14	09-Apr-14	02-Jun-14 A	06-Jun-14 A					
Compacted Sandfill - Zone D1 - (CH305 to 355) to -2.5mPD	3	10-Apr-14	12-Apr-14	03-Jun-14 A	07-Jun-14 A					
Public Fill - Zone D1 - (CH205 to 255) to -2.5mPD	1	07-Apr-14	07-Apr-14	21-May-14 A	06-Jun-14 A					
Public Fill - Zone D1 - (CH255 to 305) to -2.5mPD	2	10-Apr-14	11-Apr-14	03-Jun-14 A	14-Jun-14 A					
Public Fill - Zone D1 - (CH305 to 355) to -2.5mPD	2	14-Apr-14	15-Apr-14	17-Jun-14 A	17-Jun-14 A					
Compacted Sandfill - Zone D1 - (CH255 to 305) to +2.5mPD	3	12-Apr-14	15-Apr-14	04-Jun-14 A	07-Jun-14 A					
Compacted Sandfill - Zone D1 - (CH305 to 355) to +2.5mPD	3	16-Apr-14	22-Apr-14	27-May-14 A	09-Jun-14 A					

Activity Name	Orig Dur	Planned Start	Planned Finish	Current Start	Current Finish	2014				
						Jun	Jul	Aug	Sep	Oct
Public Fill - Zone D1 - (CH205 to 255) to +2.5mPD	4	11-Apr-14	15-Apr-14	02-Jun-14 A	14-Jun-14 A					
Public Fill - Zone D1 - (CH255 to 305) to +2.5mPD	4	16-Apr-14	23-Apr-14	09-Jun-14 A	25-Jun-14 A					
Public Fill - Zone D1 - (CH305 to 355) to +2.5mPD	4	24-Apr-14	28-Apr-14	24-Jun-14 A	05-Jul-14					
Compacted Sandfill - Zone D1 - (CH205 to 255) to +5.0mPD	2	16-Apr-14	17-Apr-14	18-Jun-14 A	20-Jun-14 A					
Compacted Sandfill - Zone D1 - (CH255 to 305) to +5.0mPD	2	24-Apr-14	25-Apr-14	18-Jun-14 A	21-Jun-14 A					
Compacted Sandfill - Zone D1 - (CH305 to 355) to +5.0mPD	2	29-Apr-14	30-Apr-14	23-Jun-14 A	24-Jun-14 A					
Public Fill - Zone D1 - (CH205 to 255) to +5.0mPD	4	02-May-14	07-May-14	23-Jun-14 A	30-Jun-14					
Public Fill - Zone D1 - (CH255 to 305) to +5.0mPD	4	08-May-14	12-May-14	25-Jun-14 A	04-Jul-14					
Public Fill - Zone D1 - (CH305 to 355) to +5.0mPD	4	13-May-14	16-May-14	07-Jul-14	10-Jul-14					

Zone D2

Vertical Seawall

VS - Granular Filter - Zone D2 - (CH355 to 405)	4	01-Mar-14	05-Mar-14	03-Jul-14	03-Jul-14
VS - Granular Filter - Zone D2 - (CH405 to 443)	4	06-Mar-14	10-Mar-14	04-Jul-14	08-Jul-14
VS - Berm Stone - Zone D2 - (CH355 to 405)	3	05-Jul-14	08-Jul-14	25-Jul-14	28-Jul-14
VS - Berm Stone - Zone D2 - (CH405 to 443)	3	09-Jul-14	11-Jul-14	29-Jul-14	31-Jul-14
VS - Mass Concrete Coping - Zone D2 - (CH355 to 405)	8	25-Jul-14	02-Aug-14	16-Jul-14	25-Jul-14
VS - Mass Concrete Coping - Zone D2 - (CH405 to 443)	8	04-Aug-14	12-Aug-14	28-Jul-14	06-Aug-14

Sloping Seawall

SS - Armour Rock Underlayer - Zone D2 - (CH355 to 405)	5	09-Jan-14	14-Jan-14	12-Jul-14	17-Jul-14
SS - Armour Rock Underlayer - Zone D2 - (CH405 to 443)	5	15-Jan-14	20-Jan-14	18-Jul-14	23-Jul-14
SS - Armour Rock - Zone D2 - (CH355 to 405)	4	13-Jan-14	16-Jan-14	16-Jul-14	19-Jul-14
SS - Armour Rock - Zone D2 - (CH405 to 443)	4	17-Jan-14	21-Jan-14	21-Jul-14	24-Jul-14
SS - Mass Concrete Coping - Zone D2 - (CH355 to 405)	7	28-May-14	05-Jun-14	28-Jul-14	04-Aug-14
SS - Mass Concrete Coping - Zone D2 - (CH405 to 443)	7	06-Jun-14	13-Jun-14	05-Aug-14	12-Aug-14
Sloping - Rockfill Type A - Zone D2 - (CH355 to 405)	1	08-Jan-14	08-Jan-14	16-Jun-14 A	16-Jun-14 A
Sloping - Rockfill Type A - Zone D2 - (CH405 to 443)	1	17-Jan-14	17-Jan-14	09-Jun-14 A	09-Jun-14 A
Sloping - Geotextile - Zone D2 - (CH355 to 405)	1	09-Jan-14	09-Jan-14	09-Jun-14 A	09-Jun-14 A
Sloping - Geotextile - Zone D2 - (CH405 to 443)	1	18-Jan-14	18-Jan-14	09-Jun-14 A	09-Jun-14 A
Sloping - Granular Filter - Zone D2 - (CH355 to 405)	2	10-Jan-14	11-Jan-14	16-Jun-14 A	18-Jun-14 A
Sloping - Granular Filter - Zone D2 - (CH405 to 443)	2	20-Jan-14	21-Jan-14	23-Jun-14 A	23-Jun-14 A

Reclamation

Compacted Sandfill - Zone D2 - (CH355 to 405) to -2.5mPD	3	14-Apr-14	16-Apr-14	02-Jun-14 A	17-Jun-14 A
Compacted Sandfill - Zone D2 - (CH405 to 443) to -2.5mPD	2	17-Apr-14	22-Apr-14	17-Jun-14 A	03-Jul-14
Public Fill - Zone D2 - (CH355 to 405) to -2.5mPD	4	17-Apr-14	24-Apr-14	17-Jun-14 A	03-Jul-14
Public Fill - Zone D2 - (CH405 to 443) to -2.5mPD	4	25-Apr-14	29-Apr-14	04-Jul-14	08-Jul-14
Compacted Sandfill - Zone D2 - (CH355 to 405) to +2.5mPD	6	25-Apr-14	02-May-14	24-Jun-14 A	08-Jul-14
Compacted Sandfill - Zone D2 - (CH405 to 443) to +2.5mPD	5	03-May-14	09-May-14	09-Jul-14	14-Jul-14
Public Fill - Zone D2 - (CH355 to 405) to +2.5mPD	10	03-May-14	15-May-14	09-Jul-14	19-Jul-14
Public Fill - Zone D2 - (CH405 to 443) to +2.5mPD	10	16-May-14	27-May-14	21-Jul-14	31-Jul-14
Compacted Sandfill - Zone D2 - (CH355 to 405) to +5.0mPD	4	16-May-14	20-May-14	21-Jul-14	24-Jul-14
Compacted Sandfill - Zone D2 - (CH405 to 443) to +5.0mPD	4	28-May-14	31-May-14	01-Aug-14	05-Aug-14
Public Fill - Zone D2 - (CH355 to 405) to +5.0mPD	4	21-May-14	24-May-14	25-Jul-14	29-Jul-14
Public Fill - Zone D2 - (CH405 to 443) to +5.0mPD	4	03-Jun-14	06-Jun-14	06-Aug-14	09-Aug-14
Reclamation - Sand Blanket - Zone D2 - (CH405 to 443)	2	04-Apr-14	07-Apr-14	12-May-14 A	03-Jun-14 A
Reclamation - Band Drain - Zone D2 - (CH355 to 405)	5	31-Mar-14	04-Apr-14	16-Jun-14 A	19-Jun-14 A
Reclamation - Band Drain - Zone D2 - (CH405 to 443)	5	08-Apr-14	12-Apr-14	18-Jun-14 A	21-Jun-14 A


Zone C1

Vertical Seawall

VS - Seawall Block - Zone C1 - (CH443 to 493)	9	20-Feb-14	01-Mar-14	10-Apr-14 A	05-Jun-14 A
VS - Seawall Block - Zone C1 - (CH493 to 543)	9	03-Mar-14	12-Mar-14	30-Apr-14 A	18-Jun-14 A
VS - Rockfill Type A - Zone C1 - (CH443 to 493)	3	13-Mar-14	15-Mar-14	02-May-14 A	19-Jun-14 A
VS - Rockfill Type A - Zone C1 - (CH493 to 543)	3	17-Mar-14	19-Mar-14	09-Jun-14 A	24-Jun-14 A
VS - Geotextile - Zone C1 - (CH443 to 493)	2	20-Mar-14	21-Mar-14	30-Jun-14	02-Jul-14
VS - Geotextile - Zone C1 - (CH493 to 543)	2	22-Mar-14	24-Mar-14	03-Jul-14	04-Jul-14
VS - Granular Filter - Zone C1 - (CH443 to 493)	4	25-Mar-14	28-Mar-14	05-Jul-14	09-Jul-14
VS - Granular Filter - Zone C1 - (CH493 to 543)	4	29-Mar-14	02-Apr-14	10-Jul-14	14-Jul-14
VS - Berm Stone - Zone C1 - (CH443 to 493)	3	12-Jul-14	15-Jul-14	01-Aug-14	04-Aug-14
VS - Berm Stone - Zone C1 - (CH493 to 543)	3	16-Jul-14	18-Jul-14	05-Aug-14	07-Aug-14
VS - Mass Concrete Coping - Zone C1 - (CH443 to 493)	8	13-Aug-14	21-Aug-14	11-Aug-14	20-Aug-14
VS - Mass Concrete Coping - Zone C1 - (CH493 to 543)	8	22-Aug-14	30-Aug-14	20-Aug-14	28-Aug-14

Sloping Seawall

SS - Armour Rock Underlayer - Zone C1 - (CH443 to 493)	5	27-Jan-14	07-Feb-14	24-Jul-14	29-Jul-14
SS - Armour Rock Underlayer - Zone C1 - (CH493 to 543)	5	12-Feb-14	17-Feb-14	30-Jul-14	04-Aug-14
SS - Armour Rock - Zone C1 - (CH443 to 493)	4	27-Feb-14	03-Mar-14	11-Aug-14	14-Aug-14
SS - Armour Rock - Zone C1 - (CH493 to 543)	4	04-Mar-14	07-Mar-14	15-Aug-14	19-Aug-14

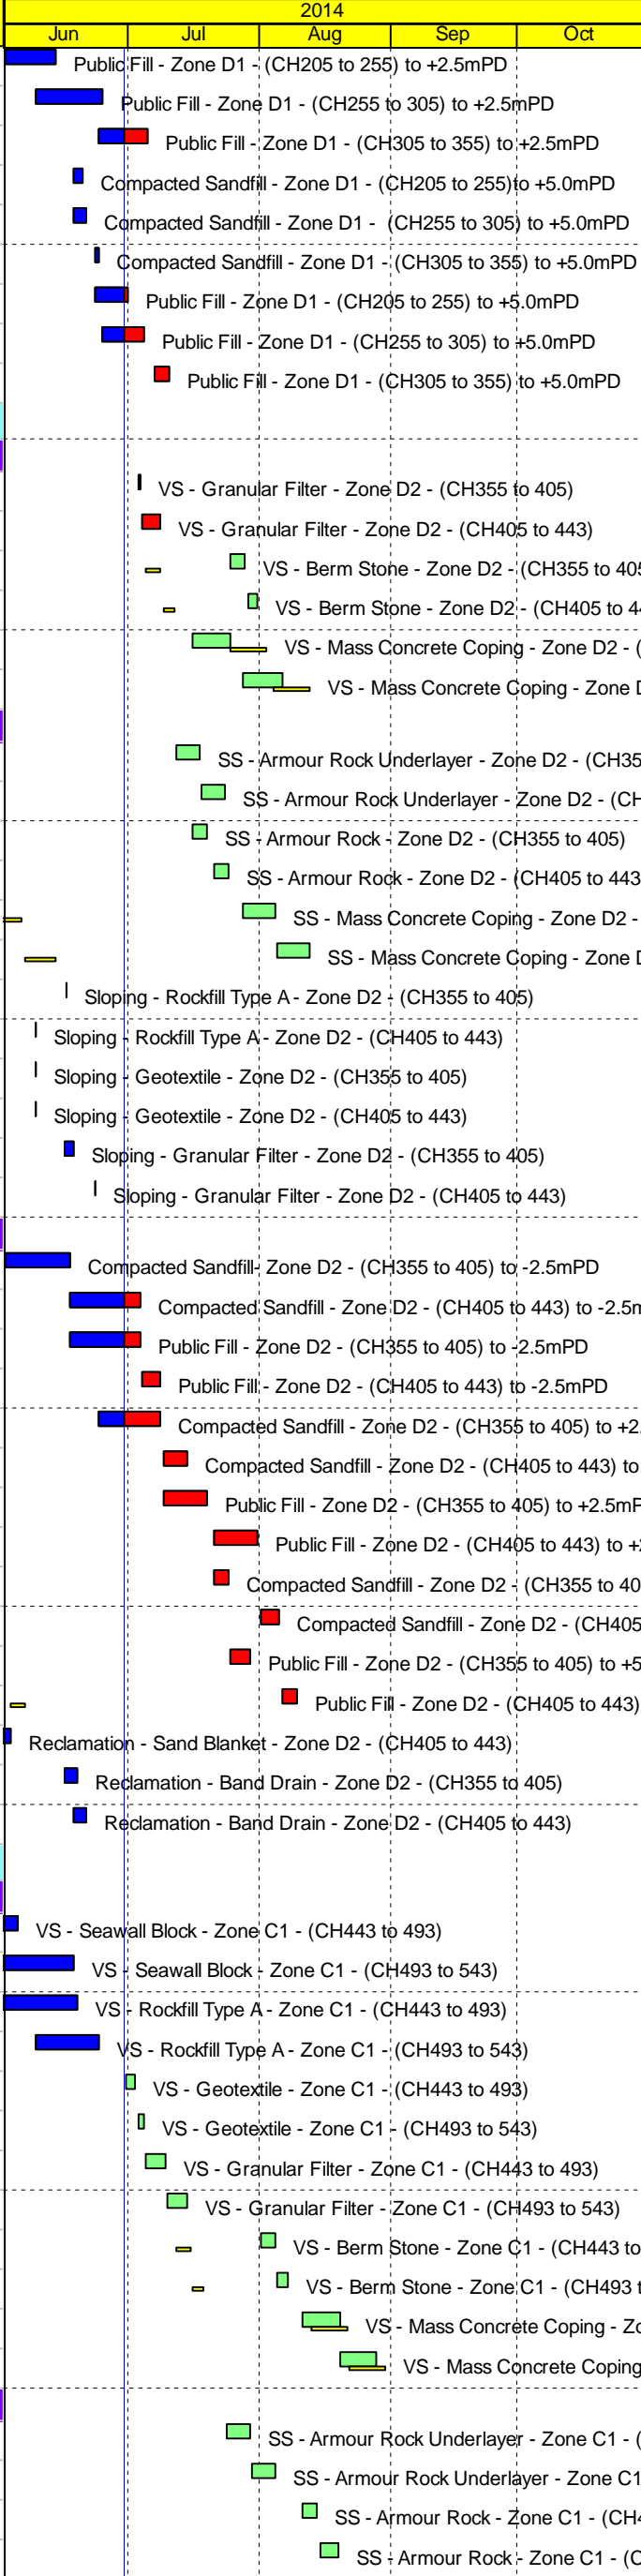

- Current Bar
- Current Bar - Critical
- Current Milestone
- DWPB Bar
- DWPB Milestone
- Progress Bar
- Progress Milestone

TMCLK - Northern Connection Sub-sea Tunnel Section
 Three-months Rolling Programme
 As of 30-Jun-2014



Date	Revision	Checked	Approved
12-Feb-14	TMCLKDBJEN/PRG98507 Rev A	WYu	SPe
08-Apr-14	TMCLKDBJEN/PRG98507 Rev B	SPe	WYu

Activity Name	Orig Dur	Planned Start	Planned Finish	Current Start	Current Finish	2014				
						Jun	Jul	Aug	Sep	Oct
SS - Mass Concrete Coping - Zone C1 - (CH443 to 493)	7	14-Jun-14	21-Jun-14	12-Aug-14	20-Aug-14					
SS - Mass Concrete Coping - Zone C1 - (CH493 to 543)	7	23-Jun-14	30-Jun-14	20-Aug-14	27-Aug-14					
Sloping - Rockfill Type A - Zone C1 - (CH443 to 493)	1	27-Jan-14	27-Jan-14	15-Jun-14 A	15-Jun-14 A					
Sloping - Rockfill Type A - Zone C1 - (CH493 to 543)	1	12-Feb-14	12-Feb-14	23-Jun-14 A	28-Jun-14 A					
Sloping - Geotextile - Zone C1 - (CH443 to 493)	1	28-Jan-14	28-Jan-14	30-Jun-14	30-Jun-14					
Sloping - Geotextile - Zone C1 - (CH493 to 453)	1	13-Feb-14	13-Feb-14	02-Jul-14	02-Jul-14					
Sloping - Granular Filter - Zone C1 - (CH443 to 493)	3	29-Jan-14	07-Feb-14	03-Jul-14 A	02-Jul-14					
Sloping - Granular Filter - Zone C1 - (CH493 to 543)	3	14-Feb-14	17-Feb-14	03-Jul-14	05-Jul-14					
Reclamation										
Compacted Sandfill - Zone C1 - (CH443 to 493) to -2.5mPD	2	28-May-14	29-May-14	19-Jun-14 A	01-Aug-14					
Compacted Sandfill - Zone C1 - (CH493 to 543) to -2.5mPD	2	30-May-14	31-May-14	19-Jun-14 A	02-Aug-14					
Public Fill - Zone C1 - (CH443 to 493) to -2.5mPD	2	30-May-14	31-May-14	02-Aug-14	04-Aug-14					
Public Fill - Zone C1 - (CH493 to 543) to -2.5mPD	2	03-Jun-14	04-Jun-14	05-Aug-14	06-Aug-14					
Compacted Sandfill - Zone C1 - (CH443 to 493) to +2.5mPD	5	03-Jun-14	07-Jun-14	05-Aug-14	09-Aug-14					
Compacted Sandfill - Zone C1 - (CH493 to 543) to +2.5mPD	5	09-Jun-14	13-Jun-14	11-Aug-14	15-Aug-14					
Public Fill - Zone C1 - (CH443 to 493) to +2.5mPD	4	09-Jun-14	12-Jun-14	11-Aug-14	14-Aug-14					
Public Fill - Zone C1 - (CH493 to 543) to +2.5mPD	4	14-Jun-14	18-Jun-14	16-Aug-14	20-Aug-14					
Compacted Sandfill - Zone C1 - (CH443 to 493) to +5.0mPD	4	13-Jun-14	17-Jun-14	15-Aug-14	19-Aug-14					
Compacted Sandfill - Zone C1 - (CH493 to 543) to +5.0mPD	4	19-Jun-14	23-Jun-14	21-Aug-14	25-Aug-14					
Public Fill - Zone C1 - (CH443 to 493) to +5.0mPD	4	18-Jun-14	21-Jun-14	20-Aug-14	23-Aug-14					
Public Fill - Zone C1 - (CH493 to 543) to +5.0mPD	4	24-Jun-14	27-Jun-14	26-Aug-14	29-Aug-14					
Reclamation - Geotextile - Zone C1 - (CH493 to 543)	4	10-Apr-14	14-Apr-14	01-Jun-14 A	02-Jun-14 A					
Reclamation - Sand Blanket - Zone C1 - (CH443 to 493)	2	10-Apr-14	11-Apr-14	02-Jun-14 A	06-Jun-14 A					
Reclamation - Sand Blanket - Zone C1 - (CH493 to 543)	2	15-Apr-14	16-Apr-14	02-Jun-14 A	20-Jun-14 A					
Reclamation - Band Drain - Zone C1 - (CH443 to 493)	4	14-Apr-14	17-Apr-14	19-Jun-14 A	11-Jul-14					
Reclamation - Band Drain - Zone C1 - (CH493 to 543)	4	22-Apr-14	25-Apr-14	12-Jul-14	16-Jul-14					
Zone C2										
Vertical Seawall										
VS - Seawall Block - Zone C2 - (CH543 to 598)	9	13-Mar-14	22-Mar-14	05-May-14 A	28-Jun-14 A					
VS - Rockfill Type A - Zone C2 - (CH543 to 598)	3	20-Mar-14	22-Mar-14	28-Jun-14 A	02-Jul-14					
VS - Geotextile - Zone C2 - (CH543 to 598)	2	25-Mar-14	26-Mar-14	05-Jul-14	07-Jul-14					
VS - Granular Filter - Zone C2 - (CH543 to 598)	4	03-Apr-14	08-Apr-14	15-Jul-14	18-Jul-14					
VS - Berm Stone - Zone C2 - (CH543 to 598)	3	19-Jul-14	22-Jul-14	08-Aug-14	11-Aug-14					
VS - Mass Concrete Coping - Zone C2 - (CH543 to 598)	8	22-Aug-14	30-Aug-14	22-Aug-14	01-Sep-14					
Sloping Seawall										
SS - Rock Grade 400 - Zone C2 - (CH543 to 598) to +2.5mPD	8	12-Feb-14	20-Feb-14	18-Mar-14 A	25-Jun-14 A					
SS - Armour Rock Underlayer - Zone C2 - (CH543 to 598)	5	21-Feb-14	26-Feb-14	05-Aug-14	09-Aug-14					
SS - Armour Rock - Zone C2 - (CH543 to 598)	4	08-Mar-14	12-Mar-14	20-Aug-14	23-Aug-14					
SS - Mass Concrete Coping - Zone C2 - (CH543 to 598)	7	02-Jul-14	09-Jul-14	28-Aug-14	04-Sep-14					
Sloping - Rockfill Type A - Zone C2 - (CH543 to 598)	1	21-Feb-14	21-Feb-14	30-Jun-14	30-Jun-14					
Sloping - Geotextile - Zone C2 - (CH543 to 598)	1	22-Feb-14	22-Feb-14	03-Jul-14	03-Jul-14					
Sloping - Granular Filter - Zone C2 - (CH543 to 598)	3	24-Feb-14	26-Feb-14	07-Jul-14	09-Jul-14					
Reclamation										
Reclamation - Geotextile - Zone C2 - (CH543 to 598)	4	15-Apr-14	22-Apr-14	10-Jul-14	14-Jul-14					
Reclamation - Sand Blanket - Zone C2 - (CH543 to 598)	2	23-Apr-14	24-Apr-14	09-Jun-14 A	28-Jun-14 A					
Reclamation - Band Drain - Zone C2 - (CH543 to 598)	4	26-Apr-14	30-Apr-14	17-Jul-14	21-Jul-14					
Public Fill - Zone C2 - (CH543 to 598) to -2.5mPD	2	09-Jun-14	10-Jun-14	11-Aug-14	12-Aug-14					
Public Fill - Zone C2 - (CH543 to 598) to +2.5mPD	6	23-Jun-14	28-Jun-14	25-Aug-14	30-Aug-14					
Public Fill - Zone C2 - (CH543 to 598) to +6.0mPD	2	30-Jun-14	02-Jul-14	01-Sep-14	02-Sep-14					
Zone B										
Vertical Seawall										
VS - Rock Grade 400 - Zone B - (CH698 to 738)	5	25-Jan-14	30-Jan-14	24-Mar-14 A	06-Jun-14 A					
VS - Levelling Stone - Zone B - (CH648 to 698)	4	08-Feb-14	12-Feb-14	09-Jun-14 A	09-Jun-14 A					
VS - Levelling Stone - Zone B - (CH698 to 738)	4	13-Feb-14	17-Feb-14	13-Jun-14 A	13-Jun-14 A					
VS - Seawall Block - Zone B - (CH598 to 648)	5	24-Mar-14	28-Mar-14	02-Jun-14 A	30-Jun-14					
VS - Seawall Block - Zone B - (CH648 to 698)	5	29-Mar-14	03-Apr-14	18-Jun-14 A	04-Jul-14					
VS - Seawall Block - Zone B - (CH698 to 738)	5	04-Apr-14	10-Apr-14	20-Jun-14 A	09-Jul-14					
VS - Rockfill Type A - Zone B - (CH598 to 648)	3	04-Apr-14	08-Apr-14	05-Jul-14	08-Jul-14					
VS - Rockfill Type A - Zone B - (CH648 to 698)	3	09-Apr-14	11-Apr-14	09-Jul-14	11-Jul-14					
VS - Rockfill Type A - Zone B - (CH698 to 738)	3	12-Apr-14	15-Apr-14	12-Jul-14	15-Jul-14					
VS - Geotextile - Zone B - (CH598 to 648)	2	12-Apr-14	14-Apr-14	12-Jul-14	14-Jul-14					
VS - Geotextile - Zone B - (CH648 to 698)	2	15-Apr-14	16-Apr-14	15-Jul-14	16-Jul-14					
VS - Geotextile - Zone B - (CH698 to 738)	2	17-Apr-14	22-Apr-14	17-Jul-14	18-Jul-14					
VS - Granular Filter - Zone B - (CH598 to 648)	4	17-Apr-14	24-Apr-14	17-Jul-14	21-Jul-14					
VS - Granular Filter - Zone B - (CH648 to 698)	4	25-Apr-14	29-Apr-14	22-Jul-14	25-Jul-14					

- Current Bar
- Current Bar - Critical
- Current Milestone
- DWPB Bar
- DWPB Milestone
- Progress Bar
- Progress Milestone



Date	Revision	Checked	Approved
12-Feb-14	TMCLKDBJEN/PRG98507 Rev A	WYu	SPe
08-Apr-14	TMCLKDBJEN/PRG98507 Rev B	SPe	WYu


Activity Name	Orig Dur	Planned Start	Planned Finish	Current Start	Current Finish	2014				
						Jun	Jul	Aug	Sep	Oct
VS - Granular Filter - Zone B - (CH698 to 738)	4	30-Apr-14	05-May-14	26-Jul-14	30-Jul-14					
VS - Berm Stone - Zone B - (CH598 to 648)	3	23-Jul-14	25-Jul-14	12-Aug-14	14-Aug-14					
VS - Berm Stone - Zone B - (CH648 to 698)	3	26-Jul-14	29-Jul-14	15-Aug-14	18-Aug-14					
VS - Berm Stone - Zone B - (CH698 to 738)	3	30-Jul-14	01-Aug-14	19-Aug-14	21-Aug-14					
VS - Mass Concrete Coping - Zone B - (CH598 to 648)	8	01-Sep-14	10-Sep-14	01-Sep-14	10-Sep-14					
VS - Mass Concrete Coping - Zone B - (CH648 to 698)	8	11-Sep-14	19-Sep-14	11-Sep-14	19-Sep-14					
VS - Mass Concrete Coping - Zone B - (CH698 to 738)	8	20-Sep-14	29-Sep-14	20-Sep-14	29-Sep-14					
Sloping Seawall										
SS - Rock Grade 400 - Zone B - (CH598 to 648) to +2.5mPD	9	21-Feb-14	03-Mar-14	26-Mar-14 A	04-Jul-14					
SS - Rock Grade 400 - Zone B - (CH648 to 698) to +2.5mPD	9	04-Mar-14	13-Mar-14	02-Apr-14 A	11-Jul-14					
SS - Rock Grade 400 - Zone B - (CH698 to 738) to +2.5mPD	10	14-Mar-14	25-Mar-14	12-May-14 A	23-Jul-14					
SS - Armour Rock Underlayer - Zone B - (CH598 to 648)	5	04-Mar-14	08-Mar-14	11-Aug-14	15-Aug-14					
SS - Armour Rock Underlayer - Zone B - (CH648 to 698)	5	14-Mar-14	19-Mar-14	16-Aug-14	21-Aug-14					
SS - Armour Rock Underlayer - Zone B - (CH698 to 738)	5	26-Mar-14	31-Mar-14	22-Aug-14	27-Aug-14					
SS - Armour Rock - Zone B - (CH598 to 648)	4	01-Apr-14	04-Apr-14	28-Aug-14	01-Sep-14					
SS - Armour Rock - Zone B - (CH648 to 698)	4	07-Apr-14	10-Apr-14	02-Sep-14	05-Sep-14					
SS - Armour Rock - Zone B - (CH698 to 738)	4	11-Apr-14	15-Apr-14	06-Sep-14	11-Sep-14					
SS - Mass Concrete Coping - Zone B - (CH598 to 648)	7	10-Jul-14	17-Jul-14	05-Sep-14	13-Sep-14					
SS - Mass Concrete Coping - Zone B - (CH648 to 698)	7	18-Jul-14	25-Jul-14	15-Sep-14	22-Sep-14					
SS - Mass Concrete Coping - Zone B - (CH698 to 738)	7	26-Jul-14	02-Aug-14	23-Sep-14	30-Sep-14					
Sloping - Rockfill Type A - Zone B - (CH598 to 648)	1	04-Mar-14	04-Mar-14	05-Jul-14	05-Jul-14					
Sloping - Rockfill Type A - Zone B - (CH648 to 698)	1	14-Mar-14	14-Mar-14	12-Jul-14	12-Jul-14					
Sloping - Rockfill Type A - Zone B - (CH698 to 738)	1	26-Mar-14	26-Mar-14	24-Jul-14	24-Jul-14					
Sloping - Geotextile - Zone B - (CH598 to 648)	1	05-Mar-14	05-Mar-14	07-Jul-14	07-Jul-14					
Sloping - Geotextile - Zone B - (CH648 to 698)	1	15-Mar-14	15-Mar-14	14-Jul-14	14-Jul-14					
Sloping - Geotextile - Zone B - (CH698 to 738)	1	27-Mar-14	27-Mar-14	25-Jul-14	25-Jul-14					
Sloping - Granular Filter - Zone B - (CH598 to 648)	2	06-Mar-14	07-Mar-14	10-Jul-14	11-Jul-14					
Sloping - Granular Filter - Zone B - (CH648 to 698)	3	17-Mar-14	19-Mar-14	15-Jul-14	17-Jul-14					
Sloping - Granular Filter - Zone B - (CH698 to 738)	3	28-Mar-14	31-Mar-14	26-Jul-14	29-Jul-14					
Reclamation										
Reclamation - Geotextile - Zone B - (CH598 to 648)	4	23-Apr-14	26-Apr-14	15-Jul-14	18-Jul-14					
Reclamation - Geotextile - Zone B - (CH488 to 698)	4	28-Apr-14	02-May-14	19-Jul-14	23-Jul-14					
Reclamation - Geotextile - Zone B - (CH598 to 738)	4	03-May-14	08-May-14	30-Jul-14	02-Aug-14					
Reclamation - Sand Blanket - Zone B - (CH598 to 648)	2	28-Apr-14	29-Apr-14	19-Jul-14	21-Jul-14					
Reclamation - Sand Blanket - Zone B - (CH648 to 698)	2	03-May-14	05-May-14	24-Jul-14	25-Jul-14					
Reclamation - Sand Blanket - Zone B - (CH698 to 738)	2	09-May-14	10-May-14	04-Aug-14	05-Aug-14					
Reclamation - Band Drain - Zone B - (CH598 to 648)	4	02-May-14	07-May-14	22-Jul-14	25-Jul-14					
Reclamation - Band Drain - Zone B - (CH648 to 698)	4	08-May-14	12-May-14	26-Jul-14	30-Jul-14					
Reclamation - Band Drain - Zone B - (CH698 to 738)	4	13-May-14	16-May-14	06-Aug-14	09-Aug-14					
Public Fill - Zone B - (CH598 to 648) to -2.5mPD	3	19-Jun-14	21-Jun-14	21-Aug-14	23-Aug-14					
Public Fill - Zone B - (CH648 to 698) to -2.5mPD	3	23-Jun-14	25-Jun-14	25-Aug-14	27-Aug-14					
Public Fill - Zone B - (CH698 to 738) to -2.5mPD	3	26-Jun-14	28-Jun-14	28-Aug-14	30-Aug-14					
Public Fill - Zone B - (CH598 to 648) to +2.5mPD	7	30-Jun-14	08-Jul-14	01-Sep-14	08-Sep-14					
Public Fill - Zone B - (CH648 to 698) to +2.5mPD	7	09-Jul-14	16-Jul-14	10-Sep-14	17-Sep-14					
Public Fill - Zone B - (CH698 to 738) to +2.5mPD	7	17-Jul-14	24-Jul-14	18-Sep-14	25-Sep-14					
Public Fill - Zone B - (CH598 to 648) to +6.0mPD	7	09-Jul-14	16-Jul-14	10-Sep-14	17-Sep-14					
Public Fill - Zone B - (CH648 to 698) to +6.0mPD	7	17-Jul-14	24-Jul-14	18-Sep-14	25-Sep-14					
Public Fill - Zone B - (CH698 to 738) to +6.0mPD	7	25-Jul-14	01-Aug-14	26-Sep-14	06-Oct-14					
Public Fill - Zone B - (CH648 to 698) to +10mPD	0			26-Sep-14	04-Oct-14					
Zone A1										
Vertical Seawall										
VS - Rock Grade 400 - Zone A1 - (CH738 to 793)	5	07-Feb-14	12-Feb-14	01-Apr-14 A	09-Jun-14 A					
VS - Levelling Stone - Zone A1 - (CH738 to 793)	4	18-Feb-14	21-Feb-14	18-Jun-14 A	21-Jun-14 A					
VS - Seawall Block - Zone A1 - (CH738 to 793)	11	11-Apr-14	26-Apr-14	10-Jul-14	22-Jul-14					
VS - Rockfill Type A - Zone A1 - (CH738 to 793)	3	28-Apr-14	30-Apr-14	23-Jul-14	25-Jul-14					
VS - Geotextile - Zone A1 - (CH738 to 793)	2	02-May-14	03-May-14	26-Jul-14	28-Jul-14					
VS - Granular Filter - Zone A1 - (CH738 to 793)	4	07-May-14	10-May-14	31-Jul-14	04-Aug-14					
VS - Berm Stone - Zone A1 - (CH738 to 793)	3	02-Aug-14	05-Aug-14	22-Aug-14	25-Aug-14					
Sloping Seawall										
SS - Rock Grade 400 - Zone A1 - (CH738 to 793) to +2.5mPD (4k/d)	5	26-Mar-14	31-Mar-14	27-May-14 A	29-Jul-14					
SS - Armour Rock Underlayer - Zone A1 - (CH738 to 793)	5	01-Apr-14	07-Apr-14	28-Aug-14	02-Sep-14					
SS - Armour Rock - Zone A1 - (CH738 to 793)	4	16-Apr-14	23-Apr-14	12-Sep-14	16-Sep-14					
Sloping - Rockfill Type A - Zone A1 - (CH738 to 793)	1	01-Apr-14	01-Apr-14	30-Jul-14	30-Jul-14					
Sloping - Geotextile - Zone A1 - (CH738 to 793)	2	02-Apr-14	03-Apr-14	31-Jul-14	01-Aug-14					
Sloping - Granular Filter - Zone A1 - (CH738 to 793)	3	04-Apr-14	08-Apr-14	02-Aug-14	05-Aug-14					

	Current Bar
	Current Bar - Critical
	Current Milestone
	DWPB Bar
	DWPB Milestone
	Progress Bar
	Progress Milestone



Date	Revision	Checked	Approved
12-Feb-14	TMCLKDBJEN/PRG98507 Rev A	WYu	SPe
08-Apr-14	TMCLKDBJEN/PRG98507 Rev B	SPe	WYu

Activity Name	Orig Dur	Planned Start	Planned Finish	Current Start	Current Finish	2014					
						Jun	Jul	Aug	Sep	Oct	
Reclamation											
Reclamation - Geotextile - Zone A1 - (CH738 to 793)	4	09-May-14	13-May-14	06-Aug-14	09-Aug-14			■	Reclamation - Geotextile - Zone A1 - (
Reclamation - Sand Blanket - Zone A1 - (CH738 to 793)	2	14-May-14	15-May-14	11-Aug-14	12-Aug-14			■	Reclamation - Sand Blanket - Zone A		
Reclamation - Band Drain - Zone A1 - (CH738 to 793)	4	17-May-14	21-May-14	13-Aug-14	16-Aug-14			■	Reclamation - Band Drain - Zone A		
Public Fill - Zone A1 - (CH738 to 793) to -2.5mPD	3	30-Jun-14	03-Jul-14	01-Sep-14	03-Sep-14				■	Public Fill - Zone A1 - (CH	
Public Fill - Zone A1 - (CH738 to 793) to +2.5mPD	7	25-Jul-14	01-Aug-14	26-Sep-14	06-Oct-14					■	Public Fill
Zone A2											
Vertical Seawall											
VS - Dredging - Zone A2 - (CH793 to 843)	3	28-Jan-14	30-Jan-14	25-Mar-14 A	01-Jun-14 A	■			VS - Dredging - Zone A2 - (CH793 to 843)		
VS - Dredging - Zone A2 - (CH843 to 893)	4	07-Feb-14	11-Feb-14	06-Apr-14 A	25-Jun-14 A	■			VS - Dredging - Zone A2 - (CH843 to 893)		
VS - Dredging - Zone A2 - (CH893 to 956)	11	12-Feb-14	24-Feb-14	21-Jun-14 A	25-Jun-14 A	■			VS - Dredging - Zone A2 - (CH893 to 956)		
VS - Rock Grade 400 - Zone A2 - (CH793 to 843)	5	13-Feb-14	18-Feb-14	15-Apr-14 A	25-Jun-14 A	■			VS - Rock Grade 400 - Zone A2 - (CH793 to 843)		
VS - Rock Grade 400 - Zone A2 - (CH843 to 893)	5	19-Feb-14	24-Feb-14	14-Jun-14 A	30-Jun-14	■			VS - Rock Grade 400 - Zone A2 - (CH843 to 893)		
VS - Rock Grade 400 - Zone A2 - (CH893 to 956)	16	25-Feb-14	14-Mar-14	23-Jun-14 A	26-Jul-14	■			VS - Rock Grade 400 - Zone A2 - (CH893 to		
VS - Levelling Stone - Zone A2 - (CH793 to 843)	4	25-Feb-14	28-Feb-14	02-Jul-14	05-Jul-14			■	VS - Levelling Stone - Zone A2 - (CH793 to 843)		
VS - Levelling Stone - Zone A2 - (CH843 to 893)	4	01-Mar-14	05-Mar-14	07-Jul-14	10-Jul-14			■	VS - Levelling Stone - Zone A2 - (CH843 to 893)		
VS - Levelling Stone - Zone A2 - (CH893 to 956)	9	06-Mar-14	15-Mar-14	11-Jul-14	21-Jul-14			■	VS - Levelling Stone - Zone A2 - (CH893 to 956)		
VS - Seawall Block - Zone A2 - (CH793 to 843)	7	28-Apr-14	07-May-14	23-Jul-14	30-Jul-14			■	VS - Seawall Block - Zone A2 - (CH793 to 8		
VS - Seawall Block - Zone A2 - (CH843 to 893)	7	08-May-14	15-May-14	31-Jul-14	07-Aug-14			■	VS - Seawall Block - Zone A2 - (CH843		
VS - Seawall Block - Zone A2 - (CH893 to 956)	17	16-May-14	05-Jun-14	08-Aug-14	27-Aug-14			■	VS - Seawall Block - Zone A2		
VS - Rockfill Type A - Zone A2 - (CH793 to 843)	3	16-May-14	19-May-14	08-Aug-14	11-Aug-14			■	VS - Rockfill Type A - Zone A2 - (CH7		
VS - Rockfill Type A - Zone A2 - (CH843 to 893)	3	06-Jun-14	09-Jun-14	28-Aug-14	30-Aug-14			■	VS - Rockfill Type A - Zone A		
VS - Rockfill Type A - Zone A2 - (CH893 to 956)	7	10-Jun-14	17-Jun-14	01-Sep-14	08-Sep-14			■	VS - Rockfill Type A - Z		
VS - Geotextile - Zone A2 - (CH793 to 843)	2	10-Jun-14	11-Jun-14	01-Sep-14	02-Sep-14			■	VS - Geotextile - Zone A2		
VS - Geotextile - Zone A2 - (CH843 to 893)	2	12-Jun-14	13-Jun-14	03-Sep-14	04-Sep-14			■	VS - Geotextile - Zone A2		
VS - Geotextile - Zone A2 - (CH893 to 956)	5	14-Jun-14	19-Jun-14	05-Sep-14	11-Sep-14			■	VS - Geotextile - Zone		
VS - Granular Filter - Zone A2 - (CH793 to 843)	4	14-Jun-14	18-Jun-14	05-Sep-14	10-Sep-14			■	VS - Granular Filter - Z		
VS - Granular Filter - Zone A2 - (CH843 to 893)	4	19-Jun-14	23-Jun-14	11-Sep-14	15-Sep-14			■	VS - Granular Filter		
VS - Granular Filter - Zone A2 - (CH893 to 956)	10	24-Jun-14	05-Jul-14	16-Sep-14	26-Sep-14			■	VS - Granular		
VS - Berm Stone - Zone A2 - (CH793 to 843)	3	06-Aug-14	08-Aug-14	10-Sep-14	12-Sep-14			■	VS - Berm Stone - Zc		
VS - Berm Stone - Zone A2 - (CH843 to 893)	3	09-Aug-14	12-Aug-14	16-Sep-14	18-Sep-14			■	VS - Berm Stone -		
VS - Berm Stone - Zone A2 - (CH893 to 956)	7	13-Aug-14	20-Aug-14	27-Sep-14	07-Oct-14			■	VS - Berm		
Sloping Seawall											
SS - Dredging - Zone A2 - (CH793 to 843)	5	25-Mar-14	29-Mar-14	17-Apr-14 A	01-Jul-14 A	■			SS - Dredging - Zone A2 - (CH793 to 843)		
SS - Dredging - Zone A2 - (CH843 to 893)	6	31-Mar-14	07-Apr-14	17-May-14 A	06-Aug-14	■			SS - Dredging - Zone A2 - (CH843 to 8		
SS - Dredging - Zone A2 - (CH893 to 956)	7	08-Apr-14	15-Apr-14	13-Aug-14	20-Aug-14			■	SS - Dredging - Zone A2 - (CH8		
SS - Rock Grade 400 - Zone A2 - (CH793 to 843) to +2.5mPD (4k/d)	6	01-Apr-14	08-Apr-14	10-Jun-14 A	06-Aug-14	■			SS - Rock Grade 400 - Zone A2 - (CH7		
SS - Rock Grade 400 - Zone A2 - (CH843 to 893) to +2.5mPD (4k/d)	6	09-Apr-14	15-Apr-14	07-Aug-14	20-Aug-14			■	SS - Rock Grade 400 - Zone A2		
SS - Rock Grade 400 - Zone A2 - (CH893 to 956) to +2.5mPD (4k/d)	7	16-Apr-14	26-Apr-14	21-Aug-14	04-Sep-14			■	SS - Rock Grade 400 - Z		
SS - Armour Rock Underlayer - Zone A2 - (CH793 to 843)	5	09-Apr-14	14-Apr-14	03-Sep-14	08-Sep-14			■	SS - Armour Rock Unde		
SS - Armour Rock Underlayer - Zone A2 - (CH843 to 893)	5	16-Apr-14	24-Apr-14	10-Sep-14	15-Sep-14			■	SS - Armour Rock U		
SS - Armour Rock Underlayer - Zone A2 - (CH893 to 956)	5	28-Apr-14	03-May-14	16-Sep-14	20-Sep-14			■	SS - Armour Rock		
SS - Armour Rock - Zone A2 - (CH793 to 843)	4	05-May-14	09-May-14	22-Sep-14	25-Sep-14			■	SS - Armour R		
SS - Armour Rock - Zone A2 - (CH843 to 893)	4	10-May-14	14-May-14	26-Sep-14	30-Sep-14			■	SS - Armour		
Sloping - Rockfill Type A - Zone A2 - (CH793 to 843)	1	09-Apr-14	09-Apr-14	07-Aug-14	07-Aug-14			■	Sloping - Rockfill Type A: Zone A2 - (C		
Sloping - Rockfill Type A - Zone A2 - (CH843 to 893)	1	16-Apr-14	16-Apr-14	21-Aug-14	21-Aug-14			■	Sloping - Rockfill Type A - Zone /		
Sloping - Rockfill Type A - Zone A2 - (CH893 to 956)	1	28-Apr-14	28-Apr-14	05-Sep-14	05-Sep-14			■	Sloping - Rockfill Type A -		
Sloping - Geotextile - Zone A2 - (CH793 to 843)	2	10-Apr-14	11-Apr-14	08-Aug-14	09-Aug-14			■	Sloping - Geotextile - Zone A2 - (CH7		
Sloping - Geotextile - Zone A2 - (CH843 to 893)	2	17-Apr-14	22-Apr-14	22-Aug-14	23-Aug-14			■	Sloping - Geotextile - Zone A2 -		
Sloping - Geotextile - Zone A2 - (CH893 to 956)	2	29-Apr-14	30-Apr-14	06-Sep-14	08-Sep-14			■	Sloping - Geotextile - Z		
Sloping - Granular Filter - Zone A2 - (CH793 to 843)	3	12-Apr-14	15-Apr-14	11-Aug-14	13-Aug-14			■	Sloping - Granular Filter - Zone A2 -		
Sloping - Granular Filter - Zone A2 - (CH843 to 893)	3	23-Apr-14	25-Apr-14	25-Aug-14	27-Aug-14			■	Sloping - Granular Filter - Zo		
Sloping - Granular Filter - Zone A2 - (CH893 to 956)	3	02-May-14	05-May-14	10-Sep-14	12-Sep-14			■	Sloping - Granular Fil		
Reclamation											
Reclamation - Geotextile - Zone A2 - (CH793 to 843)	4	14-May-14	17-May-14	14-Aug-14	18-Aug-14			■	Reclamation - Geotextile - Zone A		
Reclamation - Geotextile - Zone A2 - (CH843 to 893)	4	19-May-14	22-May-14	28-Aug-14	01-Sep-14			■	Reclamation - Geotextile -		
Reclamation - Geotextile - Zone A2 - (CH893 to 956)	3	23-May-14	26-May-14	13-Sep-14	16-Sep-14			■	Reclamation - Geot		
Reclamation - Sand Blanket - Zone A2 - (CH793 to 843)	2	19-May-14	20-May-14	19-Aug-14	20-Aug-14			■	Reclamation - Sand Blanket - Zo		
Reclamation - Sand Blanket - Zone A2 - (CH843 to 893)	3	23-May-14	26-May-14	02-Sep-14	04-Sep-14			■	Reclamation - Sand Blank		
Reclamation - Sand Blanket - Zone A2 - (CH893 to 956)	5	27-May-14	31-May-14	17-Sep-14	22-Sep-14			■	Reclamation - Sa		
Reclamation - Band Drain - Zone A2 - (CH793 to 843)	4	22-May-14	26-May-14	21-Aug-14	25-Aug-14			■	Reclamation - Band Drain - Zc		
Reclamation - Band Drain - Zone A2 - (CH843 to 893)	4	27-May-14	30-May-14	05-Sep-14	10-Sep-14			■	Reclamation - Band D		
Reclamation - Band Drain - Zone A2 - (CH893 to 956)	5	03-Jun-14	07-Jun-14	23-Sep-14	27-Sep-14			■	Reclamation -		
Public Fill - Zone A2 - (CH793 to 843) to -2.5mPD	6	04-Jul-14	10-Jul-14	04-Sep-14	11-Sep-14			■	Public Fill - Zone A2 -		
Public Fill - Zone A2 - (CH843 to 893) to -2.5mPD	6	11-Jul-14	17-Jul-14	12-Sep-14	18-Sep-14			■	Public Fill - Zone A		



Date	Revision	Checked	Approved
12-Feb-14	TMCLKDBJEN/PRG98507 Rev A	WYu	SPo
08-Apr-14	TMCLKDBJEN/PRG98507 Rev B	SPo	WYu

Activity Name	Orig Dur	Planned Start	Planned Finish	Current Start	Current Finish	2014					
						Jun	Jul	Aug	Sep	Oct	
Public Fill - Zone A2 - (CH893 to 956) to -2.5mPD	4	18-Jul-14	22-Jul-14	29-Sep-14	04-Oct-14						Public Fill -
Zone F											
CH137 to CH184											
F - Backfilling up to -7.5mPD & T1 Installation - CH137 to CH184	4	16-Jan-14	19-Jan-14	30-Jun-14	03-Jul-14						F - Backfilling up to -7.5mPD & T1 Installation - CH137 to
F - Backfilling up to -4.5mPD - CH137 to CH184	2	20-Jan-14	21-Jan-14	04-Jul-14	05-Jul-14						F - Backfilling up to -4.5mPD - CH137 to CH184
F - Backfilling up to +0.5mPD & T3 Installation - CH137 to CH184	6	22-Jan-14	27-Jan-14	06-Jul-14	11-Jul-14						F - Backfilling up to +0.5mPD & T3 Installation - CH1
F - Backfilling up to +3.0mPD - CH137 to CH184	2	28-Jan-14	29-Jan-14	12-Jul-14	13-Jul-14						F - Backfilling up to +3.0mPD - CH137 to CH184
F - Backfilling up to +6.0mPD - CH137 to CH184	2	30-Jan-14	31-Jan-14	14-Jul-14	15-Jul-14						F - Backfilling up to +6.0mPD - CH137 to CH184
F - Anchor Wall Installation - CH160 to CH184	2	07-Mar-14	08-Mar-14	13-Aug-14	14-Aug-14						F - Anchor Wall Installation - CH160
CH184 to CH231											
F - Marine Sheet Piling (H2) - CH184 to CH231	3	16-Jan-14	18-Jan-14	31-May-14 A	24-Jun-14 A						F - Marine Sheet Piling (H2) - CH184 to CH231
F - Marine Sheet Piling (H1) - CH184 to CH231	3	20-Jan-14	22-Jan-14	25-Apr-14 A	18-Jun-14 A						F - Marine Sheet Piling (H1) - CH184 to CH231
F - Backfilling up to -7.5mPD & T1 Installation - CH184 to CH231	4	23-Jan-14	26-Jan-14	04-Jul-14	07-Jul-14						F - Backfilling up to -7.5mPD & T1 Installation - CH184
F - Backfilling up to -4.5mPD - CH184 to CH231	2	27-Jan-14	28-Jan-14	08-Jul-14	09-Jul-14						F - Backfilling up to -4.5mPD - CH184 to CH231
F - Backfilling up to +0.5mPD & T3 Installation - CH184 to CH231	6	29-Jan-14	03-Feb-14	12-Jul-14	17-Jul-14						F - Backfilling up to +0.5mPD & T3 Installation - C
F - Backfilling up to +3.0mPD - CH184 to CH231	2	04-Feb-14	05-Feb-14	18-Jul-14	19-Jul-14						F - Backfilling up to +3.0mPD - CH184 to CH231
F - Backfilling up to +6.0mPD - CH184 to CH231	2	06-Feb-14	07-Feb-14	20-Jul-14	21-Jul-14						F - Backfilling up to +6.0mPD - CH184 to CH231
F - Anchor wall Installation - CH184 to CH231	4	10-Mar-14	13-Mar-14	15-Aug-14	19-Aug-14						F - Anchor wall Installation - CH184 to CH231
F - Backfilling up to 0.0mPD & G2 Installation to Anchor Wall- CH184 to	3	14-Mar-14	16-Mar-14	20-Aug-14	22-Aug-14						F - Backfilling up to 0.0mPD & G
F - Backfilling up to +3.0mPD & G1 Installation to Anchor Wall- CH184 to	2	17-Mar-14	18-Mar-14	23-Aug-14	24-Aug-14						F - Backfilling up to +3.0mPD &
F - Backfilling up to +6.0mPD to Anchor Wall - CH184 to CH231	2	19-Mar-14	20-Mar-14	25-Aug-14	26-Aug-14						F - Backfilling up to +6.0mPD
F - Backfilling to +6.0mPD to Existing Seawall - CH184 to CH231	1	21-Mar-14	21-Mar-14	27-Aug-14	27-Aug-14						F - Backfilling to +6.0mPD to
CH231 to CH278											
F - Marine Sheet Piling (H1) - CH231 to CH278	4	23-Jan-14	27-Jan-14	18-Jun-14 A	30-Jun-14						F - Marine Sheet Piling (H1) - CH231 to CH278
F - Marine Sheet Piling (H2) - CH231 to CH278	4	18-Mar-14	21-Mar-14	24-Jun-14 A	15-Aug-14						F - Marine Sheet Piling (H2) - CH278 to CH231
F - Backfilling up to -7.5mPD & T1 Installation - CH231 to CH278	4	22-Mar-14	25-Mar-14	16-Aug-14	19-Aug-14						F - Backfilling up to -7.5mPD & T
F - Backfilling up to -4.5mPD - CH231 to CH278	2	26-Mar-14	27-Mar-14	20-Aug-14	21-Aug-14						F - Backfilling up to -4.5mPD - C
F - Backfilling up to +0.5mPD & T3 Installation - CH231 to CH278	6	28-Mar-14	02-Apr-14	22-Aug-14	27-Aug-14						F - Backfilling up to +0.5mPD
F - Backfilling up to +3.0mPD - CH231 to CH278	2	03-Apr-14	04-Apr-14	28-Aug-14	29-Aug-14						F - Backfilling up to +3.0mPD
F - Backfilling up to +6.0mPD - CH231 to CH278	2	05-Apr-14	06-Apr-14	30-Aug-14	31-Aug-14						F - Backfilling up to +6.0mPD
F - Anchor wall Installation - CH231 to CH278	4	07-Apr-14	10-Apr-14	01-Sep-14	04-Sep-14						F - Anchor wall Installation
F - Backfilling up to 0.0mPD & G2 Installation to Anchor Wall- CH231 to	3	11-Apr-14	13-Apr-14	05-Sep-14	07-Sep-14						F - Backfilling up to 0.0m
F - Backfilling up to +3.0mPD & G1 Installation to Anchor Wall - CH231 to	2	14-Apr-14	15-Apr-14	08-Sep-14	09-Sep-14						F - Backfilling up to +3.0
F - Backfilling up to +6.0mPD to Anchor Wall - CH231 to CH278	2	16-Apr-14	17-Apr-14	10-Sep-14	11-Sep-14						F - Backfilling up to +6
F - Backfilling to +6.0mPD to Existing Seawall - CH231 to CH278	1	18-Apr-14	18-Apr-14	12-Sep-14	12-Sep-14						F - Backfilling to +6.0
CH278 to CH327											
F - Pre-boring for Marine Sheet Pile - CH278 to CH327	6	28-Jan-14	10-Feb-14	02-Jul-14	08-Jul-14						F - Pre-boring for Marine Sheet Pile - CH278 to CH327
F - Marine Sheet Piling (H1) - CH278 to CH327	5	25-Feb-14	01-Mar-14	23-Jul-14	28-Jul-14						F - Marine Sheet Piling (H1) - CH278 to CH
F - Marine Sheet Piling (H2) - CH278 to CH327	5	12-Mar-14	17-Mar-14	07-Aug-14	12-Aug-14						F - Marine Sheet Piling (H2) - CH278
F - Backfilling up to -3.5mPD & T2 Installation - CH278 to CH327	5	18-Mar-14	22-Mar-14	13-Aug-14	17-Aug-14						F - Backfilling up to -3.5mPD & T2
F - Backfilling up to +0.5mPD - CH278 to CH327	4	23-Mar-14	26-Mar-14	18-Aug-14	21-Aug-14						F - Backfilling up to +0.5mPD - C
F - Backfilling up to +3.0mPD & T4 Installation - CH278 to CH327	5	27-Mar-14	31-Mar-14	22-Aug-14	26-Aug-14						F - Backfilling up to +3.0mPD
F - Backfilling up to +6.0mPD - CH278 to CH327	2	01-Apr-14	02-Apr-14	27-Aug-14	28-Aug-14						F - Backfilling up to +6.0mPD
F - Anchor wall Installation - CH278 to CH327	4	11-Apr-14	15-Apr-14	05-Sep-14	10-Sep-14						F - Anchor wall Installa
F - Backfilling up to 0.0mPD & G2 Installation to Anchor Wall - CH278 to	3	16-Apr-14	18-Apr-14	11-Sep-14	13-Sep-14						F - Backfilling up to 0
F - Backfilling up to +3.0mPD & G1 Installation to Anchor Wall - CH278 to	3	19-Apr-14	21-Apr-14	14-Sep-14	16-Sep-14						F - Backfilling up to
F - Backfilling up to +6.0mPD to Anchor Wall - CH278 to CH327	3	22-Apr-14	24-Apr-14	17-Sep-14	19-Sep-14						F - Backfilling up to
F - Backfilling to +6.0mPD to Existing Seawall - CH278 to CH327	1	25-Apr-14	25-Apr-14	20-Sep-14	20-Sep-14						F - Backfilling to +
CH327 to CH381											
F - Pre-boring for Marine Sheet Pile - CH327 to CH381	6	11-Feb-14	17-Feb-14	09-Jul-14	15-Jul-14						F - Pre-boring for Marine Sheet Pile - CH327 to C
F - Marine Sheet Piling (H1) - CH327 to CH381	4	03-Mar-14	06-Mar-14	29-Jul-14	01-Aug-14						F - Marine Sheet Piling (H1) - CH327 to C
F - Marine Sheet Piling (H2) - CH327 to CH381	4	07-Mar-14	11-Mar-14	02-Aug-14	06-Aug-14						F - Marine Sheet Piling (H2) - CH327 to
F - Backfilling up to -3.5mPD & T2 Installation - CH327 to CH381	4	12-Mar-14	15-Mar-14	07-Aug-14	10-Aug-14						F - Backfilling up to -3.5mPD & T2 Ins
F - Backfilling up to +0.5mPD - CH327 to CH381	3	16-Mar-14	18-Mar-14	11-Aug-14	13-Aug-14						F - Backfilling up to +0.5mPD - CH3
F - Backfilling up to +3.0mPD & T4 Installation - CH327 to CH381	5	19-Mar-14	23-Mar-14	14-Aug-14	18-Aug-14						F - Backfilling up to +3.0mPD & T
F - Backfilling up to +6.0mPD - CH327 to CH381	3	24-Mar-14	26-Mar-14	19-Aug-14	21-Aug-14						F - Backfilling up to +6.0mPD - C
F - Anchor wall Installation - CH327 to CH381	3	16-Apr-14	22-Apr-14	11-Sep-14	13-Sep-14						F - Anchor wall Instal
F - Backfilling up to 0.0mPD & G2 Installation to Anchor Wall - CH327 to	3	23-Apr-14	25-Apr-14	14-Sep-14	16-Sep-14						F - Backfilling up to
F - Backfilling up to +3.0mPD & G1 Installation to Anchor Wall - CH327 to	3	26-Apr-14	28-Apr-14	17-Sep-14	19-Sep-14						F - Backfilling up to
F - Backfilling up to +6.0mPD to Anchor Wall - CH327 to CH381	2	29-Apr-14	30-Apr-14	20-Sep-14	21-Sep-14						F - Backfilling up
F - Backfilling to +6.0mPD to Existing Seawall - CH327 to CH381	1	01-May-14	01-May-14	22-Sep-14	22-Sep-14						F - Backfilling to
Box Culvert Extension											
Construction											
CH000 to CH137											
Predrilling - CH27 to CH137	24	02-May-14	30-May-14	30-Apr-14 A	21-Jul-14						Predrilling - CH27 to CH137

Activity Name	Orig Dur	Planned Start	Planned Finish	Current Start	Current Finish	2014				
						Jun	Jul	Aug	Sep	Oct
Bored Pile Construction - A43 to A62 (4 Rigs) & Land Sheet Piling	96	31-May-14	23-Sep-14	22-Jul-14	13-Nov-14					
CH137 to CH184										
Predrilling - CH137 to CH184	24	07-Feb-14	06-Mar-14	16-Jul-14	12-Aug-14					
Bored Pile Construction - A42 to A35	160	07-Mar-14	19-Sep-14	13-Aug-14	28-Feb-15					
CH184 to CH231										
Predrilling - CH184 to CH231	24	22-Mar-14	23-Apr-14	28-Aug-14	25-Sep-14					
Bored Pile Construction - A34 to A27	156	22-Mar-14	30-Sep-14	28-Aug-14	11-Mar-15					
CH231 to CH278										
Predrilling - CH231 to CH278	24	22-Apr-14	21-May-14	13-Sep-14	13-Oct-14					
Bored Pile Construction - A26 to A19	143	22-Apr-14	13-Oct-14	13-Sep-14	11-Mar-15					
CH278 to CH327										
Predrilling - CH278 to CH327	24	26-Apr-14	26-May-14	22-Sep-14	21-Oct-14					
CH327 to CH381										
Predrilling - CH327 to CH381	24	02-May-14	30-May-14	23-Sep-14	22-Oct-14					

North Shafts Construction & Tunnel Structure

Construction						
North Launching Shaft ELS Foundation & Capping Beam (Cell 1 to 3)						
E - Setup for Launching Shaft ELS	18	28-Mar-14	22-Apr-14	12-May-14 A	07-Jun-14 A	E - Setup for Launching Shaft ELS
E - Cell 1-3 - Diaphragm Wall & Toe Grouting - Shaft ELS	54	02-May-14	07-Jul-14	07-Jun-14 A	05-Sep-14	E - Cell 1-3 - Diaphragm
E - Cell 1-3 - Diaphragm Wall & Toe Grouting - Perm Barette	26	08-Jul-14	06-Aug-14	06-Sep-14	17-Sep-14	E - Cell 1-3 - Diaph
E - Cell 1-3 - Capping beam Installation	18	08-Jul-14	28-Jul-14	06-Sep-14	27-Sep-14	E - Cell 1-3 - C
E - Cell 1-3 - Instrumentation & Pump well Installation	6	31-Jul-14	06-Aug-14	18-Sep-14	24-Sep-14	E - Cell 1-3 - In
E - Pumping Test for TBM Lanuching Shaft ELS - Cell 1-3	5	07-Aug-14	11-Aug-14	25-Sep-14	29-Sep-14	E - Pumping

Portion N6 - CLP Substation

Construction						
CLP Substation - E&M, BS Installation	0			05-May-14 A	02-Jul-14	CLP Substation - E&M, BS Installation
Substation - ABWF works	0			26-Apr-14 A	30-May-14 A	Substation - ABWF works
Substation - Metal works & Remaining civil works	0			04-Jun-14 A	02-Jul-14	Substation - Metal works & Remaining civil works
Substation - E&M works	0			05-May-14 A	02-Jul-14	Substation - E&M works
Pre-Electrical Access Inspection	0		31-May-14		03-Jun-14 A	Pre-Electrical Access Inspection
Electrical Access	0		30-Jun-14		03-Jul-14	Electrical Access
1st Batch - CLP Installation & Commissioning	108	02-Jul-14	07-Nov-14	04-Jul-14	10-Nov-14	
11kV Equipment / Switch Room installation by JV	48	13-Aug-14	10-Oct-14	22-Aug-14	21-Oct-14	

North Surface works for TBM Tunnelling

Construction						
Zone E						
Zone E - Vibro-compaction (CH150-205)	0			30-Jun-14	13-Jul-14	Zone E - Vibro-compaction (CH150-205)
Zone E - Unreinforced Separation D-wall	0			14-Jul-14	29-Jul-14	Zone E - Unreinforced Separation D-wall
Zone E - Granular Material for B/Cement Base	0			30-Jul-14	08-Aug-14	Zone E - Granular Material for B/Cement
Zone E - TBM Crown Ground Treatment	0			14-Jul-14	24-Sep-14	Zone E - TBM C
Zone E - Jet Grouting for TBM Break-in Plug (Section 1)	0			21-Jul-14	02-Aug-14	Zone E - Jet Grouting for TBM Break-in P
Zone E - Jet Grouting for TBM Break-in Plug (Section 2)	0			04-Aug-14	06-Sep-14	Zone E - Jet Grouting fo
Zone E - Jet Grouting for TBM Break-in Plug (Section 3 - interface with N	0			08-Sep-14	15-Oct-14	Zone
Zone E - CSM for TBM Break-in Plug (Section 1)	0			09-Aug-14	20-Sep-14	Zone E - CSM for
Zone E - CSM for TBM Break-in Plug (Section 2)	0			22-Sep-14	16-Dec-14	
Zone D1						
Zone D1 - Ground Treatment for CP55	0			11-Aug-14	03-Sep-14	Zone D1 - Ground Treatm
Zone D1 - Vibro-compaction (CH205 to 255)	60	08-May-14	06-Jul-14	01-Jul-14	30-Jul-14	Zone D1 - Vibro-compaction (CH205 to 255
Zone D1 - Vibro-compaction (CH255 to 305)	60	13-May-14	11-Jul-14	05-Jul-14	03-Aug-14	Zone D1 - Vibro-compaction (CH255 to 3
Zone D1 - Vibro-compaction (CH305 to 355)	60	17-May-14	15-Jul-14	11-Jul-14	09-Aug-14	Zone D1 - Vibro-compaction (CH305 t
Zone D1 - Compacted Sand Excavation down to +2.0mPD	6	07-Jul-14	12-Jul-14	04-Sep-14	11-Sep-14	Zone D1 - Compacted
Zone D1 - Unreinforced Separation D-wall (1st 55m)	16	14-Jul-14	31-Jul-14	12-Sep-14	30-Sep-14	Zone D1 - U
Zone D1 - Ground Treatment for CP54	20	14-Jul-14	05-Aug-14	12-Sep-14	07-Oct-14	Zone D1
Zone D2						
Zone D2 - Vibro-compaction (CH355 to 405)	60	25-May-14	23-Jul-14	30-Jul-14	28-Aug-14	Zone D2 - Vibro-compaction
Zone D2 - Vibro-compaction (CH405 to 443)	60	07-Jun-14	05-Aug-14	10-Aug-14	08-Sep-14	Zone D2 - Vibro-compa
Zone C1						
Zone C1 - Vibro-compaction (CH355 to 405)	60	22-Jun-14	20-Aug-14	24-Aug-14	22-Sep-14	Zone C1 - Vibro
Zone C1 - Vibro-compaction (CH405 to 443)	60	28-Jun-14	26-Aug-14	30-Aug-14	28-Sep-14	Zone C1 - Vit
Zone C1 - Ground Treatment for CP52	26	27-Aug-14	26-Sep-14	29-Sep-14	30-Oct-14	
Zone C2						
Zone C2 - Drilling for Rock Fissue Grouting for CP51	21	03-Jul-14	26-Jul-14	03-Sep-14	27-Sep-14	Zone C2 - Drill
Zone C2 - Rock Fissue Grouting for CP51	44	14-Jul-14	02-Sep-14	15-Sep-14	06-Nov-14	
Zone B						
Zone B - Unreinforced Separation D-wall	13	25-Jul-14	08-Aug-14	26-Sep-14	13-Oct-14	Zone
