

AUES JOB No.: TCS00715/14

TUEN MUN - CHEK LAP KOK LINK
CONTRACT NO. HY/2013/12 –
NORTHERN CONNECTION TOLL PLAZA AND
ASSOCIATED WORKS

2nd QUARTERLY ENVIRONMENTAL MONITORING &
AUDIT SUMMARY REPORT –
(February to April 2015)

PREPARED FOR

CRBC AND KADEN JOINT VENTURE

Quality Index

Date	Reference No.	Prepared By	Certified By
27 May 2015	TCS00715/14/600/R0093v2	 Ben Tam (Environmental Consultant)	 T.W. Tam (Environmental Team Leader)

This report has been prepared by Action-United Environmental Services & Consulting with all reasonable skill, care and diligence within the terms of the Agreement with the client, incorporating our General Terms and Conditions of Business and taking account of the resources devoted to it by agreement with the client. We disclaim any responsibility to the client and others in respect of any matters outside the scope of the above. This report is confidential to the client and we accept no responsibility of whatsoever nature to third parties to whom this report, or any part thereof, is made known. Any such party relies upon the report at their own risk.

Ref.: HYDZHMBEEM00_0_3005L.15

1 June 2015

AECOM
Supervising Officer Representative's Office
No. 8 Mong Fat Street, Tuen Mun,
New Territories, Hong Kong

By Fax (2293 6300) and By Post

Attention: Mr. Roger Man

Dear Roger,

**Re: Agreement No. CE 48/2011 (EP)
Environmental Project Office for the
HZMB Hong Kong Link Road, HZMB Hong Kong Boundary Crossing Facilities,
and Tuen Mun-Chek Lap Kok Link – Investigation**

**Contract No. HY/2013/12 TM-CLKL Northern Connection Toll Plaza and
Associated Works
2nd Quarterly EM&A report for February to April 2015**

Reference is made to the Quarterly Environmental Monitoring and Audit (EM&A) Report (February to April 2015) certified by the ET Leader (AUES reference: TCS00715/14/600/L0093v2 dated 27 May 2015) provided to us via e-mail on 28 May 2015.

We are pleased to inform you that we have no adverse comments on the captioned Report.

Thank you for your kind attention. Please do not hesitate to contact the undersigned or the ENPO Leader Mr. Y. H. Hui should you have any queries.

Yours sincerely,



F. C. Tsang
Independent Environmental Checker
Tuen Mun – Chek Lap Kok Link

c.c. HyD – Mr. Stephen Chan (By Fax: 3188 6614)
HyD – Mr. Matthew Fung (By Fax: 3188 6614)
AECOM – Mr. Conrad Ng (By Fax: 3922 9797)
AUES – Mr. T. W. Tam (By Fax: 2959 6079)
CRBC – Kaden JV – Ms. Winnie Chu (By Fax: 2253 8399)

Internal: DY, YH, SLUI, ENPO Site

Q:\Projects\HYDZHMBEEM00\02_Proj_Mgt\02_Corr\HYDZHMBEEM00_0_3005L.15.doc

EXECUTIVE SUMMARY

ES.01. This is the 2nd Quarterly EM&A Summary Report for the “Tuen Mun - Chek Lap Kok Link - Northern Connection Toll Plaza and Associated Works” under Environmental Permit No. EP-354/2009/C (hereinafter “the EP”), covering the period from **1 February to 30 April 2015** (hereinafter “Reporting Period”).

ENVIRONMENTAL MONITORING AND AUDIT ACTIVITIES

ES.02. Environmental monitoring activities under the EM&A programme in the Reporting Period are summarized in the following table.

Environmental Aspect	Environmental Monitoring Parameters / Inspection	Total Occasions
Air Quality	1-hour TSP	390
	24-hour TSP	130
Cultural heritage inspection	Grave G1	13
Landfill Gas Monitoring	Oxygen; Methane & Carbon Dioxide	68 days
Landscape & Visual	Landscape & Visual Monitoring	13
Joint Site Inspection / Audit	IEC, ET, the Contractor and RE joint site Environmental Inspection and Auditing	13

BREACHES OF ACTION/LIMIT LEVELS

ES.03. In the Reporting Period, no exceedance was recorded for the measured parameter under the Contract. The summary of breach of monitoring performance is shown below.

Environmental Aspect	Monitoring Parameters	Action Level	Limit Level	Event & Action		
				NOE Issued	Investigation	Corrective Actions
Air Quality	1-hour TSP	0	0	0	0	0
	24-hour TSP	0	0	0	0	0
Landfill Gas Monitoring	Oxygen	0	0	0	0	0
	Methane	0	0	0	0	0
	Carbon Dioxide	0	0	0	0	0

ENVIRONMENTAL COMPLAINT

ES.04. No environmental complaints were received by either the RE or ENPO or HyD or the Main Contractor in the Reporting Period.

NOTIFICATION OF SUMMONS AND SUCCESSFUL PROSECUTIONS

ES.05. No environmental summons or successful prosecutions were recorded in the Reporting Period.

REPORTING CHANGES

ES.06. No reporting changes were made in the Reporting Period.

FUTURE KEY ISSUES

ES.07. In upcoming wet season, muddy water or other water pollutants from site surface runoff into the public areas will be key environment issue. Water quality mitigation measures to prevent surface runoff into public areas should be paid on special attention.

ES.08. Furthermore, air quality mitigation measures such as watering of site area for 12 times per day and covering of exposed slopes should be implemented to reduce construction dust impact as recommended in the EMIS.

ES.09. It was reminded that good housekeeping practice should be maintained. Mosquito control measures should be properly implemented to prevent mosquito breeding on site.

TABLE OF CONTENTS

1.	INTRODUCTION	1
1.1.	PROJECT BACKGROUND	1
1.2	REPORT STRUCTURE	1
2	CONTRACT ORGANIZATION AND CONSTRUCTION PROGRESS	2
2.1	CONTRACT ORGANIZATION	2
2.2	CONSTRUCTION PROGRESS	2
2.3	SUMMARY OF ENVIRONMENTAL SUBMISSIONS	2
3	SUMMARY OF IMPACT MONITORING REQUIREMENTS	4
3.1	GENERAL	4
3.2	AIR QUALITY MONITORING	4
3.3	MONITORING LOCATIONS	4
3.4	MONITORING FREQUENCY	4
3.5	MONITORING EQUIPMENT	5
3.6	DERIVATION OF ACTION/LIMIT (A/L) LEVELS	6
3.7	OTHER ENVIRONMENTAL ASPECTS	6
4	AIR QUALITY MONITORING	8
4.1	GENERAL	8
4.2	SUMMARY OF MONITORING RESULTS	8
4.3	ACTION AND LIMIT (A/L) LEVELS EXCEEDANCE	8
5	ECOLOGY MONITORING	9
5.1	GENERAL	9
5.2	PITCHER PLANTS INSPECTION	9
6	CULTURAL HERITAGE	10
6.1	GENERAL	10
6.2	GRAVE INSPECTION	10
7	LANDSCAPE AND VISUAL	11
7.1	GENERAL	11
7.2	LANDSCAPE AND VISUAL INSPECTION	11
8	LANDFILL GAS HAZARD MONITORING	12
8.1	GENERAL	12
8.2	LANDFILL GAS MONITORING RESULT	12
9	WASTE MANAGEMENT	14
9.1	GENERAL WASTE MANAGEMENT	14
9.2	RECORDS OF WASTE QUANTITIES	14
10	SITE INSPECTIONS	15
10.1	REQUIREMENTS	15
11	ENVIRONMENTAL COMPLAINT AND NON-COMPLIANCE	19
11.1	ENVIRONMENTAL COMPLAINT, SUMMONS AND PROSECUTION	19
12	IMPLEMENTATION STATUS OF MITIGATION MEASURES	20
12.1	GENERAL REQUIREMENTS	20
13	CONCLUSIONS AND RECOMMENDATIONS	21
13.1	CONCLUSIONS	21
13.2	RECOMMENDATIONS	21

LIST OF TABLES

TABLE 2-1	STATUS OF ENVIRONMENTAL LICENSES AND PERMITS OF THE CONTRACTS
TABLE 3-1	AIR QUALITY MONITORING STATIONS UNDER THE CONTRACT
TABLE 3-2	ENHANCED TSP MONITORING PLAN – CONSTRUCTION PHASE
TABLE 3-3	ACTION AND LIMIT LEVELS FOR IMPACT AIR QUALITY MONITORING
TABLE 4-1	SUMMARY OF AIR QUALITY MONITORING EXCEEDANCE
TABLE 8-1	SUMMARY OF LANDFILL GAS MEASUREMENT RESULTS IN REPORTING PERIOD
TABLE 9-1	SUMMARY OF QUANTITIES OF INERT C&D MATERIALS
TABLE 9-2	SUMMARY OF QUANTITIES OF C&D WASTES
TABLE 10-1	SITE OBSERVATIONS FOR THE CONTRACT FOR THE REPORTING PERIOD
TABLE 10-2	SUMMARY OF REMINDERS/OBSERVATIONS OF SITE INSPECTION
TABLE 11-1	STATISTICAL SUMMARY OF ENVIRONMENTAL EXCEEDANCE
TABLE 11-2	STATISTICAL SUMMARY OF ENVIRONMENTAL COMPLAINTS
TABLE 11-3	STATISTICAL SUMMARY OF ENVIRONMENTAL SUMMONS
TABLE 11-4	STATISTICAL SUMMARY OF ENVIRONMENTAL PROSECUTION
TABLE 12-1	ENVIRONMENTAL MITIGATION MEASURES

LIST OF ANNEXES

APPENDIX A	LAYOUT PLAN OF THE PROJECT
APPENDIX B	LAYOUT PLAN OF THE CONTRACT
APPENDIX C	ENVIRONMENTAL MANAGEMENT ORGANIZATION CHART
APPENDIX D	MASTER CONSTRUCTION PROGRAMME FOR
APPENDIX E	MONITORING LOCATIONS / SENSITIVE RECEIVERS FOR THE CONTRACT
APPENDIX F	EVENT AND ACTION PLAN
APPENDIX G	LANDFILL GAS MONITORING GRAPHICAL PLOTS
APPENDIX H	WASTE FLOW TABLE
APPENDIX I	IMPLEMENTATION SCHEDULE FOR ENVIRONMENTAL MITIGATION MEASURES

1. INTRODUCTION

1.1. PROJECT BACKGROUND

- 1.1.1. CRBC-Kaden Joint Venture (hereafter “CRBC-Kaden JV”) is commissioned by the Highways Department (HyD) as the Main Contractor of the Contract No. HY/2013/12 – Northern Connection Toll Plaza and Tunnel Section ((hereafter “the Contract”) and this Contract is part of the Tuen Mun – Chek Lap Kok Link (TM-CLK Link Project). TM-CLK Link Project is a Designated Project under Environmental Permit number VEP-354/2009C issued on 10 December 2014. The layout Plan of the Project and the Contract are showed in [Appendix A](#) and [B](#) respectively.
- 1.1.2. The construction works of the Contract mainly include:-
- construction of an approximately 5.4 hectares toll plaza and an associated footbridge;
 - construction of associated carriageways including approximately 0.74 kilometre land viaducts, and an approximately 230 metres vehicular underpass to connect the toll plaza and the roundabout at Lung Mun Road/Lung Fu Road;
 - site formation for the construction of the toll plaza, including associated slope works and natural terrain hazard mitigation measures;
 - modification and realignment of the existing Lung Mun Road and Lung Fu Road; and
 - associated waterworks, drainage, sewerage and landscaping works, etc..
- 1.1.3. Action-United Environmental Services & Consulting has been commissioned as an Independent ET to implement the relevant EM&A program in accordance with the approved EM&A Manual, as well as the associated duties.
- 1.1.4. This is the 2nd Quarterly EM&A Summary Report covering the period from **1 February to 30 April 2015**.

1.2 REPORT STRUCTURE

- 1.2.1 The Monthly Environmental Monitoring and Audit (EM&A) Report is structured into the following sections:-

- Section 1 Introduction*
- Section 2 Contract Organization and Construction Progress*
- Section 3 Summary of Impact Monitoring Requirements*
- Section 4 Air Quality Monitoring*
- Section 5 Ecology Monitoring*
- Section 6 Cultural Heritage*
- Section 7 Landscape and Visual*
- Section 8 Landfill gas hazard Monitoring*
- Section 9 Waste Management*
- Section 10 Site Inspections*
- Section 11 Environmental Complaints and Non-Compliance*
- Section 12 Implementation Status of Mitigation Measures*
- Section 13 Conclusions and Recommendations*

2 CONTRACT ORGANIZATION AND CONSTRUCTION PROGRESS

2.1 CONTRACT ORGANIZATION

2.1.1 The Contract organization and contact details of key personnel are shown in [Appendix C](#).

2.2 CONSTRUCTION PROGRESS

2.2.1 In the Reporting Period, the major construction activity conducted under the Contract is summarized in below. Moreover, the master construction program is enclosed in [Appendix D](#).

February 2015

- Bridge Work – Portion X
- Site Formation – Portion X
- Underpass – Portion X
- Retaining Wall Structure TP_F & RW_B – Portion X
- Footbridge FB1 – Portion X
- Ground Investigation Works – Various Locations
- Site Clearance – Various Locations
- Tree Felling – Various Locations

March 2015

- Instrumentation and Monitoring
- Site Formation to Slope A, B, C, D, E, TP_F and Upgrading Works
- Excavation to Slope A, B,C,D & E
- Vehicular Underpass TN-01
- Construction of Culvert 1-Stage 4 & Conforming design
- Bridge TD1, Bridge G1, G2, Bridge H1 & Footbridge
- Retaining Structure RW_B-Section 1
- Ground Investigation Works – Various Locations
- Site Clearance – Various Locations
- Tree Felling – Various Locations
- Natural terrain hazard mitigation measures

April 2015

- Site Formation to Slope A, B, C, D, E, TP_F and Upgrading Works
- Toll Plaza Decking TD1, TD2
- Retaining Structure RW_B-Section 1
- Instrumentation and Monitoring
- Bridge TD1, TD2, Bridge G1, G2, Bridge H1 & Footbridge
- Construction of Culvert 1-Stage 4
- Site Clearance
- Tree Felling

2.3 SUMMARY OF ENVIRONMENTAL SUBMISSIONS

2.3.1 In according to the EP, the required documents have submitted to EPD for retention which listed in below:

- Monitoring Plan on Construction Dust (submission refer to Contract HY/2012/08)
- Landscape and Visual Plan (not yet endorsed by EPD)
- Waste Management Plan (endorsed by EPD on 16 March 2015)
- Baseline Monitoring Report (not yet endorsed by EPD)

2.3.2 Summary of the relevant permits, licenses, and/or notifications on environmental protection for the Project of each contracts are presented in *Table 2-1*.

Table 2-1 Status of Environmental Licenses and Permits of the Contracts

No.	Type of Permit/ License	Submission Date	Reference/ License No.	Date of Issue	Date of Expiry
1	Air pollution Control (Construction Dust) Regulation	06-08-2014	377719	06-08-2014	N/A
2	Chemical Waste Producer Registration - Waste Producers Number	06-08-2014	5117422C389301	03-09-2014	N/A
3	Water Pollution Control Ordinance - Discharge License	13-08-2014	WT00020065-2014	29-09-2014	30-09-2019
4	Waste Disposal Regulation - Billing Account for Disposal of Construction Waste	21-07-2014	7020460	01-08-2014	N/A
5	Permission to Transplant Pitcher Plant	02-12-2014	(7) in AF CON 11/13 pt.4	09-12-2014	08-06-2015
6	CNP for Multiple Task	05-12-2014	GW-RW0949-14	05-12-2014	04-05-2015
7	CNP for GI works	23-2-2015	GW-RW0134-15	16-03-2015	07-04-2015

3 SUMMARY OF IMPACT MONITORING REQUIREMENTS

3.1 GENERAL

3.1.1 The major construction activities under the Contract are land-based and no marine work will be involved. In accordance with the Project EM&A Manual requirements, the environmental aspects under the Contract shall be included air quality, ecological, cultural heritage, landscape and visual, landfill gas and site inspection during construction period. In addition, audit of the contractor's implementation of the construction noise and land-based water quality pollution control measures are also required for the Contract.

3.1.2 A summary of construction phase EM&A requirements are presented in the sub-sections below.

3.2 AIR QUALITY MONITORING

3.2.1 The construction phase monitoring air quality shall cover the following parameters:

- 1-hour TSP; and
- 24-hour TSP

3.3 MONITORING LOCATIONS

3.3.1 The air quality monitoring stations for impact monitoring are listed in *Table 3-1* and illustrated in *Appendix E*.

Table 3-1 Air Quality Monitoring Stations under the Contract

ID	Location	Air monitoring station Description
ASR1	Tuen Mun Fireboat Station	EM&A Manual
ASR5	Pillar Point Fire Station	EM&A Manual
AQMS1	Previous River Trade Golf	Enhanced TSP Level under EP condition 2.4
ASR6	Butterfly Beach Laundry	Enhanced TSP Level under EP condition 2.4
ASR10	Butterfly Beach Park	Enhanced TSP Level under EP condition 2.4

3.4 MONITORING FREQUENCY

3.4.1 As per Condition 2.4 of the EP of TM-CLKL, an enhanced monitoring plan on TSP level at Tuen Mun ("the Enhanced TSP Monitoring Plan") is required to be submitted to the DEP for approval at least 1 month before the commencement of construction of the Project. Details of the Enhanced TSP Monitoring Plan under Contract No. HY/2012/08 could be found from the project website. The air quality monitoring work under this Contract will follow the monitoring requirement of enhanced TSP monitoring under the project.

3.4.2 The air quality monitoring requirements for the Contract is summarized in *Table 3-2*.

Table 3-2 Enhanced TSP Monitoring Plan – Construction Phase

Condition	Monitoring Parameter	Monitoring Location	Frequency	Monitoring Requirement
General	1-hour TSP	ASR1, ASR5, AQMS1, ASR6, ASR10	3 times per day every six days	Throughout the Northern Connection, toll plaza and tunnel buildings construction works
	24-hour TSP	ASR1, ASR5, AQMS1, ASR6, ASR10	Daily every six days	
Special	1-hour TSP	ASR1, ASR5, AQMS1, ASR6, ASR10	3 times per day every three days	<u>Northern Connection</u> During excavation works for launching shaft, excavation work for Cut

Condition	Monitoring Parameter	Monitoring Location	Frequency	Monitoring Requirement
	24-hour TSP	ASR1, ASR5, AQMS1, ASR6, ASR10	Daily every three days	and Cover Tunnel and Cut and Cover Tunnel Construction <u>Toll Plaza</u> During excavation, slope works, construction of road and superstructures and wind erosion from open sites and stockpiling areas <u>Tunnel Buildings</u> During excavation, foundation works, construction of superstructures and wind erosion from open sites and stockpiling areas

3.5 MONITORING EQUIPMENT

- 3.5.1 The 24-hour and 1-hour TSP levels shall be measured by following the standard high volume sampling method as set out in the *Title 40 of the Code of Federal Regulations, Chapter 1 (Part 50), Appendix B*.
- 3.5.2 The filter paper of 24-hour TSP measurement shall be determined by HOKLAS accredited laboratory. A high volume sampler in compliance with the following specifications shall be used for carrying out the 1-hr and 24-hr TSP monitoring:
- (i) 0.6-1.7 m³/min (20-60 SCFM) adjustable flow range;
 - (ii) equipped with a timing/control device with +/- 5 minutes accuracy for 24 hours operation;
 - (iii) installed with elapsed-time meter with +/- 2 minutes accuracy for 24 hours operation;
 - (iv) capable of providing a minimum exposed area of 406 cm² (63 in²);
 - (v) flow control accuracy: +/- 2.5% deviation over 24-hr sampling period;
 - (vi) equipped with a shelter to protect the filter and sampler;
 - (vii) incorporated with an electronic mass flow rate controller or other equivalent devices;
 - (viii) equipped with a flow recorder for continuous monitoring;
 - (ix) provided with a peaked roof inlet;
 - (x) equipped with a manometer;
 - (xi) able to hold and seal the filter paper to the sampler housing in a horizontal position;
 - (xii) easy to change the filter; and
 - (xiii) capable of operating continuously for 24-hr period.
- 3.5.3 Calibration of dust monitoring equipment shall be conducted by the ET upon installation and in bi-monthly intervals during construction phase. The transfer standard shall be traceable to the internationally recognized primary standard and be calibrated annually. The calibration data shall be properly documented for future reference by concerned parties, such as the IEC. All the data shall be converted into standard temperature and pressure condition.
- 3.5.4 The filter paper of 24-hour TSP measurement shall be determined by HOKLAS accredited laboratory.
- 3.5.5 If the ET proposes to use a direct reading dust meter to measure 1-hr TSP levels on an ad hoc basis, he shall submit sufficient information to the IEC to prove that the instrument is capable of achieving a comparable result as that the High Volume Sampler (HVS) and may be used for the

1-hr sampling. The instrument should also be calibrated regularly and the 1-hr sampling shall be checked periodically by the HVS to check the validity and accuracy of the results measured by the direct reading method.

- 3.5.6 According to the Project EM&A Manual, wind data monitoring equipment shall also be provided and set up for logging wind speed and wind direction near the dust monitoring locations. The equipment installation location shall be proposed by the ET and agreed with the IEC. For installation and operation of wind data monitoring equipment, the following points shall be observed:
- (i) the wind sensors should be installed on masts at an elevated level 10 m above ground so that they are clear of obstructions or turbulence caused by the buildings;
 - (ii) the wind data should be captured by a data logger to be down-loaded for processing at least once a month;
 - (iii) the wind data monitoring equipment should be re-calibrated at least once every six months; and
 - (iv) wind direction should be divided into 16 sectors of 22.5 degrees each.

3.6 DERIVATION OF ACTION/LIMIT (A/L) LEVELS

- 3.6.1 The baseline monitoring results formed the basis for determining the air quality criteria for the impact monitoring. The ET shall compare the impact monitoring results with air quality criteria set up for 24-hour TSP and 1-hour TSP. Based on results of the approved Baseline Monitoring Report of HyD Contract HY/2012/08, the Action and Limit Levels for impact dust monitoring are shown in *Tables 3-3*.

Table 3-3 Action and Limit Levels for Impact Air Quality Monitoring

Air Quality Monitoring Stations	24-hour TSP ($\mu\text{g}/\text{m}^3$)		1-hour TSP ($\mu\text{g}/\text{m}^3$)	
	Action Level	Limit Level	Action Level	Limit Level
ASR1	213	260	331	500
ASR5	238	260	340	500
AQMS1	213	260	335	500
ASR6	238	260	338	500
ASR10	214	260	337	500

- 3.6.2 Should non-compliance of the environmental quality criteria occurs, remedial actions will be triggered according to the Event and Action Plan which presented in *Appendix F*.

3.7 OTHER ENVIRONMENTAL ASPECTS

Noise

- 3.7.1 The TM-CLKL EIA study stated that no existing noise sensitive receiver (NSR) was identified within the Study Area at Tuen Mun. Therefore, no noise monitoring is required for the construction phase of the Contract.
- 3.7.2 Regular site inspections and audits will be carried out during the construction phase in order to confirm the construction works under the Contract comply with the regulatory noise requirements.

Water Quality

- 3.7.3 No marine works will be undertaken under the Contract. Therefore, no water quality monitoring is required for the construction phase of the Contract.

Ecology

- 3.7.4 No marine works will be undertaken under the Contract and generated marine ecological impact, no dolphin monitoring is required for the construction phase of the Contract.

- 3.7.5 During construction phase, the ET will perform Pitcher Plants inspection at least once every week to report the growth condition and protection measures.

Landscape and Visual

- 3.7.6 Measures to mitigate landscape and visual impact during construction should be checked and monitored by a Registered Landscape Architect to ensure compliance with the intended aims of the mitigation measures in accordance with the EM&A Manual.

Cultural Heritage

- 3.7.7 Grave G1 as a heritage resource is situated near the proposed toll plaza in Tuen Mun. Site inspections should be undertaken at least once per week throughout the construction period to ensure compliance with the intended aims of recommended mitigation measures.

Landfill Gas

- 3.7.8 During EIA study, landfill gas hazards are likely to be generated from the Pillar Point Valley (PPV) Landfill. Landfill gas monitoring is recommended during construction of the Contract to ensure the works area is free of landfill gas before the worker entered the concerned area.

4 AIR QUALITY MONITORING

4.1 GENERAL

4.1.1 The air quality impact monitoring and enhanced Total Suspended Particulates (TSP) level monitoring at five proposed locations are currently carried out by the ET of Contract HY/2012/08. Sharing of impact air quality monitoring data between HY/2012/08 and HY/2013/12 is agreed by all relevant parties. The Contract is not required to conduct its own dust monitoring exercise until the Contract HY/2012/08 ends.

4.2 SUMMARY OF MONITORING RESULTS

4.2.1 In the Reporting Period, 1- hour and 24-hour TSP monitoring at the five proposed locations are continued to perform by the ET of Contract HY/2012/08. Therefore, no air quality monitoring was conducted by the ET of Contract HY/2013/12. Details information of air quality monitoring results could be referred to the Monthly EM&A Reports of the Contract HY /2012 /08 (*February 2015, March 2015 and April 2015*).

4.3 ACTION AND LIMIT (A/L) LEVELS EXCEEDANCE

4.3.1 According to the air quality monitoring result provided by Contract HY/2012/08, no exceedances in 1-hour and 24-hour TSP were recorded in the Reporting Period. No Notification on Exceedances (NOEs) was issued by the ET of Contract HY/2012/08. The summary of air quality exceedance in the Reporting Period is shown in *Table 4-1*.

Table 4-1 Summary of Air Quality Monitoring Exceedance

Date of Exceedance	Monitoring Station	Air Quality Parameter	Result	Exceed
NA	NA	NA	--	--

4.4 AIR QUALITY EXCEEDANCE INVESTIGATION

4.4.1 No investigation for exceedance is required for the Reporting Period.

5 ECOLOGY MONITORING

5.1 GENERAL

5.1.1 According to the EM&A Manual requirements, regularly inspection for Pitcher Plants at least once every week to report its growth and protection measure situation shall be conducted during construction period.

5.2 PITCHER PLANTS INSPECTION

5.2.1 In the Reporting Period, inspections for implementation status of mitigation measures for the Pitcher Plants were carried out by the ET on 3rd, 10th, 17th and 24th February 2015, 3rd, 10th, 17th, 24th and 31st March 2015, 8th, 14th, 21st and 28th April 2015. Trial transplantation of pitcher plant from the nursery site to final receptor site was carried out on 15 April 2015 and a total of 5% of pitcher plant was transplanted.

5.2.2 During weekly site inspection, the transplanted Pitcher Plants at the nursery zone were overall in fair to poor condition. The scaffold structure and chain link fence of protection were implemented properly, no repair or maintenance was required. Moreover, no construction activities were conducted nearby the nursery zone.

5.2.3 Random checking was undertaken for the protected areas Zones 8, 9 and 10 during weekly site inspection. During each occasion of site inspection, no construction activities were found to be conducted nearby the protected areas of Pitcher Plants. The chain link fence provided at the protected areas was properly erected. The growths of Pitcher Plants as retained at the protected areas were in fair to poor condition.

6 CULTURAL HERITAGE

6.1 GENERAL

6.1.1 According to the EM&A Manual requirements, regular inspection for heritage resource, Grave G1, shall be audited by the ET at least once every week to ensure recommended mitigation measures implemented during construction period. The aim of the survey is to prevent any possible damage to the grave and to ensure the proposed mitigation measures are implemented. The broad scope of the audit will involve supervision of the following:

- Non-contact effects of the engineering works, such as vibration from pneumatic drills which could cause damage, such as foundation or wall cracks and loosening of tiles or fixtures; and
- Contact between the historic structures and equipment and materials associated with the engineering works.

6.1.2 Specifically, the monitoring programme will entail the following tasks:

- The extent of the agreed works areas should be regularly checked during the construction phase to ensure the buffer is being maintained; and
- Ensure no stockpiling or equipment storage is affecting the structure.

6.1.3 In the event of non-compliance the responsibilities of the relevant parties is detailed in the Event/Action Plan in [Appendix F](#).

6.2 GRAVE INSPECTION

6.2.1 In the Reporting Period, site inspection for the Grave G1 was undertaken on **3rd, 10th, 17th and 24th February 2015, 3rd, 10th, 17th, 24th and 31st March 2015, 8th, 14th, 21st and 28th April 2015**. During site inspection, buffer zone between the working area and the Grave was maintained and no construction material or equipment was stored nearby the Grave.

6.2.2 Mitigation measures undertaken by the Contractor has fully implemented the EM&A Manual requirements.

7 LANDSCAPE AND VISUAL

7.1 GENERAL

7.1.1 According to EM&A Manual requirements, monitoring of Contractor's operations during construction period to report on Contractor's compliance should be carried out on weekly basis. Measure to mitigate landscape and visual impact during construction should be checked and monitored by a Registered Landscape Architect to ensure compliance with the intended aims of the mitigation measures. Moreover, the progress of the engineering works shall be regularly reviewed on site to identify the earliest practical opportunities for the landscape works to be undertaken.

7.2 LANDSCAPE AND VISUAL INSPECTION

7.2.1 In the Reporting Period, site inspection for landscape and visual mitigation measures was undertaken by the Registered Landscape Architect on **6th, 13th, 17th and 27th February 2015, 6th, 13th, 20th and 27th March 2015, 2nd, 10th, 17th, 24th and 30th April 2015.**

7.2.2 Most of the landscape works such as planting was not yet commenced. The detailed inspection checklists can be referred to the Monthly EM&A Reports (February 2015, March 2015 and April 2015) of the contract.

8 LANDFILL GAS HAZARD MONITORING

8.1 GENERAL

- 8.1.1 During EIA study, landfill gas hazards are likely to be generated from the Pillar Point Valley (PPV) Landfill. Hence, regular landfill gas monitoring is recommended during construction of the proposed toll plaza.
- 8.1.2 During construction, a Safety Officer should be appointed to carry out the monitoring works. The monitoring frequency and areas to be monitored should be set down prior to commencement of ground-works either by the Safety Officer or an approved and appropriated qualified person. The routine monitoring should be carried out in all excavations, manholes, chambers, relocation of monitoring wells and any other confined spaces that may have been created. All measurements in excavations should be made with the extended monitoring tube located not more than 10 mm from the exposed ground surface. Monitoring should be performed properly to make sure that the area is free of landfill gas before any man enters in the area.
- 8.1.3 For excavations deeper than 1m, measurements should be carried out:
- at the ground surface before excavation commences;
 - immediately before any worker enters the excavation;
 - at the beginning of each working day for the entire period the excavation remains open; and
 - periodically through the working day whilst workers are in the excavation.
- 8.1.4 For excavations between 300mm and 1m deep, measurements should be carried out:
- directly after the excavation has been completed; and
 - periodically whilst the excavation remains open
- 8.1.5 For excavations less than 300mm deep, monitoring may be omitted, at the discretion of the Safety Officer or other appropriately qualified person.
- 8.1.6 To ensure the accuracy of the monitoring data, zeroing of the gas analyser shall be undertaken at the start of each day's monitoring. As part of the QA/QC, calibration of the gas analyser shall be conducted at least once every two weeks according to the specification of the manufacturer's operation manual.

8.2 LANDFILL GAS MONITORING RESULT

- 8.2.1 In the Reporting Period, landfill gas monitoring was conducted at the construction of Retaining Wall B and Retaining Wall F and the locations are illustrated in [Appendix E](#). A BIOGAS 5000 gas analysis was used for the landfill gas monitoring.
- 8.2.2 There were total **68** workings days monitoring were carried by the Safety Officer or an approved and qualified persons in this reporting period. **Table 8-1** is summarized landfill gas measurement results. Moreover, graphical plot are attached in [Appendix G](#).

Table 8-1 Summary of Landfill Gas Measurement Results in Reporting Period

Landfill Gas Parameter	Action Level	Limit Level	Detectable at Retaining Wall B		Detectable at Retaining Wall F	
			Min	Max	Min	Max
Methane	>10% LEL (>0.5% v/v)	>20% LEL (>1% v/v)	0%	0.2%	0%	0.2%
Oxygen	<19%	<18%	21.0%	21.2%	21.0%	21.2%
Carbon Dioxide	>0.5%	>1.5%	0%	0.2%	0%	0.2%

- 8.2.3 The measurement results shown that slightly methane concentration was detected and all oxygen concentration were over 21.0% and Carbon Dioxide was between 0 and 0.2 %. No corrective action was required accordingly.

9 WASTE MANAGEMENT

9.1 GENERAL WASTE MANAGEMENT

9.1.1 Waste management was carried out by an on-site Environmental Officer or an Environmental Supervisor from time to time.

9.2 RECORDS OF WASTE QUANTITIES

9.2.1 All types of waste arising from the construction work are classified into the following:

- Construction & Demolition (C&D) Material;
- Chemical Waste;
- General Refuse; and
- Excavated Soil.

9.2.2 Whenever possible, materials were reused on-site as far as practicable. The quantities of waste for disposal in the Reporting Period are summarized in *Tables 9-1* and *9-2* and the Waste Flow Table is presented in *Appendix H*.

Table 9-1 Summary of Quantities of Inert C&D Materials

Type of Waste	Quantity			Disposal Location
	Feb 15	Mar 15	Apr 15	
Reused in this Project (Inert) (in '000 m ³)	24.411	13.473	8.06	-
Reused in other Projects (Inert) (in '000 m ³)	25.313	26.648	11.209	HY/2012/08
Disposal as Public Fill (Inert) (in '000 m ³)	0.629	2.042	9.765	Tuen Mun Area 38

Table 9-2 Summary of Quantities of C&D Wastes

Type of Waste	Quantity			Disposal Location
	Feb 15	Mar 15	Apr 15	
Recycled Metal (in '000kg)	0	0	0	-
Recycled Paper / Cardboard Packing (in '000kg)	0	0.05	0	-
Recycled Plastic (in '000kg)	0	0	0	-
Chemical Wastes (in '000kg)	0	0	0	-
General Refuses (in '000m ³)	0.01	0.01	0.003	WENT

9.2.3 To control the site performance on waste management, the Contractor shall ensure that all solid and liquid waste management works are fully in compliance with the relevant license/permit requirements, such as the effluent discharge license and the chemical waste producer registration. The Contractor is also reminded to implement the recommended environmental mitigation measures according to the Environmental Monitoring and Audit Manual.

10 SITE INSPECTIONS**10.1 REQUIREMENTS**

10.1.1 According to the approved EM&A Manual, the environmental site inspection shall be formulation by ET Leader. Weekly environmental site inspections should carry out to confirm the environmental performance.

10.1.2 During the Reporting Period, **14** events of the joint site inspections were undertaken to evaluate the site environmental performance. The summaries of the findings during site inspection are presented in *Tables 10-1 and 10-2*.

Table 10-1 Site Observations for the Contract for the Reporting Period

Date	Findings / Deficiencies	Follow-Up Status
3 Feb 2015	<ul style="list-style-type: none"> • Stockpile without cover was observed. Dust mitigation measures should be applied to minimize dust generation. • General refuse scattered on site was observed. The contractor was reminded to clean and provide more rubbish bin on site. • As a reminder, tree protection zone should be set up for the retained tree on site to prevent cause any damage due site activities. 	<ul style="list-style-type: none"> • Stockpile without cover was removed before site inspection on 10 February 2015. • General refuse scattered on site has cleared during site inspection on 10 February 2015. • Not required for reminder.
10 Feb 2015	<ul style="list-style-type: none"> • General refuse placing outside the waste skip was observed. The contractor was reminded all general refuse should be disposal into proper containers to maintain the site clean and tidy. • The contractor was reminded that the sump pit should be regularly cleanup to maintain the drainage system function properly. • Mitigation measures for dust and noise should be implemented for the works area near Lung Mun Road to reduce public impact. 	<p>2. General refuse as placed outside the waste skip has been properly disposal.</p> <ul style="list-style-type: none"> • Not required for reminder. • Not required for reminder.
17 Feb 2015	<ul style="list-style-type: none"> • Free standing chemical container without drip tray was observed. The contractor was reminded to provide drip tray underneath. • During the dry season, dust mitigation measures should be implemented to reduce dust impact. 	<ul style="list-style-type: none"> • The free standing chemical container without drip tray has removed during site inspection on 24 February 2015. • Not required for reminder.
24 Feb 2015	<ul style="list-style-type: none"> • As a reminder, dust mitigation measures should be implemented for breaking/excavating activities to reduce construction dust impact. • As a reminder, stagnant water cumulated inside the u-channel or gully should be drained away to prevent mosquito breeding. 	<ul style="list-style-type: none"> • Not required for reminder. • Not required for reminder.

Date	Findings / Deficiencies	Follow-Up Status
3 March 2015	<ul style="list-style-type: none"> • Dusty haul road was observed near the retaining wall works area. The contractor should provide water spraying at those area to minimize dust generation and make sure the frequency of water spraying comply with the EP requirement. • Ponding water cumulated in the site was observed. To prevent mosquito breeding, the contractor was reminded to cleanup. • It was reminded that dust mitigation measures should implement to reduce construction dust emission during rock breaking and excavating activities at the dry season. 	<ul style="list-style-type: none"> • Water spraying of dust mitigation measures has been provided and no dust emission observed was generated from the vehicles passing through haul road. • Ponding water has been removed before site inspection on 10 March 2015. • Not required for reminder.
10 March 2015	<ul style="list-style-type: none"> • Drilling work was observed to conduct near the public areas, extra barrier or hoarding should be provided to reduce noise impact. • Mud/soil trails were observed at the site exit. The contractor should provide wheel washing facilities at all construction site exit to make sure all the vehicles leaving from site is clean. • It was reminded that the contractor should display all the EP and discharge license at all the site entrance. • As a reminder, dust mitigation measures should be implemented to minimize dust impact as came form the dust materials stockpile, haul roads and construction activities during the dry and windy season 	<ul style="list-style-type: none"> • During site inspection on 17 March 2015, drill rig has relocated far from the public area. No any noisy construction activities observed to conduct near the public area. • No mud/soil trails were observed at the site exit during site inspection 17 March 2015. The deficiency has rectified. • Not required for reminder. • Not required for reminder.
17 March 2015	<ul style="list-style-type: none"> • No vaild EP and discharge license was displayed at the site entrance. The contractor strongly reminded that the EP and all relevant licenses shall display at site entrance. • Stockpile without cover was observed. The contractor shall provide proper dust mitigation measures to reduce dust generation. • Dust generation observed during loading and unloading from truck. Water spraying shall be provide to reduce dust generation. 	<ul style="list-style-type: none"> • Vaild EP and discharge license has displayed at site entrance • The stockpile has removed and no dust generation was observed in this area during the inspection on 31 March 2015. • Dust generation during loading and unload was not observed. Addition, Water spraying to reduce dust generation from haul road was observed during site inspection 24 March 2015.

Date	Findings / Deficiencies	Follow-Up Status
	<ul style="list-style-type: none"> Earth bund or temporary drainage system is reminded installation to prevent the surface run-off damage the nursery zone. 	<ul style="list-style-type: none"> Temporary barriers has provided at the site boundary.
24 March 2015	<ul style="list-style-type: none"> Muddy water observed near site boundary. Temporary drain channel should be provide to divert the muddy surface run-off to the de-silting facilities and prevent mosquito breeding Oil drum without drip tray was observed. The contractor should provide drip tray underneath. It was reminded that stockpiles located within the site area should provide proper dust mitigation measures to prevent dust generation. 	<ul style="list-style-type: none"> Temporary barrier was provided at the site boundary to prevent surface runoff flow out of site boundary. Underneath oil drum, drip tray has provided to prevent land contamination. Not required for reminder.
31 March 2015	<ul style="list-style-type: none"> No environmental issue was observed during the site inspection 	<ul style="list-style-type: none"> NA
8 April 2015	<ul style="list-style-type: none"> Oil leakage from backhoe was observed. The contractor should clean up the contaminate area and provide maintenance to the plant to prevent further leakage Chemical containers without drip tray was observed. The contractor should provide drip tray underneath. Broken tarpaulin covered on the stockpile was observed. The contractor was reminded to replace the broken tarpaulin sheets to minimize dust generation 	<ul style="list-style-type: none"> The leakage excavator has been fixed and no leakage observed from the excavator or the other plants Chemical containers without drip tray was removed. Not required for reminder.
14 April 2015	<ul style="list-style-type: none"> Chemical containers without drip tray was observed. The contractor should provide drip tray underneath. Turbidity water discharged from site was observed. The contractor should treat the water before discharge from site. To remind that Stagnant water cumulated on site should be cleanup to prevent mosquito breeding. To remind that The updated EP and license should be display at all site entrance. 	<ul style="list-style-type: none"> Chemical containers without drip tray was removed No turbidity water discharged from site was observed. Not required for reminder. Not required for reminder.

Date	Findings / Deficiencies	Follow-Up Status
21 April 2015	<ul style="list-style-type: none"> The traces of soil and mud were observed at the site exit near Firestation. The contractor was requested to clean to maintain the site exit clean and tidy. At Portion X-2, earth bund with tarpaulin should be provide for the stockpile prevent soil loss to clog up nearby gully. 	<ul style="list-style-type: none"> All the site exits has been cleaned regularly. No soil and mud traces were observed at site exits. Tarpaulin was provided for stockpiles which located on site.
28 April 2015	<ul style="list-style-type: none"> Diesel oil drums underneath without drip tray were observed at the work platform +23mPD. The contractor should provide drip tray to prevent land contamination. Dust emission observed from the breaking and drilling work. The contractor should provide mitigation measures to reduce dust generation. Stockpile without cover was observed. The contractor should provide mitigation measures to reduce dust impact. 	<ul style="list-style-type: none"> A drip tray has provided underneath the diesel oil drums. Water spray of dust mitigation measures has provided during the breaking and drilling work Tarpaulin was provided for stockpiles which located on site.

Table 10-2 Summary of Reminders/Observations of Site Inspection

Reporting Period	Date of site inspection	Nos. of findings / reminders	Follow-Up Status
February 2015	3 rd , 10 th , 17 th , and 24 th February 2015	10	Completed
March 2015	3 rd , 10 th , 17 th , 24 th and 31 st March 2015	14	Completed
April 2015	8 th , 14 th , 21 st and 28 th April 2015	12	Completed

10.1.3 In the Reporting Period, no non-compliance was recorded, however, 36 observations/ reminders were recorded during the site inspections. Minor deficiencies found in the weekly site inspection were in general rectified within the specified deadlines. The environmental performance of the Project was therefore considered satisfactory.

10.1.4 In the upcoming wet season, muddy water or other water pollutants from site surface runoff into the public areas will be key environment issue. Water quality mitigation measures to prevent surface runoff into public areas should be paid on special attention.

10.1.5 For waste management, good practice for daily housekeeping is reminded. Furthermore, clean-up frequency of the waste skips and wastewater treatment system should be increased to ensure these facilities functional and effective.

11 ENVIRONMENTAL COMPLAINT AND NON-COMPLIANCE**11.1 ENVIRONMENTAL COMPLAINT, SUMMONS AND PROSECUTION**

11.1.1 For the Contract, no environmental complaint, summons and prosecution were received in the Reporting Period. Moreover, no exceedances of the environmental performance limit (Action and Limit Level) were recorded. The statistical summary table of environmental exceedance, complaint, summons and prosecution is presented in *Tables 11-1, 11-2, 11-3 and 11-4*.

Table 11-1 Statistical Summary of Environmental Exceedance

Reporting Period	Environmental Aspect / Parameter	Environmental Performance	Event Exceedance		
			Reporting Period	Previous Periods	Cumulative
1 February 2015 – 30 April 2015	Air Quality - 1-hr TSP	Action Level	0	4	4
		Limit Level	0	0	0
	Air Quality - 24-hr TSP	Action Level	0	0	0
		Limit Level	0	0	0

Table 11-2 Statistical Summary of Environmental Complaints

Reporting Period	Environmental Complaint Statistics		
	Frequency	Cumulative	Complaint Nature
23 October 2014 – 31 January 2015	0	0	NA
1 February 2015 – 30 April 2015	0	0	NA

Table 11-3 Statistical Summary of Environmental Summons

Reporting Period	Environmental Complaint Statistics		
	Frequency	Cumulative	Complaint Nature
23 October 2014 – 31 January 2015	0	0	NA
1 February 2015 – 30 April 2015	0	0	NA

Table 11-4 Statistical Summary of Environmental Prosecution

Reporting Period	Environmental Complaint Statistics		
	Frequency	Cumulative	Complaint Nature
23 October 2014 – 31 January 2015	0	0	NA
1 February 2015 – 30 April 2015	0	0	NA

11.1.2 In the Reporting Period, no warning letter related to environmental issue was received from the EPD or CEDD.

12 IMPLEMENTATION STATUS OF MITIGATION MEASURES

12.1 GENERAL REQUIREMENTS

12.1.1 The environmental mitigation measures that recommended in the Environmental Mitigation and Enhancement Measures Implementation Schedule (EMIS) for in the Project EM&A Manual covered the issues of air quality, cultural heritage, ecology, landfill gas hazard, landscape & visual, noise, water and waste. The updated EMIS for the Contract is shown in [Appendix I](#).

12.1.2 The Contractor shall implement the required environmental mitigation measures according to the EM&A Manual as subject to the site condition. The environmental mitigation measures implemented by the Contract in this Reporting Period are summarized in [Table 12-1](#) and [Appendix I](#).

Table 12-1 Environmental Mitigation Measures

Issues	Environmental Mitigation Measures
Air Quality	<ul style="list-style-type: none"> • Maintain damp / wet surface on access road • Keep slow speed in the sites • All vehicles must use wheel washing facility before off site • Sprayed water during rock breaking works • During transportation by truck, materials loaded lower than the side and tail boards, and covered before transport • Compacted all soil stockpiles • Part of the exposed slopes covered geotextile net
Cultural Heritage	<ul style="list-style-type: none"> • Set a buffer zone between the working area and the Grave • All construction materials and equipment store far from the Grave • Inspection the Grave to ensure provision mitigation measures effective
Ecology	<ul style="list-style-type: none"> • Wire fencing provided for temporary protect Pitcher Plants • Undertake weekly inspection of Pitcher Plants
Landfill Gas Hazard	<ul style="list-style-type: none"> • Landfill Gas measurement undertake during trench excavation
Water Quality	<ul style="list-style-type: none"> • Temporary drainage system provide for surface runoff prevent discharge to public area • Wastewater to be treated by sedimentation tank before discharge.
Noise	<ul style="list-style-type: none"> • Restrain operation time of plants from 07:00 to 19:00 on any working day except for Public Holiday and Sunday. • Keep good maintenance of plants • The noisy plants or works provide mobile noise barriers • Shut down the plants when not in used
Waste and Chemical Management	<ul style="list-style-type: none"> • On-site sorting prior to disposal • Follow requirements and procedures of the “Trip-ticket System” • Predict required quantity of concrete accurately • Collect the unused fresh concrete at designated locations in the sites for subsequent disposal
General	<ul style="list-style-type: none"> • The site was generally kept tidy and clean.

13 CONCLUSIONS AND RECOMMENDATIONS

13.1 CONCLUSIONS


- 13.1.1 This is 2nd Quarterly EM&A report presenting the monitoring results and inspection findings for the Reporting Period from **1 February 2015 to 30 April 2015**.
- 13.1.2 No air quality monitoring including 1-hour and 24-hour TSP exceedance was recorded in the Reporting Period. Although air quality monitoring result complied with the performance criteria, the Contractor was reminded to fully implement the dust control measures.
- 13.1.3 In this Reporting Period, no noise complaint was received by RE, the Contractor, ENPO or HyD. No Action Level exceedances were triggered and no NOE or the associated corrective actions were therefore issued.
- 13.1.4 Site inspection for landscape and visual was conducted on weekly basis by the Landscape Architect to ensure if the existing condition compliance with the intended aims of the mitigation measures. Most of the landscape works such as planting was not yet commenced.
- 13.1.5 Site inspection was performed for the transplanted Pitcher Plants in the nursery site and protected Zones 8 to 10. The transplanted Pitcher Plant in nursery site was protected by the scaffold structure which surrounded by chain link fencing and the protected Pitcher Plants in Zones 8 to 10 were fenced off by chain link fencing. The condition of the transplanted pitcher plant was in fair to poor condition. No construction activities were found to conduct nearby the nursery site and protection zones.
- 13.1.6 Moreover, trial transplantation of pitcher plant from the nursery site to final receptor site was carried out on 15 April 2015 and a total of 5% of pitcher plant was transplanted. The condition of the transplanted pitcher plant will be kept in view.
- 13.1.7 Landfill gas monitoring was conducted at the construction of Retaining Wall B and Retaining Wall F by the Safety Officer. The monitoring results shown no exceedances were triggered.
- 13.1.8 No documented a complaint, notification of summons or successful prosecution is received by the Contract.
- 13.1.9 During the Reporting Period, **13** events of the joint site inspections were undertaken to evaluate the site environmental performance. No adverse environmental impacts were observed during the weekly site inspection and environmental audit of the Reporting Period, indicating the implemented mitigation measures for air quality, construction noise and water quality were effective. Minor deficiencies found in the weekly site inspection were in general rectified within the specified deadlines. The environmental performance of the Project was therefore considered satisfactory.
- 13.1.10 No documented a complaint, notification of summons or successful prosecution is received by the Contract.

13.2 RECOMMENDATIONS

- 13.2.1 During wet season, muddy water or other water pollutants from site surface runoff into the public areas will be key environment issue. Water quality mitigation measures prevent surface runoff into the public areas should be paid on special attention.
- 13.2.2 Furthermore, air quality mitigation measures such as watering of site area for 12 times per day and covering of exposed slopes should be implemented to reduce construction dust impact as recommended in the EMIS.
- 13.2.3 Moreover, good practice for daily housekeeping is reminded. Addition, clean-up frequency of the waste skips and wastewater treatment system should be increased to ensure these facilities functional and effective.

Appendix A

Layout plan of the Project

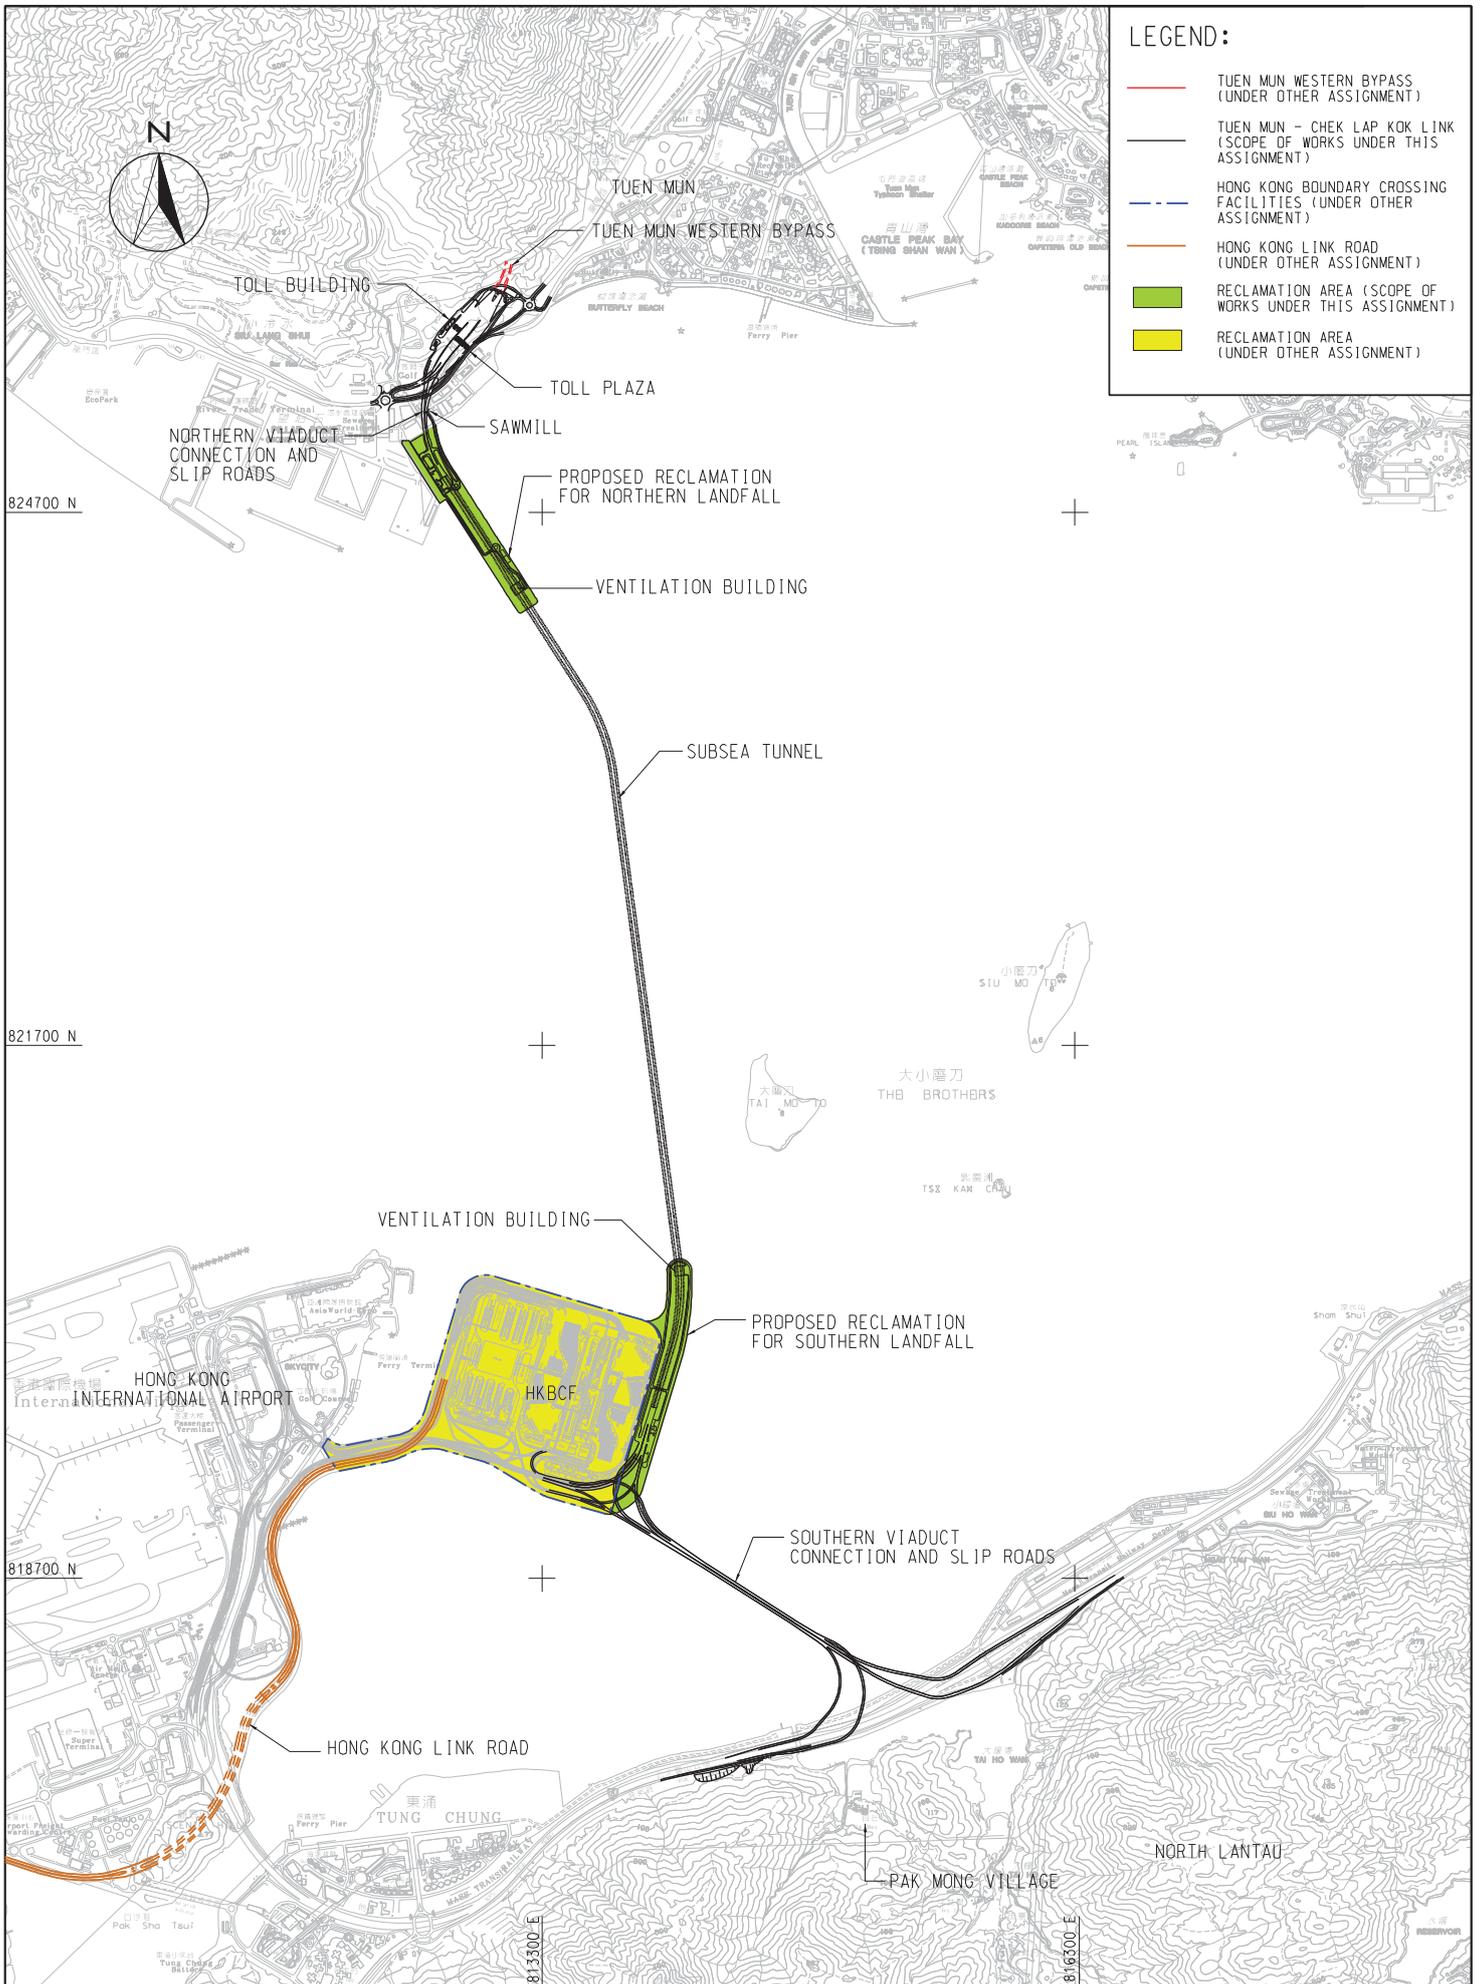

LEGEND:

- TUEN MUN WESTERN BYPASS (UNDER OTHER ASSIGNMENT)
- TUEN MUN - CHEK LAP KOK LINK (SCOPE OF WORKS UNDER THIS ASSIGNMENT)
- HONG KONG BOUNDARY CROSSING FACILITIES (UNDER OTHER ASSIGNMENT)
- HONG KONG LINK ROAD (UNDER OTHER ASSIGNMENT)
- RECLAMATION AREA (SCOPE OF WORKS UNDER THIS ASSIGNMENT)
- RECLAMATION AREA (UNDER OTHER ASSIGNMENT)

PROJECT NO. 60044963

AECOM



AGREEMENT NO. CE 52/2007(HY)
 TUEN MUN - CHEK LAP KOK LINK - INVESTIGATION
 GENERAL LAYOUT OF TM-CLKL

SCALE	A3 1:30000	DATE	JUL. 2009
CHECK	--	DRAWN	WYP
JOB NO.	60044963	DRAWING NO.	Fig 2.1
		REV	A

Appendix B

Layout plan of the Contract

Project Management Initials: Designer: PI Checked: ALCF Approved: CWN ISO A1 594mm x 841mm
 Plot File by: LINDO 2014/05/19 PATH: P:\Projects\60240249\DRAWING\CONTRACT\C3\1005C3_05E1.dgn

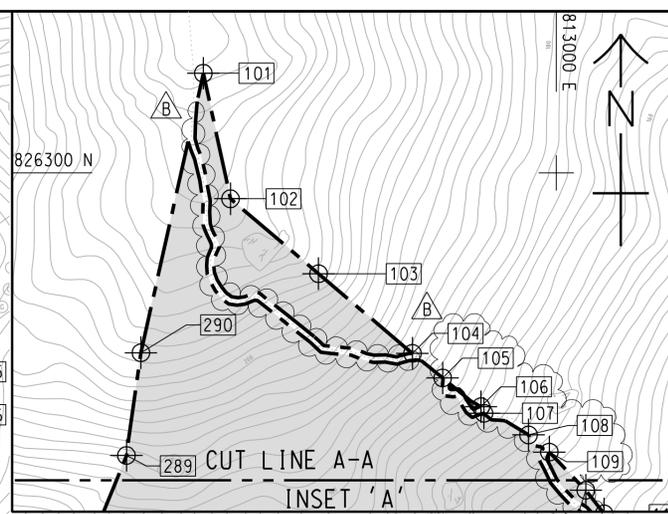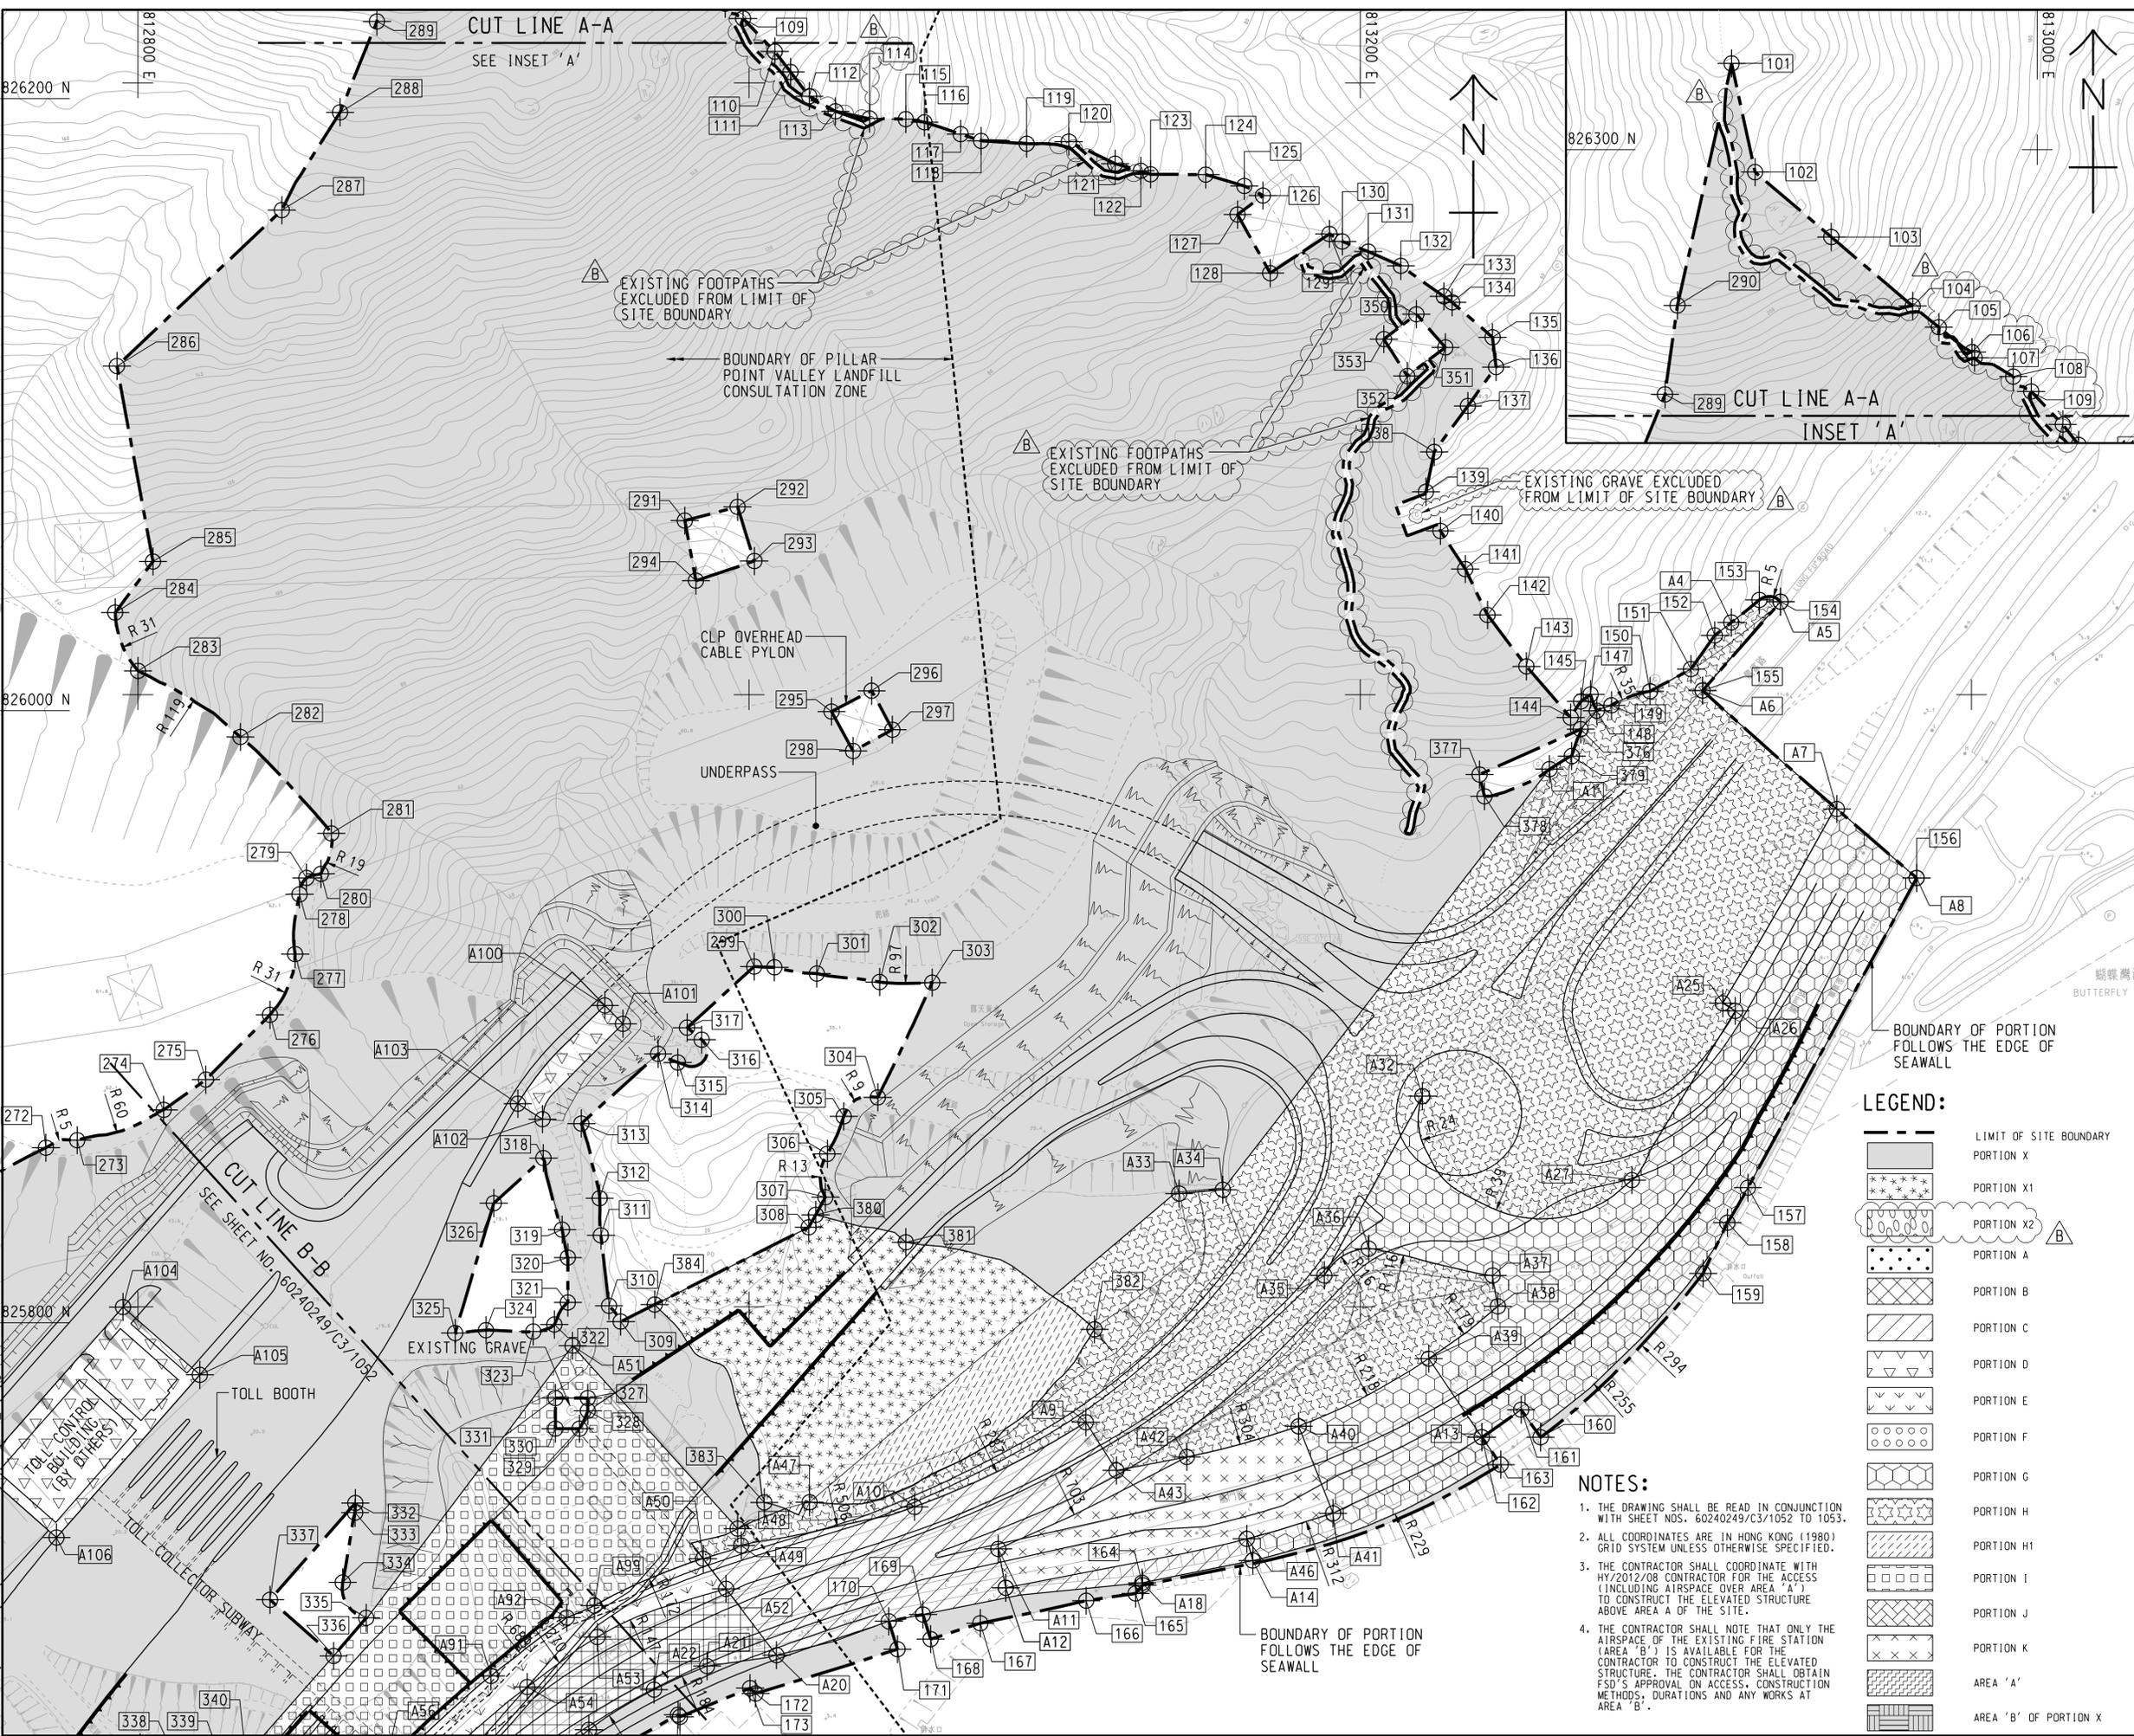

LEGEND:

	LIMIT OF SITE BOUNDARY
	PORTION X
	PORTION X1
	PORTION X2
	PORTION A
	PORTION B
	PORTION C
	PORTION D
	PORTION E
	PORTION F
	PORTION G
	PORTION H
	PORTION H1
	PORTION I
	PORTION J
	PORTION K
	AREA 'A'
	AREA 'B' OF PORTION X

NOTES:

1. THE DRAWING SHALL BE READ IN CONJUNCTION WITH SHEET NOS. 60240249/C3/1052 TO 1053.
2. ALL COORDINATES ARE IN HONG KONG (1980) GRID SYSTEM UNLESS OTHERWISE SPECIFIED.
3. THE CONTRACTOR SHALL COORDINATE WITH HY/2012/08 CONTRACTOR FOR THE ACCESS (INCLUDING AIRSPACE OVER AREA 'A') TO CONSTRUCT THE ELEVATED STRUCTURE ABOVE AREA A OF THE SITE.
4. THE CONTRACTOR SHALL NOTE THAT ONLY THE AIRSPACE OF THE EXISTING FIRE STATION (AREA 'B') IS AVAILABLE FOR THE CONTRACTOR TO CONSTRUCT THE ELEVATED STRUCTURE. THE CONTRACTOR SHALL OBTAIN FSD'S APPROVAL ON ACCESS, CONSTRUCTION METHODS, DURATIONS AND ANY WORKS AT AREA 'B'.

AECOM

PROJECT
項目
TUEN MUN - CHEK LAP KOK LINK

CONTRACT TITLE
TUEN MUN - CHEK LAP KOK LINK - NORTHERN CONNECTION TOLL PLAZA AND ASSOCIATED WORKS

CLIENT
業主
路政署
HIGHWAYS DEPARTMENT
港務大樓香港工程管理局
Hong Kong - Zhuhai - Macao Bridge
Hong Kong Project Management Office

CONSULTANT
工程顧問公司
AECOM Asia Company Ltd.
www.aecom.com

SUB-CONSULTANTS
分判工程顧問公司

ISSUE/REVISION
修訂


I/R	DATE	DESCRIPTION	CHK.
B	MAR. 14	TENDER ADDENDUM NO. 2	CWN
A	FEB. 14	TENDER ADDENDUM NO. 1	CWN
-	JAN. 14	TENDER DRAWING	CWN

STATUS
階段

SCALE
比例
A1 1:1000

DIMENSION UNIT
尺寸單位
METRES

KEY PLAN
索引圖
1:50000



PROJECT NO.
項目編號
60240249

CONTRACT NO.
合約編號
HY/2013/12

SHEET TITLE
圖紙名稱
PORTIONS OF SITE AND SITE BOUNDARY SETTING OUT PLAN


SHEET NUMBER
圖紙編號
60240249/C3/1051B

SHEET 1 OF 3

This drawing has been prepared for the use of AECOM's client. It may not be used, modified, reproduced or relied upon by third parties, except as agreed by AECOM or as required by law. AECOM accepts no responsibility, and denies any liability whatsoever, to any party that uses or relies on this drawing without AECOM's express written consent. All measurements must be obtained from the stated dimensions.

SETTING OUT COORDINATES OF SITE BOUNDARY

SETTING OUT POINT	COORDINATES	
	EASTING	NORTHING
101	812900.000	826328.165
102	812907.687	826292.657
103	812932.657	826271.462
104	812959.255	826248.939
105	812967.809	826241.968
106	812978.687	826233.842
107	812979.543	826231.975
108	812992.172	826225.845
109	812998.046	826220.987
110	813008.394	826210.180
111	813013.551	826203.523
112	813019.680	826195.595
113	813028.256	826190.669
114	813039.418	826188.327
115	813051.242	826188.103
116	813057.382	826187.067
117	813069.235	826183.229
118	813075.914	826180.992
119	813090.821	826180.083
120	813104.589	826180.783
121	813119.757	826173.560
122	813128.170	826171.228
123	813131.357	826170.082
124	813149.404	826169.990
125	813162.041	826166.283
126	813168.123	826163.136
127	813159.825	826156.924
128	813170.488	826137.774
129	813189.868	826150.598
130	813194.079	826148.129

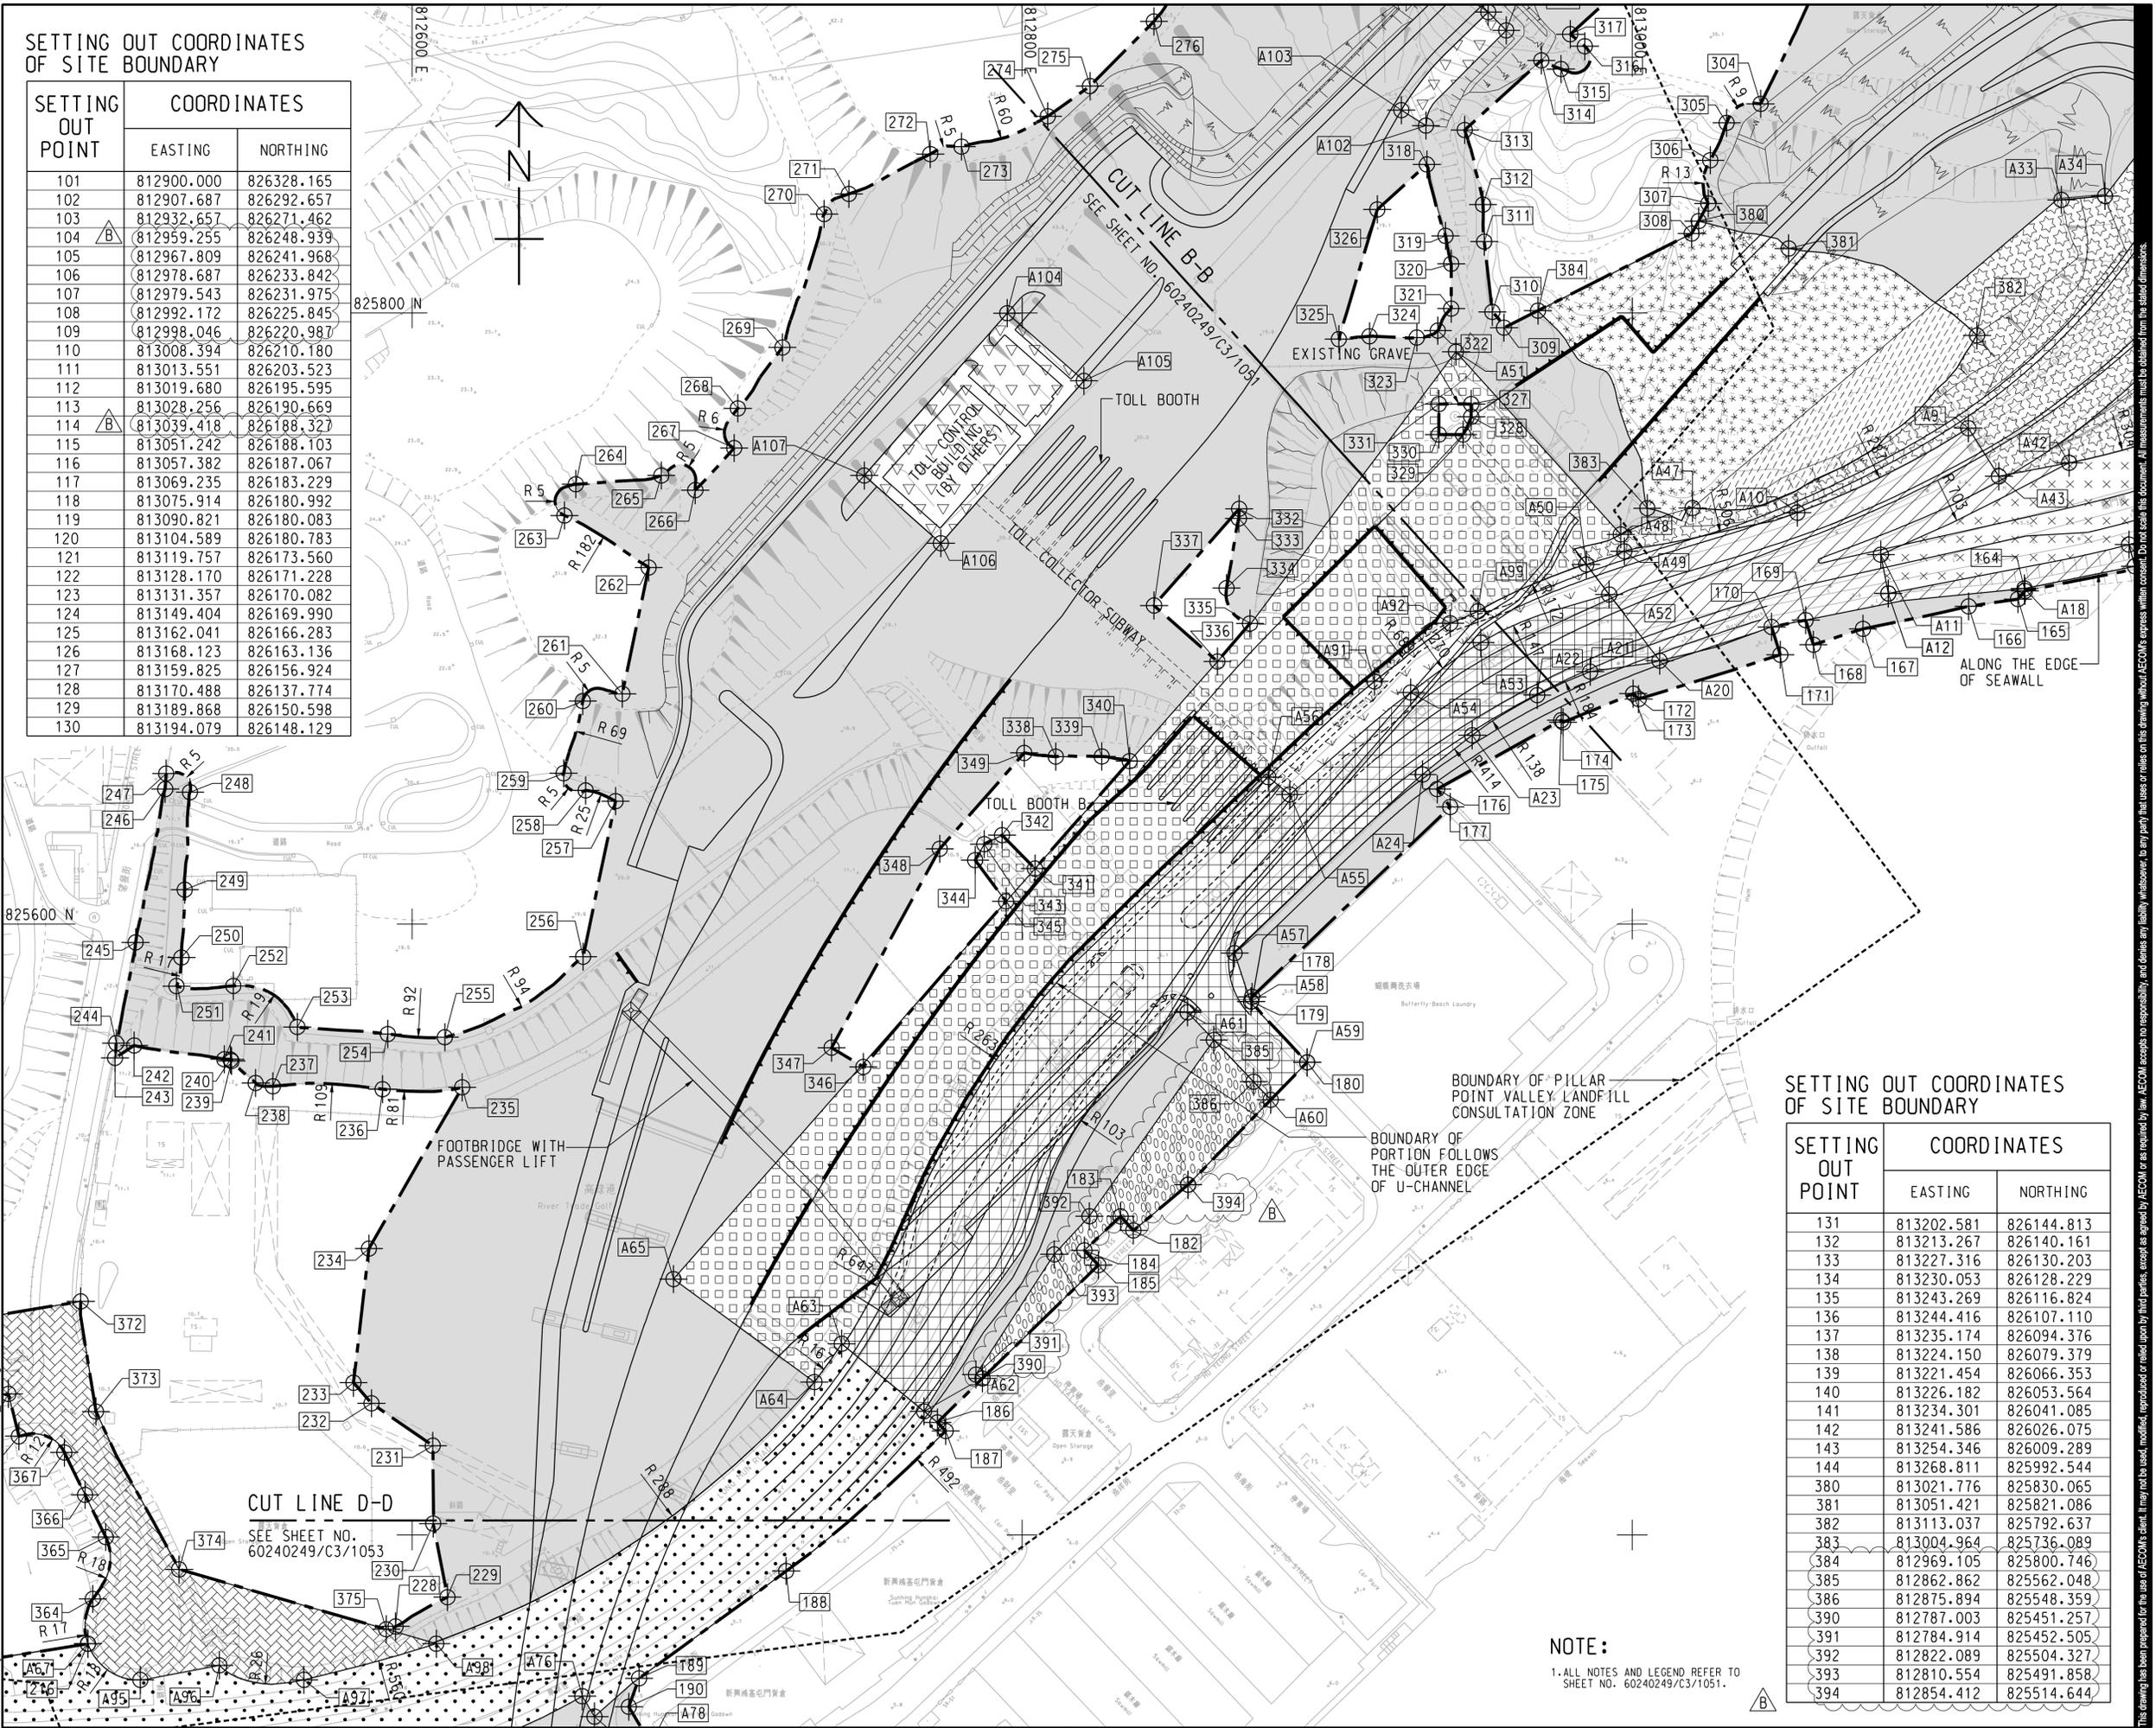

SETTING OUT COORDINATES OF SITE BOUNDARY

SETTING OUT POINT	COORDINATES	
	EASTING	NORTHING
131	813202.581	826144.813
132	813213.267	826140.161
133	813227.316	826130.203
134	813230.053	826128.229
135	813243.269	826116.824
136	813244.416	826107.110
137	813235.174	826094.376
138	813224.150	826079.379
139	813221.454	826066.353
140	813226.182	826053.564
141	813234.301	826041.085
142	813241.586	826026.075
143	813254.346	826009.289
144	813268.811	825992.544
380	813021.776	825830.065
381	813051.421	825821.086
382	813113.037	825792.637
383	813004.964	825736.089
384	812969.105	825800.746
385	812862.862	825562.048
386	812875.894	825548.359
390	812787.003	825451.257
391	812784.914	825452.505
392	812822.089	825504.327
393	812810.554	825491.858
394	812854.412	825514.644

NOTE:
 1. ALL NOTES AND LEGEND REFER TO SHEET NO. 60240249/C3/1051.



PROJECT
 TUEN MUN - CHEK LAP KOK LINK

CONTRACT TITLE
 TUEN MUN - CHEK LAP KOK LINK - NORTHERN CONNECTION TOLL PLAZA AND ASSOCIATED WORKS

CLIENT
 路政署 HIGHWAYS DEPARTMENT
 港務大樓香港工程管理局
 Hong Kong - Zhuhai - Macao Bridge
 Hong Kong Project Management Office


CONSULTANT
 AECOM Asia Company Ltd.
 www.aecom.com

SUB-CONSULTANTS
 分列工程顧問公司

ISSUE/REVISION

I/R	DATE	DESCRIPTION	CHK.
B	MAR. 14	TENDER ADDENDUM NO. 2	CWN
A	FEB. 14	TENDER ADDENDUM NO. 1	CWN
-	JAN. 14	TENDER DRAWING	CWN

SCALE
 比例 1:50000
DIMENSION UNIT
 尺寸單位 METRES




PROJECT NO.
 項目編號 60240249
CONTRACT NO.
 合約編號 HY/2013/12

SHEET TITLE
 圖紙名稱 PORTIONS OF SITE AND SITE BOUNDARY SETTING OUT PLAN

SHEET NUMBER
 圖紙編號 60240249/C3/1052B

This drawing has been prepared for the use of AECOM's client. It may not be used, modified, reproduced or relied upon by third parties, except as agreed by AECOM or as required by law. AECOM accepts no responsibility, and denies any liability whatsoever, for any party that uses or relies on this drawing without AECOM's express written consent. Do not scale this document. All measurements must be obtained from the stated dimensions.

Plot File by: LIXQ2 2014/03/4
 PATH: P:\Projects\60240249\DRAWING\CONTRACT\CS1000\CS_1062.dgn
 Project Management Initials: Designer: PL Checked: ALCF Approved: CWN ISO A1 594mm x 841mm

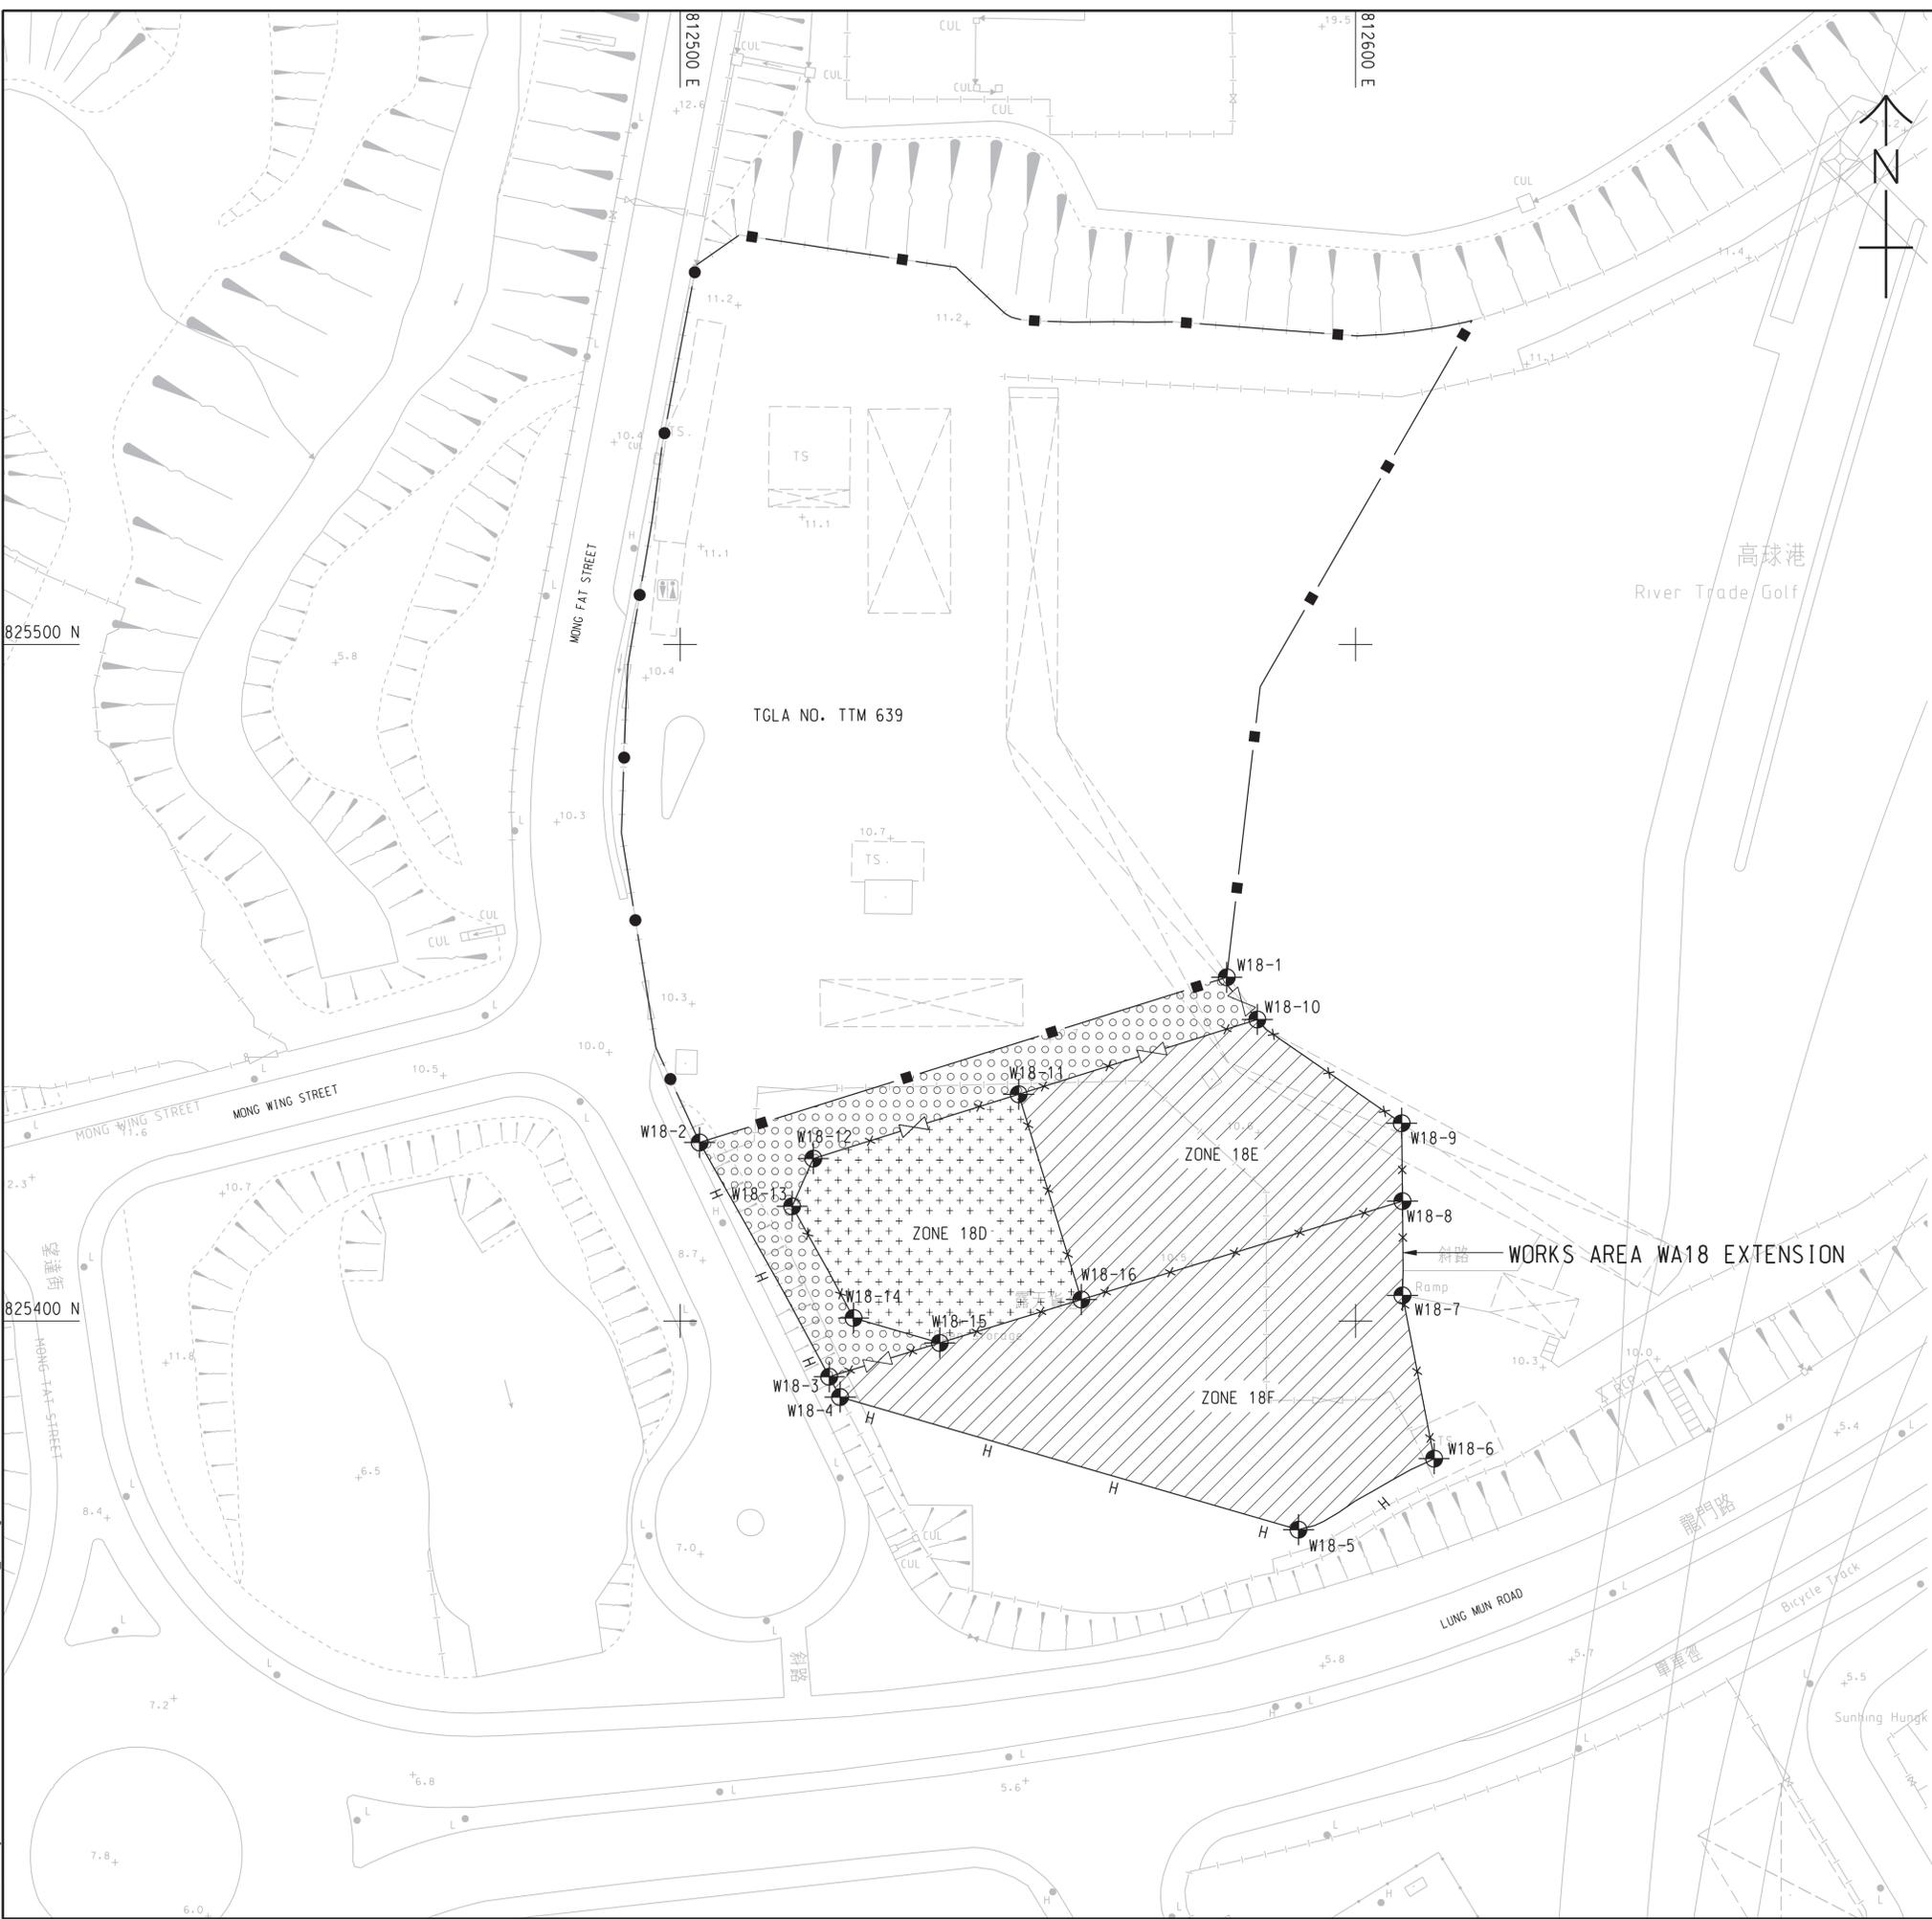

NOTES:

- THIS DRAWING SHALL BE READ IN CONJUNCTION WITH THE WORKS AREA KEY PLAN IN SHEET NO. 60240249/C3/1000.
- DEMARCATON OF THE WORKS AREA SHALL BE DETERMINED ON SITE.
- REFER TO HIGHWAYS DEPARTMENT STANDARD DRAWING NOS. H6110 AND H6111 FOR DETAILS OF HOARDING.
- REFER TO HIGHWAYS DEPARTMENT STANDARD DRAWING NOS. H6121 AND H6122 FOR DETAILS OF CHAIN LINK FENCE.
- REFER TO HIGHWAYS DEPARTMENT STANDARD DRAWING NO. H6121 FOR DETAILS OF GATE.
- CHAIN LINK FENCE SHALL BE ERRECTED ALONG THE WORKS AREA BOUNDARY. THE ALIGNMENT AND EXTENT OF HOARDING AND CHAIN LINK FENCE SHOWN ARE INDICATIVE ONLY AND SHALL BE CONFIRMED BY THE ENGINEER.
- THE LOCATION AND WIDTH OF GATE SHOWN ARE INDICATIVE ONLY AND SHALL BE CONFIRMED BY THE ENGINEER.
- THE SETTING OUT INFORMATION AND WORKS AREA CONDITIONS SHOWN IN THIS DRAWING ARE FOR REFERENCE ONLY. THE WORKS AREA BOUNDARY SHALL BE IN ACCORDANCE WITH THE ENGINEERING CONDITIONS FOR TEMPORARY GOVERNMENT LAND ALLOCATION NO. GLA-TM 639. IN CASE OF DISCREPANCY BETWEEN THE BOUNDARY SHOWN ON THIS DRAWING AND THE BOUNDARY INDICATED ON THE ENGINEERING CONDITIONS, THE LATTER SHALL PREVAIL.
- THE WORKS AREAS SHOWN ON THIS DRAWING ARE TO BE SHARED-USED AMONG THE TM-CLKL RELATED CONTRACTS. THE AREAS HATCHED WITH ARE TENTATIVELY ALLOCATED FOR THE USE BY THE CONTRACT.
- THE COMMON AREA SHALL BE CONCRETE PAVED BY THE CONTRACTOR.
- ZONE 18F SHALL BE USED FOR THE SITE ACCOMMODATION OF THE ENGINEER. ZONE 18E SHALL BE USED FOR SITE ACCOMMODATION OF THE CONTRACTOR.
- ZONE 18D IS TO BE USED BY THE CONTRACTOR OF CONTRACT NO. HY/2012/08-TUEN MUN-CHEK LAP KOK LINK-NORTHERN CONNECTION SUB-SEA TUNNEL SECTION TO STORE PLANT AND EQUIPMENT ASSOCIATED WITH THE TBM TUNNELS FROM THE DATE FOR COMMENCEMENT OF THE WORKS TO 126 DAYS FROM THE DATE FOR COMMENCEMENT OF THE WORKS. THE CONTRACTOR SHALL LIAISE AND PROVIDE FREE AND UNOBSTRUCTED 24-HOUR ACCESS FOR THE CONTRACTOR OF CONTRACT NO. HY/2012/08 TO ZONE 18D. THE CONTRACTOR SHALL BE GIVEN THE POSSESSION OF ZONE 18D IN ACCORDANCE WITH APPENDIX TO FORM OF TENDER-P.3.

LEGEND:

- WORKS AREA FOR THE CONTRACT
- COMMON AREA (MAINTAINED UNDER THE CONTRACT) TO BE SHARED-USED WITH OTHER CONTRACTS
- AREA TO BE USED BY THE CONTRACTOR OF CONTRACT NO. HY/2012/08 AND WORKS AREA FOR THIS CONTRACT TO BE EARLY HANDED OVER BY THE CONTRACTOR (SEE NOTES NO. 12 ABOVE)
- HOARDING AND GATE (TO BE ERRECTED AND MAINTAINED UNDER THIS CONTRACT)
- EXISTING CHAIN LINK FENCE MAINTAINED BY OTHERS
- CHAIN LINK FENCE AND GATE (TO BE ERRECTED AND MAINTAINED UNDER THIS CONTRACT)
- EXISTING HOARDING AND GATE MAINTAINED BY OTHERS

SETTING OUT CO-ORDINATES OF WORKS AREA WA18 EXTENSION

POINT	CO-ORDINATES	
	EASTING	NORTHING
W18-1	812580.934	825450.791
W18-2	812502.880	825426.380
W18-3	812522.068	825391.750
W18-4	812523.679	825388.756
W18-5	812591.556	825369.151
W18-6	812611.638	825379.647
W18-7	812606.954	825403.769
W18-8	812606.951	825417.705
W18-9	812606.832	825429.231
W18-10	812585.456	825444.557
W18-11	812550.126	825433.508
W18-12	812519.715	825423.997
W18-13	812516.580	825416.947
W18-14	812525.682	825400.438
W18-15	812538.435	825396.754
W18-16	812559.404	825403.166

AECOM

PROJECT
項目

TUEN MUN - CHEK LAP KOK LINK

CONTRACT TITLE
TUEN MUN - CHEK LAP KOK LINK - NORTHERN CONNECTION TOLL PLAZA AND ASSOCIATED WORKS

CLIENT
業主

路政署
HIGHWAYS DEPARTMENT
港務處大樓香港工程管理處
Hong Kong - Zhuhai - Macao Bridge
Hong Kong Project Management Office

CONSULTANT
工程師有限公司

AECOM Asia Company Ltd.
www.aecom.com

SUB-CONSULTANTS
分判工程師有限公司

ISSUE/REVISION
修訂

NO.	DATE	DESCRIPTION	CHK.
B	MAR. 14	TENDER ADDENDUM NO. 2	CWN
A	FEB. 14	TENDER ADDENDUM NO. 1	CWN
-	JAN. 14	TENDER DRAWING	CWN

STATUS
階段

SCALE
比例

A1 1:500

DIMENSION UNIT
尺寸單位

METRES

KEY PLAN
索引圖

PROJECT NO.
項目編號

60240249

CONTRACT NO.
合約編號

HY/2013/12

SHEET TITLE
圖紙名稱

WORKS AREA AND HOARDING PLAN


SHEET NUMBER
圖紙編號

60240249/C3/1062B

This drawing has been prepared for the use of AECOM's client. It may not be used, modified, reproduced or relied upon by third parties, except as agreed by AECOM or as required by law. AECOM accepts no responsibility, and denies any liability whatsoever, to any party that uses or relies on this drawing without AECOM's express written consent. Do not scale this document. All measurements must be obtained from the stated dimensions.

Appendix C

Environmental Management Organization Chart

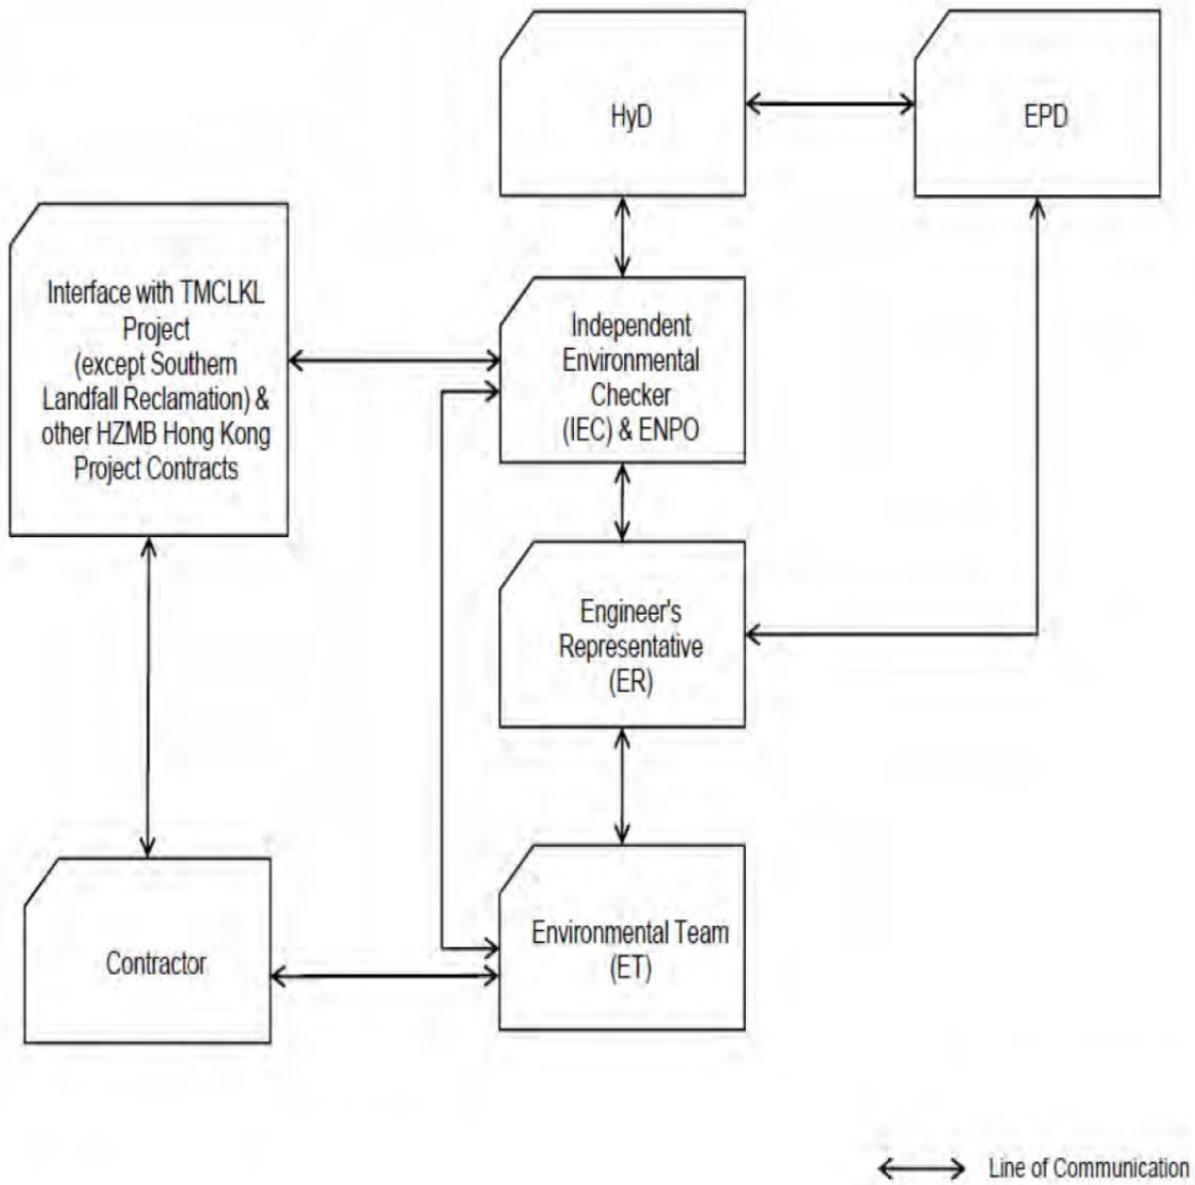

Project Organization chart

Organization chart of the Contractor

Contact Details of Key Personnel for the Contract HY/2013/12

Organization	Project Role	Name of Key Staff	Tel No	Fax No.
HyD	Employer	Mr. Stephen W.C. Chan	2762 3669	3188 6614
AECOM	Principal Resident Engineer	Mr. S.W. Fok	2218 7209	2218 7399
AECOM	Chief Resident Engineer	Mr. Roger Man	2218 7288	2218 7399
AECOM	Resident Engineer (S&E)	Mr. Kelvin Yeung	22187289	2218 7399
ENVIRON	Environmental Project Office (ENPO)	Mr. YH Hui	3465 2888	3465 2899
ENVIRON	Independent Environmental Checker (IEC)	Dr. FC Tsang	3465 2828	3465 2899
CKJV	Project Manager	Mr. Simon Tong	2253 8300	2253 8399
CKJV	Site Agent	Mr. John Wong	2253 8300	2253 8399
CKJV	Environmental Officer	Miss Ricci Poon	22733199	2375 3655
CKJV	Environmental Officer	Mr. HY Tang	2253 8300	2253 8399
CKJV	Environmental Supervisor	Miss Melody Tong	2253 8300	2253 8399
AUES	Environmental Team Leader	Mr. T. W. Tam	2959 6059	2959 6079
AUES	Environmental Consultant	Miss Nicola Hon	2959 6059	2959 6079
AUES	Environmental Consultant	Mr. Ben Tam	2959 6059	2959 6079
HKL	Registered Landscape Architect	Kenneth Ng	2866 3903	--

Legend:*HyD (Employer) –Highways Department**AECOM (Engineer) – AECOM Asia Co. Ltd.**CKJV (Main Contractor) – CRBC-Kaden Joint Venture**ENVIRON (IEC and ENPO) – Environ Hong Kong Limited**AUES (ET) – Action-United Environmental Services & Consulting**HKL(RLA) – Hong Kong Landscape*

Appendix D

Master Construction Programme

HY/2013/12 TM-CLKL Northern Connection Toll Plaza and Associated Works



Activity ID	Activity Name	Original Duration	Planned Start	Actual Start	Planned Finish	Actual Finish	Timeline (2014-2020)																							
							Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4		
HY/2013/12 Northern Connection Toll Plaza and Associated Works							HY/2013/12 Northern Connection Toll Plaza and Associated Works																							
IWP (Rev.02)							IWP (Rev.02)																							
Site Formation - Retaining Structure for Slope TP_F							Site Formation - Retaining Structure for Slope TP_F																							
Stage 3							Stage 3																							
Temporary Works Design Submission and Approval							Temporary Works Design Submission and Approval																							
RWF11000	Haul road design submission and approval	30	29-Aug-14	29-Aug-14	27-Sep-14	27-Sep-14																								
RWF11050	Open cut excavation design submission and approval	30	18-Sep-14	18-Sep-14	18-Oct-14	18-Oct-14																								
RWF11100	Formwork design submission and approval	45	27-Sep-14	27-Sep-14	11-Nov-14	11-Nov-14																								
Method Statement Submission and Approval							Method Statement Submission and Approval																							
RWF21000	Method Statement Submission and Approval for Open cut excavation	30	18-Oct-14	18-Oct-14	15-Nov-14	15-Nov-14																								
RWF21050	Method Statement Submission and Approval for Retaining Wall Construction	30	21-Oct-14	21-Oct-14	18-Nov-14	21-Oct-14																								
Retaining Structure for Slope TP_F							Retaining Structure for Slope TP_F																							
RWF31000	Form Access Road	24	27-Sep-14	26-Sep-14	30-Oct-14	30-Oct-14																								
RWF31050	Excavation of Soil (5,400m3)	43	18-Nov-14	17-Nov-14	10-Jan-15																									
RWF31100	Excavation of Rock Grade IV (4,320m3)	70	10-Jan-15	10-Jan-15	10-Apr-15																									
RWF31300	Construct Retaining Wall Bay 7 to Bay 20	168	09-Mar-15		17-Oct-15																									
RWF31325	Construct Retaining Wall Bay 4 to Bay 6 adjacent to abutment G2e	50	17-Dec-15		20-Feb-16																									
RWF31350	Construct Retaining Wall Bay 21 to Bay 28	96	04-Nov-16		03-Mar-17																									
RWF31400	Backfilling (51,449m3)	504	17-Oct-15		29-Jul-17																									
Site Formation - Slope TP_A & Associated Works							Site Formation - Slope TP_A & Associated Works																							
Stage 3							Stage 3																							
Temporary Works Design Submission and Approval							Temporary Works Design Submission and Approval																							
TPA11000	Haul road design submission for TP_A,B&C	45	09-Oct-14	01-Sep-14	20-Nov-14	18-Sep-14																								
Method Statement Submission and Approval							Method Statement Submission and Approval																							
TPA21050	Method Statement Submission for TP_A,B&C	45	23-Oct-14	18-Sep-14	04-Dec-14	21-Oct-14																								
Slope Feature - Slope TP_A							Slope Feature - Slope TP_A																							
TPA31030	Tree felling works	24	06-Feb-15	03-Sep-14	10-Mar-15																									
TPA31040	Form Access Road	24	10-Mar-15	03-Sep-14	11-Apr-15	01-Oct-14																								
TPA31050	Site Clearance	24	11-Apr-15	11-Sep-14	13-May-15																									
TPA31100	Excavation of Soil (23,933m3)	48	03-Jun-15	23-Oct-14	05-Aug-15																									
TPA31150	Excavation of Rock Grade IV (2,314m3)	18	05-Aug-15	01-Nov-14	27-Aug-15																									
TPA31200	Excavation of Rock Grade II/III (6,539m3)	60	29-Jul-15		14-Oct-15																									
TPA31250	Forming East Portal Formation and temporary ground drainage works	60	16-Oct-15		29-Dec-15																									
TPA31300	Construct Cascade A	60	30-Dec-15		12-Mar-16																									
Site Formation - Slope TP_B & Associated Works							Site Formation - Slope TP_B & Associated Works																							
Stage 3							Stage 3																							
Slope Feature - Slope TP_B							Slope Feature - Slope TP_B																							
TPB31000	Form Access Road	24	17-Sep-15	03-Sep-14	19-Oct-15	01-Oct-14																								
TPB31050	Site Clearance and Tree Felling	24	20-Oct-15	11-Sep-14	18-Nov-15	23-Oct-14																								
TPB31100	Excavation of Soil (49,155m3)	72	19-Nov-15	30-Oct-14	17-Feb-16																									
TPB31150	Excavation of Rock Grade IV (15,049m3)	80	18-Feb-16	01-Nov-14	01-Jun-16																									
TPB31210	Excavation of Rock II/III	28	23-Mar-16		29-Apr-16																									
TPB31260	Forming road formation and temporary ground drainage works	11	26-May-16		10-Jun-16																									
Site Formation - Slope TP_C & Associated Works							Site Formation - Slope TP_C & Associated Works																							
Stage 3							Stage 3																							
Slope Feature - Slope TP_C							Slope Feature - Slope TP_C																							
TPC31015	Form Access Road	24	17-Sep-15	03-Sep-14	19-Oct-15	01-Oct-14																								
TPC31030	Site Clearance and Tree Felling	24	20-Oct-15	02-Oct-14	18-Nov-15	23-Oct-14																								
TPC31060	Excavation of Soil (12,000m3)	24	18-Jan-16	30-Oct-14	17-Feb-16																									
TPC31100	Excavation of Rock II/III (12,964m3)	115	14-Dec-15		11-May-16																									
TPC31160	Forming road formation and temporary ground drainage works	11	11-May-16		26-May-16																									
Site Formation - Slope TP_D & Associated Works							Site Formation - Slope TP_D & Associated Works																							
Stage 3							Stage 3																							
Temporary Works Design Submission and Approval							Temporary Works Design Submission and Approval																							
TPD21000	Haul road design submission	30	08-Sep-14	01-Sep-14	09-Oct-14	18-Nov-14																								
Method Statement Submission and Approval							Method Statement Submission and Approval																							
TPD11050	Method Statement Submission and Approval for TP_D Slope Site Formation	30	23-Sep-14	18-Sep-14	23-Oct-14	21-Oct-14																								
Slope Feature - Slope TP_D							Slope Feature - Slope TP_D																							
TPD31000	Form Access Road	24	08-Sep-14	21-Aug-14	19-Jun-15	01-Oct-14																								
TPD31025	Site Clearance and Tree Felling	24	24-Nov-14	24-Nov-14	22-Dec-14	30-Nov-14																								
TPD31035	G.I works	17	22-Dec-14		14-Jan-15																									
TPD31100	Excavation of Soil (4,570m3)	12	14-Jan-15		28-Jan-15																									
TPD31150	Excavation of Rock Grade IV (999m3)	12	28-Jan-15		11-Feb-15																									
TPD31200	Excavation of Rock II/III (12,196m3)	92	11-Feb-15		13-Jun-15																									
TPD31250	Forming West Portal Formation and temporary ground drainage works	4	13-Jun-15		19-Jun-15																									
Site Formation - Slope TP_E & Associated Works							Site Formation - Slope TP_E & Associated Works																							
Stage 3							Stage 3																							
Temporary Works Design Submission and Approval							Temporary Works Design Submission and Approval																							
TPE11000	Haul road design submission	30	08-Sep-14	01-Sep-14	09-Oct-14	18-Sep-14																								
Method Statement Submission and Approval							Method Statement Submission and Approval																							

■ Actual Work ■ Remaining Work ■ Critical Remaining Work
◆ Milestone ▶ Summary

CRBC - Kaden JV
Programme & Progress

Date	Revision	Checked	Approved
30-Nov-14	Draft		

HY/2013/12 TM-CLKL Northern Connection Toll Plaza and Associated Works



Activity ID	Activity Name	Original Duration	Planned Start	Actual Start	Planned Finish	Actual Finish	Gantt Chart (2015-2020)																							
							Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2
TPE21000	Method Statement Submission for TP_E Slope Site Formation	45	23-Sep-14	18-Sep-14	06-Nov-14	23-Oct-14	[Gantt bar: 23-Sep-14 to 23-Oct-14]																							
Slope Feature - Slope TP_E at Toll Control Building Area							[Gantt bar: 09-Oct-14 to 21-Dec-16]																							
TPE31000	Form Access Road	72	09-Oct-14	01-Sep-14	21-Dec-16	23-Oct-14	[Gantt bar: 09-Oct-14 to 23-Oct-14]																							
TPE31050	Site Clearance, Tree Transplanting and Felling	72	11-Nov-14	12-Sep-14	06-Feb-15	23-Oct-14	[Gantt bar: 11-Nov-14 to 23-Oct-14]																							
TPE31100	Excavation of Soil (Max. 200m3/n/d; 13,958m3)	72	28-Jan-15	24-Oct-14	04-May-15		[Gantt bar: 28-Jan-15 to 04-May-15]																							
TPE31150	Excavation of Rock Grade IV (55m3/n/d; 2,810m3)	44	13-Mar-15	25-Oct-14	12-May-15		[Gantt bar: 13-Mar-15 to 12-May-15]																							
TPE31200	Excavation of Rock Grade III (45m3/n/d; 17,388m3)	129	12-May-15	31-Oct-14	29-Oct-15		[Gantt bar: 12-May-15 to 29-Oct-15]																							
TPE31250	Excavation of Rock Grade II (35m3/n/d; 85,388m3)	337	24-Aug-15	01-Nov-14	04-Nov-16		[Gantt bar: 24-Aug-15 to 04-Nov-16]																							
TPE31300	Hand Over of Portion D	13	08-Dec-16		21-Dec-16		[Gantt bar: 08-Dec-16 to 21-Dec-16]																							
Slope Feature - Slope TP_E Remaining Section							[Gantt bar: 18-Oct-14 to 21-Jul-17]																							
TPE41000	Preservation of Existing Pitcher Plants before Translocation	154	18-Oct-14	02-Oct-14	02-May-15	31-Oct-14	[Gantt bar: 18-Oct-14 to 31-Oct-14]																							
TPE41020	Translocation of Pitcher Plants	67	02-May-15		29-Jul-15		[Gantt bar: 02-May-15 to 29-Jul-15]																							
TPE41100	Excavation of Soil (Max. 200m3/n/d; 12,159m3)	40	29-Jul-15		18-Sep-15		[Gantt bar: 29-Jul-15 to 18-Sep-15]																							
TPE41150	Excavation of Rock Grade IV (55m3/n/d; 6,408m3)	60	18-Sep-15		04-Dec-15		[Gantt bar: 18-Sep-15 to 04-Dec-15]																							
TPE41200	Excavation of Rock Grade III (45m3/n/d; 14,000m3)	160	04-Dec-15		29-Jun-16		[Gantt bar: 04-Dec-15 to 29-Jun-16]																							
TPE41250	Excavation of Rock Grade II (35m3/n/d; 15,226m3)	250	29-Jun-16		19-May-17		[Gantt bar: 29-Jun-16 to 19-May-17]																							
TPE41300	Construct Cascade C	48	19-May-17		21-Jul-17		[Gantt bar: 19-May-17 to 21-Jul-17]																							
Site Formation - Slope Upgrading Works							[Gantt bar: 17-Dec-14 to 13-Aug-18]																							
Stage 3							[Gantt bar: 17-Dec-14 to 13-Aug-18]																							
Temporary Works Design Submission and Approval							[Gantt bar: 17-Dec-14 to 06-Oct-14]																							
SUW11000	General temporary works design for slope works	30	17-Dec-14	02-Oct-14	17-Jan-15	06-Oct-14	[Gantt bar: 17-Dec-14 to 06-Oct-14]																							
Method Statement Submission and Approval							[Gantt bar: 17-Dec-14 to 06-Oct-14]																							
SUW21000	General method statement for Slope Upgrading Works (soil nails, rock dowels, etc.)	45	17-Dec-14	02-Oct-14	31-Jan-15	06-Oct-14	[Gantt bar: 17-Dec-14 to 06-Oct-14]																							
Slope Feature - Slope SSE-D/C170							[Gantt bar: 06-Jan-15 to 19-Jan-15]																							
SUW31000	Implementation of TTA	14	06-Jan-15		19-Jan-15		[Gantt bar: 06-Jan-15 to 19-Jan-15]																							
SUW31050	Site Clearance and Tree Felling	15	19-Jan-15		05-Feb-15		[Gantt bar: 19-Jan-15 to 05-Feb-15]																							
SUW31100	Prepare Access Road	7	19-Jan-15		27-Jan-15		[Gantt bar: 19-Jan-15 to 27-Jan-15]																							
SUW31150	Excavation of Soil (1,240m3)	14	31-Jan-15		17-Feb-15		[Gantt bar: 31-Jan-15 to 17-Feb-15]																							
SUW31200	Excavation of Rock Grade IV (350m3)	9	17-Feb-15		03-Mar-15		[Gantt bar: 17-Feb-15 to 03-Mar-15]																							
SUW31250	Slope Works (Recompaction; Soil Nail 45 nr) and Drainage System	45	03-Mar-15		02-May-15		[Gantt bar: 03-Mar-15 to 02-May-15]																							
Other Slope Features							[Gantt bar: 31-Jan-15 to 07-May-15]																							
SUW41000	Hydroseeding SSE-D/C152	72	31-Jan-15		07-May-15		[Gantt bar: 31-Jan-15 to 07-May-15]																							
SUW42000	Hydroseeding and Erosion Control Mat SSE-D/C121	36	13-Jun-15		01-Aug-15		[Gantt bar: 13-Jun-15 to 01-Aug-15]																							
SUW43000	Hydroseeding and Erosion Control Mat SSE-D/C122	36	13-Jun-15		01-Aug-15		[Gantt bar: 13-Jun-15 to 01-Aug-15]																							
SUW45000	Hydroseeding SSE-D/C150	72	31-Jan-15		07-May-15		[Gantt bar: 31-Jan-15 to 07-May-15]																							
SUW46000	Slope Modification Works SSE-D/C14	72	29-Jul-17		02-Nov-17		[Gantt bar: 29-Jul-17 to 02-Nov-17]																							
SUW47000	Hydroseeding SSE-D/C151	72	31-Jan-15		07-May-15		[Gantt bar: 31-Jan-15 to 07-May-15]																							
SUW47500	Re-compaction, Fill and Hydroseeding SSE-D/C149, 150 and 152	72	31-Jan-15		07-May-15		[Gantt bar: 31-Jan-15 to 07-May-15]																							
SUW48000	Rock Mapping and Stabilization SSE-D/C115	72	31-Jan-15		07-May-15		[Gantt bar: 31-Jan-15 to 07-May-15]																							
SUW49000	Hydroseeding and Erosion Control Mat SSE-D/C18	136	25-May-17		18-Nov-17		[Gantt bar: 25-May-17 to 18-Nov-17]																							
SUW50000	Hydroseeding and Erosion Control Mat SSE-D/C117	148	26-Jun-17		03-Jan-18		[Gantt bar: 26-Jun-17 to 03-Jan-18]																							
SUW51000	Slope Cut SSE-D/C165 (1E - 50m3/n/d, 210m3; Soil Nail 47 nr., each 8m Long)	196	30-Mar-16		09-Dec-16		[Gantt bar: 30-Mar-16 to 09-Dec-16]																							
SUW52000	Slope Modification Works D/C21	48	02-Nov-17		30-Dec-17		[Gantt bar: 02-Nov-17 to 30-Dec-17]																							
SUW53000	Slope Modification Works D/C171	48	30-Dec-17		01-Mar-18		[Gantt bar: 30-Dec-17 to 01-Mar-18]																							
SUW54000	Drainage Hydroseeding and Erosion Control Mat SSE-D/C16	120	08-Mar-18		13-Aug-18		[Gantt bar: 08-Mar-18 to 13-Aug-18]																							
SUW55000	Slope Re-compaction SSE-D/F60	96	26-Oct-17		24-Feb-18		[Gantt bar: 26-Oct-17 to 24-Feb-18]																							
SUW56000	Slope Modification Works D/C158	48	30-Dec-17		01-Mar-18		[Gantt bar: 30-Dec-17 to 01-Mar-18]																							
SUW57000	Hydroseeding and Erosion Control Mat SSE-D/C17	48	10-Apr-18		11-Jun-18		[Gantt bar: 10-Apr-18 to 11-Jun-18]																							

Activity ID	Activity Name	Original Duration	Start	Actual Start	Finish	Actual Finish	Performance % Complete	Total Float	Gantt Chart											
									2014 Q3	2014 Q4	2015 Q1	2015 Q2	2015 Q3	2015 Q4	2016 Q1	2016 Q2	2016 Q3	2016 Q4	2017 Q1	2017 Q2
HY/2013/12 DWP Rev.3									[Gantt Chart Summary]											
Instrumentation and Monitoring									[Gantt Chart Summary]											
Ground Settlement Marker									[Gantt Chart Summary]											
IM10090	Installation of GSM11,GSM45-46(Outside site boundary)	8	25-Sep-14 A	25-Sep-14	05-Feb-18		45%	230	[Gantt Chart Summary]											
Utility Settlement Marker									[Gantt Chart Summary]											
IM60020	Installation of USM-Remain USM	90	22-Nov-14 A	22-Nov-14	02-Sep-15		20%	218	[Gantt Chart Summary]											
Piezometer/Standpipe									[Gantt Chart Summary]											
IM50025	GI for PADH13-15 and installation piezometer	7	04-Nov-14 A	04-Nov-14	03-Nov-17		66%	110	[Gantt Chart Summary]											
Toll Plaza Decking TD1-Section 1									[Gantt Chart Summary]											
Stage 1									[Gantt Chart Summary]											
Design Submission and Approval									[Gantt Chart Summary]											
TD120100	Prepare & submit draft DDA Drawings w/ICE cert(Precast beam)	24	27-Apr-15		23-Jun-15		0%	337	[Gantt Chart Summary]											
TD120110	Engineer's comments	23	27-May-15		23-Jun-15		0%	337	[Gantt Chart Summary]											
TD120180	TWD -Formwork design for Pier	24	27-Apr-15		26-May-15		0%	116	[Gantt Chart Summary]											
Method Statement Submission and Approval									[Gantt Chart Summary]											
TD120300	MSS for pier construction	24	27-Apr-15		26-May-15		0%	116	[Gantt Chart Summary]											
TD120310	Engineer's comments and approval	24	27-May-15		24-Jun-15		0%	116	[Gantt Chart Summary]											
Field Works									[Gantt Chart Summary]											
Foundation & Substructure at Northern Side of Lung Mun Road									[Gantt Chart Summary]											
Pile cap and Pier									[Gantt Chart Summary]											
TD120520	Pile cap and Pier A2-E3	91	16-Mar-15 A	16-Mar-15	25-Sep-15		20%	107	[Gantt Chart Summary]											
Foundation & Substructure at Southern Side of Lung Mun Road									[Gantt Chart Summary]											
Pile cap & Pier									[Gantt Chart Summary]											
TD120630	Pile cap & Pier E1-C1	54	27-May-15		05-Aug-15		0%	166	[Gantt Chart Summary]											
Foundation & Substructure at Central Divider of Lung Mun Road									[Gantt Chart Summary]											
GI									[Gantt Chart Summary]											
TD121060	Trial pit and monitoring point installation	10	07-Mar-15 A	07-Mar-15	21-Apr-15		80%	95	[Gantt Chart Summary]											
Bored Pile									[Gantt Chart Summary]											
TD121300	Bored Piles A1-E2(5 Nos)	61	21-Apr-15		09-Jul-15		0%	95	[Gantt Chart Summary]											
Pile cap and Pier									[Gantt Chart Summary]											
TD120540	Pile cap A1-E2	55	29-May-15		11-Aug-15		0%	141	[Gantt Chart Summary]											
Toll Plaza Decking TD2-Section 1									[Gantt Chart Summary]											
Field Works									[Gantt Chart Summary]											
G.I and Piling Works									[Gantt Chart Summary]											
DWP-G.I									[Gantt Chart Summary]											
TD220380	G.I for P1-P5	16	10-Oct-14 A	10-Oct-14	04-Nov-15 A	04-Nov-15	0%		[Gantt Chart Summary]											
Toll Plaza Footbridge-Section 1									[Gantt Chart Summary]											
Stage 1									[Gantt Chart Summary]											
Method Statement Submissions and Approval									[Gantt Chart Summary]											
TFB1060	MSS for Pile cap and pier construction	30	13-Feb-15 A	13-Feb-15	10-Sep-15		50%	152	[Gantt Chart Summary]											
Field Works									[Gantt Chart Summary]											
Pile Cap Construction									[Gantt Chart Summary]											
TFB1240	Construct pile cap for Pier P2	20	28-Mar-15 A	28-Mar-15	02-Nov-15		10%	420	[Gantt Chart Summary]											
Retaining Structure RW_B-Section 1									[Gantt Chart Summary]											
Site Formation - Retaining Structure RW_B									[Gantt Chart Summary]											
Stage 1									[Gantt Chart Summary]											
Design Submission and Approval									[Gantt Chart Summary]											
RWB10330	Alternative Design for RW_B structure submission	21	16-Mar-15 A	16-Mar-15	23-Apr-15		85%	158	[Gantt Chart Summary]											
RWB10340	Engineer's approval	21	23-Apr-15		19-May-15		0%	158	[Gantt Chart Summary]											

█ Remaining Level of Effort
 █ Remaining Work
 Summary
 Primary Baseline
 █ Critical Remaining Work
█ Actual Work
 ◆ Milestone

Date	Revision	Checked	Approved
20-Apr-15	3		

Activity ID	Activity Name	Original Duration	Start	Actual Start	Finish	Actual Finish	Performance % Complete	Total Float	Gantt Chart													
									2014	2015	2016	2017	2018									
Slope Feature - 5SE-D/C149																						
SFW10390	Slope Modification	10	16-Jan-15 A	16-Jan-15	20-Dec-16		10%	144														
Vehicular Underpass TN-01																						
Stage 3																						
Blasting Related Submission																						
Method Statment Submission and Approval																						
UDP30650	Method statement for Lining Construction	72	26-May-15		19-Aug-15		0%	413														
Road and Drainage Work at for Lung Fu Road Roundabout																						
Section 3																						
Road and drainage works under LFR R/A TTA stage 2a																						
LF20050	Slope cut/filled at LMR for the further roundabout	30	20-Apr-15		28-May-15		0%	255														
LF20100	Traffic on LMR diverted to LFR junction	7	29-May-15		06-Jun-15		0%	255														


█ Remaining Level of Effort █ Remaining Work Summary
 Primary Baseline Critical Remaining Work
 Actual Work ◆ ◆ Milestone

CRBC - Kaden JV
2 Months Rolling Programme Report Update 20-Apr-15

Date	Revision	Checked	Approved
20-Apr-15	3		

Appendix E

Monitoring Locations / Sensitive Receivers for the Contract

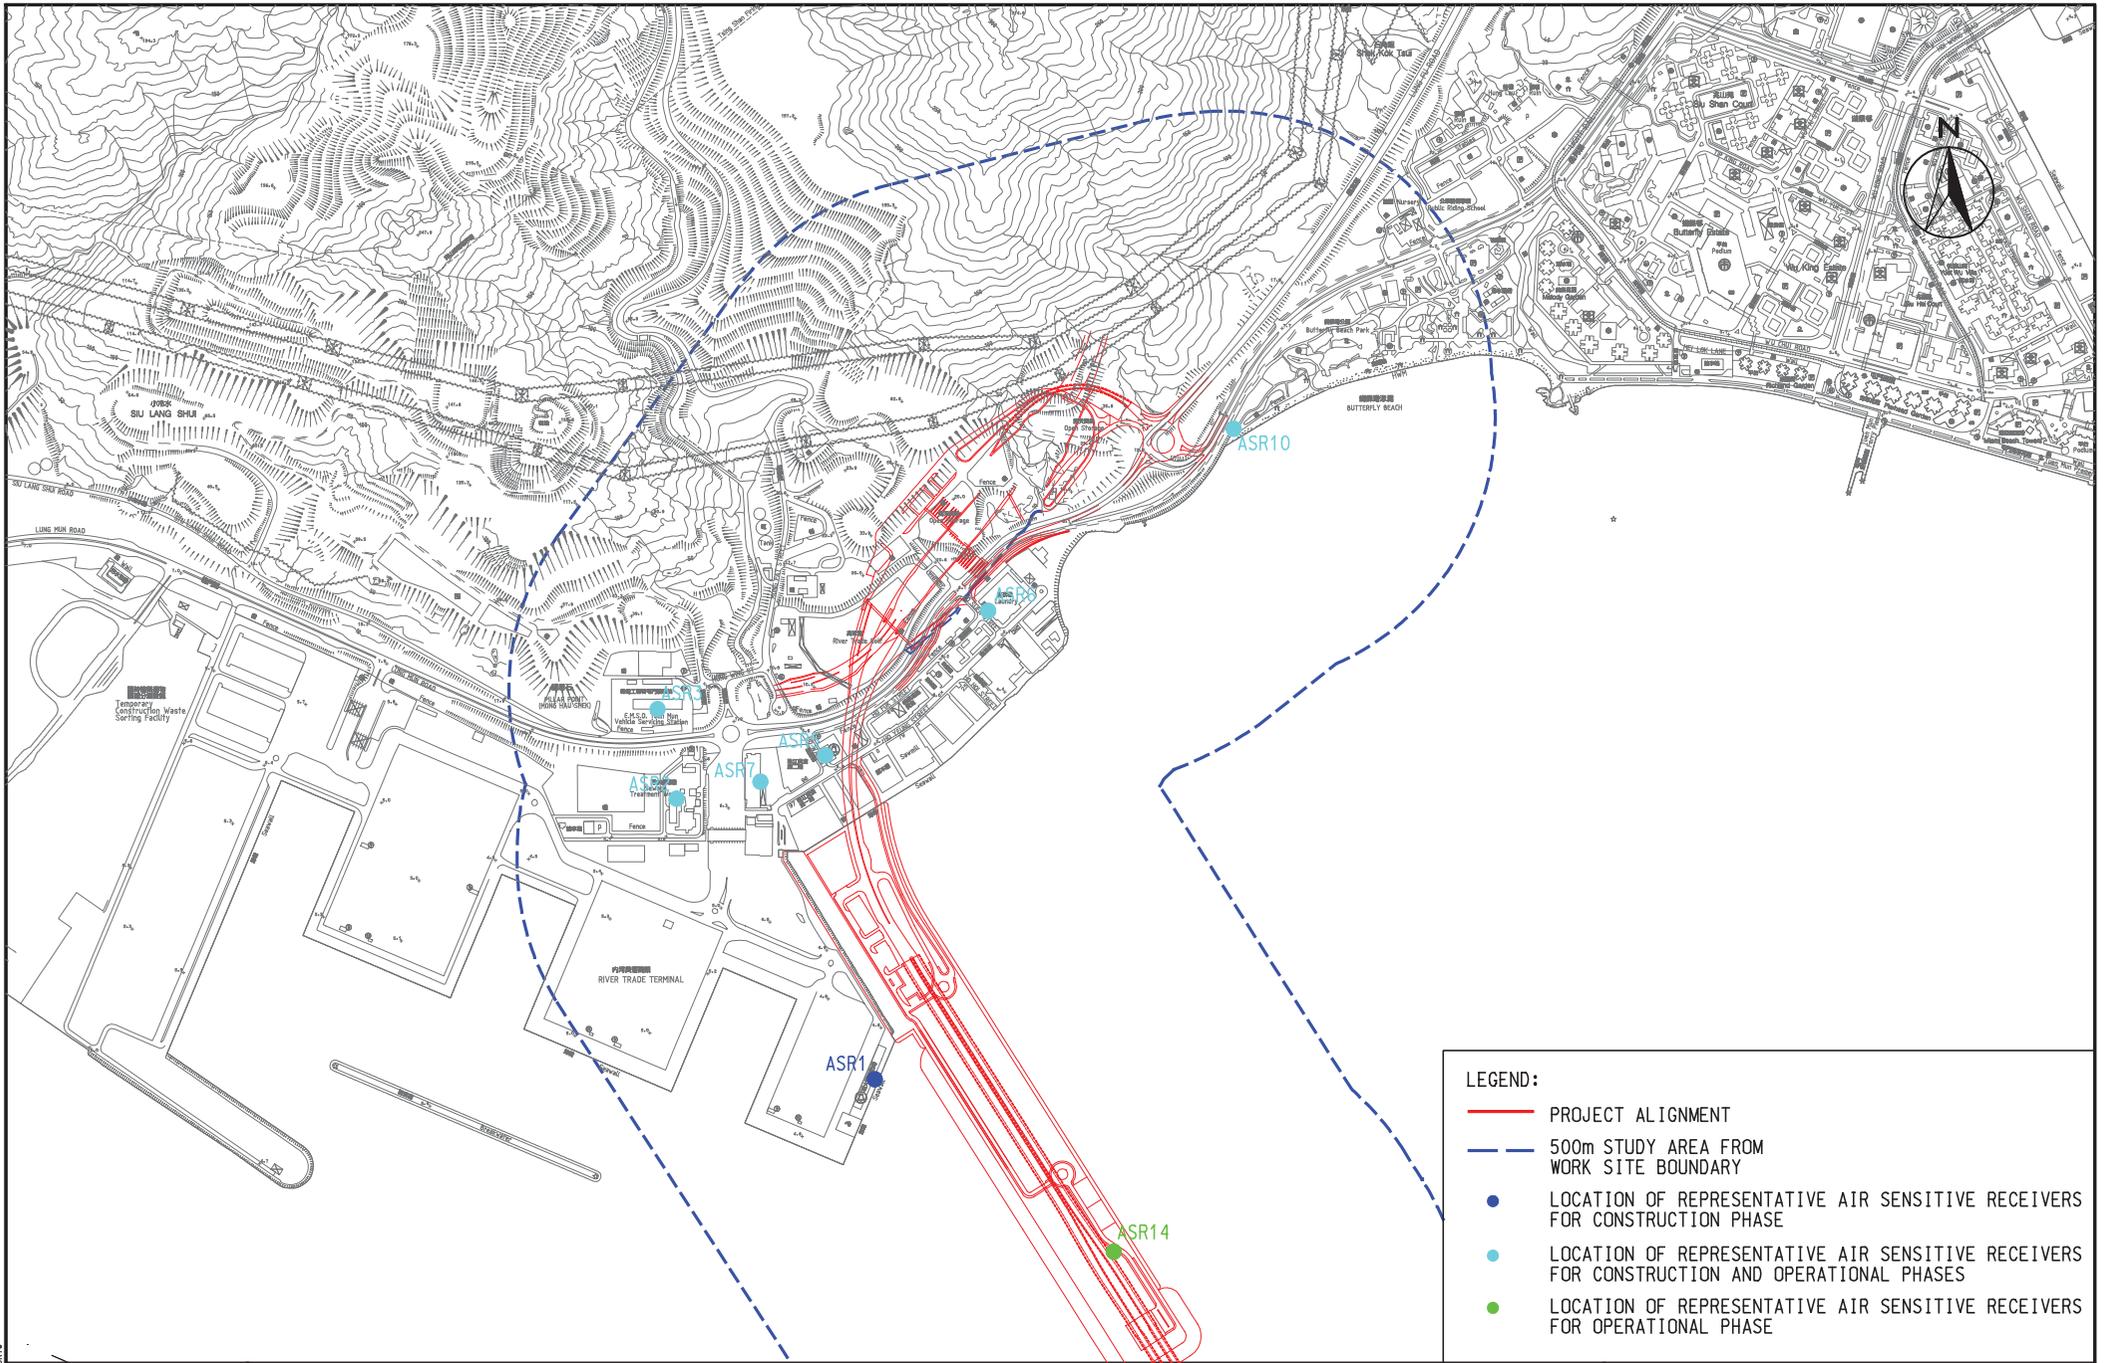

LEGEND:


- PROJECT ALIGNMENT
- - - 500m STUDY AREA FROM WORK SITE BOUNDARY
- LOCATION OF REPRESENTATIVE AIR SENSITIVE RECEIVERS FOR CONSTRUCTION PHASE
- LOCATION OF REPRESENTATIVE AIR SENSITIVE RECEIVERS FOR CONSTRUCTION AND OPERATIONAL PHASES
- LOCATION OF REPRESENTATIVE AIR SENSITIVE RECEIVERS FOR OPERATIONAL PHASE

AGREEMENT NO. CE 52/2007(HY)
 TUEN MUN - CHEK LAP KOK LINK - INVESTIGATION
REPRESENTATIVE AIR SENSITIVE RECEIVERS

SCALE	1 : 10 000	DATE	
-------	------------	------	--



Air Quality Monitoring Location

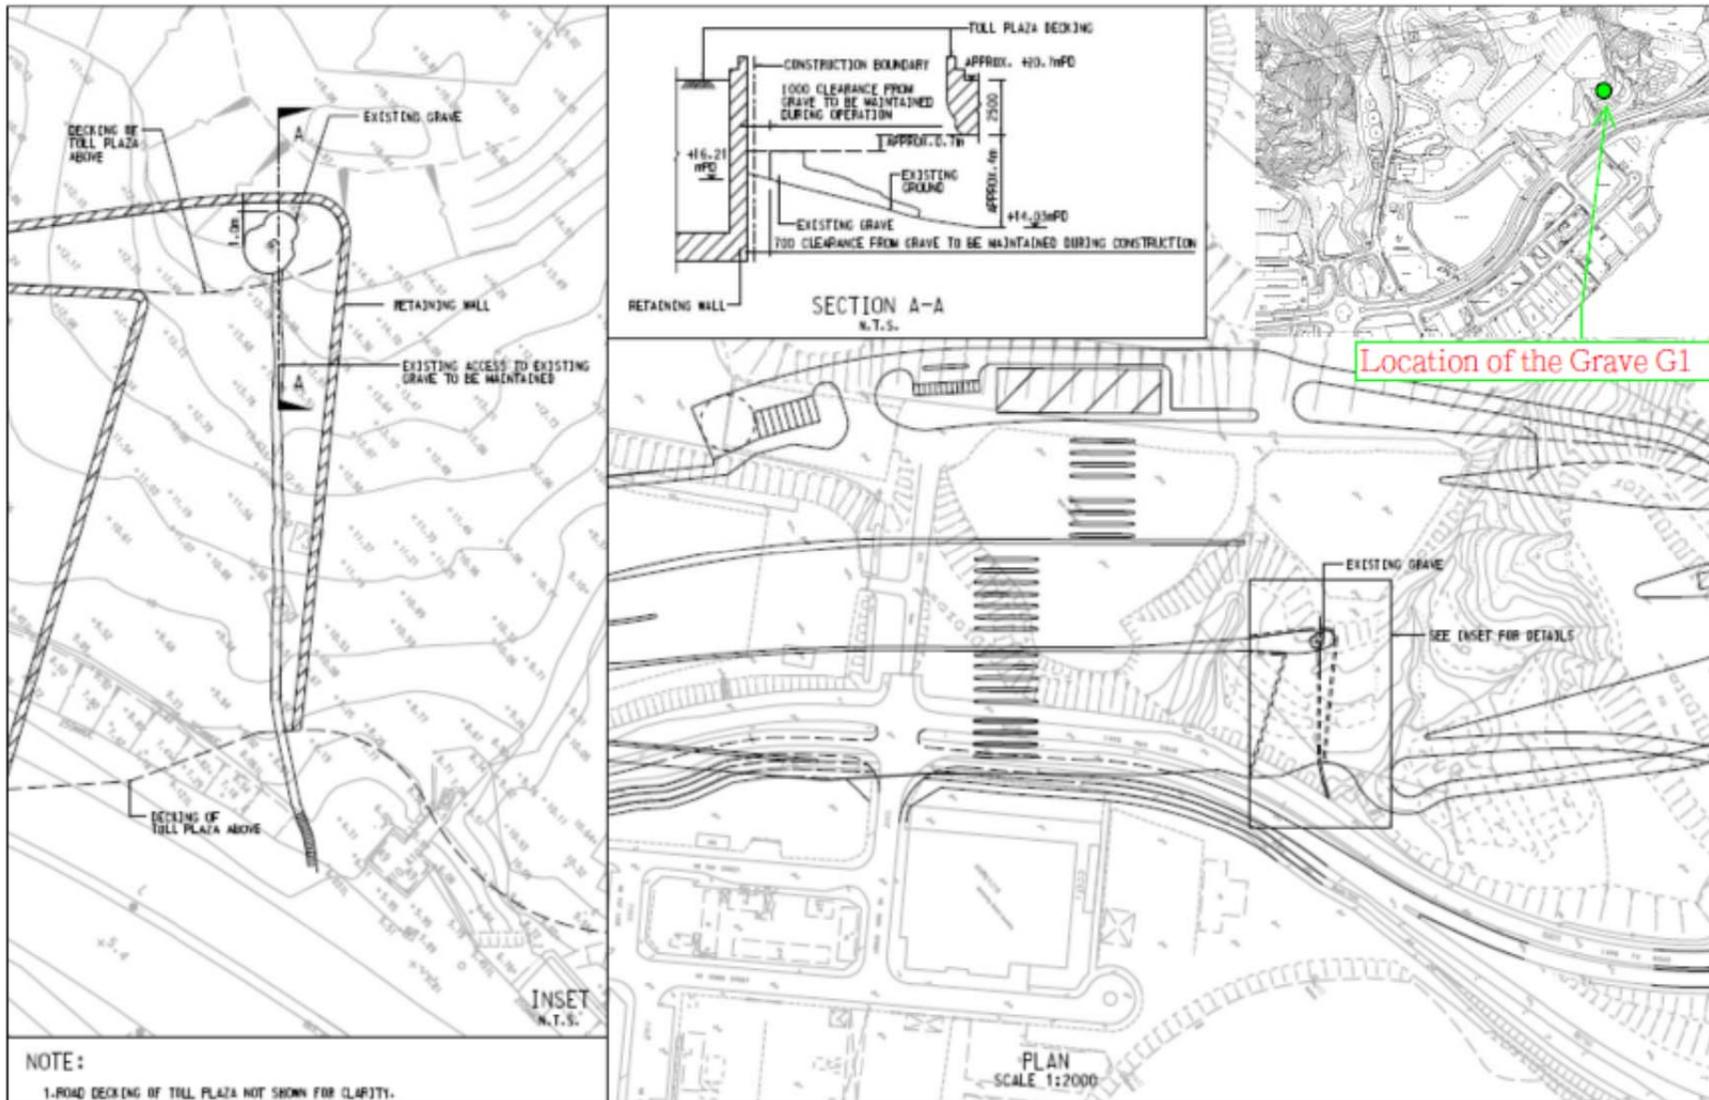


Location of the Grave G1

Project Management Initials: Designer: NCCS Checker: ALCF Approver: CWN
 ISO A1 594mm x 841mm
 Plot File by: SUSERS SDATES
 PATH: SEILES

NOTES:
 1. ALL CO-ORDINATES ARE IN ACCORDANCE WITH HK(1980) GAUSS CO-ORDINATE SYSTEM.
 2. ALL DIMENSIONS ARE IN METRES UNLESS NOTED OTHERWISE.

- LEGEND:**
- SITE BOUNDARY
 - LOCATION OF KNOWN POPULATIONS OF PITCHER PLANT
 - PROPOSED ALIGNMENT OF FENCING (EXACT ALIGNMENT TO BE DETERMINED ON SITE)
 - LOCATION OF PROPOSED NURSERY SITE
 - LOCATION OF PROPOSED RECEPTOR SITE
 - - - UNDERPASS WORKS AREA (ZONE 8-10 AND NURSERY SITE WILL NOT BE AFFECTED)

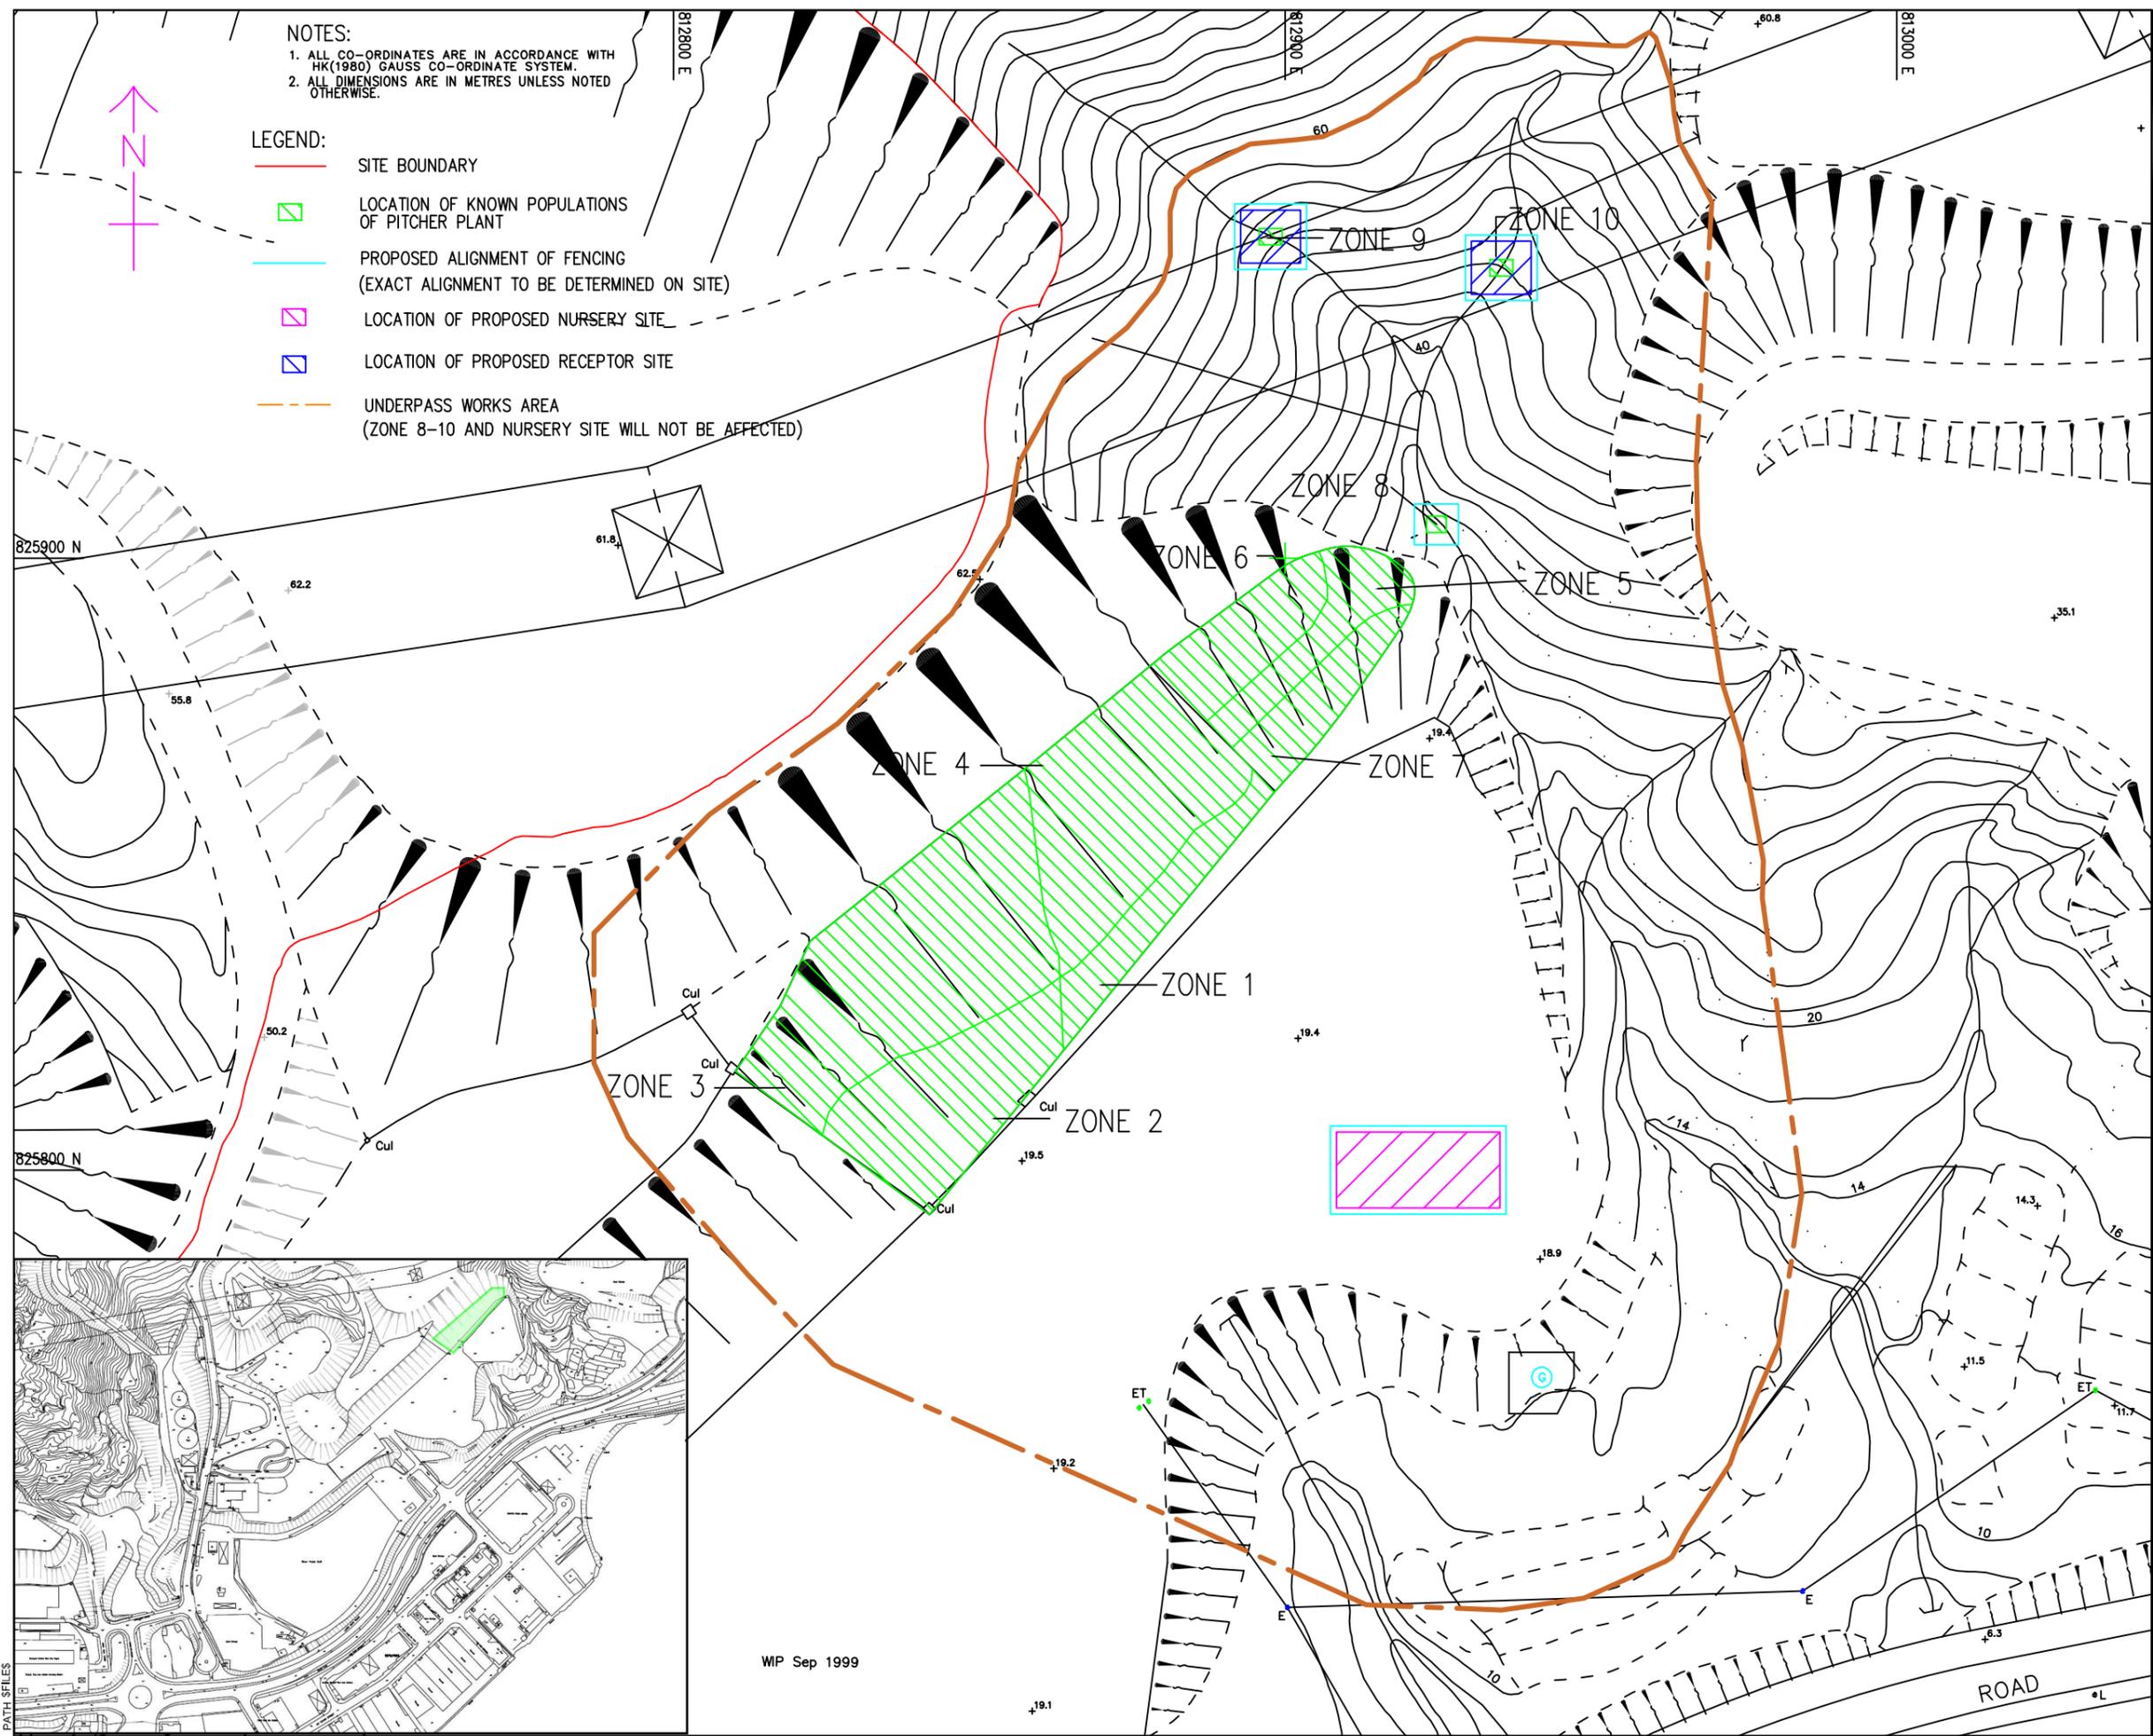

WP Sep 1999

AECOM

PROJECT
TUEN MUN - CHEK LAP KOK LINK

CONTRACT TITLE
TUEN MUN - CHEK LAP KOK LINK - NORTHERN CONNECTION TOLL PLAZA AND ASSOCIATED WORKS

CLIENT
路政署
HIGHWAYS DEPARTMENT
香港路政署工程管理部
Hong Kong - Zhuhai - Macao Bridge
Hong Kong Project Management Office

CONSULTANT
AECOM Asia Company Ltd.
www.aecom.com

SUB-CONSULTANTS

ISSUE/REVISION

NO.	DATE	DESCRIPTION	CHK.
A	FEB.14	TENDER ADDENDUM NO. 1	CWN
-	JAN.14	TENDER DRAWING	CWN

STATUS
PRELIMINARY

SCALE
A1 1 : 500

DIMENSION UNIT
METRES

KEY PLAN

PROJECT NO.
60240249

CONTRACT NO.
HY/2013/12

SHEET TITLE
LOCATION OF KNOWN POPULATION OF PITCHER PLANT AND PROPOSED TM-CLKL SITE BOUNDARY

SHEET NUMBER
60240249/C3/6503A

Appendix F

Event and Action Plan

Event and Action Plan for Air Quality

EVENT	ACTION			
	ET ⁽¹⁾	IEC ⁽¹⁾	SOR ⁽¹⁾	Contractor(s)
Action Level				
Exceedance recorded	1 Identify the source. 2 Repeat measurements to confirm findings. If two consecutive measurements exceed Action Level, the exceedance is then confirmed. 3 Inform the IEC and the SOR 4 Investigate the cause of exceedance and check Contractor's working procedures to determine possible mitigation to be implemented. 5 If the exceedance is confirmed to be Project related after investigation, increase monitoring frequency to daily. 6 Discuss with the IEC and the Contractor on remedial actions required. 7 If exceedance continues, arrange meeting with the IEC and the SOR. 8 If exceedance stops, cease additional monitoring.	1 Check monitoring data submitted by the ET. 2 Check the Contractor's working method. 3 If the exceedance is confirmed to be Project related after investigation, discuss with the ET and the Contractor on possible remedial measures. 4 Advise the SOR on the effectiveness of the proposed remedial measures. 5 Supervisor implementation of remedial measures.	1 Confirm receipt of notification of failure in writing. 2 Notify the Contractor. 3 Ensure remedial measures properly implemented.	1 Rectify any unacceptable practice. 2 Amend working methods if appropriate 3 If the exceedance is confirmed to be Project related, submit proposals for remedial actions to IEC within 3 working days of notification 4 Implement the agreed proposals 5 Amend proposal if appropriate.
Limit Level				
Exceedance recorded	1. Identify the source. 2. Repeat measurement to confirm finding. If two consecutive measurements exceed Limit Level, the exceedance is then confirmed. 3. Inform the IEC, the SOR, the DEP and the Contractor. 4. Investigate the cause of exceedance and check Contractor's working procedures to determine possible mitigation to be implemented. 5. If the exceedance is confirmed to be Project related after investigation, increase monitoring frequency to daily. 6. Carry out analysis of the Contractor's working procedures to determine possible mitigation to be implemented. 7. Arrange meeting with the IEC and the SOR to discuss the remedial actions to be taken. 8. Assess effectiveness of the Contractor's remedial actions and keep the IEC, the DEP and the SOR informed of the results. 9. If exceedance stops, cease additional monitoring.	1 Check monitoring data submitted by the ET. 2 Check Contractor's working method. 3 If the exceedance is confirmed to be Project related after investigation, discuss with the ET and the Contractor on possible remedial measures. 4 Advise the SOR on the effectiveness of the proposed remedial measures. 5 Supervisor implementation of remedial measures.	1. Confirm receipt of notification of failure in writing. 2. Notify the Contractor. 3. If the exceedance is confirmed to be Project related after investigation, in consultation with the IEC, agree with the Contractor on the remedial measures to be implemented. 4. Ensure remedial measures are properly implemented. 5. If exceedance continues, consider what activity of the work is responsible and instruct the Contractor to stop that activity of work until the exceedance is abated.	1 Take immediate action to avoid further exceedance. 2 If the exceedance is confirmed to be Project related after investigation, submit proposals for remedial actions to IEC within 3 working days of notification. 3 Implement the agreed proposals. 4 Amend proposal if appropriate. 5 Stop the relevant activity of works as determined by the SOR until the exceedance is abated.

Event and Action Plan for Landscape and Visual Impact

EVENT ACTION LEVEL	ACTION			
	ET	IEC	ER	Contractor
Design Check	<ul style="list-style-type: none"> Check final design conforms to the requirements of EP and prepare report. 	<ul style="list-style-type: none"> Check report. Recommend remedial design if necessary 	<ul style="list-style-type: none"> Undertake remedial design if necessary 	
Non- conformity on one occasion	<ul style="list-style-type: none"> Identify Source Inform IEC and ER Discuss remedial actions with IEC, ER and Contractor Monitor remedial actions until rectification has been completed 	<ul style="list-style-type: none"> Check report Check Contractor's working method Discuss with ET and Contractor on possible remedial measures Advise ER on effectiveness of proposed remedial measures. Check implementation of remedial measures 	<ul style="list-style-type: none"> Notify Contractor Ensure remedial measures are properly implemented 	<ul style="list-style-type: none"> Amend working methods Rectify damage and undertake any necessary replacement
Repeated Non-conformity	<ul style="list-style-type: none"> Identify Source Inform IEC and ER Increase monitoring frequency Discuss remedial actions with IEC, ER and Contractor Monitor remedial actions until rectification has been completed If nonconformity stops, cease additional monitoring 	<ul style="list-style-type: none"> Check monitoring report Check Contractor's working method Discuss with ET and Contractor on possible remedial measures Advise ER on effectiveness of proposed remedial measures Supervise implementation of remedial measures 	<ul style="list-style-type: none"> Notify Contractor Ensure remedial measures are properly implemented 	<ul style="list-style-type: none"> Amend working methods Rectify damage and undertake any necessary replacement

Event / Action Plan for Cultural Heritage

Action Level	ET	IC (E)	ER	Contractor
Non-conformity on one occasion	<ol style="list-style-type: none"> 1. Identify Source 2. Inform the IEC and the ER 3. Discuss remedial actions with the IEC, the ER and the Contractor 4. Monitor remedial actions until rectification has been completed 	<ol style="list-style-type: none"> 1. Check report 2. Check the Contractor's working method 3. Discuss with the ET and the Contractor on possible remedial measures 4. Advise the ER on effectiveness of proposed remedial measures. 5. Check implementation of remedial measures. 	<ol style="list-style-type: none"> 1. Notify Contractor 2. Ensure remedial measures are properly implemented 	<ol style="list-style-type: none"> 1. Amend working methods 2. Rectify damage and undertake any necessary replacement
Repeated Non-conformity	<ol style="list-style-type: none"> 1. Identify Source 2. Inform the IC(E) and the ER 3. Increase monitoring frequency 4. Discuss remedial actions with the IC(E), the ER and the Contractor 5. Monitor remedial actions until 6. rectification has been completed 7. If exceedance stops, cease additional monitoring 	<ol style="list-style-type: none"> 1. Check monitoring report 2. Check the Contractor's working method 3. Discuss with the ES and the Contractor on possible remedial measures 4. Advise the ER on effectiveness of proposed remedial measures 5. Supervise implementation of remedial measures. 	<ol style="list-style-type: none"> 1. Notify the Contractor 2. Ensure remedial measures are properly implemented 	<ol style="list-style-type: none"> 1. Amend working methods 2. Rectify damage and undertake any necessary replacement

Note:

ET – Environmental Specialist, IEC – Independent Environmental Checker, ER – Engineer's Representative

Event / Action Plan for General Ecology

Action Level	ET	IEC	ER	Contractor
Non-conformity on one occasion	<ul style="list-style-type: none"> Identify Source Inform the IEC and the ER Discuss remedial actions with the IEC, the ER and the Contractor Monitor remedial actions until rectification has been completed 	<ul style="list-style-type: none"> Check report Check the Contractor's working method Discuss with the ET and the Contractor on possible remedial measures Advise the ER on effectiveness of proposed remedial measures. Check implementation of remedial measures. 	<ul style="list-style-type: none"> Notify Contractor Ensure remedial measures are properly implemented Consider and instruct, if necessary, the Contractor to slow down or to stop all or part of the works in the case of a serious nonconformity until situation rectified. 	<ul style="list-style-type: none"> Amend working methods Rectify damage and undertake any necessary replacement
Repeated Non conformity	<ul style="list-style-type: none"> Identify Source Inform the IC(E) and the ER Increase monitoring frequency Discuss remedial actions with the IC(E), the ER and the Contractor Monitor remedial actions until rectification has been completed If exceedance stops, cease additional monitoring 	<ul style="list-style-type: none"> Check monitoring report Check the Contractor's working method Discuss with the ES and the Contractor on possible remedial measures Advise the ER on effectiveness of proposed remedial measures Supervise implementation of remedial measures 	<ul style="list-style-type: none"> Notify the Contractor Ensure remedial measures are properly implemented Consider and instruct, if necessary, the Contractor to slow down or to stop all or part of the works in the case of a serious nonconformity until situation rectified. 	<ul style="list-style-type: none"> Amend working methods Rectify damage and undertake any necessary replacement


Note: ET – Environmental Specialist, IC(E) – Independent Checker (Environmental), ER – Engineer's Representative

Actions in the Event of Landfill Gas being Detected in Excavation / Confined Area

Parameter	Measurement	Action
Oxygen	< 19%	- Ventilate to restore oxygen to > 19%
	< 18%	- Stop work - Evacuate personnel / prohibit entry - Increase ventilation to restore to > 19%
Methane	> 10% LEL (> 0.5% v/v)	- Prohibit hot work - Ventilate to restore methane to < 10% LEL
	> 20% LEL (>1% v/v)	- Stop work - Evacuate personnel / prohibit entry - Increase ventilation to restore to < 10%
Carbon Dioxide	> 0.5%	- Ventilate to restore oxygen to < 0.5%
	> 1.5%	- Stop work - Evacuate personnel / prohibit entry - Increase ventilation to restore to < 0.5%


Appendix G

Landfill Gas Monitoring Graphical Plots

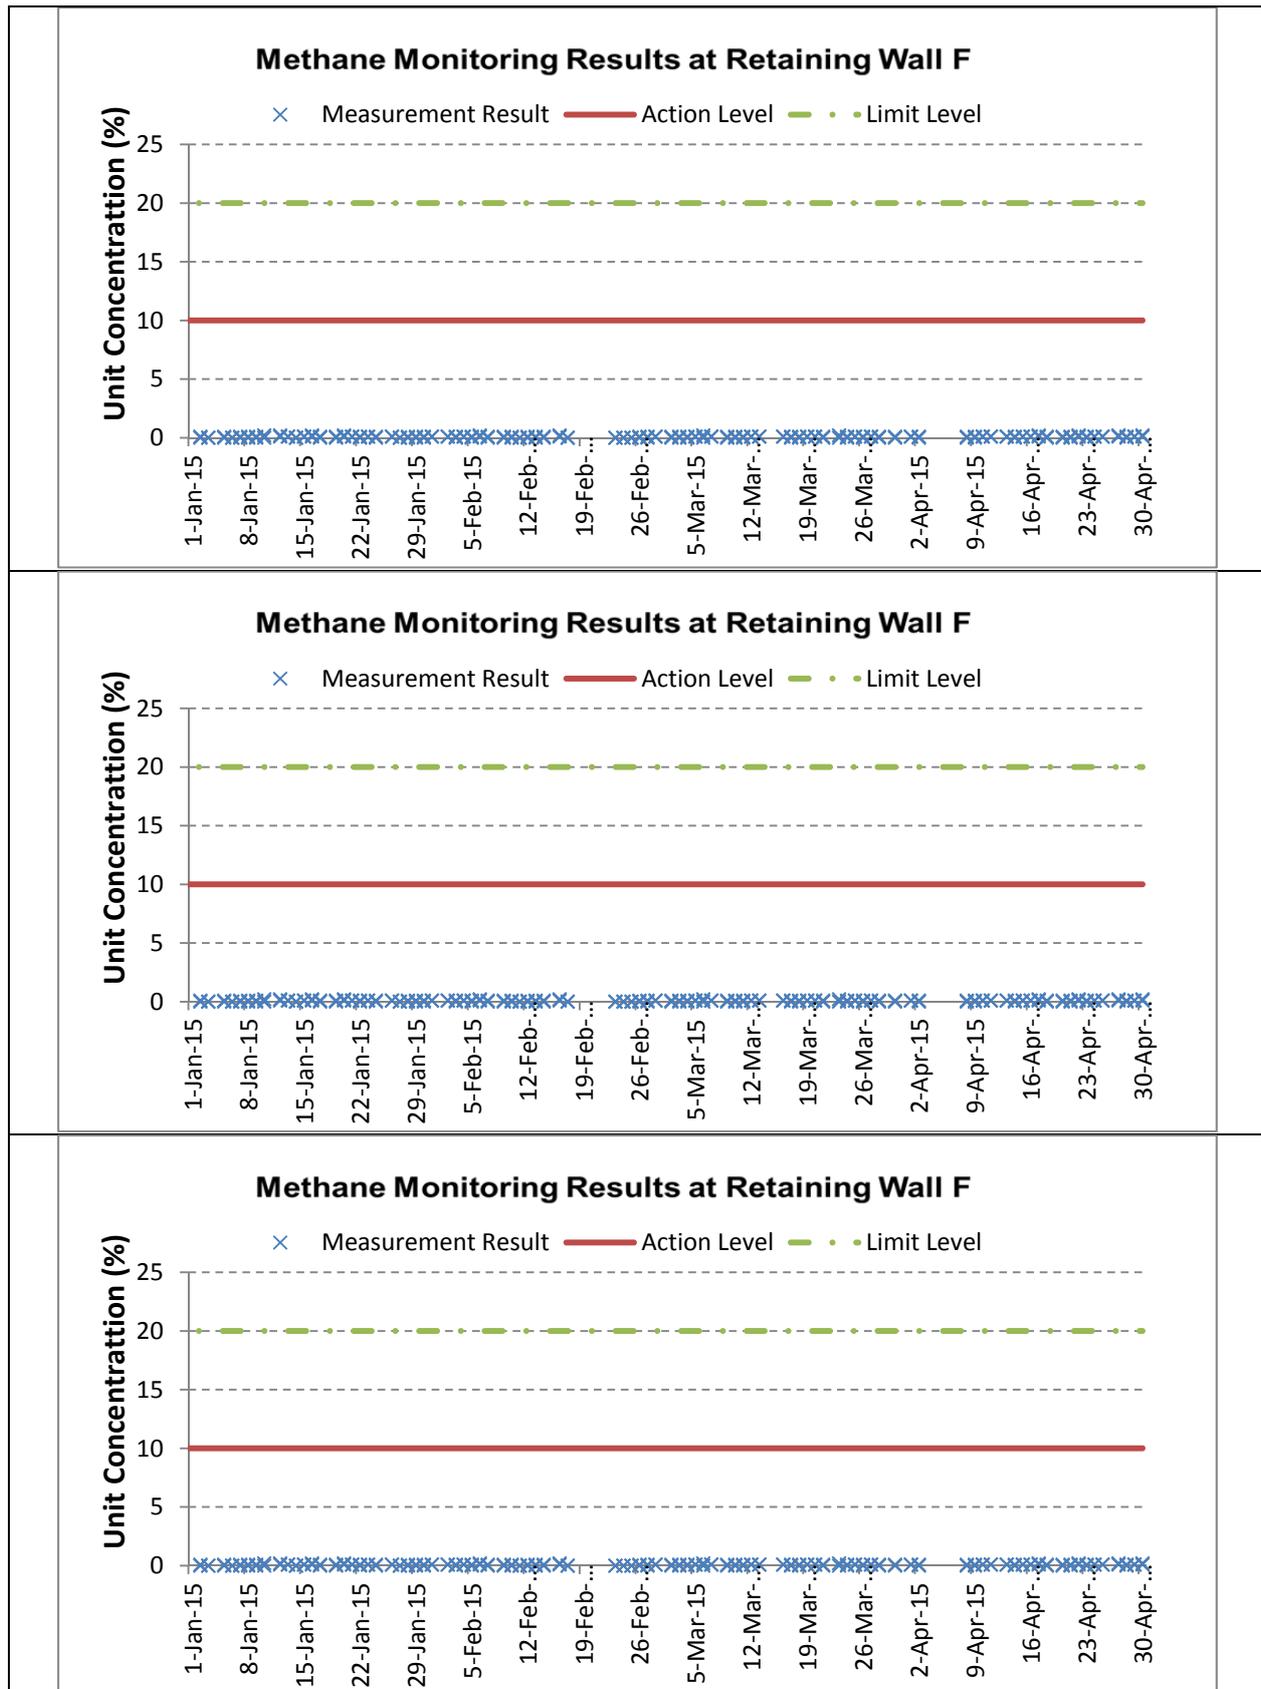

Annotation:

During 1 January to 30 April 2015, major construction activity was construction of retaining wall F and the specified works included excavation, rock breaking, blinding, formworking, steel-fixing and concreting. The weather condition varied from sunny to rainy. The monitoring data was provided by the Contractor followed to their QA/QC control.

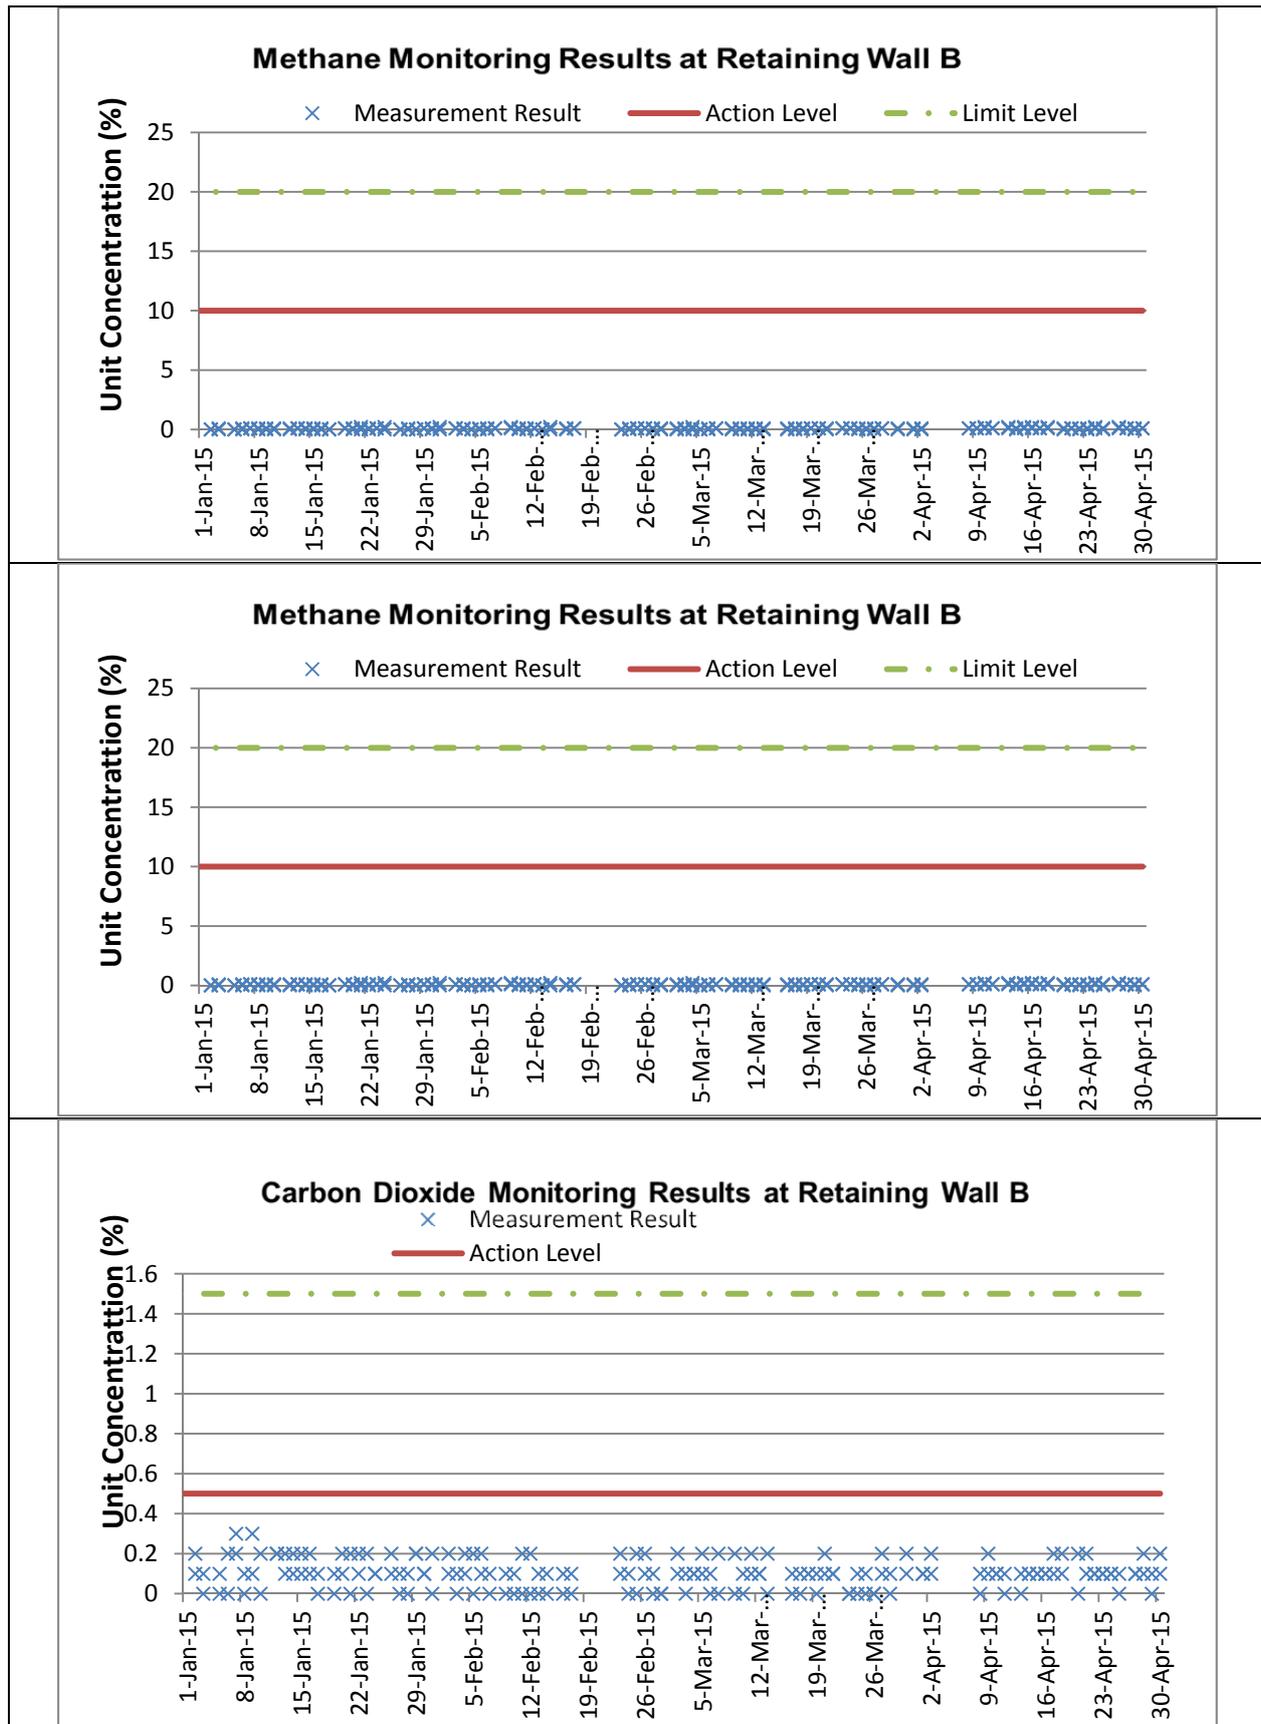

Annotation:

During 1 January to 30 April 2015, major construction activity was construction of retaining wall B and the specified works included excavation, rock breaking, blinding, formworking, steel-fixing and concreting. The weather condition varied from sunny to rainy. The monitoring data was provided by the Contractor followed to their QA/QC control.

Appendix H

Waste Flow Table

Monthly Waste Flow Table

Monthly Summary Waste Flow Table for 2015 (year)

Month	Annual Quantities of Inert C&D Materials Generated Monthly						Annual Quantities of C&D Wastes Generated Monthly				
	Total Quantity Generated	Broken Concrete	Reused in the Contract	Reused in other Projects	Disposed as Public Fill	Imported Fill	Metals	Paper / cardboard packaging	Plastics (see note 2)	Chemical Waste	Others (general refuse)
	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000m ³)
Jan	40.959	0.000	11.915	23.31	5.664	0	0.000	0.000	0.000	0.000	0.07
Feb	50.363	0.000	24.411	25.313	0.629	0	0.000	0.000	0.000	0.000	0.01
Mar	42.223	0.000	13.473	26.648	2.042	0	0.000	0.050	0.000	0.000	0.01
Apr	29.037	0.000	8.06	11.209	9.765	0	0.000	0.000	0.000	0.000	0.003
May	-	-	-	-	-	-	-	-	-	-	-
June	-	-	-	-	-	-	-	-	-	-	-
Sub-total	-	-	-	-	-	-	-	-	-	-	-
July	-	-	-	-	-	-	-	-	-	-	-
Aug	-	-	-	-	-	-	-	-	-	-	-
Sept	-	-	-	-	-	-	-	-	-	-	-
Oct	-	-	-	-	-	-	-	-	-	-	-
Nov	-	-	-	-	-	-	-	-	-	-	-
Dec	-	-	-	-	-	-	-	-	-	-	-
Total	162.582	0.000	57.859	86.480	18.100	0.000	0.000	0.050	0.000	0.000	0.093

Notes:

- 1 The waste flow table shall also include C&D materials that are specified in the contract to be imported for use at the Site.
- 2 Plastics refer to plastic bottles/containers, plastic sheets/foam from packaging materials.
- 3 Broken concrete for recycling into aggregates.

Appendix I

Implementation Schedule for Environmental Mitigation Measures

CONTRACT NO. HY/2013/12

**TUEN MUN – CHECK LAP KOK LINK – NORTHERN CONNECTION TOLL PLAZA AND ASSOCIATED WORKS
ENVIRONMENTAL MITIGATION AND ENHANCEMENT MEASURE IMPLEMENTATION SCHEDULE**

Air Quality									
EIA reference	EM&A Manual reference	Environmental Protection Measures	Location/ Timing	Implementation Agent	Relevant Standard or Requirement	Implementation Stages			Status *
						D	C	O	
4.8.1	3.8	An effective watering programme of twice daily watering with complete coverage, is estimated to reduce by 50%. This is recommended for all areas in order to reduce dust levels to a minimum;	All areas / throughout construction period	Contractor	TMEIA Avoid smoke impacts and disturbance		Y		✓
4.8.1	3.8	Watering of the construction sites in Lantau for 8 times/day and in Tuen Mun for 12 times/day to reduce dust emissions by 87.5% and 91.7% respectively and shall be undertaken.	All areas / throughout construction period	Contractor	TMEIA Avoid dust generation		Y		<>
4.8.1	3.8	The Contractor shall, to the satisfaction of the Engineer, install effective dust suppression measures and take such other measures as may be necessary to ensure that at the Site boundary and any nearby sensitive receiver, dust levels are kept to acceptable levels.	All areas / throughout construction period	Contractor	TMEIA Avoid dust generation		Y		✓
4.8.1	3.8	The Contractor shall not burn debris or other materials on the works areas.	All areas / throughout construction period	Contractor	TMEIA Avoid dust generation		Y		✓
4.8.1	3.8	In hot, dry or windy weather, the watering programme shall maintain all exposed road surfaces and dust sources wet.	All unpaved haul roads / throughout construction period in hot, dry or windy weather	Contractor	TMEIA Avoid smoke impacts and disturbance		Y		<>
4.8.1	3.8	Where breaking of oversize rock/concrete is required, watering shall be implemented to control dust. Water spray shall be used during the handling of fill material at the site and at active cuts, excavation and fill sites where dust is likely to be created.	All areas / throughout construction period	Contractor	TMEIA Avoid dust generation		Y		<>
4.8.1	3.8	Open dropping heights for excavated materials shall be controlled to a maximum height of 2m to minimise the fugitive dust arising from unloading.	All areas / throughout construction period	Contractor	TMEIA Avoid dust generation		Y		✓

CONTRACT NO. HY/2013/12

**TUEN MUN – CHECK LAP KOK LINK – NORTHERN CONNECTION TOLL PLAZA AND ASSOCIATED WORKS
ENVIRONMENTAL MITIGATION AND ENHANCEMENT MEASURE IMPLEMENTATION SCHEDULE**

4.8.1	3.8	During transportation by truck, materials shall not be loaded to a level higher than the side and tail boards, and shall be dampened or covered before transport.	All areas / throughout construction period	Contractor	TMEIA Avoid dust generation		Y		✓
4.8.1	3.8	Materials having the potential to create dust shall not be loaded to a level higher than the side and tail boards, and shall be covered by a clean tarpaulin. The tarpaulin shall be properly secured and shall extend at least 300mm over the edges of the side and tail boards.	All areas / throughout construction period	Contractor	TMEIA Avoid dust generation		Y		✓
4.8.1	3.8	No earth, mud, debris, dust and the like shall be deposited on public roads. Wheel washing facility shall be usable prior to any earthworks excavation activity on the site.	construction period	Contractor	TMEIA Avoid dust generation		Y		✓
4.8.1	3.8	Areas of exposed soil shall be minimized to areas in which works have been completed shall be restored as soon as is practicable.	All exposed surfaces / throughout construction period	Contractor	TMEIA Avoid dust generation		Y		✓
4.8.1	3.8	All stockpiles of aggregate or spoil shall be enclosed or covered and water applied in dry or windy condition.	All areas / throughout construction period	Contractor	TMEIA Avoid dust generation		Y		✓
4.11	Section 3	EM&A in the form of 1 hour and 24 hour dust monitoring and site audit	All representative existing ASRs / throughout construction period	Contractor	EM&A Manual		Y		✓

Cultural Heritage

EIA reference	EM&A Manual reference	Environmental Protection Measures	Location/ Timing	Implementation Agent	Relevant Standard or Requirement	Implementation Stages			Status
						D	C	O	
11.8	Section 9	EM&A in the form of audit of the mitigation measures	All areas / throughout construction period	Highways Department	EIAO-TM		Y		✓

Ecology

EIA reference	EM&A Manual reference	Environmental Protection Measures	Location/ Timing	Implementation Agent	Relevant Standard or Requirement	Implementation Stages			Status
						D	C	O	

CONTRACT NO. HY/2013/12

**TUEN MUN – CHECK LAP KOK LINK – NORTHERN CONNECTION TOLL PLAZA AND ASSOCIATED WORKS
ENVIRONMENTAL MITIGATION AND ENHANCEMENT MEASURE IMPLEMENTATION SCHEDULE**

7.13#	6.3, 6.5#	Fencing or other physical barriers for protection of Pitcher Plant around Zones 8, 9 and 10 and the temporary nursery site	Tuen Mun Area 46 shrubland/ Detailed/ Prior to construction	Design Consultant/ Contractor	TMEIA	Y	Y		✓
7.13	6.5	Audit Pitcher Plant protection measures	Tuen Mun Area 46	Contractor	TMEIA		Y		✓
7.13	6.5	The loss of habitat shall be supplemented by enhancement planting in accordance with the landscape mitigation schedule.	All areas / As soon as accessible	Contractor	TMEIA		Y		✓
7.13	6.5	Spoil heaps shall be covered at all times.	All areas / Throughout construction period	Contractor	TMEIA		Y		✓
7.13	6.5	Avoid damage and disturbance to the remaining and surrounding natural habitat	All areas / Throughout construction period	Contractor	TMEIA		Y		✓
7.13	6.5	Placement of equipment in designated areas within the existing disturbed land	All areas / Throughout construction period	Contractor	TMEIA		Y		✓
7.13	6.5	Disturbed areas to be reinstated immediately after completion of the works.	All areas / Throughout construction period	Contractor	TMEIA		Y		✓
7.13	6.5	Construction activities should be restricted to the proposed works boundary	All areas / Throughout construction	Contractor	TMEIA		Y		✓

Landfill Gas Hazard Assessment

EIA reference	EM&A Manual reference	Environmental Protection Measures	Location/ Timing	Implementation Agent	Relevant Standard or Requirement	Implementation Stages			Status
						D	C	O	
14.12.2	14.2	<u>Appointment of Safety Officer</u> Appoint a properly trained safety officer and provide with appropriate equipment to measure and monitor LFG hazard. The monitoring frequency and areas to be monitored should be set down prior to commencement of ground-works either by the Safety Officer or an approved and appropriately qualified person.	Construction Stage	Contractor	EPD/TR8/97 - Landfill Gas Hazard Assessment Guidance Note		Y		✓
14.12.2	-	<u>Safety Measures - Excavation</u>	Construction Stage	Contractor	EPD/TR8/97 -		Y		✓

CONTRACT NO. HY/2013/12

**TUEN MUN – CHECK LAP KOK LINK – NORTHERN CONNECTION TOLL PLAZA AND ASSOCIATED WORKS
ENVIRONMENTAL MITIGATION AND ENHANCEMENT MEASURE IMPLEMENTATION SCHEDULE**

		Staff should receive appropriate training on working in areas susceptible to landfill gas, fire and explosion hazards. Excavation procedures and code of practice should be implemented.			Landfill Gas Hazard Assessment Guidance Note				
14.12.2	-	<u>Safety Measures – Welding, Flame- Cutting and Hot works</u> Hot works should be confined to open areas away from any trench or excavation. Should hot works must be carried out in trenches or confined space, “permit to work” procedures should be followed.	Construction Stage	Contractor	EPD/TR8/97 - Landfill Gas Hazard Assessment Guidance Note		Y		✓
14.12.2	-	<u>Safety Measures – Enclosed Spaces</u> Site offices or buildings located within PPV Landfill Consultation Zone which have the capacity to accumulate landfill gas, then they should either be located in an area which has been proven to be free of landfill gas; or be raised clear of the ground by a minimum of 500mm.	Site office, building, tunnel, subway, confined area / Construction Stage	Contractor	EPD/TR8/97 - Landfill Gas Hazard Assessment Guidance Note		Y		✓
14.12.2	-	<u>Safety Measures – Electrical Equipment</u> Any electrical equipment, such as motors and extension cords, should be intrinsically safe.	Construction Stage	Contractor	EPD/TR8/97 - Landfill Gas Hazard Assessment Guidance Note		Y		✓
14.12.2	-	<u>Safety Measures – Piping</u> During piping assembly or conduiting construction, all valves/seals should be closed immediately after installation. As construction progresses, all valves/seals should be closed as installed to prevent the migration of gases through the pipeline/conduit. All piping/conduiting should be capped at the end of each working day.	Services & utilities / Construction Stage	Contractor	EPD/TR8/97 - Landfill Gas Hazard Assessment Guidance Note		Y		✓
14.12.2	-	<u>Safety Measures – Fire Safety</u> Adequate fire safety equipments should be provided on site. Workers and visitors should be notified of the potential fire hazards. Safety notices should be	Construction Stage	Contractor	EPD/TR8/97 - Landfill Gas Hazard Assessment		Y		✓

CONTRACT NO. HY/2013/12

**TUEN MUN – CHECK LAP KOK LINK – NORTHERN CONNECTION TOLL PLAZA AND ASSOCIATED WORKS
ENVIRONMENTAL MITIGATION AND ENHANCEMENT MEASURE IMPLEMENTATION SCHEDULE**

		posted around the site warning the anger and potential hazards.			Guidance Note				
14.12.1	-	<u>Safety Measures – Confined Spaces</u> Precautionary measures should include ensuring that staff members are aware of the potential hazards of working in confined spaces, and that appropriate monitoring procedures are in place to prevent hazards in confined spaces.	Confined space / Construction Stage	Contractor	EPD/TR8/97 - Landfill Gas Hazard Assessment Guidance Note		Y		✓
14.12.1	-	<u>Monitoring</u> Periodically during ground-works within the Consultation Zone, the works area should be monitored for methane, carbon dioxide and oxygen using appropriately calibrated portable gas detection equipment. Depending on the results of the measurements, actions required will vary. As a minimum these should encompass those actions specified in Table 14.8 of the EIA Report or Table 14.1 of the EM&A Manual.	Construction Stage	Contractor	EPD/TR8/97 - Landfill Gas Hazard Assessment Guidance Note		Y		✓

Landscape and Visual

EIA reference	EM&A Manual reference	Environmental Protection Measures	Location/ Timing	Implementation Agent	Relevant Standard or Requirement	Implementation Stages			Status
						D	C	O	
10.9	7.6	Existing trees on boundary of the Project Area shall be carefully protected during construction. Detailed Tree Protection Specification shall be provided in the Contract Specification. Under this specification, the Contractor shall be required to submit, for approval, a detailed working method statement for the protection of trees prior to undertaking any works adjacent to all retained trees, including trees in contractor's works areas. (Tree protection measures will be detailed at Tree Removal Application stage) (CM1)	All areas/detailed design/ during construction	Design Consultant/ Contractor	TMEIA	Y	Y		✓
10.9	7.6	Trees unavoidably affected by the works shall be transplanted where practical. Trees will be	All areas/detailed design/ during	Design Consultant/	TMEIA	Y	Y		✓

CONTRACT NO. HY/2013/12

**TUEN MUN – CHECK LAP KOK LINK – NORTHERN CONNECTION TOLL PLAZA AND ASSOCIATED WORKS
ENVIRONMENTAL MITIGATION AND ENHANCEMENT MEASURE IMPLEMENTATION SCHEDULE**

		transplanted straight to their final receptor site and not held in a temporary nursery. A detailed Tree Transplanting Specification shall be provided in the Contract Specification. Sufficient time for necessary tree root and crown preparation periods shall be allowed in the project programme (CM2)	construction	Contractor					
10.9	7.6	Hillside and roadside screen planting to proposed roads, associated structures and slope works (CM3)	All areas/detailed design/ during Construction/ post construction	Design Consultant/ Contractor	TMEIA	Y	Y		✓
10.9	7.6	Hydroseeding or sheeting of soil stockpiles with visually unobtrusive material (in earth tone) (CM4)	All areas/detailed design/ during Construction/ post construction	Design Consultant/ Contractor	TMEIA	Y	Y		✓
10.9	7.6	Screening of construction works by hoardings around works area in visually unobtrusive colours, to screen works (CM5)	All areas/detailed design/ during Construction	Design Consultant/ Contractor	TMEIA	Y	Y		✓
10.9	7.6	Control night-time lighting and glare by hooding all lights (CM6)	All areas/detailed design/ during Construction	Design Consultant/ Contractor	TMEIA	Y	Y		✓
10.9	7.6	Ensure no run-off into water body adjacent to the Project Area (CM7)	All areas/detailed design/ during Construction	Design Consultant/ Contractor	TMEIA	Y	Y		✓
10.9	7.6	Avoidance of excessive height and bulk of buildings and structures (CM8)	All areas/detailed design/ during Construction	Design Consultant/ Contractor	TMEIA	Y	Y		✓
10.9	7.6	Recycle/Reuse all felled trees and vegetation, e.g. mulching (CM9)	All areas/detailed design/ during Construction	Design Consultant/ Contractor	TMEIA	Y	Y		✓
10.9	7.6	Compensatory tree planting shall be provided to the satisfaction of relevant Government departments. Required numbers and locations of compensatory trees shall be determined and agreed separately with Government during the Tree Felling Application process under ETWBTC 3/2006 (CM10)	All areas/detailed design/ during Construction	Design Consultant/ Contractor	TMEIA	Y	Y		✓
10.9	7.6	Re-vegetation of affected woodland/shrubland with	All areas/detailed design/ during Construction	Design	TMEIA	Y	Y	Y	N/A

CONTRACT NO. HY/2013/12

**TUEN MUN – CHECK LAP KOK LINK – NORTHERN CONNECTION TOLL PLAZA AND ASSOCIATED WORKS
ENVIRONMENTAL MITIGATION AND ENHANCEMENT MEASURE IMPLEMENTATION SCHEDULE**

		native species (OM1)	during Construction/ post construction	Consultant/ Contractor					
10.9	7.6	Tall buffer screen tree / shrub / climber planting where appropriate should be incorporated to soften hard engineering structures and facilities (OM2)	All areas/detailed design/ during Construction/ post construction	Design Consultant/ Contractor	TMEIA	Y	Y	Y	N/A
10.9	7.6	Streetscape elements (e.g. paving, signage, street furniture, lighting etc.) shall be sensitively designed in a manner that responds to the local context, and minimises potential negative landscape and visual impacts. Lighting units should be directional and minimize unnecessary light spill (OM3)	All areas/detailed design/ during Construction/ post construction	Design Consultant/ Contractor	TMEIA	Y	Y	Y	N/A
10.9	7.6	Structure, ornamental tree / shrub / climber planting should be provided along roadside amenity strips, central dividers and newly formed slopes to enhance the townscape quality and further greenery enhancement (OM4)	All areas/detailed design/ during Construction/ post construction	Design Consultant/ Contractor	TMEIA	Y	Y	Y	N/A
10.9	7.6	Aesthetically pleasing design (visually unobtrusive and non-reflective) as regard to the form, material and finishes shall be incorporated to all buildings, engineering structures and associated infrastructure facilities (OM5)	All areas/detailed design/ during Construction/ post construction	Design Consultant/ Contractor	TMEIA	Y	Y	Y	N/A
10.9	7.6	Avoidance of excessive height and bulk of buildings and structures (OM6)	All areas/detailed design/ during Construction/ post construction	Design Consultant/ Contractor	TMEIA	Y	Y	Y	N/A
Waste									
EIA reference	EM&A Manual reference	Environmental Protection Measures	Location/ Timing	Implementation Agent	Relevant Standard or Requirement	Implementation Stages			Status
						D	C	O	
12.6		The Contractor shall identify a coordinator for the management of waste.	Contract mobilisation	Contractor	TMEIA		Y		✓
12.6		The Contractor shall prepare and implement a Waste Management Plan which specifies procedures such	Contract mobilisation	Contractor	TMEIA, Works Branch		Y		✓

CONTRACT NO. HY/2013/12

**TUEN MUN – CHECK LAP KOK LINK – NORTHERN CONNECTION TOLL PLAZA AND ASSOCIATED WORKS
ENVIRONMENTAL MITIGATION AND ENHANCEMENT MEASURE IMPLEMENTATION SCHEDULE**

		as a ticketing system, to facilitate tracking of loads and to ensure that illegal disposal of wastes does not occur, and protocols for the maintenance of records of the quantities of wastes generated, recycled and disposed. A recording system for the amount of waste generated, recycled and disposed (locations) should be established.			Technical Circular No. 5/99 for the Trip-ticket System for Disposal of Construction and Demolition Material				
12.6		The Contractor shall apply for and obtain the appropriate licenses for the disposal of public fill, chemical waste and effluent discharges.	Contract mobilisation	Contractor	TMEIA, Land (Miscellaneous Provisions) Ordinance (Cap 28); Waste Disposal Ordinance (Cap 354); Dumping at Sea Ordinance (Cap 466); Water Pollution Control Ordinance.		Y		✓
12.6	8.1	Training shall be provided to workers about the concepts of site cleanliness and appropriate waste management procedures including waste reduction, reuse and recycling	Contract mobilisation	Contractor	TMEIA		Y		✓
12.6	8.1	The extent of cutting operation should be optimised where possible. Earth retaining structures and bored pile walls should be proposed to minimize the extent of cutting.	All areas / throughout construction period	Contractor	TMEIA		Y		✓

CONTRACT NO. HY/2013/12

**TUEN MUN – CHECK LAP KOK LINK – NORTHERN CONNECTION TOLL PLAZA AND ASSOCIATED WORKS
ENVIRONMENTAL MITIGATION AND ENHANCEMENT MEASURE IMPLEMENTATION SCHEDULE**

12.6	8.1	Inert C&D materials from the toll plaza cut slopes shall be reused for construction of the raised platform for the toll plaza where possible.	Toll Plaza / toll plaza construction period	Contractor	TMEIA		Y		✓
12.6	8.1	The site and surroundings shall be kept tidy and litter free.	All areas / throughout construction period	Contractor	TMEIA		Y		✓
12.6	8.1	No waste shall be burnt on site.	All areas / throughout construction period	Contractor	TMEIA		Y		✓
12.6	8.1	The Contractor shall be prohibited from disposing of C&D materials at any sensitive locations. The Contractor should propose the final disposal sites in the EMP and WMP for approval before implementation.	All areas / throughout construction period	Contractor	TMEIA		Y		✓
12.6	8.1	Stockpiled material shall be covered by tarpaulin and /or watered as appropriate to prevent windblown dust/ surface run off.	All areas / throughout construction period	Contractor	TMEIA		Y		◇
12.6	8.1	Excavated material in trucks shall be covered by tarpaulins to reduce the potential for spillage and dust generation.	All areas / throughout construction period	Contractor	TMEIA		Y		✓
12.6	8.1	Wheel washing facilities shall be used by all trucks leaving the site to prevent transfer of mud onto public roads.	All areas / throughout construction period	Contractor	TMEIA		Y		✓
12.6	8.1	Standard formwork or pre-fabrication should be used as far as practicable so as to minimise the C&D materials arising. The use of more durable formwork/ plastic facing for construction works should be considered. The use of wooden hoardings should be avoided and metal hoarding should be used to facilitate recycling. Purchasing of construction materials should avoid over-ordering and wastage.	All areas / throughout construction period	Contractor	TMEIA		Y		✓
12.6	8.1	The Contractor should recycle as many C&D materials (this is a waste section) as possible on-site. The public fill and C&D waste should be segregated and stored in separate containers or skips to facilitate the reuse or recycling of materials and proper	All areas / throughout construction period	Contractor	TMEIA		Y		✓

CONTRACT NO. HY/2013/12

**TUEN MUN – CHECK LAP KOK LINK – NORTHERN CONNECTION TOLL PLAZA AND ASSOCIATED WORKS
ENVIORNMENTAL MITIGATION AND ENHANCEMENT MEASURE IMPLEMENTATION SCHEDULE**

		disposal. Where practicable, the concrete and masonry should be crushed and used as fill materials. Steel reinforcement bar should be collected for use by scrap steel mills. Different areas of the sites should be considered for segregation and storage activities.							
12.6	8.1	All falsework will be steel instead of wood.	All areas / throughout construction period	Contractor	TMEIA		Y		◇
12.6	8.1	Chemical waste producers should register with the EPD. Chemical waste should be handled in accordance with the Code of Practice on the Packaging, Handling and Storage of Chemical Wastes as follows: <ul style="list-style-type: none"> • suitable for the substance to be held, resistant to corrosion, maintained in good conditions and securely closed; • Having a capacity of <450L unless the specifications have been approved by the EPD; and • Displaying a label in English and Chinese according to the instructions prescribed in Schedule 2 of the Regulations. • Clearly labelled and used solely for the storage of chemical wastes; • Enclosed with at least 3 sides; • Impermeable floor and bund with capacity to accommodate 110% of the volume of the largest container or 20% by volume of the chemical waste stored in the area, whichever is greatest; • Adequate ventilation; • Sufficiently covered to prevent rainfall entering (water collected within the bund must be tested and disposed of as chemical waste, if necessary); and • Incompatible materials are adequately separated. 	All areas / throughout construction period	Contractor	TMEIA		Y		✓
12.6	8.1	Waste oils, chemicals or solvents shall not be	All areas / throughout	Contractor	TMEIA		Y		✓

CONTRACT NO. HY/2013/12

**TUEN MUN – CHECK LAP KOK LINK – NORTHERN CONNECTION TOLL PLAZA AND ASSOCIATED WORKS
ENVIRONMENTAL MITIGATION AND ENHANCEMENT MEASURE IMPLEMENTATION SCHEDULE**

		disposed of to drain,	construction period						
12.6	8.1	Adequate numbers of portable toilets should be provided for on-site workers. Portable toilets should be maintained in reasonable states, which will not deter the workers from utilising them.	All areas / throughout construction period	Contractor	TMEIA		Y		✓
12.6	8.1	Night soil should be regularly collected by licensed collectors.	All areas / throughout construction period	Contractor	TMEIA		Y		✓
12.6	8.1	General refuse arising on-site should be stored in enclosed bins or compaction units separately from C&D and chemical wastes. Sufficient dustbins shall be provided for storage of waste as required under the Public Cleansing and Prevention of Nuisances By-laws. In addition, general refuse shall be cleared daily and shall be disposed of to the nearest licensed landfill or refuse transfer station. Burning of refuse on construction sites is prohibited.	All areas / throughout construction period	Contractor	TMEIA		Y		◇
12.6	8.1	All waste containers shall be in a secure area on hardstanding;	All areas / throughout construction period	Contractor	TMEIA		Y		✓
12.6	8.1	Training shall be provided to workers about the concepts of site cleanliness and appropriate waste management procedure, including waste reduction, reuse and recycling.	All areas / throughout construction period	Contractor	TMEIA		Y		✓
12.6	8.1	Office wastes can be reduced by recycling of paper if such volume is sufficiently large to warrant collection. Participation in a local collection scheme by the Contractor should be advocated. Waste separation facilities for paper, aluminum cans, plastic bottles, etc should be provided on-site.	Site Offices/ throughout construction period	Contractor	TMEIA		Y		✓
12.6	Section 8	EM&A of waste handling, storage, transportation, disposal procedures and documentation through the site audit programme shall be undertaken.	All areas / throughout construction period	Contractor	EM&A Manual		Y		✓
Water Quality									
EIA reference	EM&A Manual reference	Environmental Protection Measures	Location/ Timing	Implementation Agent	Relevant Standard or Requirement	Implementation Stages			Status
						D	C	O	

CONTRACT NO. HY/2013/12

**TUEN MUN – CHECK LAP KOK LINK – NORTHERN CONNECTION TOLL PLAZA AND ASSOCIATED WORKS
ENVIORNMENTAL MITIGATION AND ENHANCEMENT MEASURE IMPLEMENTATION SCHEDULE**

Land Works									
6.10	-	Wastewater from temporary site facilities should be controlled to prevent direct discharge to surface or marine waters.	All areas/ throughout construction period	Contractor	TM-EIAO		Y		◇
6.10	-	Sewage effluent and discharges from onsite kitchen facilities shall be directed to Government sewer in accordance with the Requirements of the WPCO or collected for disposal offsite. The use of soakaways shall be avoided.	All areas/ throughout construction period	Contractor	TM-EIAO		Y		✓
6.10	-	Storm drainage shall be directed to storm drains via adequately designed sand/silt removal facilities such as sand traps, silt traps and sediment basins. Channels, earth bunds or sand bag barriers should be provided on site to properly direct stormwater to such silt removal facilities. Catchpits and perimeter channels should be constructed in advance of site formation works and earthworks.	All areas/ throughout construction period	Contractor	TM-EIAO		Y		✓
6.10	-	Silt removal facilities, channels and manholes shall be maintained and any deposited silt and grit shall be removed regularly, including specifically at the onset of and after each rainstorm.	All areas/ throughout construction period	Contractor	TM-EIAO		Y		✓
6.10	-	Temporary access roads should be surfaced with crushed stone or gravel.	All areas/ throughout construction period	Contractor	TM-EIAO		Y		◇
6.10	-	Rainwater pumped out from trenches or foundation excavations should be discharged into storm drains via silt removal facilities.	All areas/ throughout construction period	Contractor	TM-EIAO		Y		◇
6.10	-	Measures should be taken to prevent the washout of construction materials, soil, silt or debris into any drainage system.	All areas/ throughout construction period	Contractor	TM-EIAO		Y		◇
6.10	-	Open stockpiles of construction materials (e.g. aggregates and sand) on site should be covered with tarpaulin or similar fabric during rainstorms.	All areas/ throughout construction period	Contractor	TM-EIAO		Y		◇
6.10	5.8	Manholes (including any newly constructed ones) should always be adequately covered and temporarily sealed so as to prevent silt, construction	All areas/ throughout construction period	Contractor	TM-EIAO		Y		◇

CONTRACT NO. HY/2013/12

**TUEN MUN – CHECK LAP KOK LINK – NORTHERN CONNECTION TOLL PLAZA AND ASSOCIATED WORKS
ENVIRONMENTAL MITIGATION AND ENHANCEMENT MEASURE IMPLEMENTATION SCHEDULE**

		materials or debris from getting into the drainage system, and to prevent storm run-off from getting into foul sewers.							
6.10	-	Discharges of surface run-off into foul sewers must always be prevented in order not to unduly overload the foul sewerage system.	All areas/ throughout construction period	Contractor	TM-EIAO		Y		✓
6.10	-	All vehicles and plant should be cleaned before they leave the construction site to ensure that no earth, mud or debris is deposited by them on roads. A wheel washing bay should be provided at every site exit.	All areas/ throughout construction period	Contractor	TM-EIAO		Y		✓
6.10	-	Section of construction road between the wheel washing bay and the public road should be surfaced with crushed stone or coarse gravel.	All areas/ throughout construction period	Contractor	TM-EIAO		Y		✓
6.10	-	Wastewater generated from concreting, plastering, internal decoration, cleaning work and other similar activities, shall be screened to remove large objects.	All areas/ throughout construction period	Contractor	TM-EIAO		Y		✓
6.10	-	Vehicle and plant servicing areas, vehicle wash bays and lubrication facilities shall be located under roofed areas. The drainage in these covered areas shall be connected to foul sewers via a petrol interceptor in accordance with the requirements of the WPCO or collected for off site disposal.	All areas/ throughout construction period	Contractor	TM-EIAO		Y		✓
6.10	-	The Contractor shall prepare an oil / chemical cleanup plan and ensure that leakages or spillages are contained and cleaned up immediately.	All areas/ throughout construction period	Contractor	TM-EIAO		Y		✓
6.10	-	Waste oil should be collected and stored for recycling or disposal, in accordance with the Waste Disposal Ordinance.	All areas/ throughout construction period	Contractor	TM-EIAO Waste Disposal Ordinance		Y		✓
6.10	-	All fuel tanks and chemical storage areas should be provided with locks and be sited on sealed areas. The storage areas should be surrounded by bunds with a capacity equal to 110% of the storage capacity of the largest tank.	All areas/ throughout construction period	Contractor	TM-EIAO		Y		◇

CONTRACT NO. HY/2013/12
TUEN MUN – CHECK LAP KOK LINK – NORTHERN CONNECTION TOLL PLAZA AND ASSOCIATED WORKS
ENVIRONMENTAL MITIGATION AND ENHANCEMENT MEASURE IMPLEMENTATION SCHEDULE

6.10	Section 5	All construction works shall be subject to routine audit to ensure implementation of all EIA recommendations and good working practice.	All areas/ throughout construction period	Contractor	EM&A Manual		Y		✓
------	-----------	---	---	------------	-------------	--	---	--	---

Remarks:

- ✓ Compliance of Mitigation Measures
- <> Compliance of Mitigation Measures but need improvement.
- × Non-compliance of Mitigation Measures
- ▲ Non-compliance of Mitigation Measures but rectified by Contractor
- △ Deficiency of Mitigation Measures but rectified by Contractor
- N/A Not Applicable in Reporting Period
- # Amended against condition 3.13 of EP-354/2009/C

Legend: D=Design, C=Construction, O=Operation

Note: Funding Agent for all mitigation measures will be the Highways Department of the Hong Kong SAR Government
