


Appendix B

Construction Programme

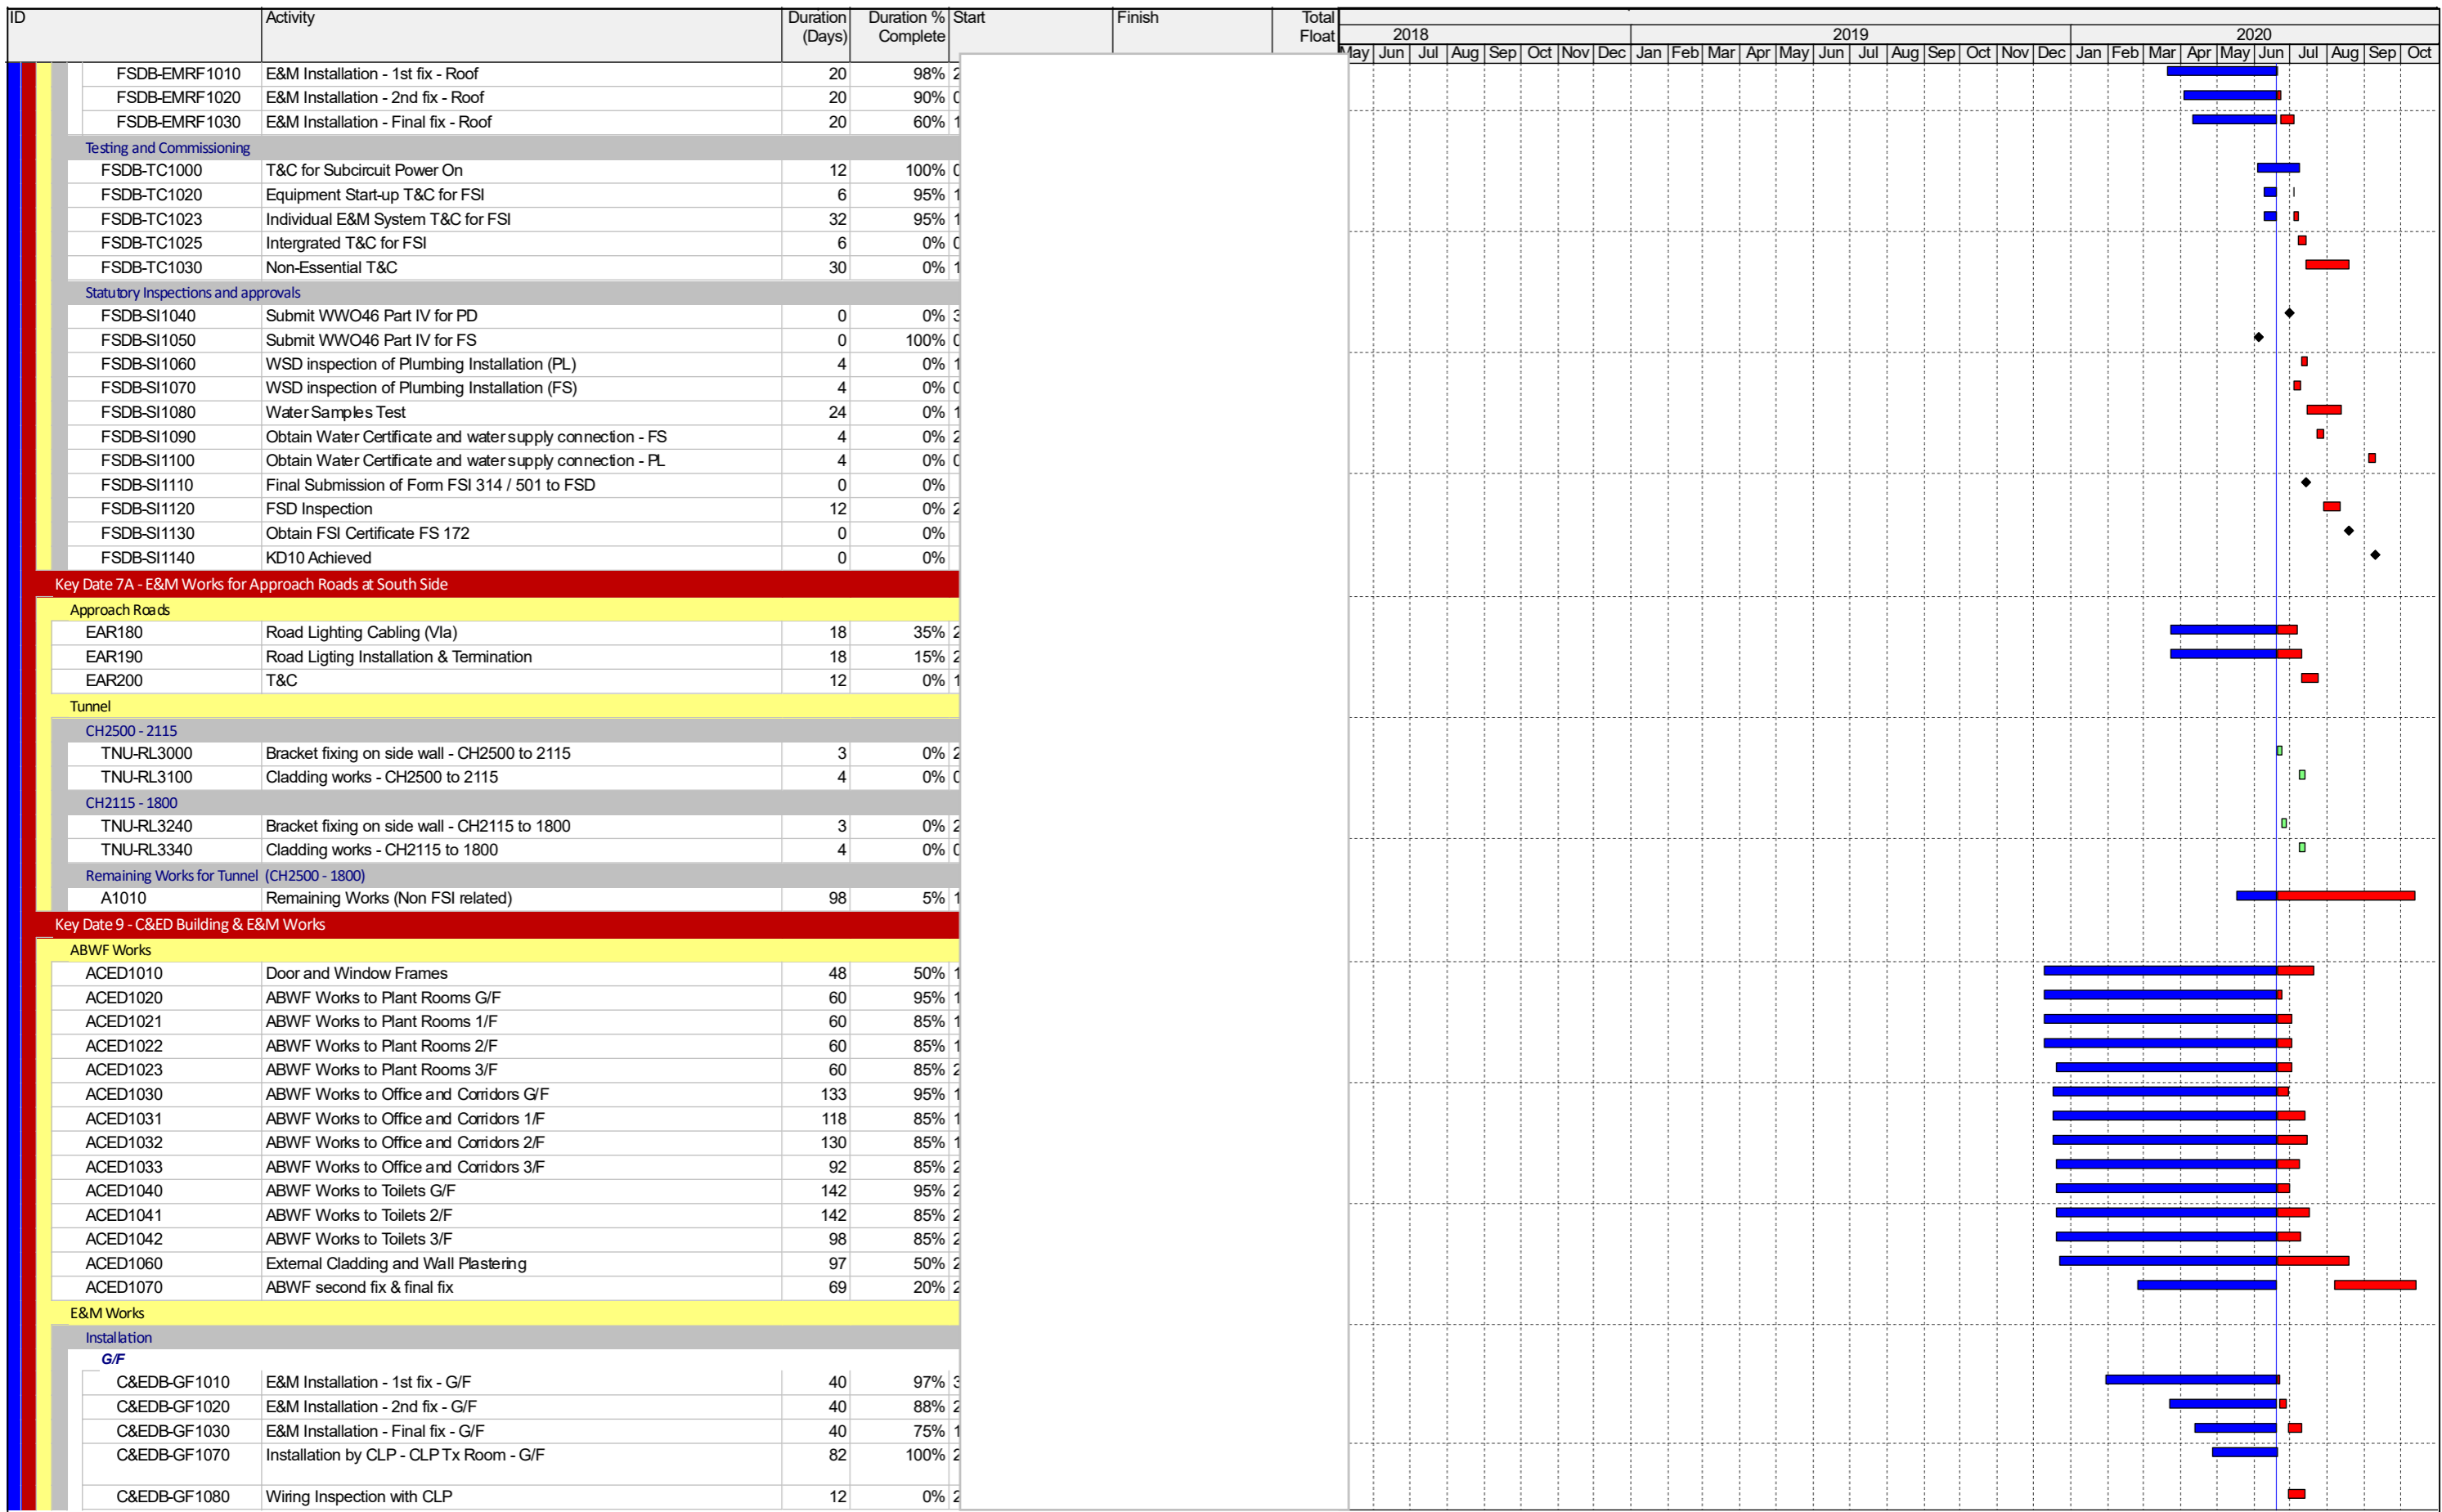

CONTRACT NO. HY2017/10

TM-CLKL NORTHERN CONNECTION TUNNEL BUILDINGS, E&M WORKS

THREE MONTHLY PROGRAMME AS OF 20 Jun 2020

P 5	Date	Revision	Checked	Approved
	20-May-20			

ID	Activity	Duration (Days)	Duration % Complete	Start	Finish	Total Float	2018												2019												2020											
							May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct						
SL130	Works Substantially Completed at South Side (KD7A)	0	0%																																							
SL140	Landscape Soft Works at South Side (wet season)	102	0%																																							
Trees Protection																																										
SL202	Protection Existing Trees & Submit Report with Photographic Record No.13	41	90.24%																																							
SL203	Protection Existing Trees & Submit Report with Photographic Record No.14	41	0%																																							
SL204	Protection Existing Trees & Submit Report with Photographic Record No.15	40	0%																																							
Key Date 8 - All Works for Tunnel Commissioning & Opening																																										
Petrol Filling Station																																										
Structure																																										
PS140	Petrol Filling Station Roof	14	0%																																							
PS180	Concrete Plinth	12	0%																																							
E&M Works																																										
EPS110	Miscellaneous ABWF Works	42	0%																																							
EPS130	E&M Installation	30	100%																																							
EPS140	T&C	12	0%																																							
Statutory Inspections and approvals																																										
Administration Building																																										
ADB-SI1010	Submit WWO46 Part IV for PD	0	0%																																							
ADB-SI1030	WSD inspection of Plumbing Installation (PL)	4	0%																																							
ADB-SI1070	Obtain Water Certificate and water supply connection - PL	4	0%																																							
ADB-SI1110	Submit CT2B	0	100%																																							
ADB-SI1120	EMSD examines site acceptance report and acceptance	36	0%																																							
ADB-SI1130	Submit WWO46 part IV for CT plumbing works	0	0%																																							
ADB-SI1140	WSD inspection and water connection for CT plumbing works	6	0%																																							
Maintenance Depot																																										
MD-SI1040	Submit WWO46 Part IV for PD	0	0%																																							
MD-SI1060	WSD inspection of Plumbing Installation (PL)	4	0%																																							
MD-SI1090	Obtain Water Certificate and water supply connection - FS	4	50%																																							
MD-SI1100	Obtain Water Certificate and water supply connection - PL	4	0%																																							
North Ventilation Building																																										
NVB-SI1090	Submit WWO46 Part IV for PD	0	0%																																							
NVB-SI1110	WSD inspection of Plumbing Installation (PL)	4	0%																																							
NVB-SI1130	Water Samples Test	24	0%																																							
NVB-SI1140	Obtain Water Certificate and water supply connection - PL	4	0%																																							
Petrol Filling Station																																										
PFS-SI1010	T&C of E&M System	6	0%																																							
PFS-SI1030	DG Inspection	18	0%																																							
PFS-SI1040	Obtain DG Licence	0	0%																																							
PFS-SI1050	Final Submission of form FSI 314/501	0	0%																																							
PFS-SI1060	FSD Inspection	42	0%																																							
Underpass & Plant Room																																										
VUP-SI1095	Obtain Water Certificate and water supply connection - FS	4	0%																																							
VUP-SI2000	Final Submission of Form FSI 314 / 501 to FSD	0	0%																																							
VUP-SI2010	FSD Inspection	42	0%																																							
VUP-SI2020	Obtain FSI Certificate FS 172	0	0%																																							
Toll Control Building & Toll Collector Subway																																										
TCB-SI2000	Submit WWO46 Part IV for PD	0	0%																																							
TCB-SI2020	WSD inspection of Plumbing Installation (PL)	4	0%																																							
TCB-SI2030	WSD inspection of Plumbing Installation (FS)	4	50%																																							
TCB-SI2040	Water Samples Test	24	0%																																							
TCB-SI2045	Obtain Water Certificate and water supply connection - FS	4	0%																																							
TCB-SI2050	Obtain Water Certificate and water supply connection - PL	4	0%																																							
TCB-SI3000	Submit CT2B	0	100%																																							
TCB-SI3010	EMSD examines site acceptance report and acceptance	36	0%																																							
TCB-SI3020	Submit WWO46 part IV for CT plumbing works	0	0%																																							
TCB-SI3030	WSD inspection and water connection for CT plumbing works	4	0%																																							
Satellite Control Building																																										
SCB-SI1040	Submit WWO46 Part IV for PD	0	0%																																							

CONTRACT NO. HY2017/10

TM-CLKL NORTHERN CONNECTION TUNNEL BUILDINGS, E&M WORKS

THREE MONTHLY PROGRAMME AS OF 20 Jun 2020

P 7	Date	Revision	Checked	Approved
	20-May-20			

