

東業德勤測試顧問有限公司 ETS-TESTCONSULT LIMITED

8/F., Block B, Veristrong Industrial Centre, 34-36 Au Pui Wan Street, Fotan, Hong Kong

Tel: 2695 8318 Fax: 2695 3944 E-mail : etl@ets-testconsult.com Web site : www.ets-testconsult.com

CHINA HARBOUR ENGINEERING CO. LTD.

CONTRACT NO.: HY/2013/02 HONG
KONG – ZHUHAI- MACAO BRIDGE
HONG KONG BOUNDARY CROSSING
FACILITIES – INFRASTRUCTURE
WORKS STAGE I (WESTERN
PORTION)

MONTHLY EM&A REPORT NO. 17

(01 APRIL - 30 APRIL 2016)

Prepared by:

Tsui, Ho Lam

Assistant Environmental Officer

Certified by:

LAU, Chi Leung

Environmental Team Leader

Issued Date: 7 May 2016

Report No.:ENA61697

This report shall not be reproduced unless with prior written approval from this laboratory



Ref.: HYDHZMBEEM00 0 4156L.16

11 May 2016

By Fax (3468 2076) and By Post

AECOM Asia Co. Ltd. The PRE's Office 5 Ying Hei Road, Tung Chung, Lantau Hong Kong

Attention: Mr. Ringo Tso

Dear Sir,

Re: Agreement No. CE 48/2011 (EP)

Environmental Project Office for the

HZMB Hong Kong Link Road, HZMB Hong Kong Boundary Crossing Facilities, and Tuen Mun-Chek Lap Kok Link – Investigation

Contract No. HY/2013/02 - HZMB HKBCF - Infrastructure Works Stage I (Western Portion)

Monthly Environmental Monitoring & Audit Report for April 2016

Reference is made to the Environmental Team's submission of Monthly Environmental Monitoring & Audit Report for April 2016 certified by the ET Leader (ET's ref.: "OC/60237/CLL" dated 11 May 2016) and provided to us via e-mail on 11 May 2016.

We are pleased to inform you that we have no adverse comment on the captioned submission. We write to verify the captioned submission in accordance with Condition 5.4 of the Environmental Permit No. EP-353/2009/K.

Thank you very much for your attention and please feel free to contact the undersigned should you require further information.

Yours faithfully, For and on behalf of Ramboll Environ Hong Kong Limited

Raymond Dai

Independent Environmental Checker

c.c. HvD

Ronguet

 HyD
 Mr. Matthew Fung
 (By Fax: 3188 6614)

 HyD
 Mr. Chee-Kuen Yu
 (By Fax: 3188 6614)

 ETS
 Mr. C. L. Lau
 (By Fax: 2695 3944)

CHEC Mr. Kenny Yu (By Fax: 3915 0300)

Internal: DY, YH, CL, ENPO Site



東業德勤測試顧問有限公司 ETS-TESTCONSULT LIMITED

8/F., Block B, Veristrong Industrial Centre, 34-36 Au Pui Wan Street, Fotan, Hong Kong

: 2695 8318

E-mail: etl@ets-testconsult.com

Fax : 2695 3944

Web site : www.ets-testconsult.com





Your Ref.: ---

Our Ref.: OC/60237/CLL

11 May 2016

Ramboll Environ Hong Kong Limited Room 2403, Jubilee Centre 18 Fenwick Street, Wan Chai Hong Kong

By E-mail

Attn: Mr. Raymond Dai

Dear Mr. Dai,

Contract No. HY/2013/02 Hong Kong - Zhuhai - Macao Bridge Hong Kong Boundary Crossing Facilities – Infrastructure Works Stage I (Western Portion) Monthly EM&A Report for April 2016

In accordance with the requirement specified in Condition 5.4 of the Environmental Permit No. EP-353/2009/K, we are pleased to submit the certified EM&A Report for April 2016 revised with the IEC's comment for your onward verification.

Yours faithfully,

ETS-TESTCONSULT LIMITED

Mr. C. L. Lau

Environmental Team Leader

CLL/pn



ENA61697 Monthly EM&A Report No.17

TABLE OF CONTENTS

EXEC	CUTIVE SUMMARY	Page
1	INTRODUCTION	1-2
1.1	Basic Project Information	1
1.2	Project Organization	2
1.3	Construction Programme	2
1.4	Construction Works Undertaken During the Reporting Period	2
2	AIR QUALITY MONITORING	3-4
2.1	Monitoring Locations	3
2.2	Monitoring Requirements	4
2.3	Monitoring Results	4
3	NOISE MONITORING	5
3.1	Monitoring Locations	5
3.2	Monitoring Requirements	5
3.3	Monitoring Results	5
4	WATER QUALITY MONITORING	6-7
4.1	Monitoring Locations	6
4.2	Monitoring Requirements	6 7
4.3	Monitoring Locations	1
5	DOLPHIN MONITORING	8
5.1	Monitoring Locations	8
5.2	Monitoring Requirements	8
5.3	Monitoring Locations	8
6	ENVIRONMENTAL SITE INSPECTION AND AUDIT	9-11
6.1	Site Inspection	9
6.2	Advice on the Solid and Liquid Waste Management Status	9-10
6.3	Environmental Licenses and Permits	10
6.4	Implementation Status of Environmental Mitigation Measures	10-11
6.5	Summary of Exceedance of the Environmental Quality Performance Limit	11
6.6	Summary of Complaints, Notification of Summons and Successful Prosecution	11
7	FUTURE KEY ISSUES	12
7.1	Construction Programme for the Coming Months	12
7.2	Environmental Site Inspection Schedule for the Coming Month	12
8	CONCLUSION	12
8.1	Conclusions	12

FIGURES

Figure 1	Air Quality and Noise Monitoring Stations for HKBCF
Figure 2	Water Quality Monitoring Stations(construction phases)
Figure 3	Dolphin Monitoring Transect Line and Layout Map



ENA61697 Monthly EM&A Report No.17

Table	
Table 1.1	Contact Information of Key Personnel
Table 2.1	Air Quality Monitoring Locations
Table 2.2	Action and Limit Levels for 1-hour TSP
Table 2.3	Action and Limit Levels for 24-hour TSP
Table 3.1	Construction Noise Monitoring Locations
Table 3.2	Action and Limit Levels for Construction Noise
Table 4.1	Water Quality Monitoring Stations(construction phases)
Table 4.2	Action and Limit Levels for Water Quality
Table 5.1a	Action and Limit Levels for Chinese White Dolphin Monitoring – Approach to Define Action Level (AL) and Limit Level (LL)
Table 5.1b Table 6.1	Action and Limit Levels for Chinese White Dolphin Monitoring – Summary of marine sediment disposed to dumping site via Contract No. HY/2013/03
Table 7.1	Construction Activities for coming month

APPENDICES

Location of Works Areas
Project Organization for Environmental Works
Construction Programme
Event and Action Plan
Monthly Summery of Waste Flow Table & Monthly Summery of Marine Sediment
Environmental Licenses and Permits
Implementation Schedule for Environmental Mitigation Measures (EMIS)
Statistics on Environmental Complaints, Notification of Summons and Successful Prosecutions
Environmental Site Inspection Schedule



ENA61697 Monthly EM&A Report No.17

EXECUTIVE SUMMARY

This Monthly Environmental Monitoring and Audit (EM&A) Report is prepared for Contract HY/2013/02 Hong Kong–Zhuhai-Macao Bridge Hong Kong Boundary Crossing Facilities (HKBCF) – Infrastructure Works Stage I (Western Portion) (hereafter referred to as "the Contract") for the Highways Department of Hong Kong Special Administrative Region (HKSAR). The Contract was awarded to China Harbour Engineering Co., Ltd. (hereafter referred to as "the Contractor") and ETS-Testconsult Limited was appointed as the Environmental Team (ET) by the Contractor.

The Contract is part of Hong Kong – Zhuhai – Macao Bridge HKBCF which is a "Designated Project", under Schedule 2 of the Environmental Impact Assessment Ordinance (EIAO) (Cap 499) and Environmental Impact Assessment (EIA) Report (Register No. AEIAR-145/2009) was prepared for the Project. The current Environmental Permit (EP) No. EP-353/2009/K for HKBCF was issued on 11 April 2016. These documents are available through the EIA Ordinance Register. Site preparation works of the Contract was started on 25 July 2014 and the construction works of the Contract commenced on 24 November 2014.

ETS-Testconsult Limited has been appointed by the Contractor to implement the Environmental Monitoring & Audit (EM&A) programme for the Contract in accordance with the Updated EM&A Manual for HKBCF (Version 1.0) and provide environmental team services to the Contract.

This is the Seventeenth Monthly Environmental Monitoring and Audit (EM&A) Report for the Contract which summaries findings of the EM&A works conducted during the reporting period from 01 April 2016 to 30 April 2016.

Site Activities

As informed by the Contractor, site activities were carried out in this reporting month:

- Bored piles works in Portion A1, D, C1& F;
- Pier / Abutment & Pile Cap in Portion D;
- Temporary marine loading and unloading point for segment delivery in Portion A1;
- Pre-bored H-pile for sign gantries in Portion D;
- Filling works in Portion A:
- UU Detection Works in Portion I;
- Pit excavation work and duct laying in Portion I;
- Footing construction of directional signs in Portion I;
- Construction of alternative site entrance: &
- Marine sediment excavation activities from the land-based works and corresponding disposal at the designated disposal sites.

Environmental Monitoring and Audit Progress

The monthly EM&A programme was undertaken in accordance with the Updated EM&A Manual for HKBCF (Version 1.0). It should be noted that the air quality and noise monitoring works for the Contract are covered by Contract No. HY/2010/02 Hong Kong-Zhuhai-Macao Bridge HKBCF – Reclamation Works and Contract No. HY/2011/03 Hong Kong-Zhuhai-Macao Bridge Hong Kong Link Road – Section between Scenic Hill and HKBCF. The ET of the Contract or another ET of the HZMB project is required to conduct impact air quality monitoring at AMS6 and AMS7, noise monitoring at NMS2 and NMS3B, water quality monitoring show in **Figure 2** and dolphin monitoring show in **Figure 3** as part of EM&A programme if these monitoring stations are no longer covered under Contract No. HY/2010/02 and HY/2011/03. However, this is subject to ENPO's final decision on which ET should carry out the monitoring works at these stations. The dates of site inspection during the reporting period are listed below:

Environmental Site Inspection: 07, 15, 21 and 28 April 2016



ENA61697 Monthly EM&A Report No.17

Breaches of Action and Limit Levels

Summary of Action and Limit Level exceedance of 1-hr TSP level and 24-hr TSP level at AMS6 shall be referred to the monthly EM&A report prepared by Contract No. HY/2011/03.

There was no Action and Limit Level exceedance of 1-hr TSP level and 24-hr TSP level recorded at station AMS7 by the Environmental Team of Contract No. HY/2010/02 during the reporting period.

There was no Action and Limit Level exceedance for noise recorded at station NMS2 and station NMS3B by the Environmental Team of Contract No. HY/2010/02 during the reporting period.

There was no Action and Limit Level exceedance for water quality recorded at the monitoring stations showed at **Table 4.1** by the Environmental Team of Contract No. HY/2010/02 during the reporting period.

Impact dolphin monitoring results at all transects are reported in the EM&A Report prepared for Contract No. HY/2010/02.

Complaint Log

There was no complaint received in relation to the environmental impact during the reporting period.

Notifications of Summons and Successful Prosecutions

There were no notifications of summons or prosecutions received during the reporting period.

Reporting Change

The Environmental Permit (EP) was updated from No. EP-353/2009/J to No. EP-353/2009/K for HKBCF which was applied on 24 March 2016 and was issued on 11 April 2016. These documents are available through the EIA Ordinance Register.

Future Key Issues

The future key issues to be undertaken in the upcoming month are as follows:

- Bored piles works in Portion A1, D, C1& F, C2;
- Pier / Abutment in Portion D & A1;
- Pile Cap in Portion D & A1;
- Pre-bored H-pile for sign gantries in Portion D:.
- Filling works in Portion A;
- UU Detection Works in Portion I;
- Pit excavation work and duct laying in Portion I;
- Footing construction of directional signs in Portion I; &
- Construction of alternative site entrance.
- Marine sediment excavation activities from the land-based works and corresponding disposal at the designated disposal sites.



ENA61697 Monthly EM&A Report No.17

1 INTRODUCTION

1.1 Basic Project Information

- 1.1.1 This Monthly Environmental Monitoring and Audit (EM&A) Report is prepared for Contract HY/2013/02 Hong Kong–Zhuhai-Macao Bridge Hong Kong Boundary Crossing Facilities (HKBCF) Infrastructure Works Stage I (Western Portion) (hereafter referred to as "the Contract") for the Highways Department of Hong Kong Special Administrative Region (HKSAR). The Contract was awarded to China Harbour Engineering Co., Ltd. (hereafter referred to as "the Contractor") and ETS-Testconsult Limited was appointed as the Environmental Team (ET) by the Contractor.
- 1.1.2 The Contract is part of Hong Kong Zhuhai Macao Bridge HKBCF which is a "Designated Project", under Schedule 2 of the Environmental Impact Assessment Ordinance (EIAO) (Cap 499) and Environmental Impact Assessment (EIA) Report (Register No. AEIAR-145/2009) was prepared for the Project. The current Environmental Permit (EP) No. EP-353/2009/K for HKBCF was issued on 11 April 2016. These documents are available through the EIA Ordinance Register. Site preparation works of the Contract started on 25 July 2014 and the construction works of the Contract commenced on 24 November 2014. The works area of the Contract is shown in Appendix A.
- **1.1.3** The proposed works under this Contract comprise the following:
 - Construction of the viaducts and roads at the western portion of Hong Kong Boundary Crossing Facilities (HKBCF) mainly for connection with the Hong Kong – Zhuhai – Macao Bridge (HZMB), Hong Kong Link Road (HKLR), Hong Kong International Airport (HKIA) and the Tuen Mun-Chek Lap Kok Link (TM-CLKL);
 - Construction of the road modification at the SkyCity Interchange at Airport Island;
 - Construction of associated street lighting, street furniture, road marking, road signage, drainage, sewerage, fresh water and flushing water supply, irrigation, landscape, electrical and mechanical (E&M), utilities and services works;
 - Provisioning of civil engineering works and power supply installation for the Traffic Control and Surveillance System TCSS);
 - Other works in accordance with the Contract.
- **1.1.4** This is the Seventeenth Monthly Environmental Monitoring and Audit (EM&A) Report for the Contract which summaries the audit findings of the EM&A programme during the reporting period from 01 April 2016 to 30 April 2016.

ENA61697 Monthly EM&A Report No.17

1.2 Project Organization

1.2.1 The project organization structure and lines of communication with respect to the on-site environmental management structure is shown in **Appendix B**. The key personnel contact names and numbers are summarized in **Table 1.1**.

Table 1.1 Contact Information of Key Personnel

Party	Position	Name of Key Staff	Tel. No.	Fax No.
Engineer or Engineer's Representative (AECOM Asia Co. Ltd.)	Resident Engineer	Mr. Fred Yeung	63308293	31525116
Environmental Project Office / Independent	Environmental Project Office Leader	Mr. Y. H. Hui	34652888	34652899
Environmental Checker (Ramboll Environ Hong Kong	Independent Environmental Checker	Mr. Raymond Dai	34652888	34652899
Limited)	Environmental Site Supervisor	Mr. Ray Yan	51818165	34652899
Contractor (China	Environmental Officer	Mr. Richard Ng	59770593	39150300
Harbour Engineering Co., Ltd.)	Environmental Supervisor	Ms. Joy Chan	54005086	39150300
,	Environmental Supervisor	Ms. Selena Yang	55122662	39150300
Environmental Team (ETS-Testconsult Ltd.)	Environmental Team Leader	Mr C. L. Lau	2946 7791	2695 3944

1.3 Construction Programme

1.3.1 A copy of the Contractor's construction programme is provided in **Appendix C**.

1.4 Construction Works Undertaken During the Reporting Period

- **1.4.1** A summary of the construction activities undertaken during this reporting period is shown below:
 - Bored piles works in Portion A1, D, C1& F;
 - Pier / Abutment & Pile Cap in Portion D;
 - Temporary marine loading and unloading point for segment delivery in Portion A1;
 - Pre-bored H-pile for sign gantries in Portion D;
 - Filling works in Portion A;
 - UU Detection Works in Portion I;
 - Pit excavation work and duct laying in Portion I;
 - Footing construction of directional signs in Portion I;
 - Construction of alternative site entrance; &
 - Marine sediment excavation activities from the land-based works and corresponding disposal at the designated disposal sites.

ENA61697 Monthly EM&A Report No.17

2 AIR QUALITY MONITORING

2.1 Monitoring Locations

2.1.1 The air quality monitoring works for the Contract are covered by Contract No. HY/2010/02 Hong Kong-Zhuhai-Macao Bridge HKBCF – Reclamation Works and Contract No. HY/2011/03 Hong Kong-Zhuhai-Macao Bridge Hong Kong Link Road – Section between Scenic Hill and HKBCF. The ET of the Contract or another ET of the HZMB project is required to conduct impact air quality monitoring at AMS6 and AMS7 as part of EM&A programme if these air quality monitoring stations are no longer covered under Contract No. HY/2010/02 and HY/2011/03. Table 2.1 and Figure 1 shows the locations of air monitoring stations.

Table 2.1 Air Quality Monitoring Locations

Identification No. Location Description	
AMS6 ⁽¹⁾ Dragonair / CNAC (Group) Buidling	
AMS7 ^{(1) (2)}	Hong Kong SkyCity Marriott Hotel

Remarks:

- (1) The ET of this Contract should conduct impact air quality monitoring at the AMS listed in the table as part of EM&A programme according to latest notification from ENPO when the monitoring station(s) is/are no longer covered by another ET of the HZMB project.
- (2) The air quality monitoring location AMS7A was relocated back to the original monitoring location AMS7 of the updated EM&A Manual started from January 2016.

2.2 Monitoring Requirements

- 2.2.1 The monitoring requirements, monitoring equipment, monitoring parameters, frequency and duration, monitoring methodology, monitoring schedule, meteorological information are detailed in the monthly EM&A Reports prepared for Contract Nos. HY/2010/02 and HY/2011/03.
- **2.2.2** The Action and Limit Levels for 1-hr TSP and 24-hr TSP are provided in **Table 2.2** and **Table 2.3** respectively. The Action and Limit Levels of AMS7 are as same as its original levels and AMS7A.

Table 2.2 Action and Limit Levels for 1-hour TSP

Monitoring Station.	Action Level,µg/m³	Limit Level,µg/m³
AMS6 – Dragnair / SNAC (Group) Building (HKIA)	360	500
AMS7 – Hong Kong SkyCity Marriott Hotel	370	500

Table 2.3 Action and Limit Levels for 24-hour TSP

Monitoring Station.	Action Level,µg/m³	Limit Level,µg/m³
AMS6 – Dragnair / SNAC (Group) Building (HKIA)	173	260
AMS7 – Hong Kong SkyCity Marriott Hotel	183	260

- **2.2.3** The event and action plan is provided in **Appendix D**.
- 2.2.4 If exceedance(s) at these stations is/are recorded by the ET of the Contract or referred by the other ET under the HZMB project to the Contract, the ET of the Contract will carry out an investigation and findings will be reported in the monthly EM&A Report.



ENA61697 Monthly EM&A Report No.17

2.3 Monitoring Results

- **2.3.1** The monitoring results for AMS6 and AMS7 are reported in the monthly EM&A Reports prepared for Contract Nos. HY/2011/03 and HY/2010/02 respectively.
- 2.3.2 Summary of Action and Limit Level exceedance of 1-hr TSP level and 24-hr TSP level at AMS6 shall be referred to the monthly EM&A report prepared by Contract No. HY/2011/03.
- 2.3.3 There was no Action and Limit Level exceedance of 1-hr TSP level and 24-hr TSP level recorded at station AMS7 by the Environmental Team of Contract No. HY/2010/02 during the reporting period.

ENA61697 Monthly EM&A Report No.17

3 NOISE MONITORING

3.1 Monitoring Locations

3.1.1 The noise monitoring works for the Contract are covered by Contract No. HY/2010/02 Hong Kong-Zhuhai-Macao Bridge HKBCF – Reclamation Works. The ET of the Contract or another ET of the HZMB project is required to conduct noise monitoring at NMS2 and NMS3B as part of EM&A programme if these monitoring stations are no longer covered under Contract No. HY/2010/02. Table 3.1 and Figure 1 shows the locations of noise monitoring stations.

Table 3.1 Construction Noise Monitoring Locations

Identification No.	Location Description
NMS2 ⁽¹⁾	Sea View Crescent
NMS3B ^{(1) (2)}	Site Boundary of Site Office Area at Works Area WA2

Remarks:

- (1) The ET of this Contract should conduct impact noise monitoring at the NMS listed in the table as part of EM&A programme according to latest notification from ENPO when the monitoring station(s) is/are no longer covered by another ET of the HZMB project.
- (2) The Action and Limit Levels for schools will be applied for this alternative monitoring location.

3.2 Monitoring Requirements

- **3.2.1** The monitoring requirements, monitoring equipment, monitoring parameters, frequency and duration, monitoring methodology, monitoring schedule, meteorological information are detailed in the monthly EM&A Reports prepared for Contract No. HY/2010/02.
- 3.2.2 The Action and Limit Levels for construction noise are provided in Table 3.2

Table 3.2 Action and Limit Levels for Construction Noise

Parameter	Action Level	Limit Level
07:00 – 19:00 hours on normal weekdays	When one documented complaint is received	75 dB(A)*

Notes:

If works are to be carried out during restricted hours, the conditions stipulated in the construction noise permit issued by the Noise Control Authority have to be followed

- **3.2.3** The event and action plan is provided in **Appendix D**.
- 3.2.4 If exceedance(s) at these stations is/are recorded by the ET of the Contract or referred by the other ET under the HZMB project to the Contract, the ET of the Contract will carry out an investigation and findings will be reported in the monthly EM&A Report.

3.3 Monitoring Results

3.3.1 The monitoring results for NMS2 and NMS3B are reported in the monthly EM&A Reports prepared for Contract No. HY/2010/02. There was no exceedance for noise recorded at station NMS2 and station NMS3B by the Environmental Team of Contract No. HY/2010/02 during the reporting period.

permit issued by the Noise Control Authority have to be followed.

* Reduce to 70 dB(A) for schools and 65 dB(A) during school examination period.

ENA61697 Monthly EM&A Report No.17

4 WATER QUALITY MONITORING

4.1 Monitoring Locations

The water monitoring works for the Contract are covered by Contract No. HY/2010/02 Hong Kong-Zhuhai-Macao Bridge HKBCF – Reclamation Works. The ET of the Contract or another ET of the HZMB project is required to conduct water quality monitoring at fifteen stations (3 Impact Stations, 7 Sensitive Receiver Stations and 5 Control/Far Field Stations) as part of EM&A programme if these monitoring stations are no longer covered under Contract No. HY/2010/02. **Table 4.1** and **Figure 2** shows the locations of water quality monitoring stations.

Table 4.1 Water Quality Monitoring Stations (construction phases)

Station	Description	East	North
IS7	Impact Station (Close to HKBCF construction site)	812244	818777
IS10	Impact Station (Close to HKBCF construction site)	812577	820670
IS(Mf)11	Impact Station (Close to HKBCF construction site)	813562	820716
SR3	Sensitive receivers (San Tau SSSI)	810525	816456
SR4(N)	Sensitive receivers (Tai Ho)	814705	817859
SR5	Sensitive receivers (Artificial Reef in NE Airport)	811489	820455
SR6	Sensitive receivers (Sha Chau and Lung Kwu Chau Marine Park)	805837	821818
SR7	Sensitive receivers (Tai Mo Do)	814293	821431
SR10A [1]	Sensitive receivers (Ma Wan FCZ)1	823741	823495
SR10B(N)[1]	Sensitive receivers (Ma Wan FCZ)2	823683	823187
CS(Mf)3	Control Station	809989	821117
CS(Mf)5	Control Station	817990	821129
CS4	Control Station	810025	824004
CS6	Control Station	817028	823992
CSA [2]	Control Station	818103	823064

Note

Remarks:

The ET of this Contract should conduct impact water quality monitoring at the WQMS listed in the table as part of EM&A programme according to latest notification from ENPO when the monitoring station(s) is/are no longer covered by another ET of the HZMB project. The ET of the Contract shall communicate and share the monitoring data to the ET(s) of other works contracts if the water quality monitoring station(s) is/are as part of EM&A programme.

4.2 Monitoring Requirements

The monitoring requirements, monitoring equipment, monitoring parameters, frequency and duration, monitoring methodology, monitoring schedule, meteorological information are detailed in the monthly EM&A Reports prepared for Contract Nos. HY/2010/02.

- **4.2.1** The event and action plan is provided in **Appendix D**.
- **4.2.2** The Action and Limit Levels for Water Quality are provided in **Table 4.2**

Table 4.2 Action and Limit Levels for Water Quality

Parameters	Action	Limit
DO in mg/L (Surface, Middle	Surface and Middle 5.0	Surface and Middle 4.2
& Bottom)	Bottom 4.7	(except 5 mg/L for FCZ)
		Bottom 3.6
SS in mg/L	23.5 and 120% of	34.4 and 130% of
(depth-averaged) at all	upstream control station's SS	upstream control station's SS
monitoring stations and	at the same tide of the	at the same tide of the same
control stations	same day*	day and 10mg/L for WSD
		Seawater intakes*

^{[1]:} Additional monitoring station for Ma Wan FCZ.

^{[2]:} Additional control monitoring station for Ma Wan FCZ



ENA61697 Monthly EM&A Report No.17

Turbidity in averaged)	NTU	(depth-	27.5 and 120% of upstream control station's	47.0 and 130% of upstream control station's
,			turbidity at the same tide of the same day*	turbidity at the same tide of the same day*

^{*} Remarks: Reference is made to EPD approval of adjustment of water quality assessment criteria issued and became effective on 18 February 2013.

Notes: 1 "depth-averaged" is calculated by taking the arithmetic means of reading of all three depths.

- 2 For DO, non-compliance of the water quality limits occurs when monitoring result is lower than the limits.
- 3 For turbidity, SS, non-compliance of the water quality limits occurs when monitoring result is higher than the limits.
- 4 All the figures given in the table are used for reference only and the EPD may amend the figures whenever it is considered as necessary.
- 5 The 1%-ile of baseline data for dissolved oxygen (surface and middle) and dissolved oxygen (bottom) are 4.2mg/L and 3.6mg/L respectively
- **4.2.3** If exceedance(s) at these stations is/are recorded by the ET of the Contract or referred by the other ET under the HZMB project to the Contract, the ET of the Contract will carry out an investigation and findings will be reported in the monthly EM&A Report.

4.3 Monitoring Result

4.3.1 The monitoring results for the monitoring stations showed in **Table 4.1** are reported in the monthly EM&A Report prepared for Contract No. HY/2010/02. There was no Action and Limit Level exceedance was recorded by the Environmental Team of Contract No. HY/2010/02 during the reporting period.



ENA61697 Monthly EM&A Report No.17

5 DOLPHIN MONITORING

5.1 Monitoring Locations

The dolphin monitoring works for the Contract are covered by Contract No. HY/2010/02 Hong Kong-Zhuhai-Macao Bridge HKBCF – Reclamation Works. The ET of the Contract or another ET of the HZMB project is required to conduct dolphin monitoring at 23 transects as part of EM&A programme if these transects are no longer covered under Contract No. HY/2010/02. The dolphin monitoring should adopt line-transect vessel survey method. The survey follows pre-set and fixed transect lines in the two areas defined by AFCD as: Northeast Lantau survey area; and Northwest Lantau survey area. **Figure 3** shows the co-ordinates for the transect lines and layout map Remarks:

The ET of this Contract should conduct impact dolphin monitoring as part of EM&A programme according to latest notification from ENPO when the monitoring station(s) is/are no longer covered by another ET of the HZMB project.

5.2 Monitoring Requirements

The monitoring requirements, monitoring equipment, monitoring parameters, frequency and duration, monitoring methodology, monitoring schedule, meteorological information are detailed in the monthly EM&A Reports prepared for Contract Nos. HY/2010/02.

- **5.2.1** The event and action plan is provided in **Appendix D**.
- 5.2.2 The Action and Limit Levels for Chinese White Dolphin Monitoring are provided in Table 5.1a & Table5.1b

Table 5.1a Action and Limit Levels for Chinese White Dolphin Monitoring – Approach to Define Action Level (AL) and Limit Level (LL)

	North Lantau Social Cluster		
	NEL	NWL	
Action Level	(STG < 70% of baseline) &	(STG < 70% of baseline) &	
	(ANI < 70% of baseline)	(ANI < 70% of baseline)	
Limit Level	[(STG < 40% of baseline) & (ANI < 40% of baseline)]		
	AND [(STG < 40% of baseline) & (ANI < 40% of		
	baseline)]		

For North Lantau Social Cluster, action level will be trigger if either NEL or NWL fall below the criteria; limit level will be triggered if both NEL and NWL fall below the criteria.

Table 5.1(b) Derived Value of Action Level (AL) and Limit Level (LL) for Chinese White Dolphin Monitoring

	- · · · · · · · · · · · · · · · · · · ·	
	North Lantau Social Cluster	
	NEL	NWL
Action Level	STG < 4.2) & (ANI < 15.5)	(STG < 6.9) & (ANI < 31.3)
Limit Level	[(STG < 2.4) & (ANI < 8.9)] AND [(STG < 3.9) & (AN	I < 17.9)]

5.2.3 If exceedance(s) at these transects is/are recorded by the ET of the Contract or referred by the other ET under the HZMB project to the Contract, the ET of the Contract will carry out an investigation and findings will be reported in the monthly EM&A Report.

5.3 Monitoring Result

The dolphin survey results for all transects are reported in the monthly EM&A Reports prepared for Contract No. HY/2010/02.



ENA61697 Monthly EM&A Report No.17

6 ENVIRONMENTAL SITE INSPECTION AND AUDIT

6. 1 Site Inspection

- **6.1.1** Site Inspections were carried out on a weekly basis to monitor the implementation of proper environmental pollution control mitigation measures for the project. During the reporting period, site inspections were carried out on 07, 15, 21 and 28 April 2016.
- **6.1.2** Particular observations during the site inspections are described below:

07 April 2016

- (a) Unpaved area and haul was observed dry. The watering frequency was enhanced. This observation was closed on 15 April 2016.
- (b) Stagnant water was observed on the concrete block at Portion D. The Stagnant water was removed. This observation was closed on 15 April 2016.

15 April 2016

- (a) Generator without NRMM label was observed at Portion D. The NRMM label was provided. This observation was closed on 21 April 2016.
- (b) Stagnant water was observed on the concrete block at Portion D. The Stagnant water was removed. This observation was closed on 21 April 2016.
- (c) General refuse was observed at Portion D. The refuse was collected. This observation was closed on 21 April 2016.
- (d) Oil container without drip tray was observed at Portion D. The oil container was removed. This observation was closed on 21 April 2016.

21 April 2016

(a) Chemical waste observed improper storage at Portion C. The chemical waste was removed. This observation was closed on 28 April 2016.

28 April 2016

- (a) Stagnant water was observed on the plastic barrier at Portion D. The contractor was reminded to clean the stagnant water. Follow-actions for outstanding observation will be inspected during the next site inspection.
- (b) Oil container was observed improper storage at Portion C. The contractor was reminded to remove the oil container. Follow-actions for outstanding observation will be inspected during the next site inspection.

6. 2 Advice on the Solid and Liquid Waste Management Status

- **6.2.1** The Contractor registered as a chemical waste producer for the Contract. Sufficient numbers of receptacles were available for general refuse collection and sorting.
- **6.2.2** 4240 m³ of excavated marine sediment was generated in this reporting period.

6.2.3 Disposal of Marine Sediment

6.2.3.1 For the marine sediment disposal, after the acceptance of the review of the approved Sediment Quality Report (SQR) for this Project under EPD letter dated 19 August 2015, an approval to dispose the marine sediment extracted from bored piling for this Project was then approved under memo from Secretary, Marine Fill Committee of CEDD dated 20 August 2015 for the disposal of marine sediment extracted from bored piling works. The disposal sites allocated to this Project are the Mud Pit CMP2 of the Confined Marine Sediment Disposal Facility to the South of The Brothers (or at the East of Sha Chau). As advised by CEDD in the memo dated 19 February 2016, from 00:00 on 22 March 2016 onward, the disposal space at CMP2 of the South of The Brothers is closed and all disposal of contaminated sediment is to be carried out at CMP Vd to the East of Sha Chau (ESC). As a practical means, the disposal operation is managed by one contractor who is also responsible for applying dumping permit and its subsequent extension applications from EPD. Contract No. HY/2013/03 has



ENA61697 Monthly EM&A Report No.17

been assigned to coordinate and arrange for disposal of extracted marine sediment from Contract Nos. HY/2013/02, HY/2013/03 and HY/2013/04.

- **6.2.3.2** For the dumping arrangement, the barge for disposal of marine sediment will moor at the temporary loading and unloading at the east shore of the HKBCF Island, which has been being used by contractor Contract No. HY/2010/02 for reclamation activities. In terms of safety consideration and to avoid mixing of sediment between contracts, each dumping date will be allocated to one Contract. The quantity of marine sediment disposed on each date is from one Contract.
- 6.2.3.3 During dumping, HY/2013/02 is responsible for transporting the marine sediment from his site area to the barge by Land transportation. The estimated quantity of marine sediment in each truck is confirmed by Resident Site Staff of each Contract. The trip tickets for transportation and disposal of marine sediment are collected and checked. Contract No. HY/2013/03 as the dumping permit holder (EP/MD/16-202 and EP/MD/17-007 in this reporting period) is responsible for reporting to EPD the quantity disposed of as the condition stipulated in the dumping permit.
- 6.2.4 Marine sediment extracted from bored piling in this Contract was disposed to allocated dumping site via Contract No. HY/2013/03 on 02, 06, 07, 13, 14, 15, 16, 17 & 26 April 2016. The quantity disposed up to end of April 2016 was 9816 m³. The Monthly Summary of Marine sediment disposed to dumping site was provided in **Appendix E** and **Table 6.1**.

Table 6.1 Summary of marine sediment disposed to dumping site via Contract No. HY/2013/03

Month/Year	Quantity disposed (m ³)
January 2016	1272
February 2016	2816
March 2016	600
April 2016	5128
Total =	9816

- **6.2.5** The Contractor shall ensure no spilling and overflowing of materials during loading / transportation is allowed.
- **6.2.6** The monthly summary of waste flow table is detailed in **Appendix E**.
- 6.2.7 The Contractor was reminded that chemical waste containers should be properly treated and stored temporarily in designated chemical waste storage area on site in accordance with the Code of Practice on the Packing, Labelling and Storage of Chemical Waste.

6.3 Environmental Licenses and Permits

The valid environmental licenses and permits during the reporting period are summarized in **Appendix F**.

6.4 Implementation Status of Environmental Mitigation Measures

- **6.4.1** In response to the site audit findings, the Contractor carried out corrective actions.
- **6.4.2** The Contractor waters 8 times per day on all exposed soil within the project site and associated works areas when construction activities are being undertaken.
- **6.4.3** The Contractor was reminded to provide well-maintained plant operated on-site and plant served regularly;
- **6.4.4** The Contractor was reminded to switch off vehicles and equipment while not in use;
- **6.4.5** The Contractor was reminded to schedule the construction works to minimize noise nuisance etc.



ENA61697 Monthly EM&A Report No.17

- 6.4.6 Training material of Regular Marine Travel Route Plan was prepared. Since the training material is under review, and marine delivery operation still not commence, the RMTRP training is not yet started. There have not any vessel in or out the BCF perimeter silt curtain so that no Marine Travel Route was recorded.
- **6.4.7** The tool box training of dolphin was carried out in Dec 2015. According to the action plan and communication flow chart of dolphin instruction, if any dolphin intruded BCF perimeter silt curtain, ETL should be informed. There was no notification received on any dolphin intrusion during the reporting period.
- **6.4.8** A summary of the implementation Schedule of Environmental Mitigation Measures (EMIS) is presented in **Appendix G**. Most of the necessary mitigation measures were implemented properly.
- 6.5 Summary of Exceedance of the Environmental Quality Performance Limit
- 6.5.1 Summary of Action and Limit Level exceedance of 1-hr TSP level and 24-hr TSP level at AMS6 shall be referred to the monthly EM&A report prepared by Contract No. HY/2011/03.
- 6.5.2 There was no Action and Limit Level exceedance of 1-hr TSP level and 24-hr TSP level recorded at station AMS7 by the Environmental Team of Contract No. HY/2010/02 during the reporting period.
- 6.5.3 There was no Action and Limit Level exceedance for noise recorded at station NMS2 and station NMS3B by the Environmental Team of Contract No. HY/2010/02 during the reporting period.
- 6.5.4 There was no Action and Limit Level exceedance for water quality recorded at the monitoring stations showed at **Table 4.1** by the Environmental Team of Contract No. HY/2010/02 during the reporting period.
- **6.5.5** Impact dolphin monitoring results at all transects are reported in the EM&A Reports prepared for Contract No. HY/2010/02.
- 6.6 Summary of Complaints, Notification of Summons and Successful Prosecution
- **6.6.1** There were no complaints received during the reporting period.
- **6.6.2** There were no notifications of summons or prosecutions received during the reporting period.
- **6.6.3** Statistics on environmental complaints, notifications of summons and successful prosecutions are summarized in **Appendix H.**



ENA61697 Monthly EM&A Report No.17

7 FUTURE KEY ISSUES

7.1 Construction Programme for the Coming Months

7.1.1 As informed by the Contractor, the major construction activities for May 2016 are summarized in **Table 7.1**.

Table 7.1 Construction Activities for Coming Month

Site Area	Description of Activities		
Portion A1, D, C1, F&C2	Bored Piles Works		
Portion A1 & D	Pier / Abutment		
Portion A1& D.	Pile Cap		
Portion A	Filling works		
Portion D	Pre-bored H-pile for sign gantries in Portion		
Portion I	Pit excavation work and duct laying		
Portion I	UU Detection Works		
Portion I	Footing construction of directional signs		
	Construction of alternative site entrance.		
	Marine sediment excavation activities from the land-		
	based works and corresponding disposal at the		
	designated disposal sites.		

7.2 Environmental Site Inspection Schedule for the Coming Month

7.2.1 The tentative schedule for weekly site inspections for May 2016 is provided in Appendix I

8 CONCLUSION.

8.1 Conclusions

- **8.1.1** The site preparation work of the Contract was started on 25 July 2014 and the construction works of the Contract commenced on 24 November 2014.
- **8.1.2** Summary of Action and Limit Level exceedance of 1-hr TSP level and 24-hr TSP level at AMS6 shall be referred to the monthly EM&A report prepared by Contract No. HY/2011/03.
- **8.1.3** There was no Action and Limit Level exceedance of 1-hr TSP level and 24-hr TSP level recorded at station AMS7 by the Environmental Team of Contract No. HY/2010/02 during the reporting period.
- **8.1.4** There was no Action and Limit Level exceedance for noise recorded at station NMS2 and station NMS3B by the Environmental Team of Contract No. HY/2010/02 during the reporting period.
- **8.1.5** There was no Action and Limit Level exceedance for water quality recorded at the monitoring stations showed at **Table 4.1** by the Environmental Team of Contract No. HY/2010/02 during the reporting period.
- **8.1.6** Impact dolphin monitoring results at all transects are reported in the EM&A Reports prepared for Contract No. HY/2010/02.
- **8.1.7** There were no complaints received during the reporting period.
- **8.1.8** There were no notifications of summons or prosecutions received during the reporting period.

- END OF REPORT -



FIGURES



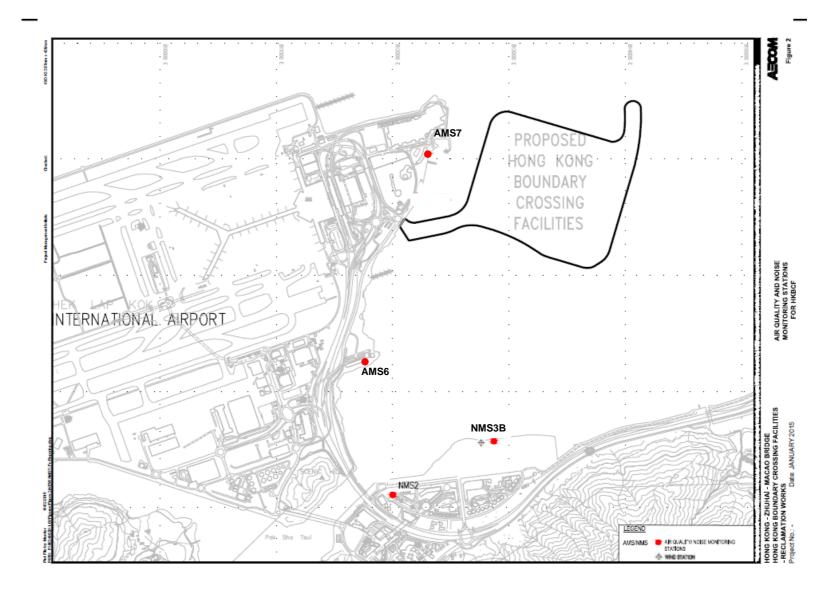


Figure 1 Air Quality and Noise Monitoring Stations for HKBCF


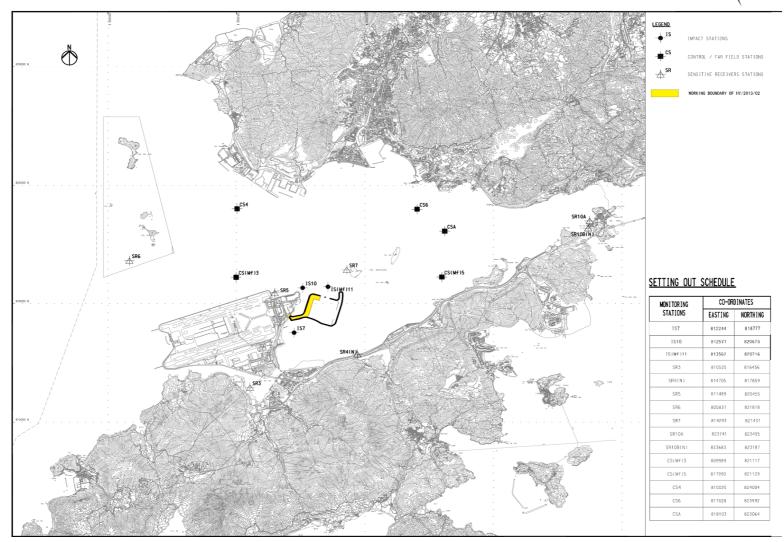


Figure 2 Water Quality Monitoring Stations(construction phases)



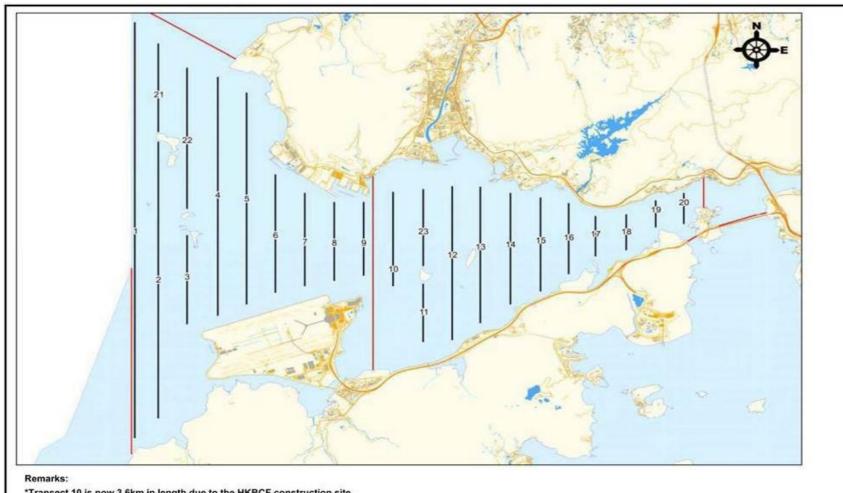

*Transect 10 is now 3.6km in length due to the HKBCF construction site.

^Coordinates for transect lines 1, 2, 7, 8, 9 and 11 have been updated in respect to the Proposal for Alteration of Transect Line for Dolphin Monitoring approved by EPD on 19 August 2015. The total transect length for both NEL and NWL combined is 108km.


Dolphin Monitoring Transect Line and Layout Map Figure 3




Appendix A


Location of Works Areas



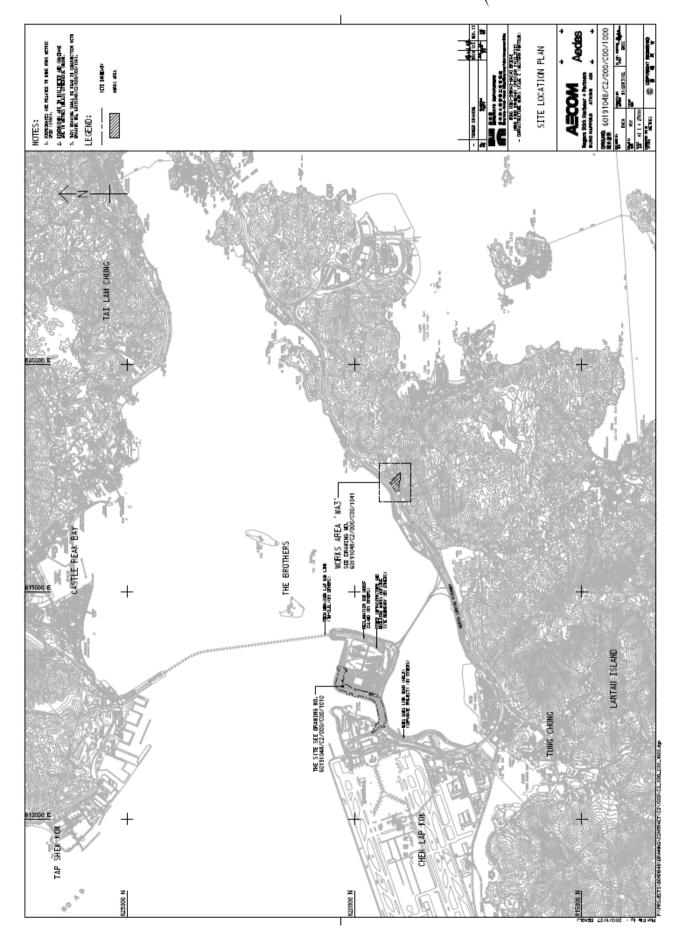



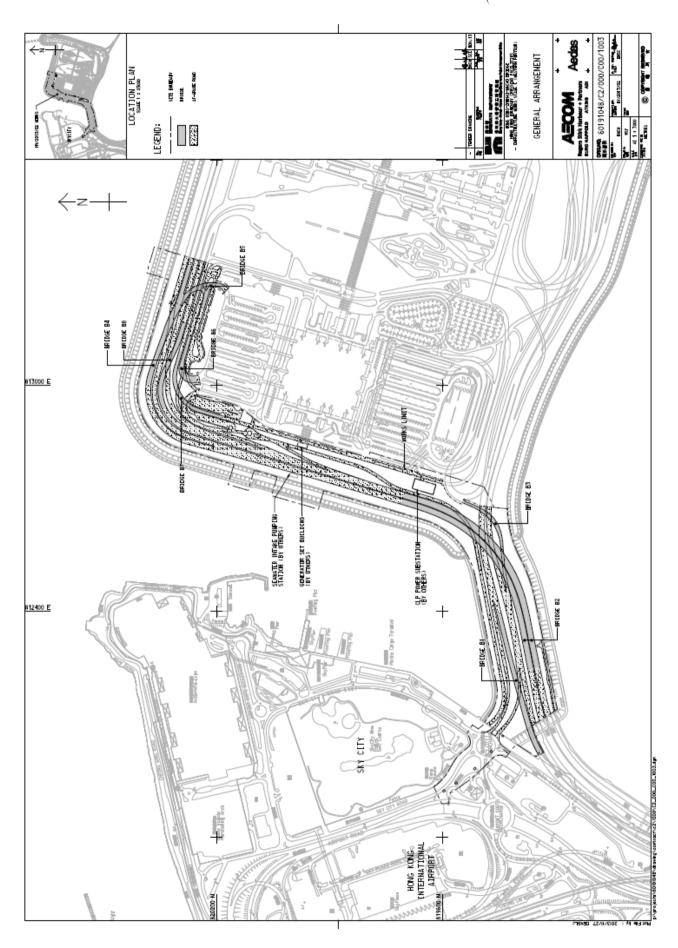

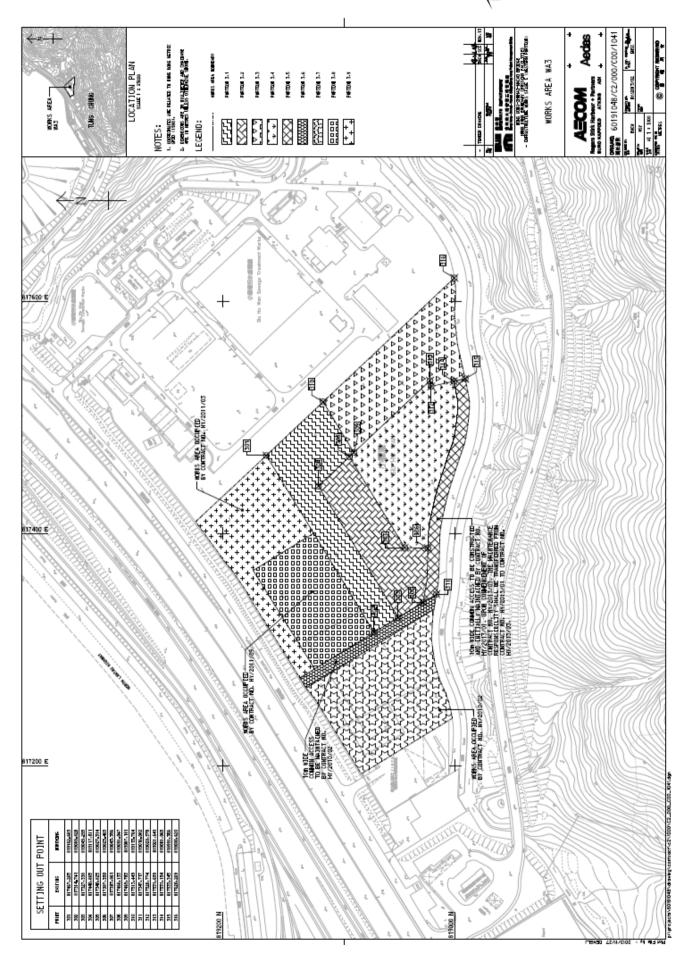




Appendix B

Project Organization for Environmental Works



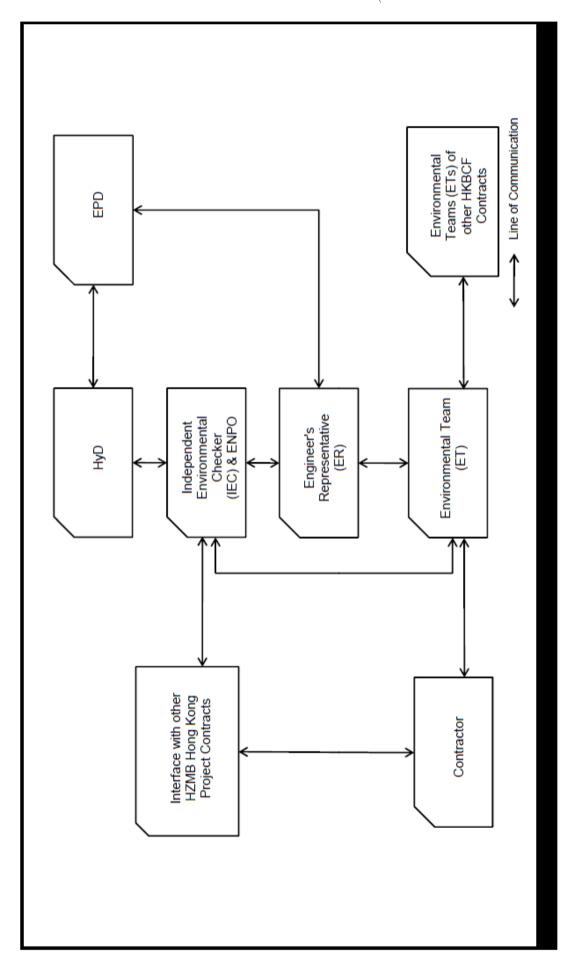




Appendix C

Construction Programme




Production Product P	
79 2404.16 72.07-17 WP-7d 1125 0 2404.16 24.04.17 WP-7d 1120 0 2404.16 24.04.17 WP-7d 1120 0 2404.16 26.04.17 WP-7d 1120 0 2404.16 24.04.17 WP-7d 1120 0 2404.16 24.04.17 WP-7d 1120 0 24.04.16 24.04.17 WP-7d 24.04 0 24.04.16 24.04.17 WP-7d 24	
0 24.04.16 24.04.1	
O	
And Pertien A S (COW-A3864) 0 2-40-416 0 0 W WP-7d - 253 not of Pertien A S (COW-A3864) 0 2-40-416 0 0 W WP-7d - 253 not of Pertien A S (COW-A3864) 0 2-40-416 0 0 W WP-7d - 152 not of Pertien F (COW-48764) 0 2-40-416 0 0 W WP-7d - 152 A S over supply to C op Park System (COW-6100) 0 2-40-411 0 0 W WP-7d - 129 A S over supply to C op Park System (COW-6100) 0 2-40-411 0 0 W WP-7d - 129 A S over supply to C op Park System (COW-6100) 0 2-40-411 0 0 W WP-7d - 129 A S over supply to C op Park System (COW-6100) 0 2-40-411 0 0 W WP-7d - 129 A S over supply to C op Park System (COW-6100) 0 2-40-411 0 0 W WP-7d - 1204 A S over supply to C op Park System (COW-6100) 0 2-40-411 0 0 W WP-7d - 1204 A S over supply to C op Park System (COW-6100) 0 2-40-411 0 0 W WP-7d - 1204 A S over supply to C op Park System (COW-6100) 0 2-40-411 0 0 W WP-7d - 1204 A S over supply to C op Park System (COW-6100) 0 2-40-411 0 0 W WP-7d - 1204 A S over supply to C op Park System (COW-6100) 0 0 2-40-411 0 0 W WP-7d - 1204 A S over supply to C op Park System (COW-6100) 0 0 2-40-411 0 0 W WP-7d - 1204 A S over supply to C op Park System (COW-6100) 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0	
And Pertion 6 (COW+41744) 10 0 24-04-16 10 0 34-04-16 10 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0	
An of Pertition (CLOUA-48.6.7) A Part of Pertition (CLOUA-48.6.7) B Power supply to Cap Part's System (COW-61.0.6) C Part of Pertition (CLOUA-48.6.7) C Pertition (A. A.) C Per	
Servers against to the control of	
8 Power supply to Cap Pair's System (COW-610d) 0 24-04-11 0% WP-74 -39 eabling of ther then portion AA, 52, 68 F (COW-920c 0 2-04-11 0% WP-74 -39 eabling for portion AA, 52, 68 F (COW-920c) 0 24-04-11 0% WP-74 -129 indexer of Portion AA, 52, 68 F (COW-920d) 0 24-04-11 0% WP-74 -1204 indexer of Portion AA, 52, 68 F (COW-920d) 0 24-04-11 0% WP-74 -1204 indexer of Portion AA, 88 to HY2013/04 (COW-250d) 0 24-04-11 0% WP-74 -1204 indexer of Portion AA, 88 to HY2013/04 (COW-250d) 0 24-04-11 0% WP-74 -1204 of Portion A2, (ED15) 0 24-04-11 0% WP-74 -1204 of Portion A2, (ED15) 0 24-04-11 0% WP-74 -1204 of Portion H(CD11) 1204 of Abutment at Bridge Sb (AS06) 0 24-04-16 0% WP-74 -1204 Contracted Bridge Company of Portion H(CD11) 1204 of Abutment at Bridge Sb (AS06) 0 24-04-16 0% WP-74 -1204 Contracted Bridge Company of Portion H(CD11) 1204 of Abutment at Bridge Sb (AS06) 0 24-04-16 0% WP-74 -1204 Contracted Bridge Sb (AS06) 0 24-04-16 0% WP-74 -1304 Contracted Bridge WP-74 -1204 Contracted Bridge Sb (AS06) 0 24-04-16 0% WP-74 -1304 Contracted Bridge WP-74 -1204 Contracted Bridge	
eabling other then portion A4, A5, E & F (COW+230) o	
Peabling for portion A4, A5, E & F (COW+5104) Peabling for portion A4, A5, E & F (COW+5104) Peabling for portion A2, A5, E & F (COW+5104) Robert of Pertion A2, B3 to HY2033 (COW+5204) Robert of Pertion A2, B3 to HY2033 (COW+5204) Pertion B2 (KD15) Pertion B2 (KD15) Pertion B3 (KD15) Pertion B4 (KD15) Pertio	
Indexer of Portion R2 to In/2013/03 (COW4-2504) 0 24-04-11 0% WP-7d 1204 Indexer of Portion R2 to In/2013/04 (COW4-2504) 0 24-04-11 0% WP-7d 1204 Indexer of Portion R2 to In/2013/04 (COW4-2504) 0 24-04-11 0% WP-7d 1204 Indexer of Portion R2 (EUS) 0 24-04-11 0% WP-7d 1204 Indexer of Portion R3 (EUS) 0 24-04-11 0% WP-7d 1204 Indexer of Portion R3 (EUS) 0 24-04-11 0% WP-7d 1204 Indexer of Portion R3 (EUS) 0 24-04-11 0% WP-7d 1204 Indexer of Portion R4 (EUS) 0 24-04-11 0% WP-7d 1204 Indexer of Abutment at Bridge Sb (ASOS) 0 24-04-11 0% WP-7d 1204 Indexer of Abutment at Bridge Sb (ASOS) 0 24-04-16 0% WP-7d 1204 Indexer of Abutment at Bridge Sb (ASOS) 0 24-04-16 0% WP-7d 1204 Indexer Building, Wrake & died 0 24-04-16 0% WP-7d 1204 Indexer Building, Wrake & died 0 24-04-16 0% WP-7d 1204 Indexer Building to PCB 0 24-04-16 0% WP-7d 1204 Indexer Building to PCB 0 24-04-16 0% WP-7d 1204 Indexer Building to PCB 0 24-04-16 0% WP-7d 1204 Indexer Building to PCB 0 24-04-16 0% WP-7d 1204 Indexer Building to PCB 0 24-04-16 0% WP-7d 1204 Indexer Cap const work start 0 12-04-16 17-07-16 18-07-16 0% WP-7d 1304 Indexer Cap const work start 0 12-07-16 0% WP-7d 1204 Indexer Cap const work start 0 12-07-16 0% WP-7d 1204 Indexer Cap const work start 0 12-07-16 0% WP-7d 1204 Indexer Cap const work start 0 12-07-16 0% WP-7d 1204 Indexer Cap const work start 0 12-07-16 0% WP-7d 1204 Indexer Cap const work start 0 12-07-16 0% WP-7d 1204	
ridover of Portion A.2 & B.3 to HY/2013/04 (COW+35) 0 24-04-14 0% WP-7d 1204 of Portion A.2 (KD15) 0 24-04-14 0% WP-7d 1204 of Portion B.2 (KD15) 0 24-04-14 0% WP-7d 1204 of Portion B.2 (KD15) 0 24-04-14 0% WP-7d 1204 of Portion B.2 (KD15) 0 24-04-14 0% WP-7d 1204 of Portion B.2 (KD15) 0 24-04-16 0% WP-7d 1204 of Portion B.2 (KD15) 0 24-04-16 0% WP-7d 1204 of Portion B.2 (KD15) 0 24-04-16 0% WP-7d 1204 of Abutment at Bridge 6 0 24-04-16 0% WP-7d 1204 of Abutment at Bridge 6 0 24-04-16 0% WP-7d 1204 of Abutment at Bridge 6 0 24-04-16 0% WP-7d 1204 of Abutment at Bridge 6 0 24-04-16 0% WP-7d 1204 of Abutment at Bridge 6 0 24-04-16 0% WP-7d 1204 of Abutment at Bridge 6 0 24-04-16 1204 of Portion B.2 (WP-7d 120	
of Pertion A2 (RD15) 0 24-04-16 WWP-76 1204 of Pertion R2 (RD15) 0 24-04-16 0% WP-76 1204 of Pertion R2 (RD15) 0 24-04-17 0% WP-76 1204 of Pertion R2 (RD15) 0 24-04-17 0% WP-76 1204 of Pertion R2 (RD15) 0 24-04-17 0% WP-76 1204 of Pertion R2 (RD15) 0 24-04-16 0% WP-76 1204 of Aburnet at Bridges 0 24-04-16 24-04-11 0% WP-76 1304 of Aburnet at Bridges 0 24-04-16 0% WP-76 131 0 0 of Aburnet at Bridges 0 24-04-16 0% WP-76 1324 0 0 0 of Aburnet at Bridges 0 24-04-16 0% WP-76 1324 0	
Orderion A2 (RO16)	
of Portion 82 (KD15) 0 24-04-16 0% WP-7d 1204 of Portion 82 (KD15) 0 24-04-16 0% WP-7d 1204 of Portion 83 (KD15) 0 24-04-16 0% WP-7d 1204 of Portion 14 (KD11) 0 0 24-04-16 0% WP-7d 1204 of Portion 83 (KD15) 0 0 24-04-16 0% WP-7d 1204 of Portion 83 (KD15) 0 0 24-04-16 0% WP-7d 1204 of Portion 83 (KD16) 0 0 24-04-16 0% WP-7d 1204 of Portion 83 (KD16) 0 0 24-04-16 0% WP-7d 1204 of Portion 83 (KD16) 0 0 24-04-16 0% WP-7d 1204 of Portion 83 (KD16) 0 0 24-04-16 0% WP-7d 1204 of Portion 83 (KD16) 0 0 24-04-16 0% WP-7d 1204 of Portion 83 (KD16) 0 0 24-04-16 0% WP-7d 1204 of Portion 83 (KD16) 0 0 24-04-16 0% WP-7d 1204 of Portion 83 (KD16) 0 0 24-04-16 0% WP-7d 1204 of Portion 83 (KD16) 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0	
of Pertion B (kD16) 0 24-04-11 0% WP-7d 1204 cor Pertion H (KD11) 0 24-04-11 0% WP-7d 1204 cor Corporate Building 0 24-04-14 0% WP-7d 1204 cor Corporate Building 0 24-04-16 0% WP-7d 1204 cor Corporate Building 0 24-04-16 0% WP-7d 1204 cof Aburment at Bridge 0 24-04-16 0% WP-7d 1204 cof Aburment at Bridge 0 24-04-16 0% WP-7d 1204 cof Aburment at Bridge 0 24-04-16 0% WP-7d 1204 cof Aburment at Bridge 0 24-04-16 0% WP-7d 1204 cof Aburment at Bridge 0 24-04-16 0% WP-7d 1204 cof Aburment at Bridge 0 24-04-16 0% WP-7d 1204 cof Aburment at Bridge 0 24-04-16 0% WP-7d 1204 cof Aburment at Bridge 0 24-04-16 0% WP-7d 1204 cof R2 to VCF for there works 0 <td></td>	
10 12 12 12 12 12 12 12	
O 24.04-16 24.04-1	
See Character Building to Perform there works 0 24-04-16 0 WP-7d 1204 WP-7d WP	
PCB for there works 0 24-04-16 ON WP-7d 1204 at 8 Bridge 6 0 0 24-04-16 ON WP-7d 1204 at 8 Bridge 8 Color 1 24-04-16 ON WP-7d 1204 building to PCB 0 24-04-16 ON WP-7d 1204 for there works 0 24-04-16 DATE 1204 building to PCB 0 12-04-16 ON WP-7d 1204 for there works 1 0 12-04-16 ON WP-7d 1204 const work start 0 12-04-16 ON WP-7d 1204 or 12-04-16 ON WP-7d 12	
to Bridge So (Aside So (As	
to the finding intake & died 0 24-04-14 0% WP-7d 23 Station, Genset Building, intake & died 0 24-04-14 0% WP-7d 1204 Midding to PCB 0 24-04-15 0 0% WP-7d 1204 Station Construction 0 24-04-16 0 0% WP-7d 1204 For there works Construction 0 24-04-16 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0	
Stration, General Building, Irrake & died 0 24-04-11 095 WP-7d 1204 Last Commission of the Commission	
12 12 12 12 12 12 12 12	
120 120	
Secretary Continue works	
12-04-16 12-07-14	
const work start 0 29 G4-16 12 G4-16 <td></td>	
0 29-04-16	
0 12.05.16 12.05.14 0WP-74 0 12.07.16 12.07.14 0WP-74 0 12.07.14 0WP-74 0 12.07.15 17.07.11 0WP-74 0 12.07.15 17.07.11 0WP-74 0 12.07.15 17.07.11 0WP-74 0 12.07.15 17.07.11 0WP-74 0 12.07.14 0WP-74 0 12.07.15 17.07.11 0WP-74 0 12.07.15 17.07.15 1	
0 12-05-16 0% WP-7d 0 12-07-16 12-07-16 0% WP-7d 0 12-07-16 0% WP-	
84 Substructure - Cap const work start	
64 Substructure - Cap const work start	•
0 12.07.16 12.07.16 WP-7d 85 Substructure - Cap const work start 0 12-07-16 0% WP-7d	٠
0 12-07-16 0% WP-7d	<u> </u>
	•
ructure 266	
151 07-01-16 30-07-1f 6d/h -	
120 07:01:16 10:06:1f 64/h	
49 07-01-16 28-05-1f 42.86% 6d/h	
29 02 06 16 30 07 1t 6d/h	
27-06-1¢ 0% 6d/h	
hos) 21 20-06-16 14-07-1f 0% 6d/h	
4. U/-U/-1b 30-U/-1b	
Die 8 Ahrtemant D205 D204 (2 acc)	
U/DO %0)T-/0-47 OT-50:07 45	
31-/0-05 91-/0-14 PV	
83-0070 83 - Falsowork & Base FW/ IP3G-5-P3GA 14 15-07-10 19-007-10 10-00-10-0	
11/no %0 31-/0-05 01-/0-01 to	
213 30-10-15 27-07-16 66/h -211	
Remaining Level of Effort — Remaining Work	Date Revision Chec Approved
Critical Remaining Work	
•	



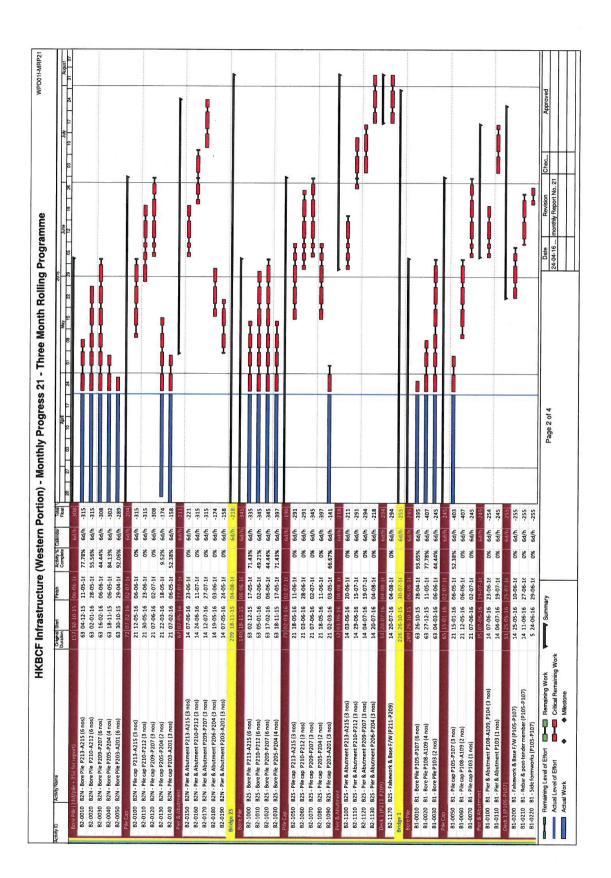

13 0.0-7.16 0.0-7.17 0.0% 6d/h 21 13 0.0-7.16 0.0-7.17 0.0% 6d/h 21 13 0.0-16 1.0-9.11 0.0-7.17 0.0-7.17 21 0.0-0.7.16 1.0-9.11 0.0-7.17 0	3. M371.1 (23m) 300mm
D1-0540 M76AA19-M45A.2 (39m) 450mm 20 16-07-16 08-08-16 0% 6d/h -144 Stand Deline about 43.3m (2m/dsh)	19m 450mm 20 15-07-16 08-08-16 0% 64/h 182 25-04-16 12-08-16 64/h 182 25-04-16 12-06-16 64/h 25-04-16 26-06-16 64/h

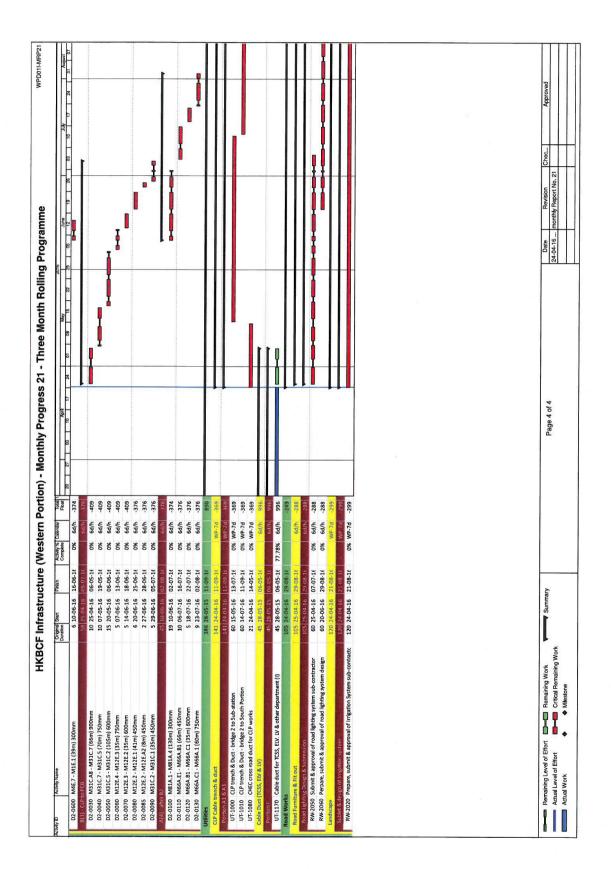



Appendix D

Event and Action Plan



Event/Action Plan for Air Quality

EVENT	ACTION					
	ET	IEC	ER	CONTRACTOR		
ACTION LEVEL			L	1		
Exceedance for one sample	Identify source, investigate the causes of exceedance and propose remedial measures; Inform IEC and ER; Repeat measurement to confirm finding; Increase monitoring frequency to daily.	Check monitoring data submitted by ET; Check Contractor's working method.	Notify Contractor.	Rectify any unacceptable practice; Amend working methods if appropriate.		
Exceedance for two or more consecutive samples	1. Identify source; 2. Inform IEC and ER; 3. Advise the ER on the effectiveness of the proposed remedial measures; 4. Repeat measurement s to confirm findings; 5. Increase monitoring frequency to daily; 6. Discuss with IEC and Contractor on remedial actions required; 7. If exceedance continues, arrange meeting with IEC and ER; 8. If exceedance stops, cease additional monitoring.	1. Check monitoring data submitted by ET; 2. Check Contractor's working method; 3. Discuss with ET and Contractor on possible remedial measures; 4. Advise the ER on the effectiveness of the proposed remedial measures; 5. Supervise Implementation of remedial measures.	Confirm receipt of notification of failure in writing; Notify Contractor; Ensure remedial measures properly implemented.	1. Submit proposals for remedial to ER within 3 working days of notification; 2. Implement the agreed proposals; 3. Amend proposal if appropriate.		



EVENT		ACTI	ON	
	ET	IEC	ER	CONTRACTOR
LIMIT LEVEL				
Exceedance for one sample	Identify source, investigate the causes of exceedance and propose remedial measures; Inform ER, Contractor and EPD; Repeat measurement to confirm finding; Increase monitoring frequency to daily; Assess effectiveness of Contractor's remedial actions and keep IEC, EPD and ER informed of the results.	Check monitoring data submitted by ET; Check Contractor's working method; Discuss with ET and Contractor on possible remedial measures; Advise the ER on the effectiveness of the proposed remedial measures; Supervise implementation of remedial measures.	Confirm receipt of notification of failure in writing; Notify Contractor; Ensure remedial measures properly implemented.	Take immediate action to avoid further exceedance; Submit proposals for remedial actions to IEC within 3 working days of notification; Implement the agreed proposals; Amend proposal if appropriate.
Exceedance for two or more consecutive samples	1. Notify IEC, ER, Contractor and EPD; 2. Identify source; 3. Repeat measurement to confirm findings; 4. Increase monitoring frequency to daily; 5. Carry out analysis of Contractor's working procedures to determine possible mitigation to be implemented; 6. Arrange meeting with IEC and ER to discuss the remedial actions to be taken; 7. Assess effectiveness of Contractor's remedial actions and keep IEC, EPD and ER informed of the results; 8. If exceedance stops, cease additional monitoring.	1. Discuss amongst ER, ET, and Contractor on the potential remedial actions; 2. Review Contractor's remedial actions whenever necessary to assure their effectiveness and advise the ER accordingly; 3. Supervise the implementation of remedial measures.	1. Confirm receipt of notification of failure in writing; 2. Notify Contractor; 3. In consultation with the IEC, agree with the Contractor on the remedial measures to be implemented; 4. Ensure remedial measures properly implemented; 5. If exceedance continues, consider what portion of the work is responsible and instruct the Contractor to stop that portion of work until the exceedance is abated.	1. Take immediate action to avoid further exceedance; 2. Submit proposals for remedial actions to IEC within 3 working days of notification; 3. Implement the agreed proposals; 4. Resubmit proposals if problem still not under control; 5. Stop the relevant portion of works as determined by the ER until the exceedance is abated.



Event / Action Plan for Construction Noise Monitoring

EVENT	of Refore Service	ACTION		
	ET CONTRACTOR	JEC	ER	CONTRACTOR
Action Level	Notify IEC and Contractor; Identify source, investigate the causes of exceedance and propose remedial measures; Report the results of investigation to the IEC, ER and Contractor; Discuss with the Contractor and formulate remedial measures; Increase monitoring frequency to check mitigation effectiveness.	Review the analysed results submitted by the ET; Review the proposed remedial measures by the Contractor and advise the ER accordingly; Supervise the implementation of remedial measures.	Confirm receipt of notification of failure in writing; Notify Contractor; Require Contractor to propose remedial measures for the analysed noise problem; Ensure remedial measures are properly implemented.	Submit noise mitigation proposals to IEC; Implement noise mitigation proposals.
Limit Level	1. Inform IEC, ER, EPD and Contractor; 2. Identify source; 3. Repeat measurements to confirm findings; 4. Increase monitoring frequency; 5. Carry out analysis of Contractor's working procedures to determine possible mitigation to be implemented; 6. Inform IEC, ER and EPD the causes and actions taken for the exceedances; 7. Assess effectiveness of Contractor's remedial actions and keep IEC, EPD and ER informed of the results; 8. If exceedance stops, cease additional monitoring.	Discuss amongst ER, ET, and Contractor on the potential remedial actions; Review Contractors remedial actions whenever necessary to assure their effectiveness and advise the ER accordingly; Supervise the implementation of remedial measures.	Confirm receipt of notification of failure in writing; Notify Contractor; Require Contractor to propose remedial measures for the analysed noise problem; Ensure remedial measures properly implemented; If exceedance continues, consider what portion of the work is responsible and instruct the Contractor to stop that portion of work until the exceedance is abated.	1. Take immediate action to avoid further exceedance; 2. Submit proposals for remedial actions to IEC within 3 working days of notification; 3. Implement the agreed proposals; 4. Resubmit proposals if problem still not under control; 5. Stop the relevant portion of works as determined by the ER until the exceedance is abated.



Event and Action Plan for Water Quality

Event	ET Leader	IEC	ER	Contractor
Action level being exceeded by one sampling day	1. Repeat in situ measurement on next day of exceedance to confirm findings; 2. Identify source(s) of impact; 3. Inform IEC, contractor and ER; 4. Check monitoring data, all plant, equipment and Contractor's working methods;	Confirm receipt of notification of noncompliance in writing; Notify Contractor	Confirm receipt of notification of noncompliance in writing; Notify Contractor	Inform the ER and confirm notification of the noncompliance in writing; Rectify unacceptable practice; Amend working methods if appropriate.
Action level being exceeded by two or more consecutive sampling days	1. Repeat in situ measurement to confirm findings; 2. Identify source(s) of impact; 3. Inform IEC, Contractor and ER; 4. Check monitoring data, all plant, equipment and Contractor's working methods; 5. Discuss mitigation measures with IEC, ER and Contractor; 6. Ensure mitigation measures are implemented; 7. Increase the monitoring frequency to daily until no exceedance of Action level; 8. Repeat measurement on next day of exceedance to confirm findings.	Check monitoring data submitted by ET and Contractor's working method; Discuss with ET and Contractor on possible remedial actions; Review the proposed mitigation measures submitted by Contractor and advise the ER accordingly; Assess the effectiveness of the implemented mitigation measures.	1. Confirm receipt of notification of noncompliance in writing; 2. Discuss with IEC on the proposed mitigation measures; 3. Make agreement on mitigation measures to be implemented; 4. Ensure mitigation measures are properly implemented; 5. Assess the effectiveness of the implemented mitigation measures.	1. Inform the Engineer and confirm notification of the noncompliance in writing; 2. Rectify unacceptable practice; 3. Check all plant and equipment and consider changes of working methods; 4. Discuss with ET and IEC on possible remedial actions and propose mitigation measures to IEC and ER within 3 working days of notification; 5. Implement the agreed mitigation measures; 6. Amend working methods if appropriate.
Limit level being exceeded by one sampling day	1. Repeat in-situ measurement to confirm findings; 2. Identify source(s) of impact; 3. Inform IEC, Contractor, ER and EPD; 4. Check monitoring data, all plant, equipment and Contractor's working methods; 5. Discuss mitigation measures with IEC, ER and Contractor; 6. Ensure mitigation measures are implemented; 7. Increase the monitoring frequency to daily until no exceedance of Limit level.	Check monitoring data submitted by ET and Contractor's working method; Discuss with ET and Contractor on possible remedial actions; Review the proposed mitigation measures submitted by Contractor and advise the ER accordingly; Assess the effectiveness of the implemented mitigation measures.	Confirm receipt of notification of failure in writing; Discuss with IEC, ET and Contractor on the proposed mitigation measures; Request Contractor to critically review the working methods; Ensure mitigation measures are properly implemented; Assess the effectiveness of the implemented mitigation measures	1. Inform the ER and confirm notification of the noncompliance in writing; 2. Rectify unacceptable practice; 3. Check all plant and equipment and consider changes of working methods; 4. Submit proposal of mitigation measures to ER within 3 working days of notification and discuss with ET, IEC and ER; 5. Implement the agreed mitigation measures; 6. Amend working methods if appropriate.
Limit level being exceeded by two or more consecutive sampling days	1. Repeat in-situ measurement to confirm findings; 2. Identify source(s) of impact; 3. Inform IEC, contractor, ER and EPD; 4. Check monitoring data, all plant, equipment and Contractor's working methods; 5. Discuss mitigation measures with IEC, ER and Contractor;	Check monitoring data submitted by ET and Contractor's working method; Discuss with ET and Contractor on possible remedial actions; Review the Contractor's mitigation measures whenever necessary to assure their effectiveness and advise the ER accordingly.	Confirm receipt of notification of failure in writing; Discuss with IEC, ET and Contractor on the proposed mitigation measures; Request Contractor to critically review the working methods; Make agreement on the mitigation measures to be implemented;	1. Inform the ER and confirm notification of the noncompliance in writing; 2. Take immediate action to avoid further exceedance; 3. Rectify unacceptable practice; 4. Check all plant and equipment and consider changes of working methods;



6. Ensure mitigation measures are implemented; 7. Increase the monitoring frequency to daily until no exceedance of Limit level for two consecutive days	5. Ensure mitigation measures are properly implemented; 6. Assess the effectiveness of the implemented mitigation measures; 7. Consider and instruct, if necessary, the Contractor to slow down or to stop all or part of the construction activities until no exceedance of Limit level.	5. Submit proposal of mitigation measures to ER within 3 working days of notification and discuss with ET, IEC and ER; 6. Implement the agreed mitigation measures; 7. Resubmit proposals of mitigation measures if problem still not under control; 8. As directed by the engineer, to slow down or to stop all or part of the
		8. As directed by the engineer, to slow down or to stop all or part of the construction activities until no exceedance of Limit level.



Fuent	/ A ation	Diam fo	r Dalahia	Monitoring
-vent	/ Action	Plan to	rıbolonin	Ivionitorina

Event	ET Leader	IEC	ER / SOR	Contractor
Action Level	1. Repeat statistical data analysis to confirm findings; 2. Review all available and relevant data, including raw data and statistical analysis results of other parameters covered in the EM&A, to ascertain if differences are as a result of natural variation or previously observed seasonal differences; 3. Identify source(s) of impact; 4. Inform the IEC, ER/SOR and Contractor; 5. Check monitoring data. 6. Review to ensure all the dolphin protective measures are fully and properly implemented and advise on additional measures if necessary.	1. Check monitoring data submitted by ET and Contractor; 2. Discuss monitoring results and finding with the ET and the Contractor. Ontractor.	Discuss monitoring with the IEC and any other measures proposed by the ET; If ER/SOR is satisfied with the proposal of any other measures, ER/SOR to signify the agreement in writing on the measures to be implemented.	Inform the ER/SOR and confirm notification of the non-compliance in writing; Discuss with the ET and the IEC and propose measures to the IEC and the ER/SOR; Implement the agreed measures.
Limit Level	1. Repeat statistical data analysis to confirm findings; 2. Review all available and relevant data, including raw data and statistical analysis results of other parameters covered in the EM&A, to ascertain if differences are as a result of natural variation or previously observed seasonal differences; 3. Identify source(s) of impact; 4. Inform the IEC, ER/SOR and Contractor of findings; 5. Check monitoring data; 6. Repeat review to ensure all the dolphin protective measures are fully and properly implemented and advise on additional measures if necessary. 7. If ET proves that the source of impact is caused by any of the construction activity by the works contract, ET to arrange a meeting to discuss with IEC, ER/SOR and Contractor the necessity of additional dolphin monitoring and/or any other potential mitigation measures (e.g., consider to modify the perimeter silt curtain or consider to control/temporarily stop relevant construction activity etc.) and submit to IEC a proposal of additional dolphin monitoring and/or mitigation measures where necessary.	Check monitoring data submitted by ET and Contractor; Discuss monitoring results and findings with the ET and the Contractor; Attend the meeting to discuss with ET, ER/SOR and Contractor the necessity of additional dolphin monitoring and any other potential mitigation measures. Review proposals for additional monitoring and any other mitigation measures submitted by ET and Contractor and advise ER/SOR of the results and findings accordingly. Supervise / Audit the implementation of additional monitoring and/or any other mitigation measures and advise ER/SOR the results and findings accordingly.	1. Attend the meeting to discuss with ET, IEC and Contractor the necessity of additional dolphin monitoring and any other potential mitigation measures. 2. If ER/SOR is satisfied with the proposals for additional dolphin monitoring and/or any other mitigation measures submitted by ET and Contractor and verified by IEC, ER/SOR to signify the agreement in writing on such proposals and any other mitigation measures. 3. Supervise the implementation of additional monitoring and/or any other mitigation measures.	1. Inform the ER/SOR and confirm notification of the non-compliance in writing; 2. Attend the meeting to discuss with ET, IEC and ER/SOR the necessity of additional dolphin monitoring and any other potential mitigation measures. 3. Jointly submit with ET to IEC a proposal of additional dolphin monitoring and/or any other mitigation measures when necessary. 4. Implement the agreed additional dolphin monitoring and/or any other mitigation measures.



Appendix E

Waste Flow Table





Monthly Summary Waste Flow Table for 2016 (year)

Name of Person completing the record: Joy CHAN / ES

Project: Hong Kong - Zhuhai - Macao Bridge, Hong Kong Crossing Boundary Facilities - Infrastructure Works Stage I (Western Portion)

Contract No.: HY/2013/02

	8	Actual Quantitie	s of Inert C&I	Materials Gen	erated Monthly	7		Actual Quantit	ies of C&D Wastes C	enerated Monthly	
Month	Total Quantity Generated (in '000m³)	Quantity Generated (in (in 1000cm²)	Broken Reused in the Contract Note 1)	Reused in other Projects	Disposed as Public Fill	Imported Fill	Metals	Paper/ cardboard packaging	Plastics (see Note 2)	Chemical Waste	Others, e.g. general refuse (see Note 3)
i				(in '000m³)	(in '000m ³)	'000m ³) (in '000kg) (in '000kg) (in '000kg) (in '000kg)	(in '000 kg)	kg) (in '000kg) (in '000kg)	(in '000kg)	(in '000 m ³)	
Jan	0	0	0	0	0	0	0	0.069	2.66	0	0.0195
Feb	0	0	0	0	0	0	0	0	0	0	0.0455
Mar	0	0	0	0	0	0	0	0.069	0	0	0.0325
Apr	0	0	0	0	0	11.5920	0	0	0	0	0.0455
May		18							39	:	
Jun							7.			16	V.
Sub-total	0	0	0	0	0	11.5920	0	0.1380	2.66	0	0.1430
Jul		j,						,			
Aug		(0)									
Sep											
Oct											
Nov											re-
Dec								6	2		
Total	0	0	0	0	0	11.5920	0	0.1380	2.66	0	0.1430

Notes: (1) The waste flow table shall also include C&D materials that are specified in the Contract to be imported for use at the Site.

- (2) Plastics refer to plastic bottles/containers, plastic sheets/ foam from packaging materials.
- (3) Broken concrete for recycling into aggregates.



China Harbour Engineering Company Limited Monthly Summary of Marine Sediment for 2016

Month	a. Estimated Volume of Marine Sediment Generated (m ³)	b.Volume of Marine Sediment Disposed (m ³)	c.Estimated Volume of Marine Sediment Stored on Site (m ³) ⁽²⁾
Jan	4029 ⁽¹⁾	1272	2757
Feb	1133	2816	1074
Mar	414	600	888
Apr	4240	5128	0
May			
Jun			
Jul			
Aug			
Sep			
Oct			
Nov			
Dec			
Total	9816	9816	0

Note: 1) 2771 m³ Marine Sediment Generated has been brought froward from pervious year

2) c=(c in pervious month+a-b)



Appendix F

Environmental Licenses and Permits



Environmental Licenses and Permits

Item No.	Type of Permit / Licence	Reference No.	Application Date	Date of Issue	Date of Expiry	
1	Environmental Permit under EIAO	EP-353/2009/K	24 Mar 2016	11 Apr 2016	NA	Issued
2	Construction Dust Notification (Western Portion)	Acknowledge Receipt: 377883	5 Aug 2014	11 Aug 2014	NA	Notified
3	Construction Dust Notification (Works Area WA3)	Acknowledge Receipt: 377884	5 Aug 2014	18 Aug 2014	NA	Notified
4	Construction Waste Disposal Account	Billing Account No.: 7020516	5 Aug 2014	15 Aug 2014	NA	Account approved
5	Registration as a Chemical Waste Producer (Works Area WA3)	Waste Producer Number (WPN): 5213-961- C1186-23	1 Sep 2014	17 Oct 2014	NA	Registration completed
6	Registration as a Chemical Waste Producer (Western Portion)	Waste Producer Number (WPN): 5213-961- C1186-27	20 Oct 2014	24 Nov 2014	NA	Registration completed
7	Discharge License under WPCO (Works Area WA3)	License No.: WT00020194-2014	21 Aug 2014	27 Oct 2014	31 Oct 2019	License approved
8	Discharge License under WPCO(Western Portion)	License No.: WT00020597-2014	25 Sep 2014	16 Mar 2015	31 Mar 2020	License approved
9	Construction Noise Permit under NCO for HKBCF(Western Portion)	License No.: GW-RS0072-15	6 Jan 2015	22 Jan 2015	21 Jul 2015	Permit was surrendered with effective on 12 Feb 2015.
10	Construction Noise Permit under NCO for HKBCF(Western Portion)	License No.: GW-RS0087-16	20 Jan 2016	5 Feb 2016	5 Aug 2016	Permit approved
11	Construction Noise Permit under NCO for HKBCF(Western Portion)	License No.: GW-RS0432-16	19 April 2016	3 May 2016	10 Nov 2016	Permit approved



Appendix G

Implementation Schedule for Environmental Mitigation Measures (EMIS)

Environmental Mitigation Implementation Schedule – Hong Kong Boundary Crossing Facilities (Superstructures and Infrastructures)

EIA Ref.	EM&A Log Ref	Environmental Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Who to implement the measures?	Location	When to implement the measures?	What requirements or standards for the measure to achieve?	Implementation Status
Air Quality	/							
S5.5.6.1 of HKBCFEIA	A1	The contractor shall follow the procedures and requirements given in the Air Pollution Control (Construction Dust) Regulation	Good construction site practices to control the dust impact at the nearby sensitive receivers to within the relevant criteria		All construction sites	Construction stage	To control the dust impact to within the HKAQO and TM-EIA criteria(Ref. 1-hr and 24 hr TSP levels are 500 µgm ⁻³ and 260 µgm ⁻³ respectively)	V
S5.5.6.2 of HKBCFEIA and S4.8.1 of TKCLKLEIA	A2	2) Proper watering of exposed spoil should be undertaken throughout the construction phase: Any excavated or stockpile of dusty material should be covered entirely by impervious sheeting or sprayed with water to maintain the entire surface wet and then removed or backfilled or reinstated where practicable within 24 hours of the excavation or unloading; Any dusty materials remaining after a stockpile is removed should be wetted with water and cleared from the surface of roads; A stockpile of dusty material should not be extend beyond the pedestrian barriers, fencing or traffic cones. Where practicable, vehicle washing facilities with high pressure water jet should be provided at every discernible or designated vehicle exit point. The area where vehicle washing takes place and the road section between the washing facilities and the exit point should be paved with concrete, bituminous materials or hardcores; When there are open excavation and reinstatement works, hoarding of not less than 2.4m high should be provided as far as practicable along the site boundary with provision for public crossing. Good site practice shall also be adopted by the Contractor to ensure the conditions of the	Good construction site practices to control the dust impact at the nearby sensitive receivers to within the relevant criteria		All construction sites	Construction stage	To control the dust impact to within the HKAQO and TM-EIA criteria(Ref. 1-hr and 24 hr TSP levels are 500 µgm ⁻³ and 260 µgm ⁻³ , respectively)	V

EIA Ref.	EM&A Log Ref	Environmental Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Who to implement the measures?	Location	_	What requirements or standards for the measure to achieve?	Implementation Status
		hoardings are properly maintained throughout the construction period;						
		The portion of any road leading only to construction site that is within 30m of a vehicle entrance or exit should be kept clear of dusty materials;						
		Surfaces where any pneumatic or power- driven drilling, cutting, polishing or other mechanical breaking operation takes place should be sprayed with water or a dust suppression chemical continuously;						
		Any area that involves demolition activities should be sprayed with water or a dust suppression chemical immediately prior to, during and immediately after the activities so as to maintain the entire surface wet;						
		Where a scaffolding is erected around the perimeter of a building under construction, effective dust screens, sheeting or netting should be provided to enclose the scaffolding from the ground floor level of the building, or a canopy should be provided from the first floor level up to the highest level of the scaffolding;						
		Any skip hoist for material transport should be totally enclosed by impervious sheeting;						
		Every stock of more than 20 bags of cement or dry pulverised fuel ash (PFA) should be covered entirely by impervious sheeting or placed in an area sheltered on the top and the 3 sides;						
		Cement or dry PFA delivered in bulk should be stored in a closed silo fitted with an audible high level alarm which is interlocked with the material filling line and no overfilling is allowed;						
		Loading, unloading, transfer, handling or storage of bulk cement or dry PFA should						

EIA Ref.	EM&A Log Ref	Environmental Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Who to implement the measures?	Location	When to implement the measures?	What requirements or standards for the measure to achieve?	Implementation Status
		be carried out in a totally enclosed system or facility, and any vent or exhaust should be fitted with an effective fabric filter or equivalent air pollution control system; and						
		Exposed earth should be properly treated by compaction, turfing, hydroseeding, vegetation planting or sealing with latex, vinyl, bitumen, shotcrete or other suitable surface stabiliser within six months after the last construction activity on the construction site or part of the construction site where the exposed earth lies.						
S5.5.6.3 of HKBCFEIA and S4.8.1 of TKCLKLEIA	А3	3) The Contractor should undertake proper watering on all exposed spoil and associated work areas (with at least 8 times per day) throughout the construction phase.	Control construction dust	Contractor	All construction sites	Construction stage	To control the dust impact	V
S5.5.6.4 of HKBCFEIA	A4	4) Engineer to incorporate the controlled measures into the Particular Specification (PS) for the civil work. The PS should also draw the contractor's attention to relevant latest Practice notes issued by EPD.	Control construction dust	Engineer	All construction sites	Design Stage	Air pollution Control (Construction Dust) Regulation	V
S5.5.6.4 of HKBCFEIA and S4.11 of TKCLKLEIA	A5	5) Implement regular dust monitoring under EM&A programme during the construction stage.	Monitor the 24hr and 1hr TSP levels at the representative dust monitoring stations to ensure compliance with relevant criteria throughout the construction period.	other ET under the HZMB	Selected representative dust monitoring station	Construction stage	- Air Pollution Control (Construction Dust) Regulation - To control the dust impact to within the HKAQO and TM-EIA criteria(Ref. 1-hr and 24 hr TSP levels are 500µgm ⁻³ and 260µgm ⁻³ respectively)	V
S5.5.7.1 of HKBCFEIA	A6	The following mitigation measures should be adopted to prevent fugitive dust emissions for concrete batching plant: Loading, unloading, handling, transfer or storage of any dusty materials should be carried out in totally enclosed system;	Monitor the 24hr and 1hr TSP levels at the representative dust monitoring stations to ensure compliance with relevant criteria throughout the		Selected representative dust monitoring station	Construction stage	Air Pollution Control (Construction Dust) Regulation - To control the dust impact to within the HKAQO and TM-EIA criteria(Ref. 1-hr and 24	N/A

EIA Ref.	EM&A Log Ref	Environmental Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Who to implement the measures?	Location	When to implement the measures?	What requirements or standards for the measure to achieve?	
		All dust-laden air or waste gas generated by the process operations should be properly extracted and vented to fabric filtering system to meet the emission limits for TSP;	construction period.				hr TSP levels are 500µgm ⁻³ and 260µgm ⁻³ , respectively)	
		Vents for all silos and cement/ pulverised fuel ash (PFA) weighing scale should be fitted with fabric filtering system;						
		The materials which may generate airborne dusty emissions should be wetted by water spray system;						
		All receiving hoppers should be enclosed on three sides up to 3m above unloading point;						
		All conveyor transfer points should be totally enclosed;						
		All access and route roads within the premises should be paved and wetted; and						
		Vehicle cleaning facilities should be provided and used by all concrete trucks before leaving the premises to wash off any dust on the wheels and/or body.						

	EM&A Log Ref	Environmental Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Who to implement the measures?	Location	When to implement the measures?	measure to achieve?	
S5.5.2.7 of HKBCFEIA	Α7	The following mitigation measures should be adopted to prevent fugitive dust emissions at barging point: All road surface within the barging facilities will be paved; Dust enclosures will be provided for the loading ramp; Vehicles will be required to pass through designated wheels wash facilities; and Continuous water spray at the loading points.	Control construction dust	Contractor	All construction sites	Construction stage	Air Pollution Control (Construction Dust) Regulation	N/A (Construction in process)
Constructio	n Noise	(Air borne)						
S6.4.10 of HKBCFEIA	N1	Use of good site practices to limit noise emissions by considering the following: only well-maintained plant should be operated on-site and plant should be serviced regularly during the construction programme;	Control construction airborne noise by means of good site practices	Contractor	All construction sites	Construction stage	Noise Control Ordinance	V
		machines and plant (such as trucks, cranes) that may be in intermittent use should be shut down between work periods or should be throttled down to a minimum;						
		plant known to emit noise strongly in one direction, where possible, be orientated so that the noise is directed away from nearby NSRs;						
		silencers or mufflers on construction equipment should be properly fitted and maintained during the construction works;						

EIA Ref.	EM&A Log Ref	Environmental Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Who to implement the measures?	Location	When to implement the measures?	What requirements or standards for the measure to achieve?	Implementation Status
		mobile plant should be sited as far away from NSRs as possible and practicable; material stockpiles, mobile container site officer and other structures should be effectively utilised, where practicable, to screen noise from on-site construction activities.						
S6.4.11 of HKBCFEIA	N2	2) Install temporary hoarding located on the site boundaries between noisy construction activities and NSRs. The conditions of the hoardings shall be properly maintained throughout the construction period.	Reduce the construction noise levels at low-level zone of NSRs through partial screening		All construction sites	Construction stage	- Noise Control Ordinance - Annex 5, TM_EIA	V
S6.4.12 of HKBCFEIA	N3	3) Install movable noise barriers (typically density 14kg/m²), acoustic mat or full enclosure close to noisy plants including air compressor, generators, saw.	Screen the noisy plant items to be used at all construction sites		For plant items listed in Appendix 6D of the EIA report at all construction sites	Construction stage	Noise Control Ordinance Annex 5, TM_EIA 75dB(A) for residential premises The movable barrier should achieve at least 5 dB(A) and the full enclosure should be designed to achieve 10dB(A)	N/A
S6.4.13 of HKBCFEIA	N4	4) Select "Quiet plants" which comply with the BS 5228 Part 1 or TM standards.	Reduce the noise levels of plant items	Contractor	For plant items listed In Appendix 6D of the EIA report at all construction sites	Construction stage	- Noise Control Ordinance - Annex 5, TM_EIA	V

	EM&A Log Ref	Environmental Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Who to implement the measures?	Location	When to implement the measures?	What requirements or standards for the measure to achieve?	Implementation Status
S6.4.14 of HKBCFEIA	N5	5) Sequencing operation of construction plants where practicable.	Operate sequentially within the same work site to reduce the construction airborne noise	Contractor	All construction sites where practicable	Construction stage	- Noise Control Ordinance - Annex 5, TM_EIA	V
S5.1 of TMCLKLEIA	N6	6) Implement a noise monitoring under EM&A programme.	Monitor the construction noise levels at selected representative locations	Referred by the other ET under the HZMB project to the Contract.	Selected representative noise monitoring station	Construction stage	 Noise Control Ordinance Annex 5, TM_EIA 75dB(A) for residential premises 	V
Sediment		<u> </u>						
S7.3	S1	The requirements as recommended un ETWB TC 34/2002 Management of Dredged/Excavated Sediment shall be included in the Particular Specification as appropriate.	Develop sediment disposal arrangement	Engineer	All construction site areas	Design stage	- Waste Disposal Ordinance - ETWB TC 34/2002	V
	S2	Before re-deposition the contaminated sediment, a layer of geotextile shall be placed at the bottom of the sheet pile cellular structures to avoid direct contact of the contaminated sediment and the bottom sediment.	Develop sediment disposal arrangement	Engineer	All construction site areas	Design stage	- Waste Disposal Ordinance - ETWB TC 34/2002	V
	S3	A miniumum of 2m thick sand fill or public fill shall be placed on top of the contaminated sediment to protect and cover the sediment after redeposition.	Develop sediment disposal arrangement	Engineer	All construction site areas	Design stage	- Waste Disposal Ordinance - ETWB TC 34/2002	V

EIA Ref.	EM&A Log Ref	Environmental Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Who to implement the measures?	Location	When to implement the measures?	What requirements or standards for the measure to achieve?	Implementation Status
	S4	The contaminated sediment shall not be disturbed after re-deposition. No piling works or deep foundation which may disturb the contaminated sediment is allowed within the cellular structures.	Develop sediment disposal arrangement	Engineer	All construction site areas	Design stage	- Waste Disposal Ordinance - ETWB TC 34/2002	V
Waste mana	gement	(Construction Waste)		l	<u> </u>	1		
S12.6 of TMCLKLEIA	WM1		Proper implementation of WMP	Contractor	Contractor All construction sites	Construction		V
S12.6 of TMCLKLEIA	WM2	appropriate licenses for the disposal of public fill,	Proper control of wastes disposal in accordance to relevant ordinances	Contractor	All construction sites	Construction stage	Land (Miscellaneous Provisions) Ordinance (Cap28); Waste Disposal Ordinance (Cap 354); Dumping at Sea Ordinance (Cap 466); Water Pollution Control Ordinance.	V

	EM&A Log Ref	Environmental Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Who to implement the measures?	Location	When to implement the measures?	What requirements or standards for the measure to achieve?	Implementation Status
S12.6 of TMCLKLEIA	WM3	EM&A of waste handling, storage, transportation, disposal procedures and documentation through the site audit programme shall be undertaken.	Ensure proper implementation mitigation measures stated in WMP	Contractor	All construction sites		Construction stage	V
S8.3.8 of HKBCFEIA and S12.6 of TMCLKLEIA	WM4	Construction and Demolition Material The following mitigation measures should be implemented in handling the waste: Maintain temporary stockpiles and reuse excavated fill material for backfilling and reinstatement; Carry out on-site sorting; Make provisions in the Contract documents to allow and promote the use of recycled aggregates where appropriate; Adopt 'Selective Demolition' technique to demolish the existing structures and facilities with a view to recovering broken concrete effectively for recycling purpose, where possible; Implement a trip-ticket system for each works contract to ensure that the disposal of C&D materials are properly documented and verified; Implement an enhanced Waste Management Plan similar to ETWBTC (Works) No. 19/2005 – "Environmental Management on Construction Sites" to encourage on-site sorting of C&D materials and to minimize their generation during the course of construction; In addition, disposal of the C&D materials onto any sensitive locations such as agricultural lands, etc. should be avoided. The Contractor shall propose the final disposal sites to the Project Proponent and get its approval before implementation;	Good site practice to minimize and recycle the C&D material as far as practicable so as to reduce the amount for final disposal	Contractor	All construction site areas	Construction stage	- Land (Miscellaneous Provisions) Ordinance - Waste Disposal Ordinance - ETWB TC 19/2005	V

EIA Ref.	EM&A Log Ref	Environmental Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Who to implement the measures?	Location	When to implement the measures?	What requirements or standards for the measure to achieve?	
		The surplus surcharge should be transferred to a fill bank.						
S8.3.9 - S8.3.11 of HKBCFEIA and S12.6 of TMCLKLEIA	WM5	C&D Waste Standard formwork or pre-fabrication should be used as far as practicable in order to minimise the arising of C&D materials. The use of more durable formwork or plastic facing for the construction works should be considered. Use of wooden hoardings should not be used, as in other projects. Metal hoarding and falsework should be used to enhance the possibility of recycling. The purchasing of construction materials will be carefully planned in order to avoid over ordering and wastage. The Contractor should recycle as much of the C&D materials as possible on-site. Public fill and C&D waste should be segregated and stored in different containers or skips to enhance reuse or recycling of materials and their proper disposal. Where practicable, concrete and masonry can be crushed and used as fill. Steel reinforcement bar can be used by scrap steel mills. Different	Good site practice to minimize and recycle the C&D material as far as practicable so as to reduce the amount for final disposal	Contractor	All construction sites	Construction stage	- Land (Miscellaneous Provisions) Ordinance - Waste Disposal Ordinance - ETWB TC 19/2005	V

Lo	M&A .og Ref	Environmental Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Who to implement the measures?	Location	the measures?	What requirements or standards for the measure to achieve?	Implementation Status
S8.2.12 - S8.3.15 of HKBCFEIA and S12.6 of TMCLKLEIA		Chemical Waste Chemical waste that is produced, as defined by Schedule 1 of the Waste Disposal (Chemical Waste) (General) Regulation, should be handled in accordance with the Code of Practice on the Packaging, Labelling and Storage of Chemical Wastes. Containers used for the storage of chemical wastes should be suitable for the substance they are holding, resistant to corrosion, maintained in a good condition, and securely closed; have a capacity of less than 450 liters unless the specification has been approved by the EPD; and display a label in English and Chinese in accordance with instructions prescribed in Schedule 2 of the regulation. The storage area for chemical wastes should be clearly labelled and used solely for the storage of chemical waste; enclosed on at least 3 sides; have an impermeable floor and bunding of sufficient capacity to accommodate 110% of the volume of the largest container or 20 % of the total volume of waste stored in that area, whichever is the greatest; have adequate ventilation; covered to prevent rainfall entering; and arranged so that incompatible materials are adequately separated. Disposal of chemical waste should be via a licensed waste collector; be to a facility licensed to receive chemical waste, such as the Chemical Waste Treatment Centre which also offers a chemical waste collection service and can supply the necessary storage containers; or be to a reuser of the waste, under approval from the EPD.	Control the chemical waste and ensure proper storage, handling and disposal.	Contractor	All construction sites	Construction stage	- Waste Disposal(Chemical Waste) General Regulation - Code of Practice on the Packaging, Labeling and Storage of Chemical Waste	V

	EM&A Log Ref	Environmental Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Who to implement the measures?	Location	the measures?	What requirements or standards for the measure to achieve?	Implementation Status
S8.3.16 of HKBCFEIA and S12.6 of TMCLKLEIA	WM7	Sewage Adequate numbers of portable toilets should be provided for the workers. The portable toilets should be maintained in a state, which will not deter the workers from utilizing these portable toilets. Night soil should be collected by licensed collectors regularly.	Proper handling of sewage from worker to avoid odour, pest and litter impacts.	Contractor	All construction sites	Construction stage	Waste Disposal Ordinance	V
S8.3.17 of HKBCFEIA and S12.6 of TMCLKLEIA	WM8	General Refuse The site and surroundings shall be kept tidy and litter free. General refuse generated on-site should be stored in enclosed bins or compaction units separately from construction and chemical wastes. A reputable waste collector should be employed by the Contractor to remove general refuse from the site, separately from construction and chemical wastes, on a daily basis to minimize odour, pest and litter impacts. Burning of refuse on construction sites is prohibited by law. Aluminium cans are often recovered from the waste stream by individual collectors if they are segregated and made easily accessible. Separate labelled bins for their deposit should be provided if feasible. Office wastes can be reduced through the recycling of paper if volumes are large enough to warrant collection. Participation in a local collection scheme should be considered by the Contractor. In addition, waste separation facilities for paper, aluminum cans, plastic bottles etc., should be provided. Training should be provided to workers about the concepts of site cleanliness and appropriate waste management procedure, including reduction, reuse and recycling of wastes. Sufficient dustbins shall be provided for storage	Minimize production of the general refuse and avoid odour, pest and litter impacts.		All construction sites	Construction stage	Waste Disposal Ordinance	V

EIA Ref.	EM&A Log Ref	Environmental Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Who to implement the measures?	Location	When to implement the measures?	What requirements or standards for the measure to achieve?	Implementation Status
		of waste as required under the Public Cleansing and Prevention of Nuisances By-laws. In addition, general refuse shall be cleared daily and shall be disposed of to the nearest licensed landfill or refuse transfer station.						
		All waste containers shall be in a secure area on hardstanding.						
Water Quali	ity (Cons	truction Phase)			l	I		
	W1	Mitigation during the marine works to reduce	To control construction water quality	Contractor	During dredging and filling	Construction stage	TM-EIAO	V
		more than 15% public fill shall be used for reclamation filling below +2.5mPD during construction of the seawall; After the seawall is completed except for the 300m marine access as indicated in the EPs, not more than 30% public fill shall be used for						

EIA Ref.	EM&A Log Ref	Environmental Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Who to implement the measures?	Location	When to implement the measures?	What requirements or standards for the measure to achieve?	Implementation Status
		reclamation filling below +2.5mPD, unless otherwise agreement from EPD was obtained; No more than 2 grab dredgers with a maximum daily dredging rate of 12,000m3 shall be employed for dredging operation at Portion D of the Project; Upon completion of 200m leading seawall, no more than a total of 60 filling barge trips per day shall be made with a cumulative maximum daily filling rate of 60,000 m3 for HKBCF and TMCLKL southern landfall reclamation during the filling operation; and Upon completion of the whole section of seawall except for the 300m marine access as indicated in the EPs, no more than a total of 190 filling barge trips per day shall be made with a cumulative maximum daily filling rate of 190,000 m3 for the remaining filling operations for HKBCF and TMCLKL southern landfall reclamation. Closed grabs should be used for sediment dredging to reduce sediment loss when lifting the grabs to the barges. Only grab dredgers shall be used for dredging works of the Project; All mechanical grabs shall be designed and maintained to avoid spillage; The moving speed of construction vessels in the dredging area should be reduced to prevent disturbance to the seabed generating sediment plumes; Floating type silt curtains shall be installed enclosing the entire reclamation site at all time. Staggered layers of silt curtain shall be provided to prevent sediment loss at payingtion accesses.	auuress					
		spillage; The moving speed of construction vessels in the dredging area should be reduced to prevent disturbance to the seabed generating sediment plumes; Floating type silt curtains shall be installed enclosing the entire reclamation site at all time.						

EIA Ref.	EM&A Log Ref	Environmental Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Who to implement the measures?	Location	When to implement the measures?	What requirements or standards for the measure to achieve?	Implementation Status
		200m;						
		The cage-type silt-curtain with steel enclosure is proposed to be installed to enclose local pollution caused by the grab dredging.						
		The grab dredging work should be carried out within the cage-type siltcurtain;						
		Single layer silt curtain to be applied around the North-east airport water intake;						
		The silt-curtains should be maintained in good condition to ensure the sediment plume generated from dredging and filling be confined effectively within the site boundary;						
		The dredging and filling works shall be scheduled to spread the works evenly over a working day;						
		Cellular structure shall be used for seawall construction;						
		A layer of geotextile shall be placed on top of the seabed before any filling activities take place inside the cellular structures to form the seawall;						
		The conveyor belts shall be fitted with windboards and conveyor release points shall be covered with curtain to prevent any spillage of filling materials onto the surrounding waters;						
		An additional layer of silt curtain shall be installed near the active stone column installation points. A layer of geotextile with stone blanket on top shall be placed on the seabed prior to stone column installation works. Stone blanket -> with silt curtain.						

EIA Ref.	EM&A Log Ref	Environmental Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Who to implement the measures?	Location	•	What requirements or standards for the measure to achieve?	Implementation Status
		In addition, dredging operations should be undertaken in such a manner as to minimise resuspension of sediments. Standard good dredging practice measures should, therefore, be implemented including the following requirements which should be written into the dredging and filling contract.						
		trailer suction hopper dredgers shall not allow mud to overflow; use of Lean Material Overboard (LMOB) systems shall be prohibited; mechanical grabs shall be designed and maintained to avoid spillage and should seal tightly while being lifted;						
		4. barges and hopper dredgers shall have tight fitting seals to their bottom openings to prevent leakage of material; 5. any pipe leakages shall be repaired quickly. Plant should not be operated with leaking pipes; 6. loading of barges and hoppers shall be controlled to prevent splashing of dredged material to the surrounding water. Barges						
		or hoppers shall not be filled to a level which will cause overflow of materials or pollution of water during loading or transportation; 7. excess material shall be cleaned from the decks and exposed fittings of barges and hopper dredgers before the vessel is						
		moved; 8. adequate freeboard shall be maintained on barges to reduce the likelihood of decks being washed by wave action; 9. all vessels shall be sized such that adequate						

EIA Ref.	EM&A Log Ref	Environmental Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Who to implement the measures?	Location	When to implement the measures?	What requirements or standards for the measure to achieve?	Implementation Status
		clearance is maintained between vessels and the sea bed at all states of the tide to ensure that undue turbidity is not generated by turbulence from vessel movement or propeller wash; and 10. the works shall not cause foam, oil, grease, litter or other objectionable matter to be present in the water within and adjacent to the works site.						
	W2		Re-deposition of Contaminated Sediment	Contractor	Dredged Contaminated Sediment	Construction stage	Waste Disposal Ordinance ETWB TC34/2002	V
S9.11.1.3 of HKBCFEIA and S6.10 of	W3	Land Works General construction activities on land should also be governed by standard good working practice. Specific measures to be written into the	To control construction water quality	Contractor	Land-based works areas	Construction stage	TM-EIAO	V

EIA Ref.	EM&A Log Ref	Environmental Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Who to implement the measures?	Location	When to implement the measures?	What requirements or standards for the measure to achieve?	Implementation Status
TMCLKLEIA		works contracts should include: wastewater from temporary site facilities should be controlled to prevent direct discharge to surface or marine waters; Sewage effluent and discharges from on –site kitchen facilities shall be directed to Government sewer in accordance with the requirements of the WPCO or collected for disposal offsite. The use of soakaways shall be avoided; Storm drainage shall be directed to storm drains via adequately designed sand/silt removal facilities such as sand traps, silt traps and sediment basins. Channels, earth bunds or sand bag barriers should be provided on site to properly direct stormwater to such silt removal facilities. Catchpits and perimeter channels should be constructed in advance of site formation works and earthworks; silt removal facilities, channels and manholes shall be maintained and any deposited silt and grit shall be removed regularly, including specifically at the onset of and after each rainstorm; temporary access roads should be surfaced with crushed stone or gravel; rainwater pumped out from trenches or foundation excavations should be discharged into storm drains via silt removal facilities; measures should be taken to prevent the washout of construction materials, soil, silt or	address					
		debris into any drainage system; open stockpiles of construction materials (e.g. aggregates and sand) on site should be covered with tarpaulin or similar fabric during rainstorms;						

EIA Ref.	EM&A Log Ref	Environmental Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Who to implement the measures?	Location	When to implement the measures?	What requirements or standards for the measure to achieve?	Implementation Status
		manholes (including any newly constructed ones) should always be adequately covered and temporarily sealed so as to prevent silt, construction materials or debris from getting into the drainage system, and to prevent storm run-off from getting into foul sewers;						
		discharges of surface run-off into foul sewers must always be prevented in order not to unduly overload the foul sewerage system;						
		All vehicles and plant should be cleaned before they leave the construction site to ensure that no earth, mud or debris is deposited by them on roads. A wheel washing bay should be provided at every site exit;						
		wheel wash overflow shall be directed to silt removal facilities before being discharged to the storm drain;						
		the section of construction road between the wheel washing bay and the public road should be surfaced with crushed stone or coarse gravel;						
		wastewater generated from concreting, plastering, internal decoration, cleaning work and other similar activities, shall be screened to remove large objects;						
		Vehicle and plant servicing areas, vehicle wash bays and lubrication facilities shall be located under roofed areas. The drainage in these covered areas shall be connected to foul sewers via a petrol interceptor in accordance with the requirements of the WPCO or collected for offsite disposal;						
		the contractors shall prepare an oil / chemical cleanup plan and ensure that leakages or spillages are contained and cleaned up immediately;						
		waste oil should be collected and stored for						

EIA Ref.	EM&A Log Ref	Environmental Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Who to implement the measures?	Location	When to implement the measures?	What requirements or standards for the measure to achieve?	Implementation Status
		recycling or disposal, in accordance with the Waste Disposal Ordinance; All fuel tanks and chemical storage areas should be provided with locks and be sited on sealed areas. The storage areas should be surrounded by bunds with a capacity equal to 110% of the storage capacity of the largest tank; and						
		Surface run-off from bunded areas should pass through oil/grease traps prior to discharge to the storm water system.						
S9.14 of HKBCFEIA and S6.10 of TMCLKLEIA	W4	Implement a water quality monitoring programme	Control water quality	Contractor	At identified monitoring location	During construction period	TM-water Water Pollution Control Ordinance	V
S6.10 of TMCLKLEIA	W5	All construction works shall be subject to routine audit to ensure implementation of all EIA recommendations and good working practice.	To control construction water quality	Contractor	All construction site areas	During construction period		V
Ecology (co	nstructio	on Phase)						
S10.7 of HKBCFEIA and S8.14 of TMCLKLE IA		 Install silt curtain during the construction. Limit dredging and works fronts. Construct seawall prior to reclamation filling where practicable. Good site practices Strict enforcement of no marine dumping. Site runoff control Spill response plan 	Minimise marine water quality impacts		Seawall, reclamation area	During construction	TM-Water	V
S10.7 of HKBCFEIA	E2	Watering to reduce dust generation; prevention of siltation of freshwater habitats; Site runoff should be desilted, to reduce the potential for suspended sediments, organics and other contaminants to enter streams and standing freshwater.	Prevent Sedimentation from Land-based works areas	Contractor	Land-based works areas	During construction	TM-Water	V
S10.7 of HKBCFEIA	E3	Good site practices, including strictly following the permitted works hours, using quieter	Prevent disturbance to terrestrial fauna and	Contractor	Land-based works	During construction		V

EIA Ref.	EM&A Log Ref	Environmental Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Who to implement the measures?	Location	When to implement the measures?	What requirements or standards for the measure to achieve?	Implementation Status
and S8.14 of TMCLKLEIA		machines where practicable, and avoiding excessive lightings during night time.	habitats		areas			
S10.7 of HKBCFEIA and S8.14 of TMCLKLEIA	E4	Dolphin Exclusion Zone Dolphin watching plan	Minimize temporary marine habitat loss impact to dolphins	Contractor	Marine works	During marine works	TM-EIAO	V
S10.7 of HKBCFEIA and S8.14 of TMCLKLEIA	E5	 Decouple compressors and other equipment on working vessels Proposal on design and implementation of acoustic decoupling measures applied during dredging and reclamation works Avoidance of percussive piling 	Minimise marine noise impacts on dolphins	Contractor	Marine works	During marine works	TM-EIAO Marine Park Regulations	
S10.7 of HKBCFEIA and S8.14 of TMCLKLEIA	E6	 Control vessel speed Skipper training Predefined and regular routes for working vessels; avoid Brothers Islands 	Minimise marine traffic disturbance on dolphins	Contractor	Marine traffic	During marine works		V
S10.10 of HKBCFEIA and S8.14 of TMCLKLEIA Fisheries	E7	Vessel based dolphin monitoring	Minimise marine traffic disturbance on dolphins	Contractor	Northeast and Northwest Lantau	During marine works		V
S11.7 of HKBCFEIA	F1		Minimise marine water quality impacts	Contractor	Seawall, reclamation area	During construction	TM-Water	V

	EM&A Log Ref	Environmental Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Who to implement the measures?	Location	When to implement the measures?	What requirements or standards for the measure to achieve?	Implementation Status
S11.7 of HKBCFEIA	F2	collecting surface runoff	Minimise impacts on marine water quality impacts	Designer	Reclamation area	During Construction	TM-Water	V
Landscape	& Visual	(Detailed Design Phase)						
S14.3.3.1 of HKBCFEIA	LV1	 General design measures include: Roadside planting and planting along the edge of the reclamation is proposed; Transplanting of mature trees in good health and amenity value where appropriate and reinstatement of areas disturbed during construction by compensatory hydro-seeding and planting; Protection measures for the trees to be retained during construction activities; Maximizing new tree, shrub and other vegetation planting to compensate tree felled and vegetation removed; Providing planting area around peripheral of HKBCF for tree planting screening effect; and Providing salt-tolerant native trees along the planter strip at affected seawall and newly reclaimed coastline. 	Minimise visual & landscape impacts	Contractor	HKBCF	Design Stage		V
		(Construction Phase)	T	T -	T	T =	T	
S14.3.3.3 of HKBCFEIA and S10.9 of	LV2	Mitigate Landscape Impacts G1. Grass-hydroseed or sheeting bare soil surface and stock pile areas.	Minimise visual & landscape impacts	Contractor	All construction site areas	Construction stage		V

EIA Ref.	Log Ref	Environmental Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Who to implement the measures?	Location	When to implement the measures?	What requirements or standards for the measure to achieve?	Implementation Status
TMCLKLEIA								
S10.9 of TMCLKLEIA	LV3	LV3 Mitigate Landscape Impacts CM1. Existing trees on boundary of the Project Area shall be carefully protected during construction. Detailed Tree Protection Specification shall be provided in the Contract Specification. Under this specification, the Contractor shall be required to submit, for approval, a detailed working method statement for the protection of trees prior to undertaking any works adjacent to all retained trees, including trees in contractor's works areas. (Tree protection measures will be detailed at Tree Removal Application stage). CM2. Trees unavoidably affected by the works shall be transplanted where practical. Trees will be transplanted straight to their final receptor site and not held in a temporary nursery. A detailed Tree Transplanting Specification shall be provided in the Contract Specification. Sufficient time for necessary tree root and crown preparation periods shall be allowed in the project programme. CM7. Ensure no run-off into water body adjacent to the Project Area. CM9. Recycle/Reuse all felled trees and vegetation, e.g. mulching.	Minimise landscape impact	Contractor	All construction site areas	Construction stage		V
S14.3.3.3 of HKBCFEIA	LV4	Mitigate Visual Impacts V1. Minimize time for construction activities during construction period. V2. Provide screen hoarding at the portion of the project site/ works areas storage areas near VSRs who have close low- level views to the Project during HKBCF construction.	Minimise visual & landscape impacts	Contractor	All construction site areas	Construction stage		V

EIA Ref.	EM&A Log Ref	Environmental Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Who to implement the measures?	Location	When to implement the measures?	What requirements or standards for the measure to achieve?	Implementation Status
S10.9 of TMCLKLEIA	LV5	Mitigate Visual Impacts CM5. Screening of construction works by hoardings around works area in visually unobtrusive colours, to screen works. CM6. Control night-time lighting and glare by hooding all lights. CM8. Avoidance of excessive height and bulk of buildings and structures.	Minimise visual impact	Contractor	All construction site areas	Construction stage		V
EM&A								
S15.2.2 of HKBCFEIA	EM1	An Independent Environmental Checker needs to be employed as per the EM&A Manual.	Control EM&A Performance	Project Proponent	All construction site areas	Construction stage	-EIAO Guidance Note No. 4/2002 -TM_EIAO	V
S15.5 - S15.6 of HKBCFEIA	EM2	An Environmental Team needs to be employed as per the EM&A Manual. Prepare a systematic Environmental Management Plan to ensure effective implementation of the mitigation measures. An environmental impact monitoring needs to be implementing by the Environmental Team to ensure all the requirements given in the EM&A Manual are fully complied with.	Perform environmental monitoring & auditing	Contractor	All construction site areas	Construction stage	-EIAO Guidance Note No. 4/2002 -TM_EIAO	V

Legend: V = implemented; x = not implemented; N/A = not applicable



Appendix H

Statistics on Environmental Complaints, Notification of Summons and Successful Prosecutions



Statistics on Environmental Complaints, Notification of Summons and Successful Prosecutions

	Cumulative Statistics					
Reporting Period	Complaints	Notifications of summons	Successful prosecutions			
This reporting period	0	0	0			
From commencement date of construction to end of reporting month	4	0	0			



Appendix I

Environmental Site Inspection Schedule



Contract No.: HY/2013/02 Hong Kong – Zhuhai – Macao Bridge Hong Kong Boundary Crossing Facilities – Infrastructure Works Stage I (Western Portion)

Schedule for Weekly Environmental Site Inspection

April 2016

Sun	Mon	Tue	Wed	Thu	Fri	Sat
					1	2
3	4	5	6	7 Environmental Site Inspection	8	9
10	11	12	13	14	15 Environmental Site Inspection	16
17	18	19	20	21 Environmental Site Inspection	22	23
24	25	26	27	28 Environmental Site Inspection	29	30



Contract No.: HY/2013/02 Hong Kong – Zhuhai – Macao Bridge Hong Kong Boundary Crossing Facilities – Infrastructure Works Stage I (Western Portion)

Schedule for Weekly Environmental Site Inspection

May 2016

Sun	Mon	Tue	Wed	Thu	Fri	Sat 7
1	2	3	4	5 Environmental Site Inspection	6	7
8	9	10	11	12 Environmental Site Inspection	13	14
15	16	17	18	19	20 Environmental Site Inspection	21
22	23	24	25	26 Environmental Site Inspection	27	28
29	30	31				
