



Project	Contract	Station	Date	Parameter	Start Time	Result	Unit
HKBCF	HY/2013/04	AMS2 Tung Chung Development Pier	05-Mar-19	1-hr TSP	13:00	49	µg/m ³
HKBCF	HY/2013/04	AMS2 Tung Chung Development Pier	05-Mar-19	1-hr TSP	14:00	48	µg/m ³
HKBCF	HY/2013/04	AMS2 Tung Chung Development Pier	05-Mar-19	1-hr TSP	15:00	49	µg/m ³
HKBCF	HY/2013/04	AMS2 Tung Chung Development Pier	11-Mar-19	1-hr TSP	09:52	41	µg/m ³
HKBCF	HY/2013/04	AMS2 Tung Chung Development Pier	11-Mar-19	1-hr TSP	10:52	37	µg/m ³
HKBCF	HY/2013/04	AMS2 Tung Chung Development Pier	11-Mar-19	1-hr TSP	11:52	38	µg/m ³
HKBCF	HY/2013/04	AMS2 Tung Chung Development Pier	16-Mar-19	1-hr TSP	12:14	20	µg/m ³
HKBCF	HY/2013/04	AMS2 Tung Chung Development Pier	16-Mar-19	1-hr TSP	13:14	24	µg/m ³
HKBCF	HY/2013/04	AMS2 Tung Chung Development Pier	16-Mar-19	1-hr TSP	14:14	27	µg/m ³
HKBCF	HY/2013/04	AMS2 Tung Chung Development Pier	21-Mar-19	1-hr TSP	13:58	46	µg/m ³
HKBCF	HY/2013/04	AMS2 Tung Chung Development Pier	21-Mar-19	1-hr TSP	14:58	45	µg/m ³
HKBCF	HY/2013/04	AMS2 Tung Chung Development Pier	21-Mar-19	1-hr TSP	15:58	46	µg/m ³
HKBCF	HY/2013/04	AMS2 Tung Chung Development Pier	27-Mar-19	1-hr TSP	14:56	31	µg/m ³
HKBCF	HY/2013/04	AMS2 Tung Chung Development Pier	27-Mar-19	1-hr TSP	15:56	32	µg/m ³
HKBCF	HY/2013/04	AMS2 Tung Chung Development Pier	27-Mar-19	1-hr TSP	16:56	34	µg/m ³
HKBCF	HY/2013/04	AMS3C Ying Tung Estate Market Rooftop	05-Mar-19	1-hr TSP	08:22	29	µg/m ³
HKBCF	HY/2013/04	AMS3C Ying Tung Estate Market Rooftop	05-Mar-19	1-hr TSP	09:22	47	µg/m ³
HKBCF	HY/2013/04	AMS3C Ying Tung Estate Market Rooftop	05-Mar-19	1-hr TSP	10:22	48	µg/m ³
HKBCF	HY/2013/04	AMS3C Ying Tung Estate Market Rooftop	11-Mar-19	1-hr TSP	13:42	55	µg/m ³
HKBCF	HY/2013/04	AMS3C Ying Tung Estate Market Rooftop	11-Mar-19	1-hr TSP	14:42	65	µg/m ³
HKBCF	HY/2013/04	AMS3C Ying Tung Estate Market Rooftop	11-Mar-19	1-hr TSP	15:42	100	µg/m ³
HKBCF	HY/2013/04	AMS3C Ying Tung Estate Market Rooftop	16-Mar-19	1-hr TSP	08:11	30	µg/m ³
HKBCF	HY/2013/04	AMS3C Ying Tung Estate Market Rooftop	16-Mar-19	1-hr TSP	09:11	25	µg/m ³
HKBCF	HY/2013/04	AMS3C Ying Tung Estate Market Rooftop	16-Mar-19	1-hr TSP	10:11	21	µg/m ³
HKBCF	HY/2013/04	AMS3C Ying Tung Estate Market Rooftop	21-Mar-19	1-hr TSP	08:10	22	µg/m ³
HKBCF	HY/2013/04	AMS3C Ying Tung Estate Market Rooftop	21-Mar-19	1-hr TSP	09:10	47	µg/m ³
HKBCF	HY/2013/04	AMS3C Ying Tung Estate Market Rooftop	21-Mar-19	1-hr TSP	10:10	48	µg/m ³
HKBCF	HY/2013/04	AMS3C Ying Tung Estate Market Rooftop	27-Mar-19	1-hr TSP	08:34	39	µg/m ³
HKBCF	HY/2013/04	AMS3C Ying Tung Estate Market Rooftop	27-Mar-19	1-hr TSP	09:34	38	µg/m ³
HKBCF	HY/2013/04	AMS3C Ying Tung Estate Market Rooftop	27-Mar-19	1-hr TSP	10:34	38	µg/m ³
HKBCF	HY/2013/04	AMS7B 3RS Site Office	05-Mar-19	1-hr TSP	13:56	48	µg/m ³
HKBCF	HY/2013/04	AMS7B 3RS Site Office	05-Mar-19	1-hr TSP	14:56	48	µg/m ³
HKBCF	HY/2013/04	AMS7B 3RS Site Office	05-Mar-19	1-hr TSP	15:56	49	µg/m ³
HKBCF	HY/2013/04	AMS7B 3RS Site Office	11-Mar-19	1-hr TSP	08:46	55	µg/m ³
HKBCF	HY/2013/04	AMS7B 3RS Site Office	11-Mar-19	1-hr TSP	09:46	53	µg/m ³
HKBCF	HY/2013/04	AMS7B 3RS Site Office	11-Mar-19	1-hr TSP	10:46	48	µg/m ³
HKBCF	HY/2013/04	AMS7B 3RS Site Office	16-Mar-19	1-hr TSP	13:16	21	µg/m ³
HKBCF	HY/2013/04	AMS7B 3RS Site Office	16-Mar-19	1-hr TSP	14:16	20	µg/m ³
HKBCF	HY/2013/04	AMS7B 3RS Site Office	16-Mar-19	1-hr TSP	15:16	20	µg/m ³
HKBCF	HY/2013/04	AMS7B 3RS Site Office	21-Mar-19	1-hr TSP	12:49	47	µg/m ³
HKBCF	HY/2013/04	AMS7B 3RS Site Office	21-Mar-19	1-hr TSP	13:49	45	µg/m ³
HKBCF	HY/2013/04	AMS7B 3RS Site Office	21-Mar-19	1-hr TSP	14:49	47	µg/m ³
HKBCF	HY/2013/04	AMS7B 3RS Site Office	27-Mar-19	1-hr TSP	13:59	43	µg/m ³
HKBCF	HY/2013/04	AMS7B 3RS Site Office	27-Mar-19	1-hr TSP	14:59	31	µg/m ³
HKBCF	HY/2013/04	AMS7B 3RS Site Office	27-Mar-19	1-hr TSP	15:59	36	µg/m ³
HKBCF	HY/2013/04	AMS2 Tung Chung Development Pier	05-Mar-19	24-hr TSP	13:10	49	µg/m ³
HKBCF	HY/2013/04	AMS2 Tung Chung Development Pier	11-Mar-19	24-hr TSP	12:59	76	µg/m ³
HKBCF	HY/2013/04	AMS2 Tung Chung Development Pier	16-Mar-19	24-hr TSP	12:22	88	µg/m ³
HKBCF	HY/2013/04	AMS2 Tung Chung Development Pier	21-Mar-19	24-hr TSP	14:12	35	µg/m ³
HKBCF	HY/2013/04	AMS2 Tung Chung Development Pier	27-Mar-19	24-hr TSP	14:56	39	µg/m ³
HKBCF	HY/2013/04	AMS3C Ying Tung Estate Market Rooftop	05-Mar-19	24-hr TSP	08:30	45	µg/m ³
HKBCF	HY/2013/04	AMS3C Ying Tung Estate Market Rooftop	11-Mar-19	24-hr TSP	13:42	60	µg/m ³
HKBCF	HY/2013/04	AMS3C Ying Tung Estate Market Rooftop	16-Mar-19	24-hr TSP	08:20	78	µg/m ³
HKBCF	HY/2013/04	AMS3C Ying Tung Estate Market Rooftop	21-Mar-19	24-hr TSP	08:16	36	µg/m ³
HKBCF	HY/2013/04	AMS3C Ying Tung Estate Market Rooftop	27-Mar-19	24-hr TSP	08:39	59	µg/m ³
HKBCF	HY/2013/04	AMS7B 3RS Site Office	05-Mar-19	24-hr TSP	14:07	73	µg/m ³
HKBCF	HY/2013/04	AMS7B 3RS Site Office	11-Mar-19	24-hr TSP	08:46	72	µg/m ³
HKBCF	HY/2013/04	AMS7B 3RS Site Office	16-Mar-19	24-hr TSP	13:22	97	µg/m ³
HKBCF	HY/2013/04	AMS7B 3RS Site Office	21-Mar-19	24-hr TSP	12:57	49	µg/m ³
HKBCF	HY/2013/04	AMS7B 3RS Site Office	27-Mar-19	24-hr TSP	14:09	62	µg/m ³


Air Quality Monitoring (1-hr TSP) at AMS2

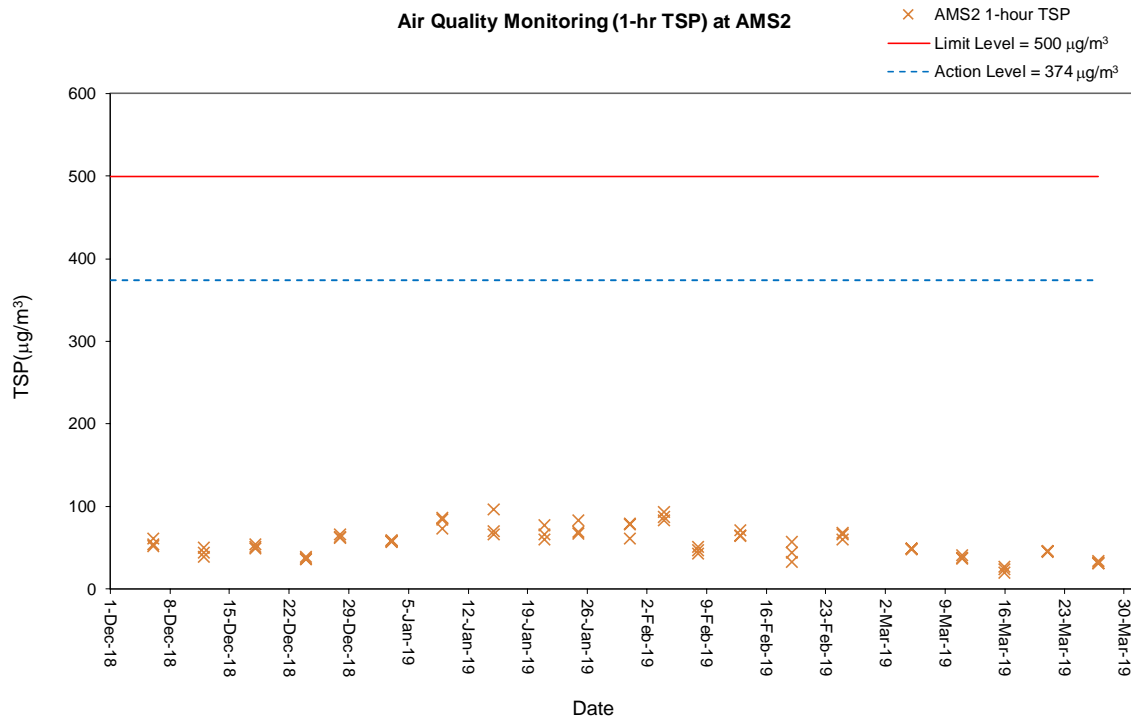


Air Quality Monitoring (1-hr TSP) at AMS3C

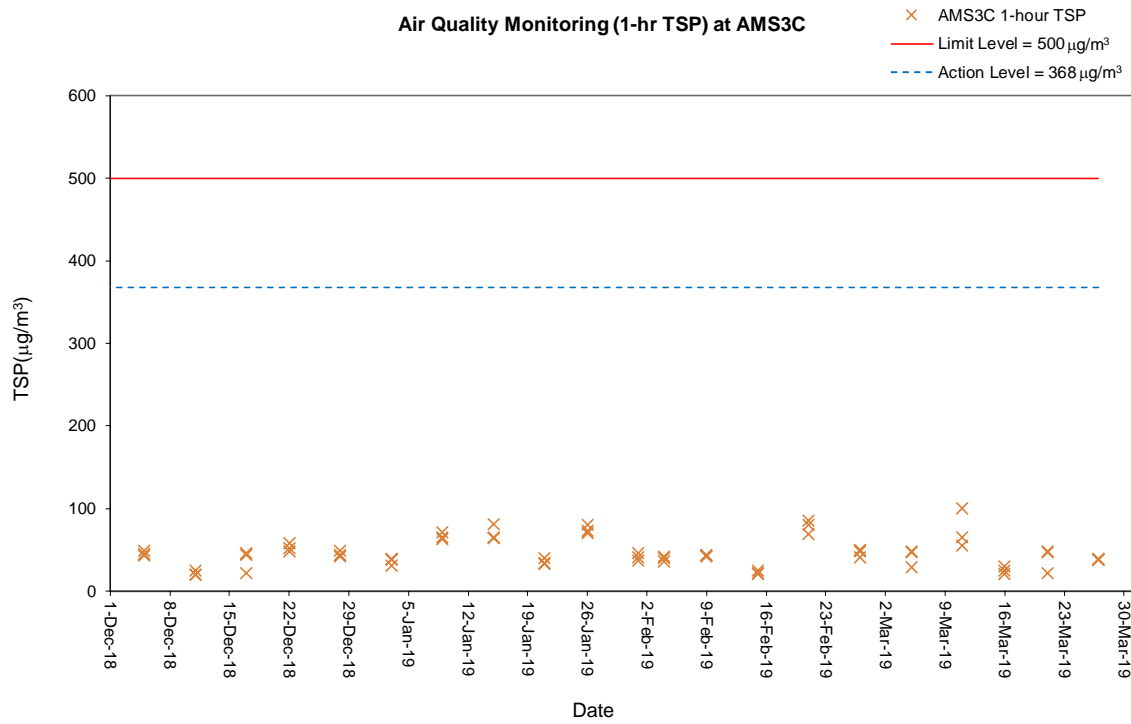


Air Quality Monitoring (1-hr TSP) at AMS7B

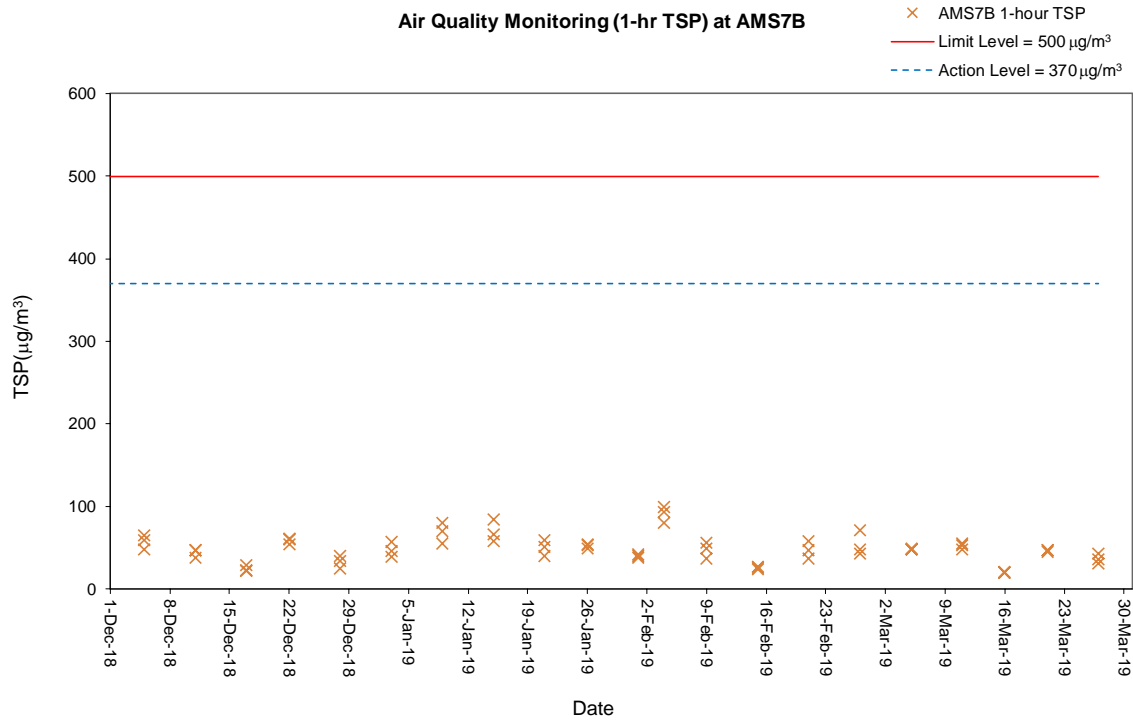


Air Quality Monitoring (24-hr TSP) at AMS2

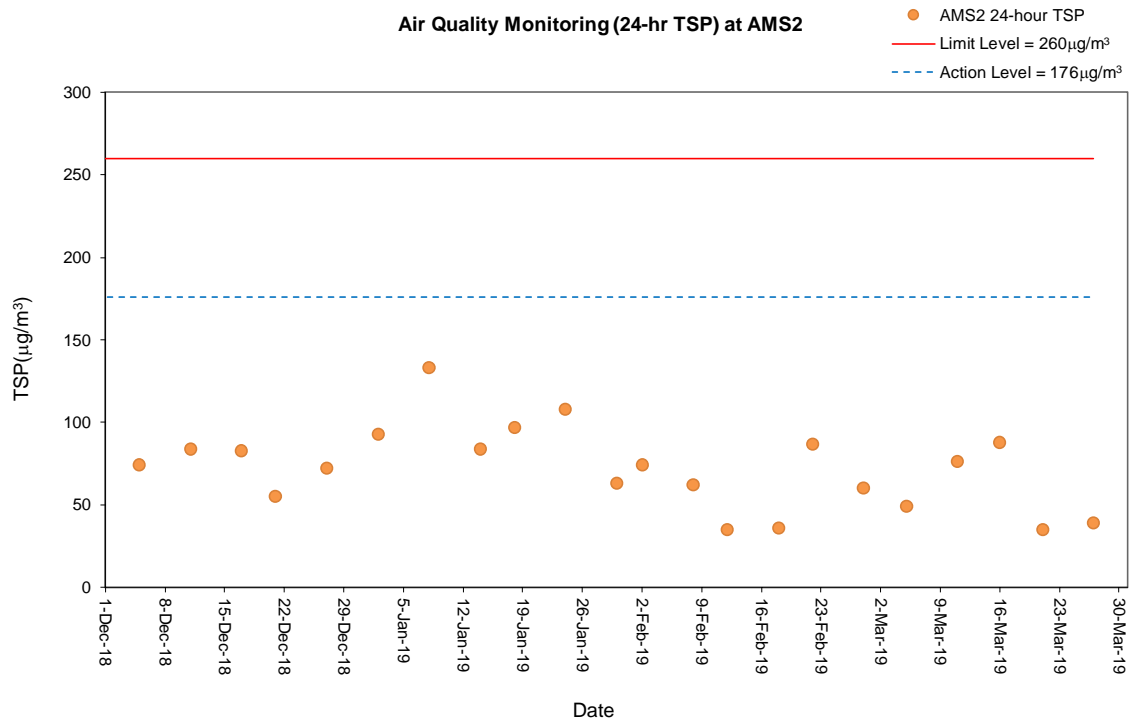

Air Quality Monitoring (24-hr TSP) at AMS3C


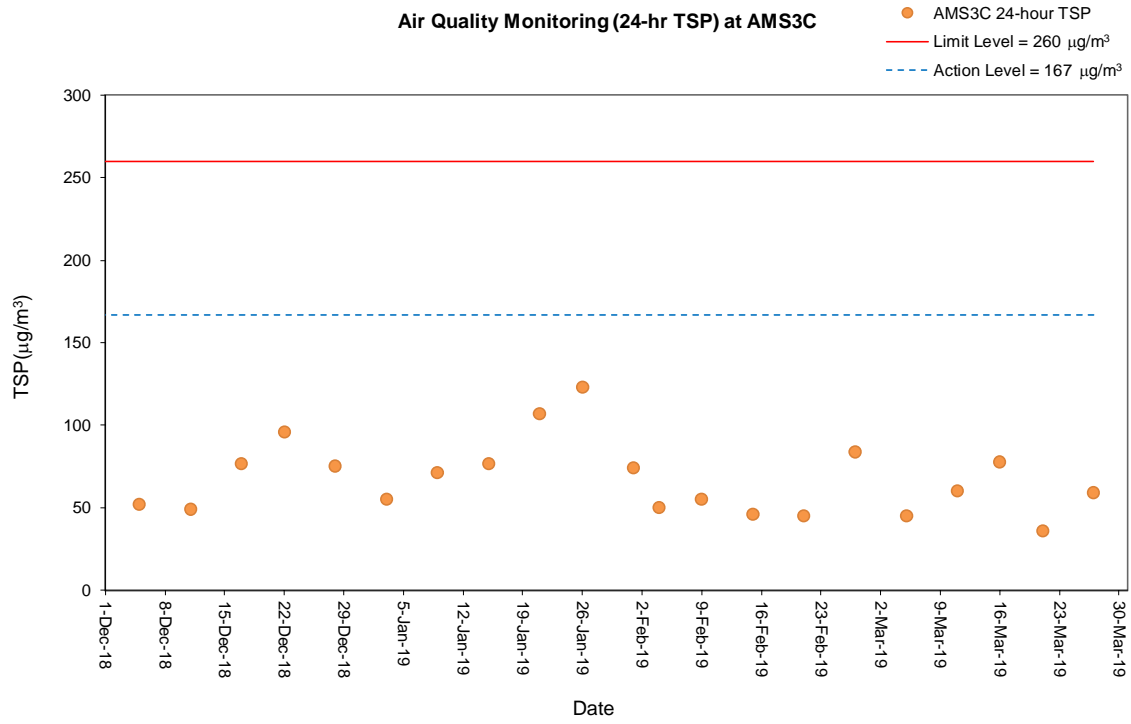


Air Quality Monitoring (24-hr TSP) at AMS7B

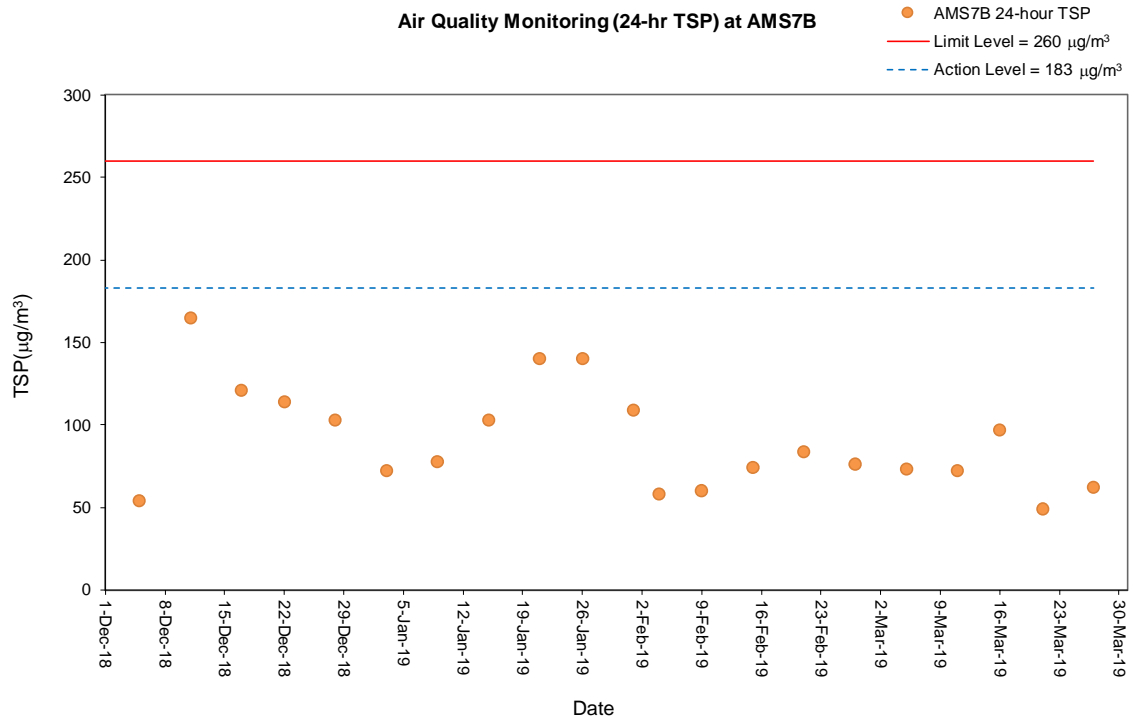

Project	Contract	Date	Station	Start Time	Noise Level for 30 min, dB(A)			Weather	Wind Speed, m/s	Facade / Free Field	Limit Level, dB(A)
					L _{eq}	L ₁₀	L ₉₀				
HKBCF	HY/2013/04	05-Mar-19	NMS2 Seaview Crescent	16:43	62	64	60	Cloudy	<5	Facade	75
HKBCF	HY/2013/04	11-Mar-19	NMS2 Seaview Crescent	10:36	66	69	62	Sunny	<5	Facade	75
HKBCF	HY/2013/04	21-Mar-19	NMS2 Seaview Crescent	14:39	64	66	61	Sunny	<5	Facade	75
HKBCF	HY/2013/04	27-Mar-19	NMS2 Seaview Crescent	11:24	65	68	60	Cloudy	<5	Facade	75
HKBCF	HY/2013/04	05-Mar-19	NMS3C Ying Tung Estate Refuse Collection Point	08:44	68	70	66	Cloudy	<5	Free Field *	70
HKBCF	HY/2013/04	11-Mar-19	NMS3C Ying Tung Estate Refuse Collection Point	15:47	67	70	62	Sunny	<5	Free Field *	70
HKBCF	HY/2013/04	21-Mar-19	NMS3C Ying Tung Estate Refuse Collection Point	10:25	63	64	60	Sunny	<5	Free Field *	70
HKBCF	HY/2013/04	27-Mar-19	NMS3C Ying Tung Estate Refuse Collection Point	08:50	65	68	62	Cloudy	<5	Free Field *	70

Remark: * Free field measurement; noise level shown includes +3dB(A) correction factor

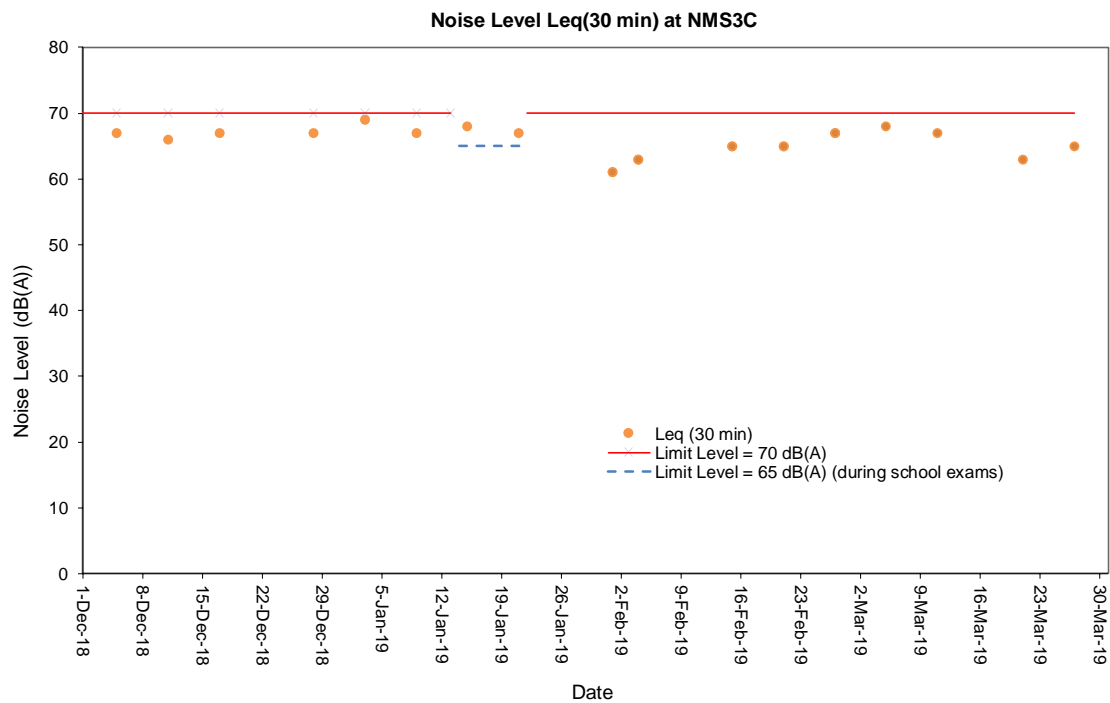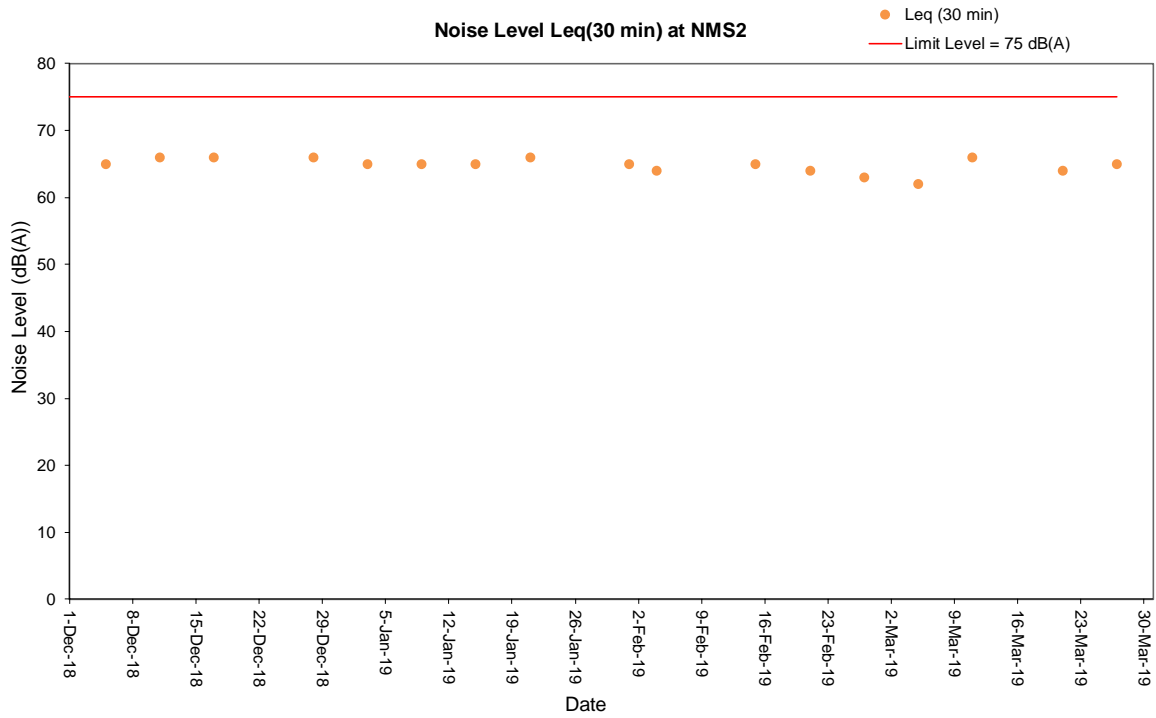

Remark: The measured noise levels recorded at NMS3C on 15 January 2019 and 21 January 2019 were 68.4 dB(A) and 66.7 dB(A) respectively, which exceeded the noise level of 65dB(A) during examination period and were higher than the baseline level of 66.3 dB(A). Therefore, baseline correction was carried out and the corrected noise levels which solely represent the noise level of construction works were 64.2 dB(A) and 56.1 dB(A) respectively, therefore there was no exceedance after correction. As such the Event and Action Plan was not triggered.
