

**Contract No. HY/2011/03 -
 Hong Kong- Zhuhai- Macao Bridge
 Hong Kong Link Road Section between Scenic Hill and Hong Kong Boundary Crossing Facilities
 Notifications of Environmental Quality Limits Exceedances** Notification No.: 181

Date of Notification: 6 June 2014

Works Inspected: Data collected from water sampling works on 14 May 2014 and the test report was issued on 22 May 2014.

Monitoring Location: Water Quality Monitoring Stations

Parameter: Dissolved Oxygen (DO)/ Suspended Solids (SS)/ Turbidity (TURB)

Action & Limit Level (AL & LL) / Measured Level:

PARAM	STATION	DEPTH	AL (mg/L)	LL (mg/L)	MEASURED AT MID-EBB TIDE (mg/L)	MEASURED AT MID-FLOOD TIDE (mg/L)
SS	SR4	DA	23.5 and 120% of upstream control station's suspended solid at the same tide of the same day (i.e. CS2: 4.48 x 120% = 5.4 mg/L for mid ebb) AND CS(Mf)5: 5.28 x 120% = 6.3 mg/L for mid flood)	34.4 and 130% of upstream control station's suspended solid at the same tide of the same day (i.e. CS2: 4.48 x 130% = 5.8 mg/L for mid ebb) AND CS(Mf)5: 5.28 x 130% = 6.9 mg/L for mid flood)	5.5	<u>36.7</u>

Notes:
 DA means depth average.
Bold Italic means AL exceedances.
Bold Italic with underline means LL exceedances.

Possible reason for Action or Limit Level Non-compliance:

On 14 May 2014, a LL exceedance was recorded at station SR4 during mid-flood tide.

The exceedance has been investigated and is considered unlikely to be related to contract works due to the following reasons:

- Formation of seawall, rock fill and stone column work at Zone 1, formation of seawall at Zone 2, formation of seawall at Zone 3A were carried out within silt curtain as recommended in the EIA Report.
- The ranges of suspended solid at station SR4 during the baseline monitoring are shown as below:

Station	Range of Suspended Solid (mg/L) Mid- Ebb Tide	Range of Suspended Solid (mg/L) Mid- Flood Tide
SR4	5.3 to 20	5.6 to 24.5

The measured value at station SR4 was above the range of suspended solid during baseline monitoring for mid-flood tide. However, there were no specific activities recorded during the monitoring period that would cause any significant impacts on the monitoring results.


- No leakage of turbid water or any abnormality or malpractice was observed during the sampling exercise.

As such, the suspended solid level is considered to be attributed to other external factors, rather than the contract works.

Actions taken/ to be taken:

As the suspended solid level recorded beyond the water quality criteria is not related to contract works, no immediate actions are considered necessary.

Location Plan:

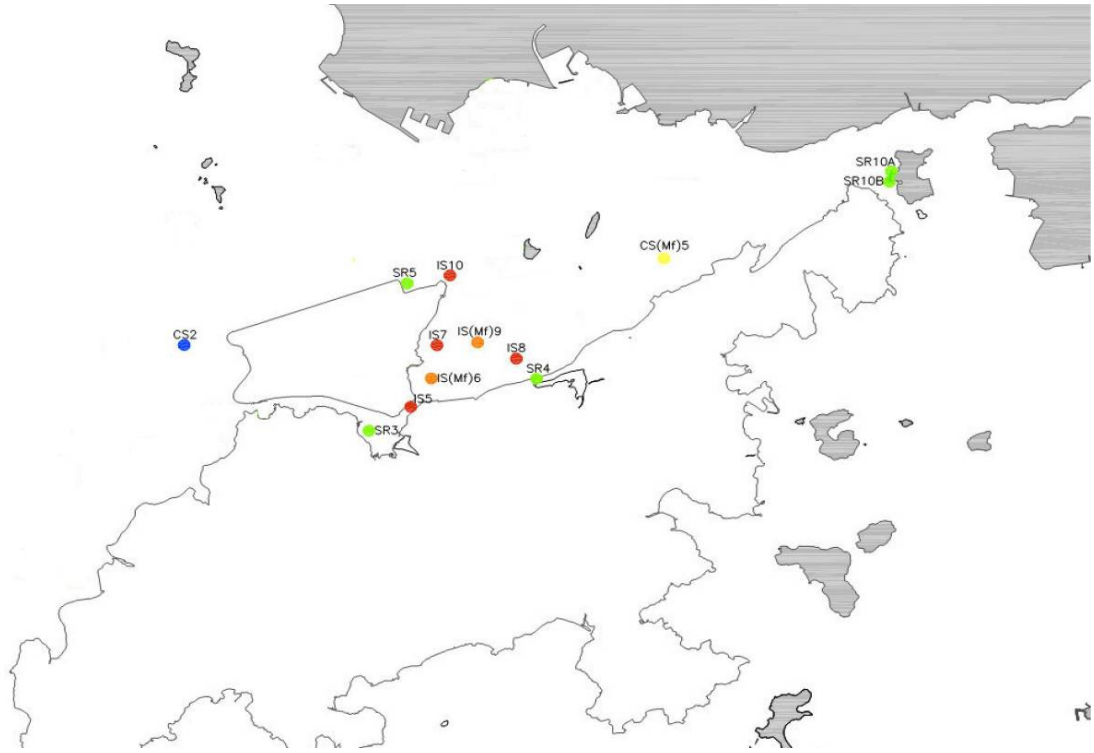

Reviewed by : Claudine Lee

Title : ET Leader



Date : 6 June 2014

Copied to : Supervising Officer, IEC, EPD, Contractor, ENPO

Summary of Notifications of Summons and Prosecutions

Total No. of Notifications of Summons / Prosecutions Received	No. of Notifications of Summons / Prosecutions Received during Reporting Period	Status of Notifications of Summons / Prosecutions
0	0	N/A
