


Appendix II Noise Monitoring Results

Project	Works	Date (yyyy-mm-dd)	Station	Weather Condition	Time (hh:mm, 24hour)	Noise Level for 30-min, dB(A)			Limit Level dB(A)	Wind Speed (m/s)	Noise Meter Model/ID	Calibrator Model/ID
						Leq	L10	L90				
TMCLKL	HY/2012/07	2015-06-02	NSR1A	Cloudy	10:36	58	60	54	75	0.7	RION NL31 (S/N 00603867)	RION NC73 (S/N 10997142)
TMCLKL	HY/2012/07	2015-06-08	NSR1A	Sunny	10:32	60	62	56	75	0.6	RION NL31 (S/N 00603867)	RION NC73 (S/N 10997142)
TMCLKL	HY/2012/07	2015-06-11	NSR1A	Sunny	9:53	58	60	54	75	0.4	RION NL31 (S/N 00603867)	RION NC73 (S/N 10997142)
TMCLKL	HY/2012/07	2015-06-17	NSR1A	Sunny	9:33	60	63	55	75	0.2	RION NL31 (S/N 00603867)	RION NC73 (S/N 10997142)
TMCLKL	HY/2012/07	2015-06-23	NSR1A	Cloudy	11:07	59	61	55	75	0.3	RION NL31 (S/N 00603867)	RION NC73 (S/N 10997142)
TMCLKL	HY/2012/07	2015-06-29	NSR1A	Sunny	11:16	59	60	55	75	0.2	RION NL31 (S/N 00603867)	RION NC73 (S/N 10997142)
						Min.	58					
						Max.	60					
						Average	59					

### Noise Monitoring Results at NSR 1A ( $L_{eq, 30min}$ )

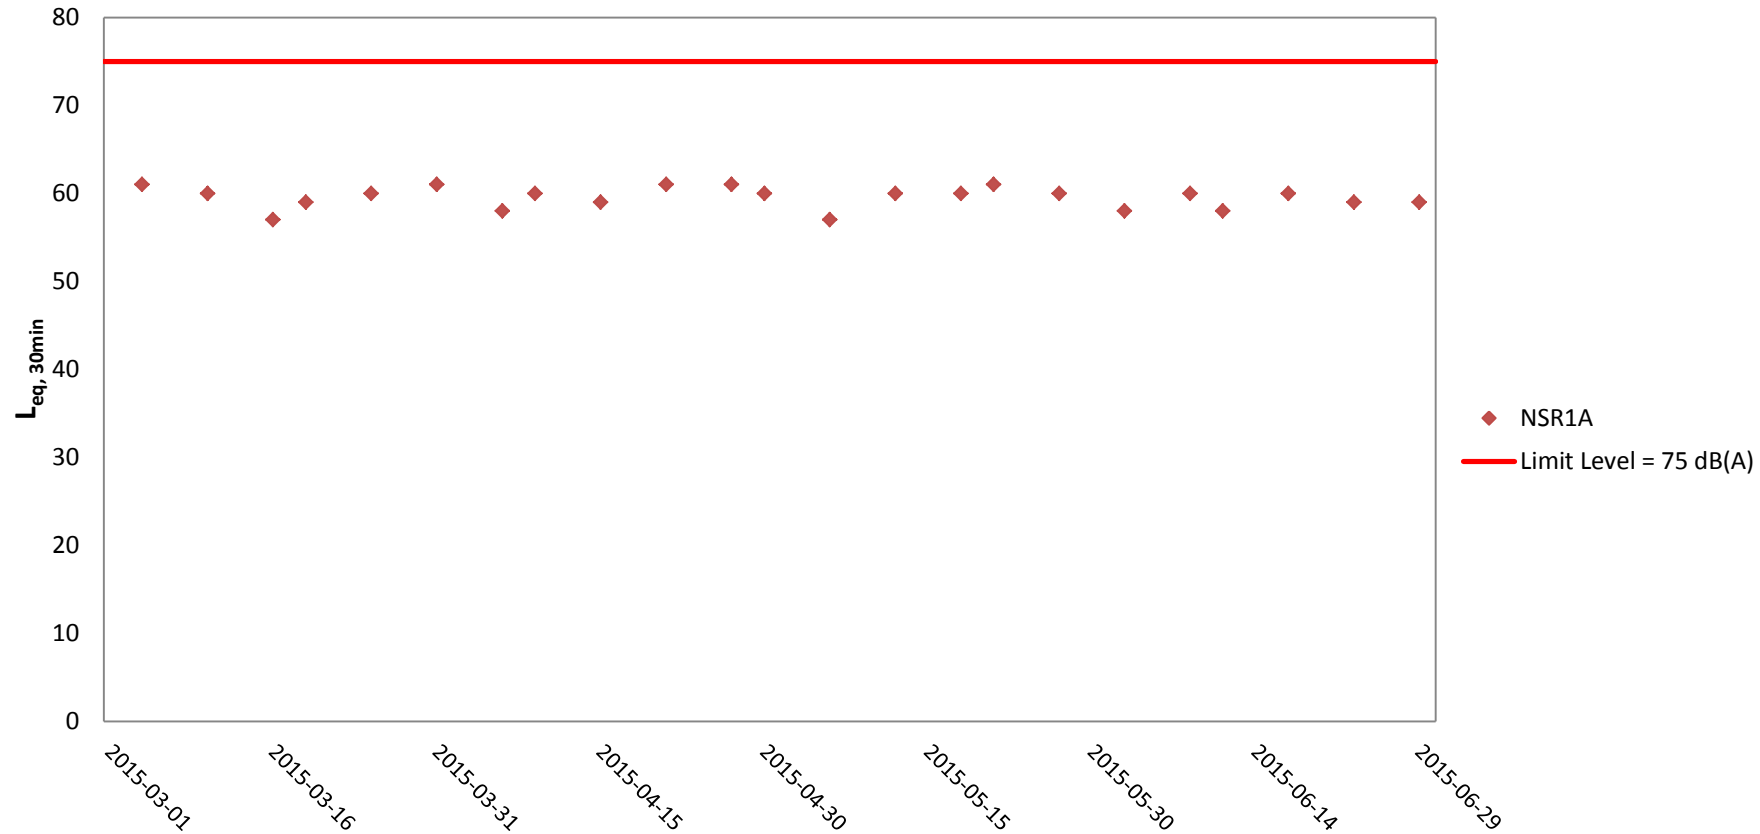

*Weather condition within the reporting period varied between sunny to rainy.*

*Major construction works undertaken within the reporting period include Construction and installation of pile caps; Pier construction; Pile cap installation; Re-alignment of Cheung Tung Road; Land piling; Pre-drilling works; Installation of pier head segment; Additional land GI, trial pits & lab testing; Relocation of MTRC fence; and Slope work of Slopes 9SE-B/C9 and 9SE-B/F85.*

*Marine works within the reporting period include Construction and installation of pile caps; Uninstallation of marine piling platform; Pier head segment installation; Pile cap installation; Pier construction; Launching gantry assembly; Marine piling and Installation of pier head segment.*
