


Noise Monitoring Results at NSR 1A ($L_{eq, 30min}$)

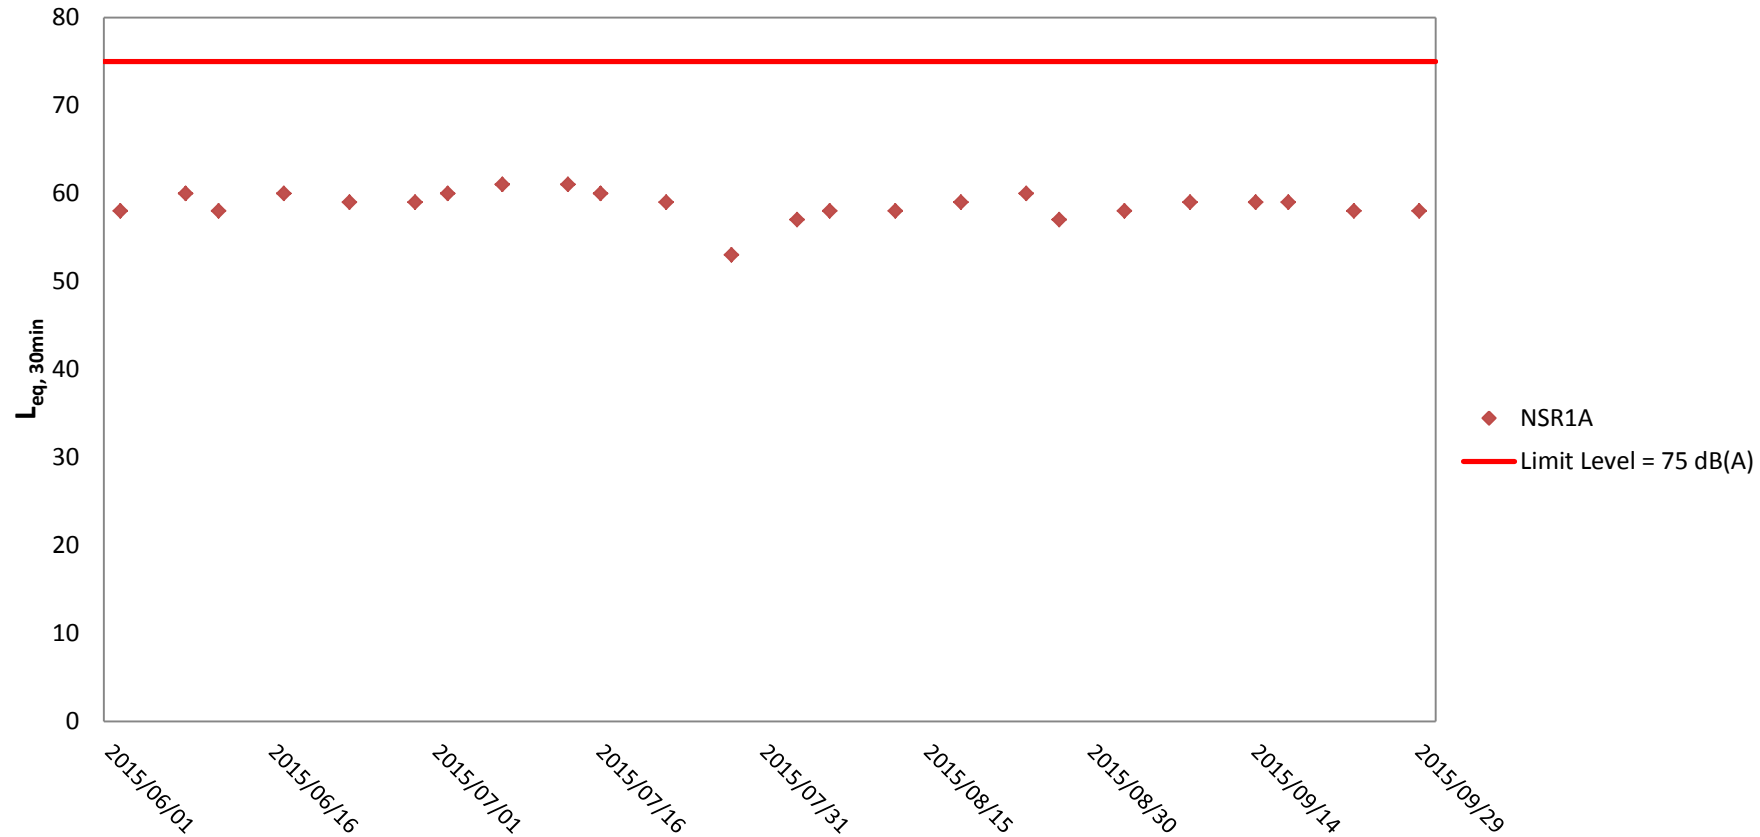

Weather condition within the reporting period varied between sunny to rainy.

Major construction works undertaken within the reporting period include Construction and installation of pile caps; Uninstallation of marine piling platform; Pile cap installation; Pier construction; Launching gantry assembly; Marine piling; and, Installation of pier head segment.

Marine works within the reporting period include Construction and installation of pile caps; Uninstallation of marine piling platform; Pile cap installation; Pier construction; Launching gantry assembly; Marine piling; and Installation of pier head segment.

Appendix II Noise Monitoring Results

Project	Works	Date (yyyy-mm-dd)	Station	Weather Condition	Time (hh:mm, 24hour)	Noise Level for 30-min, dB(A)			Limit Level dB(A)	Wind Speed (m/s)	Noise Meter Model/ID	Calibrator Model/ID
						Leq	L10	L90				
TMCLKL	HY/2012/07	2015/09/02	NSR1A	Cloudy	11:00	58	60	54	75	0.3	RION NL31 (S/N 00603867)	RION NC73 (S/N 10997142)
TMCLKL	HY/2012/07	2015/09/08	NSR1A	Sunny	9:55	59	61	54	75	0.2	RION NL31 (S/N 00603867)	RION NC73 (S/N 10997142)
TMCLKL	HY/2012/07	2015/09/14	NSR1A	Sunny	9:44	59	62	54	75	0.2	RION NL31 (S/N 00603867)	RION NC73 (S/N 10997142)
TMCLKL	HY/2012/07	2015/09/17	NSR1A	Sunny	10:05	59	61	54	75	0.2	RION NL31 (S/N 00603867)	RION NC73 (S/N 10997142)
TMCLKL	HY/2012/07	2015/09/23	NSR1A	Sunny	10:17	58	60	53	75	0.3	RION NL31 (S/N 00603867)	RION NC73 (S/N 10997142)
TMCLKL	HY/2012/07	2015/09/29	NSR1A	Sunny	10:44	58	60	53	75	0.3	RION NL31 (S/N 00603867)	RION NC73 (S/N 10997142)
						Min.	58					
						Max.	59					
						Average	59					
