


Appendix II Noise Monitoring Results

Project	Works	Date (yyyy-mm-dd)	Station	Weather Condition	Time (hh:mm, 24hour)	Noise Level for 30-min, dB(A)			Limit Level dB(A)	Wind Speed (m/s)	Noise Meter Model/ID	Calibrator Model/ID
						Leq	L10	L90				
TMCLKL	HY/2012/07	2015-12-01	NSR1A	Sunny	9:33	59	61	53	75	0.2	RION NL31 (S/N 00603867)	RION NC73 (S/N 10997142)
TMCLKL	HY/2012/07	2015-12-07	NSR1A	Cloudy	10:24	60	62	55	75	0.5	RION NL31 (S/N 00603867)	RION NC73 (S/N 10997142)
TMCLKL	HY/2012/07	2015-12-10	NSR1A	Sunny	10:13	59	61	56	75	0.2	RION NL31 (S/N 00603867)	RION NC73 (S/N 10997142)
TMCLKL	HY/2012/07	2015-12-16	NSR1A	Sunny	9:52	59	62	54	75	0.6	RION NL31 (S/N 00603867)	RION NC73 (S/N 10997142)
TMCLKL	HY/2012/07	2015-12-22	NSR1A	Sunny	10:12	59	61	54	75	0.6	RION NL31 (S/N 00603867)	RION NC73 (S/N 10997142)
TMCLKL	HY/2012/07	2015-12-28	NSR1A	Cloudy	11:20	62	64	55	75	0.5	RION NL31 (S/N 00603867)	RION NC73 (S/N 10997142)
TMCLKL	HY/2012/07	2015-12-31	NSR1A	Sunny	11:02	60	62	54	75	0.3	RION NL31 (S/N 00603867)	RION NC73 (S/N 10997142)
						Min.	59					
						Max.	62					
						Average	60					

Noise Monitoring Results at NSR 1A ($L_{eq, 30min}$)

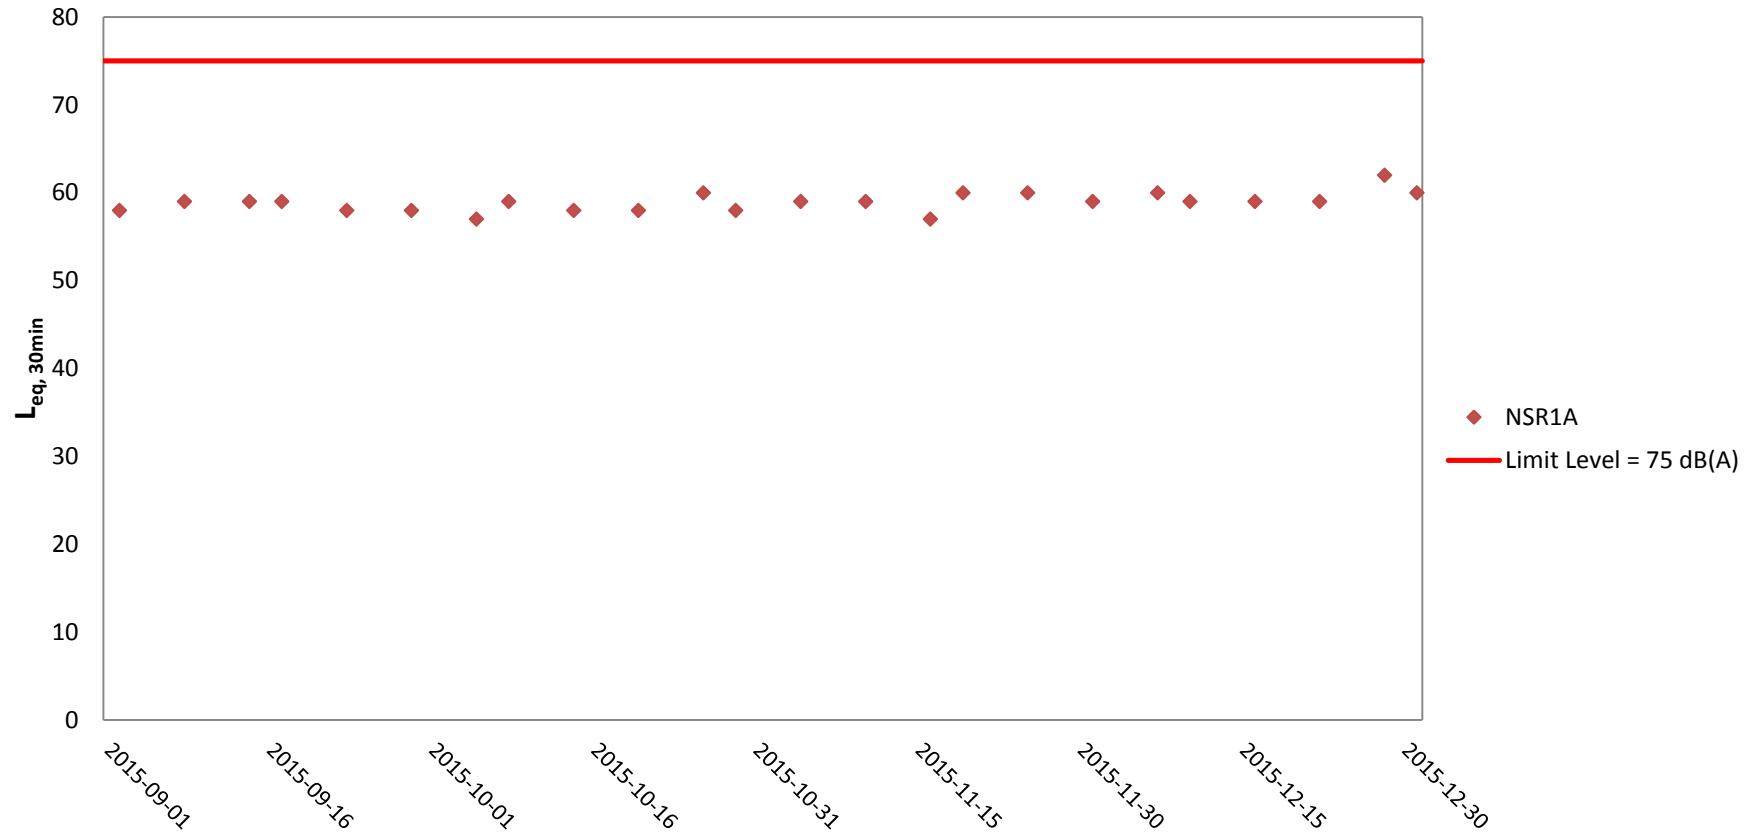

Weather condition within the reporting period varied between sunny to rainy.

Major construction works undertaken within the reporting period include Construction and installation of pile caps; Pier construction; Re-alignment of Cheung Tung Road; Predrilling at Viaduct F; Additional land GI, trial pits & lab testing; Installation of pier head segment; and Slope work of Viaducts A, B & C.

Marine works within the reporting period include Construction and installation of pile caps; Uninstallation of marine piling platform; Pier construction; Launching gantry operation; and Installation of deck segment and pier head segment.
