


Appendix II Noise Monitoring Results

Project	Works	Date (yyyy-mm-dd)	Station	Weather Condition	Time (hh:mm, 24hour)	Noise Level for 30-min, dB(A)			Limit Level dB(A)	Wind Speed (m/s)	Noise Meter Model/ID	Calibrator Model/ID
						Leq	L10	L90				
TMCLKL	HY/2012/07	2016-04-05	NSR1A	Sunny	10:23	61	63	54	75	0.3	RION NL31 (S/N 00603867)	RION NC73 (S/N 10997142)
TMCLKL	HY/2012/07	2016-04-11	NSR1A	Cloudy	10:03	59	62	54	75	0.3	RION NL31 (S/N 00603867)	RION NC73 (S/N 10997142)
TMCLKL	HY/2012/07	2016-04-14	NSR1A	Cloudy	11:03	60	62	54	75	0.2	RION NL31 (S/N 00603867)	RION NC73 (S/N 10997142)
TMCLKL	HY/2012/07	2016-04-20	NSR1A	Cloudy	9:46	60	62	54	75	0.2	RION NL31 (S/N 00603867)	RION NC73 (S/N 10997142)
TMCLKL	HY/2012/07	2016-04-26	NSR1A	Sunny	10:35	59	61	53	75	0.2	RION NL31 (S/N 00603867)	RION NC73 (S/N 10997142)
TMCLKL	HY/2012/07	2016-04-29	NSR1A	Sunny	9:40	58	60	53	75	0.3	RION NL31 (S/N 00603867)	RION NC73 (S/N 10997142)
						Min.	58					
						Max.	61					
						Average	59					

### Noise Monitoring Results at NSR 1A ( $L_{eq, 30min}$ )

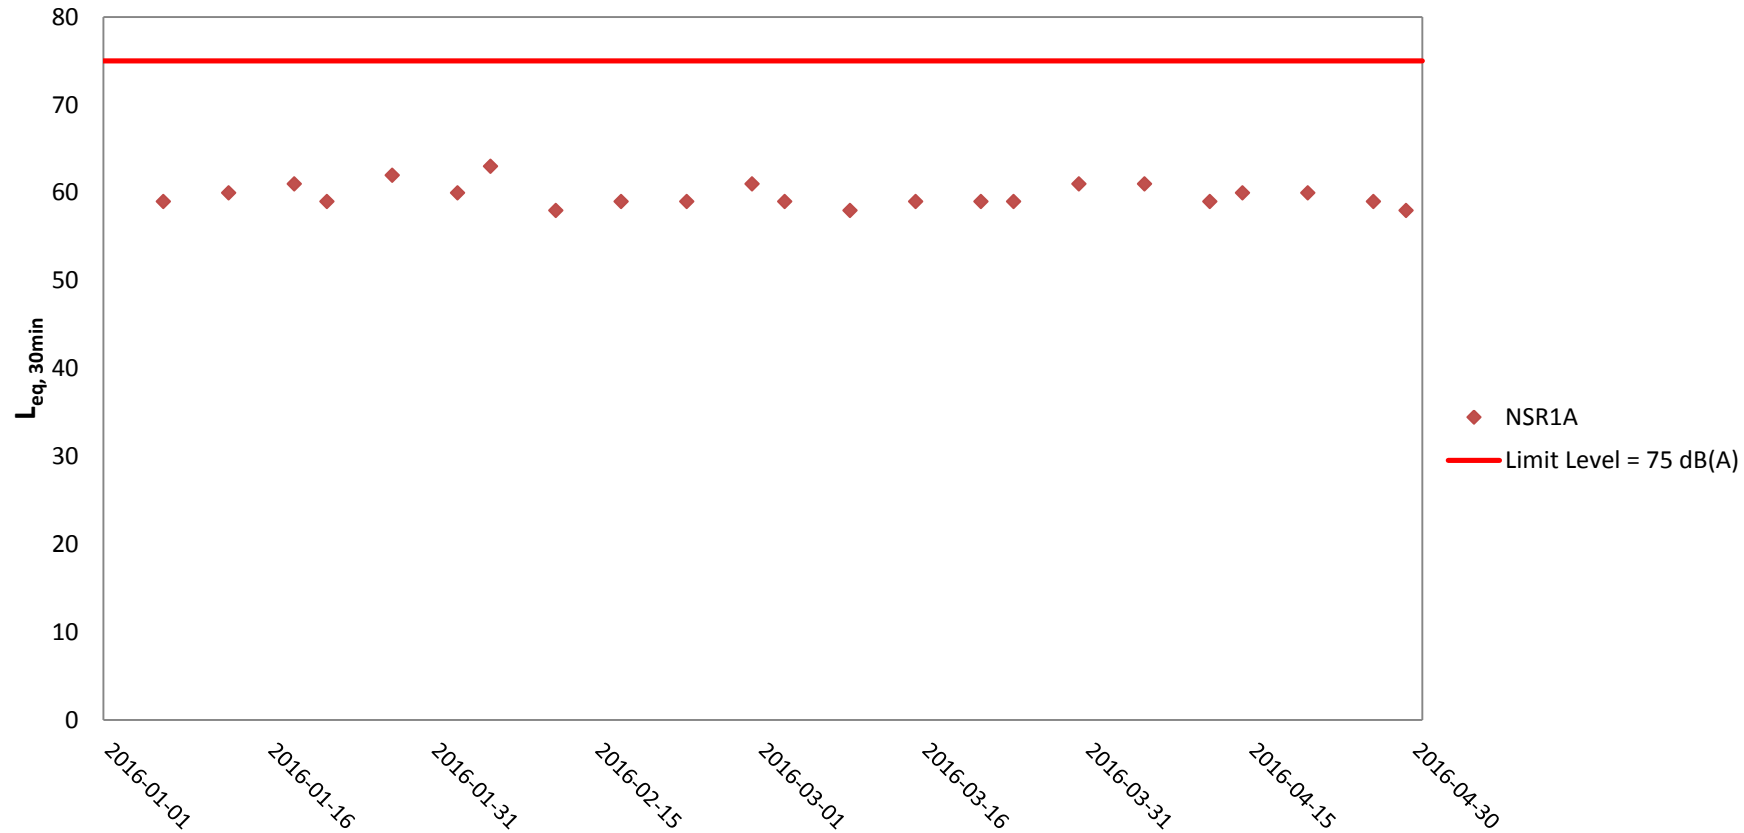

Weather condition within the reporting period varied between sunny to rainy.

Major construction works undertaken within the reporting period include Pier construction; Re-alignment of Cheung Tung Road; Construction of land section of berth at Southern Landfall; Installation of pier head and deck segments; and Slope work of Viaducts A, B & C.

Marine works within the reporting period include Construction and installation of pile caps; Uninstallation of marine piling platform; Pier construction; Construction of marine section of berth at Southern Landfall; Launching gantry operation; and Installation of deck segment and pier head segment.
