
Ducient	Works	Date (yyyy-mm-dd)	Station	Weather Condition	Time (hh:mm, 24hour)	Noise Level for 30-min, dB(A)			Limit Level	Wind Speed	Noise Meter	Calibrator
Project						Leq	L10	L90	dB(A)	(m/s)	Model/ID	Model/ID
TMCLKL	HY/2012/07	2017-02-02	NSR1A	Sunny	10:38	61	62	59	75	0.3	RION NL31 (S/N	RION NC73 (S/N
											00603867)	10997142)
TMCLKL	HY/2012/07	2017-02-08	NSR1A	Sunny	10:16	61	63	57	75	0.3	RION NL31 (S/N	RION NC73 (S/N
											00603867)	10997142)
TMCLKL	HY/2012/07	2017-02-14	NSR1A	Sunny	9:48	62	64	57	75	0.3	RION NL31 (S/N	RION NC73 (S/N
											00603867)	10997142)
TMCLKL	HY/2012/07	2017-02-20	NSR1A	Sunny	11:24	63	65	58	75	0.4	RION NL31 (S/N	RION NC73 (S/N
											00603867)	10997142)
TMCLKL	HY/2012/07	2017-02-23	NSR1A	Cloudy	10:44	63	65	60	75	0.5	RION NL31 (S/N	RION NC73 (S/N
											00603867)	10997142)
					Min.	61						
					Max.	63						
					Average	62						

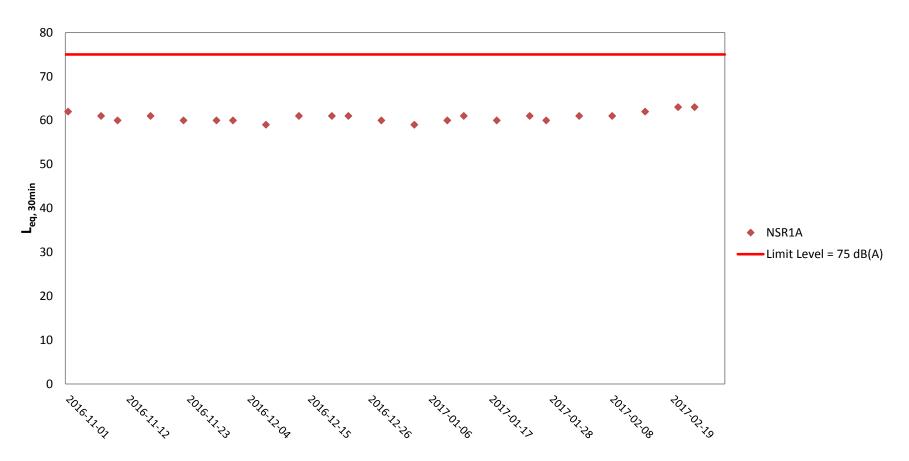

Noise Monitoring Results at NSR 1A ( $L_{eq, 30min}$ )

Weather condition within the reporting period varied between sunny to rainy.

Major construction works undertaken within the reporting period include Pier construction; Re-alignment of Cheung Tung Road; Road works along North Lantau Highway; Installation of pier head and deck segments; and Slope work of Viaducts A, B & C.

Marine works within the reporting period include Construction and installation of pile caps; Uninstallation of marine piling platform; Pier construction; Launching gantry operation; and Installation of deck segment and pier head segment.
