

1-hour TSP Monitoring Results at Air Quality Monitoring Station ASR8A

Project	Works	Date(yyyy-mm-dd)	Station	Time (hh:mm, 24hour)	Parameter	Results (ug/m3)	Action Level (ug/m3)	Limit Level (ug/m3)		
TMCLKL	HY/2012/07	2017-05-02	ASR8A	8:00	1-hr TSP	62	394	500		
TMCLKL	HY/2012/07	2017-05-02	ASR8A	9:02	1-hr TSP	54				
TMCLKL	HY/2012/07	2017-05-02	ASR8A	10:04	1-hr TSP	65				
TMCLKL	HY/2012/07	2017-05-06	ASR8A	8:22	1-hr TSP	190				
TMCLKL	HY/2012/07	2017-05-06	ASR8A	9:24	1-hr TSP	200				
TMCLKL	HY/2012/07	2017-05-06	ASR8A	10:26	1-hr TSP	189				
TMCLKL	HY/2012/07	2017-05-12	ASR8A	8:16	1-hr TSP	66				
TMCLKL	HY/2012/07	2017-05-12	ASR8A	9:18	1-hr TSP	57				
TMCLKL	HY/2012/07	2017-05-12	ASR8A	10:20	1-hr TSP	67				
TMCLKL	HY/2012/07	2017-05-18	ASR8A	8:15	1-hr TSP	97				
TMCLKL	HY/2012/07	2017-05-18	ASR8A	9:17	1-hr TSP	101				
TMCLKL	HY/2012/07	2017-05-18	ASR8A	10:19	1-hr TSP	67				
TMCLKL	HY/2012/07	2017-05-24	ASR8A	9:15	1-hr TSP	70				
TMCLKL	HY/2012/07	2017-05-24	ASR8A	10:17	1-hr TSP	56				
TMCLKL	HY/2012/07	2017-05-24	ASR8A	11:19	1-hr TSP	50				
TMCLKL	HY/2012/07	2017-05-27	ASR8A	8:37	1-hr TSP	90				
TMCLKL	HY/2012/07	2017-05-27	ASR8A	9:39	1-hr TSP	80				
TMCLKL	HY/2012/07	2017-05-27	ASR8A	10:41	1-hr TSP	78				
						Average			91	
						Min.			50	
						Max.	200			

1-hour TSP Monitoring Results at Air Quality Monitoring Station ASR9



Project	Works	Date(yyyy-mm-dd)	Station	Time (hh:mm, 24hour)	Parameter	Results (ug/m3)	Action Level (ug/m3)	Limit Level (ug/m3)		
TMCLKL	HY/2012/07	2017-05-02	ASR9	8:11	1-hr TSP	69	393	500		
TMCLKL	HY/2012/07	2017-05-02	ASR9	9:13	1-hr TSP	66				
TMCLKL	HY/2012/07	2017-05-02	ASR9	10:15	1-hr TSP	67				
TMCLKL	HY/2012/07	2017-05-06	ASR9	8:32	1-hr TSP	251				
TMCLKL	HY/2012/07	2017-05-06	ASR9	9:34	1-hr TSP	262				
TMCLKL	HY/2012/07	2017-05-06	ASR9	10:36	1-hr TSP	263				
TMCLKL	HY/2012/07	2017-05-12	ASR9	8:27	1-hr TSP	114				
TMCLKL	HY/2012/07	2017-05-12	ASR9	9:29	1-hr TSP	145				
TMCLKL	HY/2012/07	2017-05-12	ASR9	10:31	1-hr TSP	128				
TMCLKL	HY/2012/07	2017-05-18	ASR9	8:25	1-hr TSP	77				
TMCLKL	HY/2012/07	2017-05-18	ASR9	9:27	1-hr TSP	139				
TMCLKL	HY/2012/07	2017-05-18	ASR9	10:29	1-hr TSP	129				
TMCLKL	HY/2012/07	2017-05-24	ASR9	9:26	1-hr TSP	90				
TMCLKL	HY/2012/07	2017-05-24	ASR9	10:28	1-hr TSP	140				
TMCLKL	HY/2012/07	2017-05-24	ASR9	11:30	1-hr TSP	114				
TMCLKL	HY/2012/07	2017-05-27	ASR9	8:48	1-hr TSP	98				
TMCLKL	HY/2012/07	2017-05-27	ASR9	9:50	1-hr TSP	117				
TMCLKL	HY/2012/07	2017-05-27	ASR9	10:52	1-hr TSP	92				
						Average			131	
						Min.			66	
						Max.	263			

24-hour TSP Monitoring Results at Air Quality Monitoring Station ASR8A

Project	Works	Date(yyyy-mm-dd)	Station	Time (hh:mm, 24hour)	Parameter	Results (ug/m3)	Action Level (ug/m3)	Limit Level (ug/m3)
TMCLKL	HY/2012/07	2017-05-02	ASR8A	11:06	24-hr TSP	39	178	260
TMCLKL	HY/2012/07	2017-05-06	ASR8A	11:28	24-hr TSP	65		
TMCLKL	HY/2012/07	2017-05-12	ASR8A	11:22	24-hr TSP	45		
TMCLKL	HY/2012/07	2017-05-18	ASR8A	11:21	24-hr TSP	45		
TMCLKL	HY/2012/07	2017-05-24	ASR8A	12:21	24-hr TSP	44		
TMCLKL	HY/2012/07	2017-05-27	ASR8A	11:43	24-hr TSP	45		
					Average	47		
					Min.	39		
					Max.	65		

24-hour TSP Monitoring Results at Air Quality Monitoring Station ASR9



Project	Works	Date(yyyy-mm-dd)	Station	Time (hh:mm, 24hour)	Parameter	Results (ug/m3)	Action Level (ug/m3)	Limit Level (ug/m3)
TMCLKL	HY/2012/07	2017-05-02	ASR9	11:17	24-hr TSP	48	178	260
TMCLKL	HY/2012/07	2017-05-06	ASR9	11:38	24-hr TSP	67		
TMCLKL	HY/2012/07	2017-05-12	ASR9	11:33	24-hr TSP	56		
TMCLKL	HY/2012/07	2017-05-18	ASR9	11:31	24-hr TSP	60		
TMCLKL	HY/2012/07	2017-05-24	ASR9	12:32	24-hr TSP	57		
TMCLKL	HY/2012/07	2017-05-27	ASR9	11:54	24-hr TSP	65		
					Average	59		
					Min.	48		
					Max.	67		

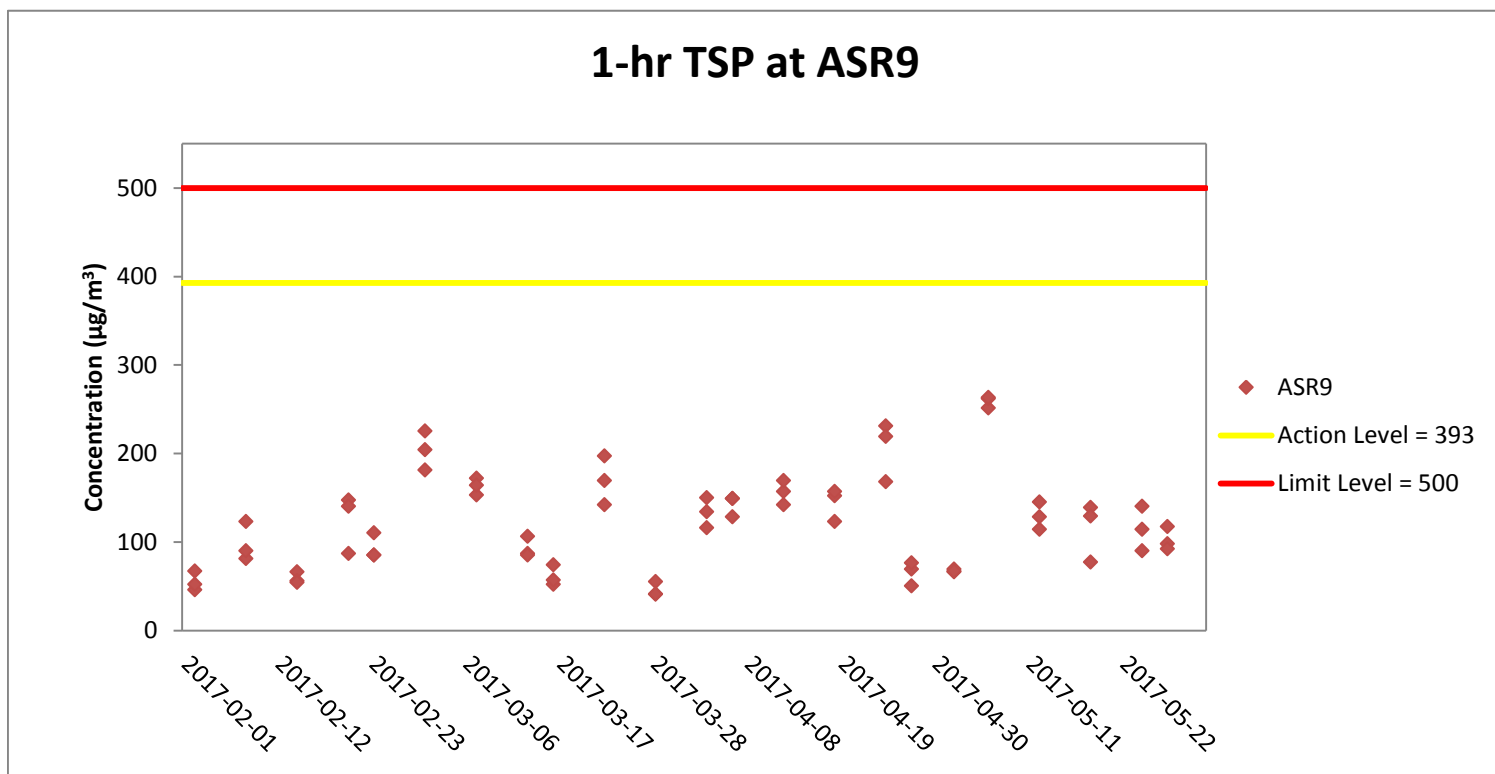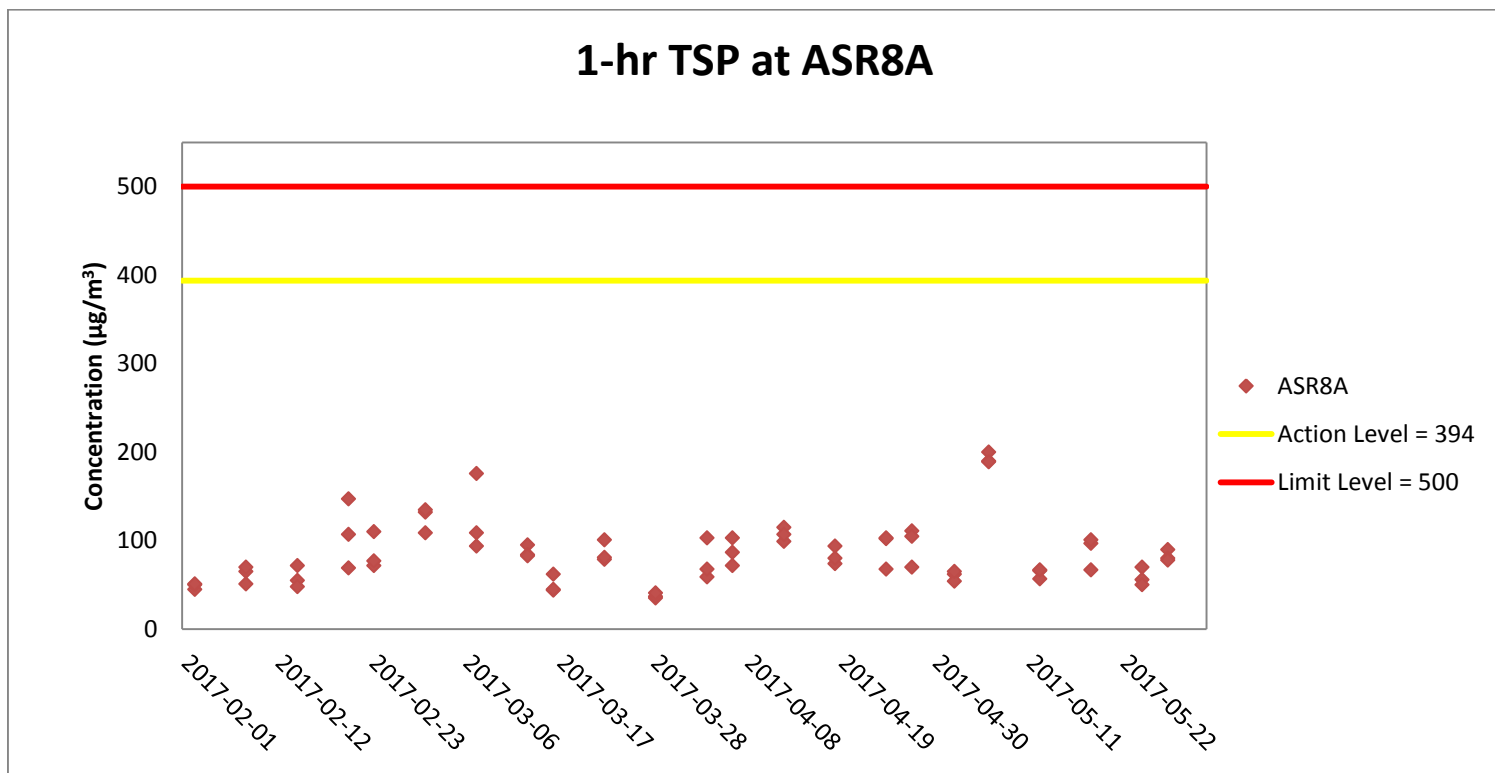

Weather condition within the reporting period varied between sunny to rainy.

Major construction works undertaken within the reporting period include Pier construction; Re-alignment of Cheung Tung Road; Road works along North Lantau Highway; Installation of pier head and deck segments; and Slope work of Viaducts A, B & C.

Marine works within the reporting period include Construction and installation of pile caps; Uninstallation of marine piling platform; Pier construction; Launching gantry operation; and Installation of deck segment and pier head segment.

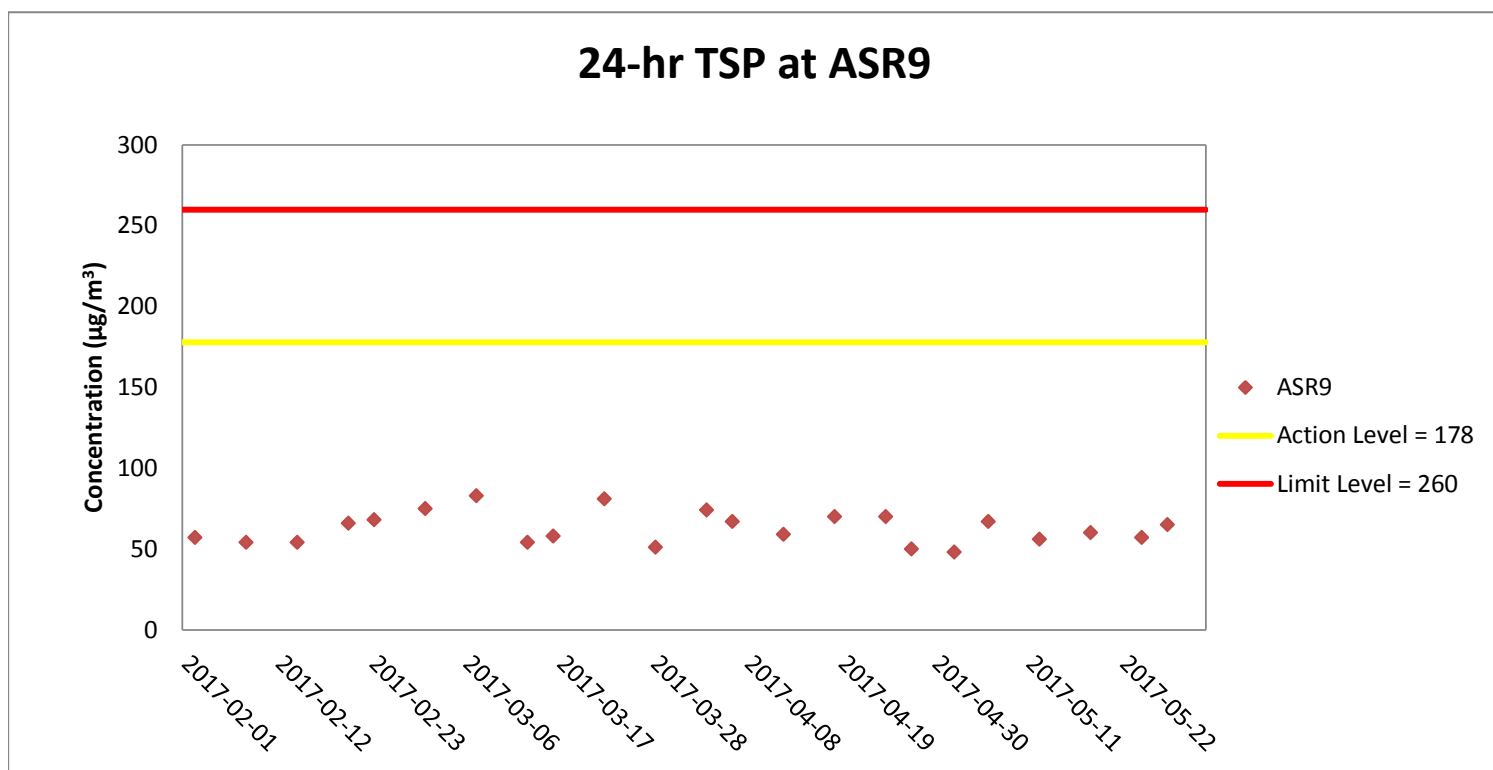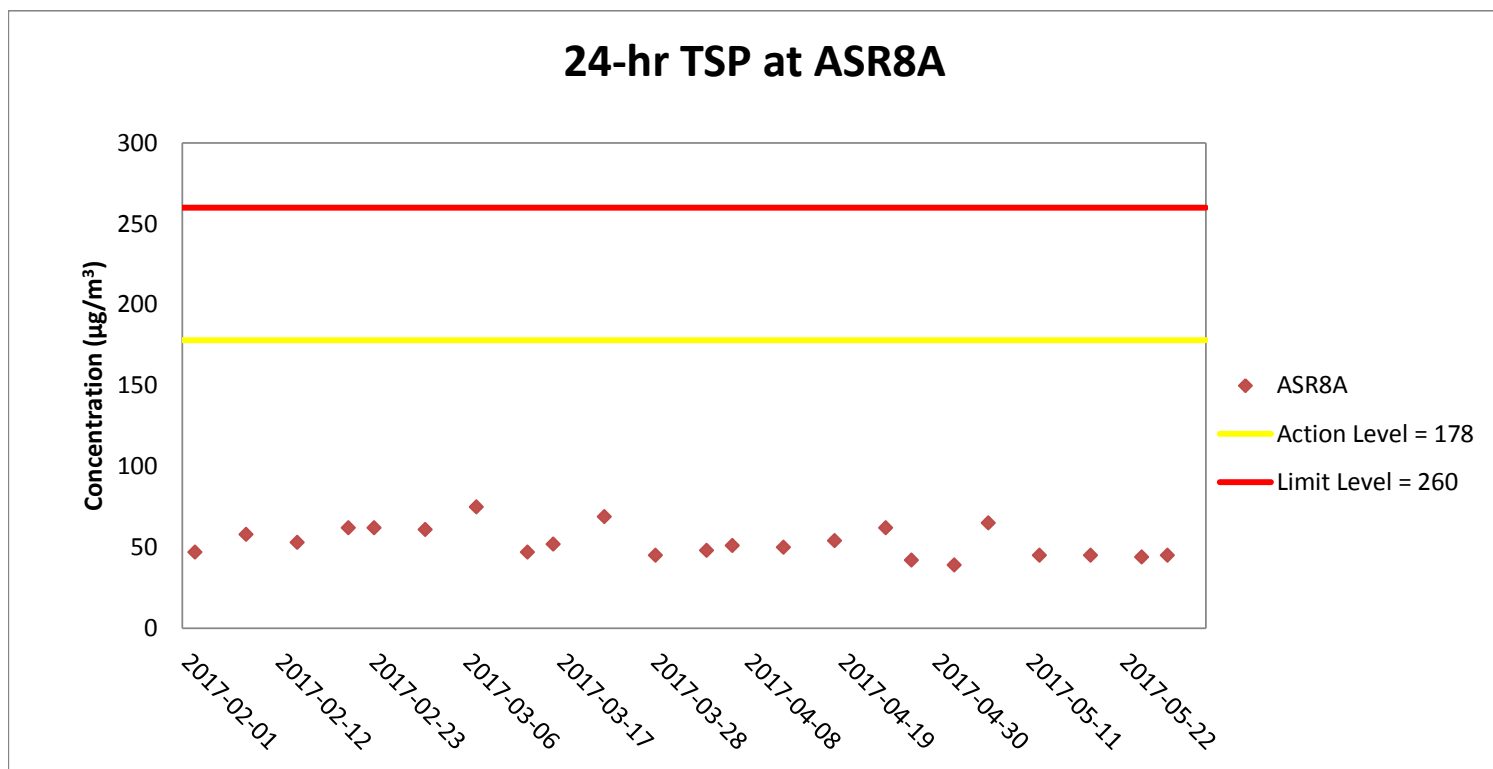

Weather condition within the reporting period varied between sunny to rainy.

Major construction works undertaken within the reporting period include Pier construction; Re-alignment of Cheung Tung Road; Road works along North Lantau Highway;; Installation of pier head and deck segments; and Slope work of Viaducts A, B & C.

Marine works within the reporting period include Construction and installation of pile caps; Uninstallation of marine piling platform; Pier construction; Launching gantry operation; and Installation of deck segment and pier head segment.
