

## 1-hour TSP Monitoring Results at Air Quality Monitoring Station ASR8A

Project	Works	Date(yyyy-mm-dd)	Station	Time (hh:mm, 24hour)	Parameter	Results (ug/m3)	Action Level (ug/m3)	Limit Level (ug/m3)		
TMCLKL	HY/2012/07	2017-06-02	ASR8A	8:14	1-hr TSP	68	394	500		
TMCLKL	HY/2012/07	2017-06-02	ASR8A	9:16	1-hr TSP	79				
TMCLKL	HY/2012/07	2017-06-02	ASR8A	10:18	1-hr TSP	55				
TMCLKL	HY/2012/07	2017-06-08	ASR8A	8:00	1-hr TSP	97				
TMCLKL	HY/2012/07	2017-06-08	ASR8A	9:02	1-hr TSP	51				
TMCLKL	HY/2012/07	2017-06-08	ASR8A	10:04	1-hr TSP	56				
TMCLKL	HY/2012/07	2017-06-14	ASR8A	9:05	1-hr TSP	82				
TMCLKL	HY/2012/07	2017-06-14	ASR8A	10:07	1-hr TSP	90				
TMCLKL	HY/2012/07	2017-06-14	ASR8A	11:09	1-hr TSP	49				
TMCLKL	HY/2012/07	2017-06-20	ASR8A	9:02	1-hr TSP	49				
TMCLKL	HY/2012/07	2017-06-20	ASR8A	10:04	1-hr TSP	38				
TMCLKL	HY/2012/07	2017-06-20	ASR8A	11:06	1-hr TSP	53				
TMCLKL	HY/2012/07	2017-06-26	ASR8A	8:54	1-hr TSP	68				
TMCLKL	HY/2012/07	2017-06-26	ASR8A	9:56	1-hr TSP	60				
TMCLKL	HY/2012/07	2017-06-26	ASR8A	10:58	1-hr TSP	44				
TMCLKL	HY/2012/07	2017-06-29	ASR8A	8:00	1-hr TSP	52				
TMCLKL	HY/2012/07	2017-06-29	ASR8A	9:02	1-hr TSP	49				
TMCLKL	HY/2012/07	2017-06-29	ASR8A	10:04	1-hr TSP	45				
				Average		60				
				Min.		38				
				Max.		97				

## 1-hour TSP Monitoring Results at Air Quality Monitoring Station ASR9



Project	Works	Date(yyyy-mm-dd)	Station	Time (hh:mm, 24hour)	Parameter	Results (ug/m3)	Action Level (ug/m3)	Limit Level (ug/m3)		
TMCLKL	HY/2012/07	2017-06-02	ASR9	8:25	1-hr TSP	94	393	500		
TMCLKL	HY/2012/07	2017-06-02	ASR9	9:27	1-hr TSP	98				
TMCLKL	HY/2012/07	2017-06-02	ASR9	10:29	1-hr TSP	110				
TMCLKL	HY/2012/07	2017-06-08	ASR9	8:10	1-hr TSP	93				
TMCLKL	HY/2012/07	2017-06-08	ASR9	9:12	1-hr TSP	120				
TMCLKL	HY/2012/07	2017-06-08	ASR9	10:14	1-hr TSP	119				
TMCLKL	HY/2012/07	2017-06-14	ASR9	9:16	1-hr TSP	97				
TMCLKL	HY/2012/07	2017-06-14	ASR9	10:18	1-hr TSP	85				
TMCLKL	HY/2012/07	2017-06-14	ASR9	11:20	1-hr TSP	75				
TMCLKL	HY/2012/07	2017-06-20	ASR9	9:13	1-hr TSP	53				
TMCLKL	HY/2012/07	2017-06-20	ASR9	10:15	1-hr TSP	46				
TMCLKL	HY/2012/07	2017-06-20	ASR9	11:17	1-hr TSP	61				
TMCLKL	HY/2012/07	2017-06-26	ASR9	9:05	1-hr TSP	110				
TMCLKL	HY/2012/07	2017-06-26	ASR9	10:07	1-hr TSP	147				
TMCLKL	HY/2012/07	2017-06-26	ASR9	11:09	1-hr TSP	119				
TMCLKL	HY/2012/07	2017-06-29	ASR9	8:10	1-hr TSP	42				
TMCLKL	HY/2012/07	2017-06-29	ASR9	9:12	1-hr TSP	85				
TMCLKL	HY/2012/07	2017-06-29	ASR9	10:14	1-hr TSP	41				
				Average		89				
				Min.		41				
				Max.		147				

**24-hour TSP Monitoring Results at Air Quality Monitoring Station ASR8A**

Project	Works	Date(yyyy-mm-dd)	Station	Time (hh:mm, 24hour)	Parameter	Results (ug/m3)	Action Level (ug/m3)	Limit Level (ug/m3)
TMCLKL	HY/2012/07	2017-06-02	ASR8A	11:20	24-hr TSP	42	178	260
TMCLKL	HY/2012/07	2017-06-08	ASR8A	11:06	24-hr TSP	45		
TMCLKL	HY/2012/07	2017-06-14	ASR8A	12:11	24-hr TSP	39		
TMCLKL	HY/2012/07	2017-06-20	ASR8A	12:08	24-hr TSP	43		
TMCLKL	HY/2012/07	2017-06-26	ASR8A	12:00	24-hr TSP	42		
TMCLKL	HY/2012/07	2017-06-29	ASR8A	11:06	24-hr TSP	38		
					Average	42		
					Min.	38		
					Max.	45		

**24-hour TSP Monitoring Results at Air Quality Monitoring Station ASR9**



Project	Works	Date(yyyy-mm-dd)	Station	Time (hh:mm, 24hour)	Parameter	Results (ug/m3)	Action Level (ug/m3)	Limit Level (ug/m3)
TMCLKL	HY/2012/07	2017-06-02	ASR9	11:31	24-hr TSP	47	178	260
TMCLKL	HY/2012/07	2017-06-08	ASR9	11:16	24-hr TSP	47		
TMCLKL	HY/2012/07	2017-06-14	ASR9	12:22	24-hr TSP	51		
TMCLKL	HY/2012/07	2017-06-20	ASR9	12:19	24-hr TSP	45		
TMCLKL	HY/2012/07	2017-06-26	ASR9	12:11	24-hr TSP	41		
TMCLKL	HY/2012/07	2017-06-29	ASR9	11:16	24-hr TSP	44		
					Average	46		
					Min.	41		
					Max.	51		

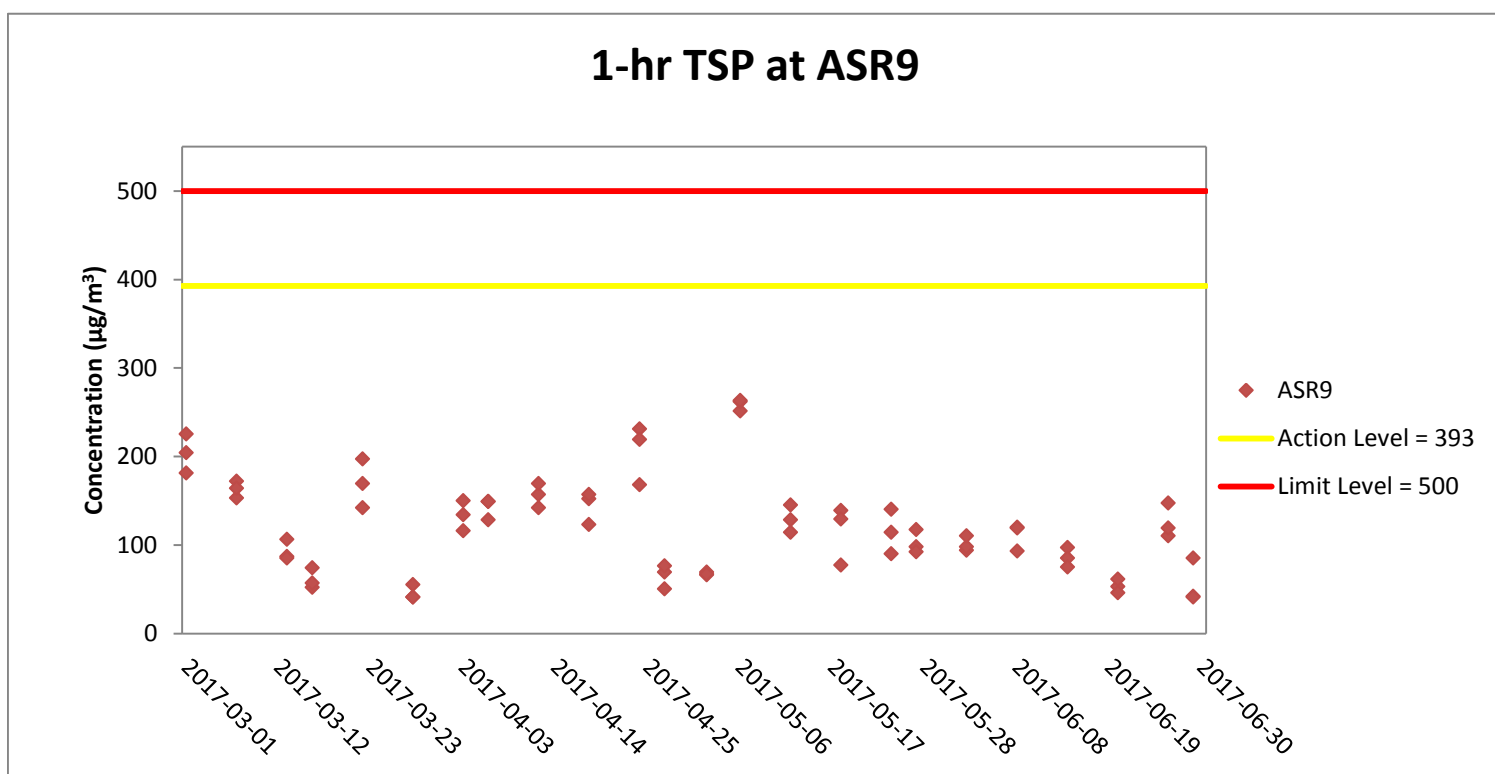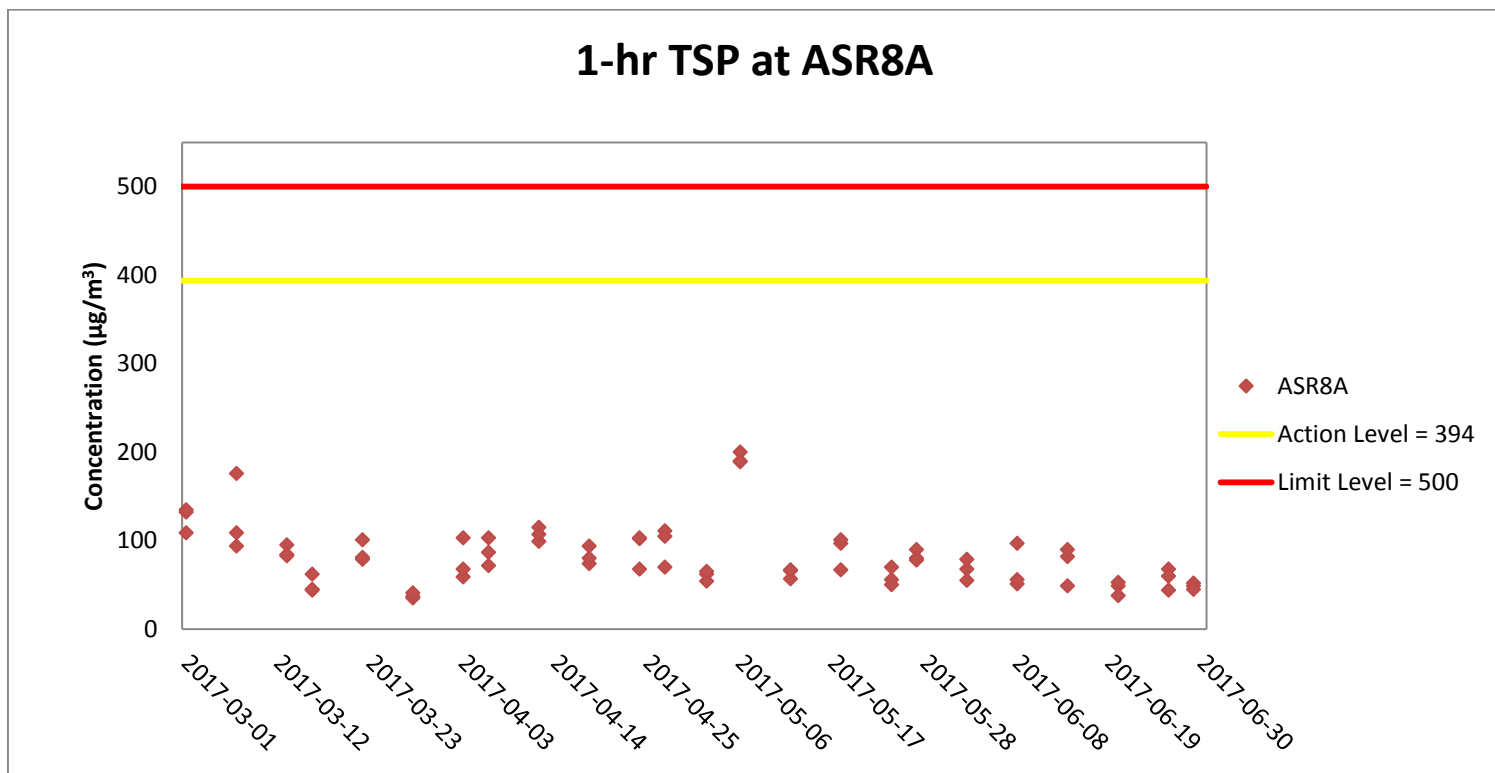

Weather condition within the reporting period varied between sunny to rainy.

Major construction works undertaken within the reporting period include Pier construction; Re-alignment of Cheung Tung Road; Road works along North Lantau Highway; Installation of pier head and deck segments; and Slope work of Viaducts A, B & C.

Marine works within the reporting period include Construction and installation of pile caps; Uninstallation of marine piling platform; Pier construction; Launching gantry operation; Installation of deck segment and pier head segment; and Construction of underslung truss scheme (no additional seabed will be occupied other than those assumed in the approved EIA Report).

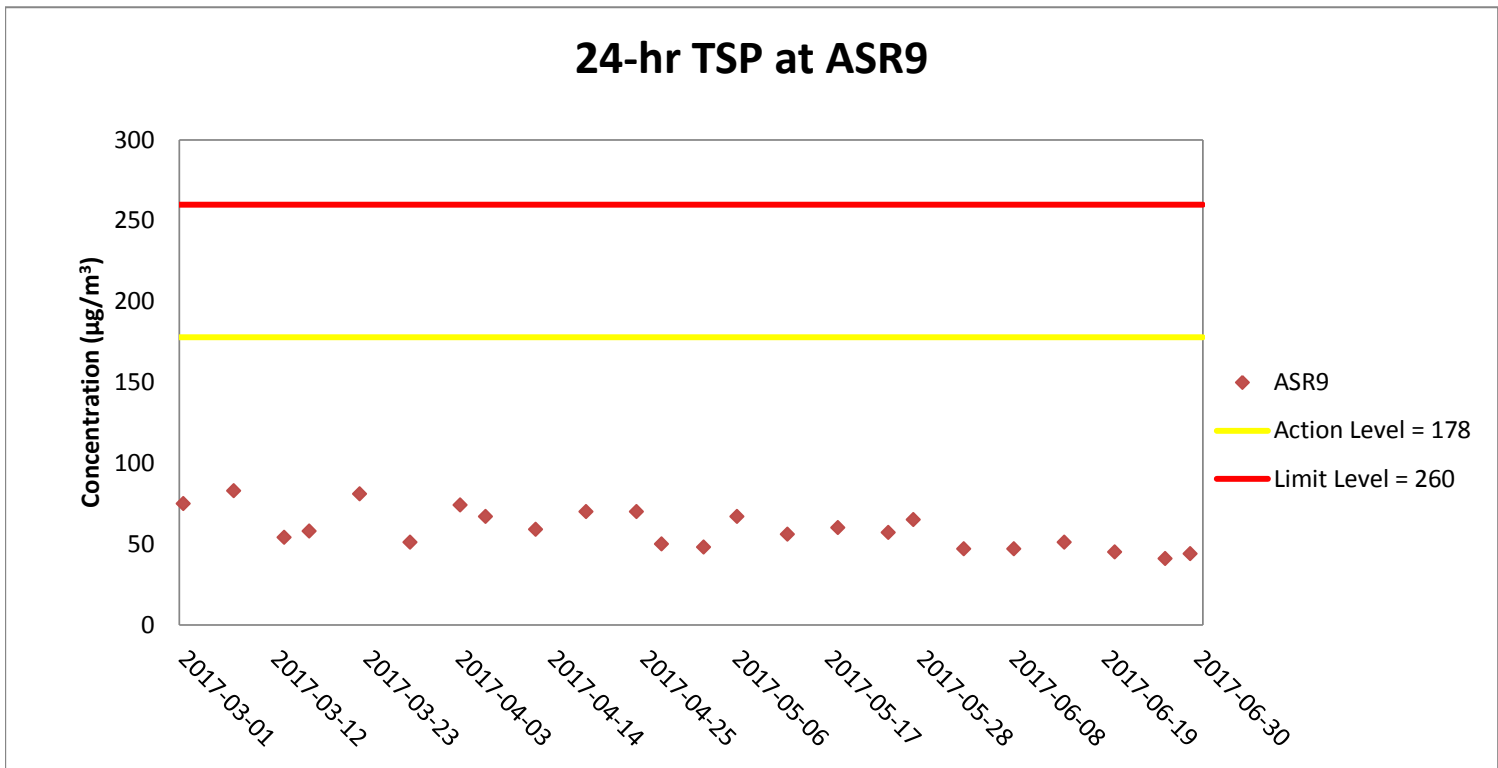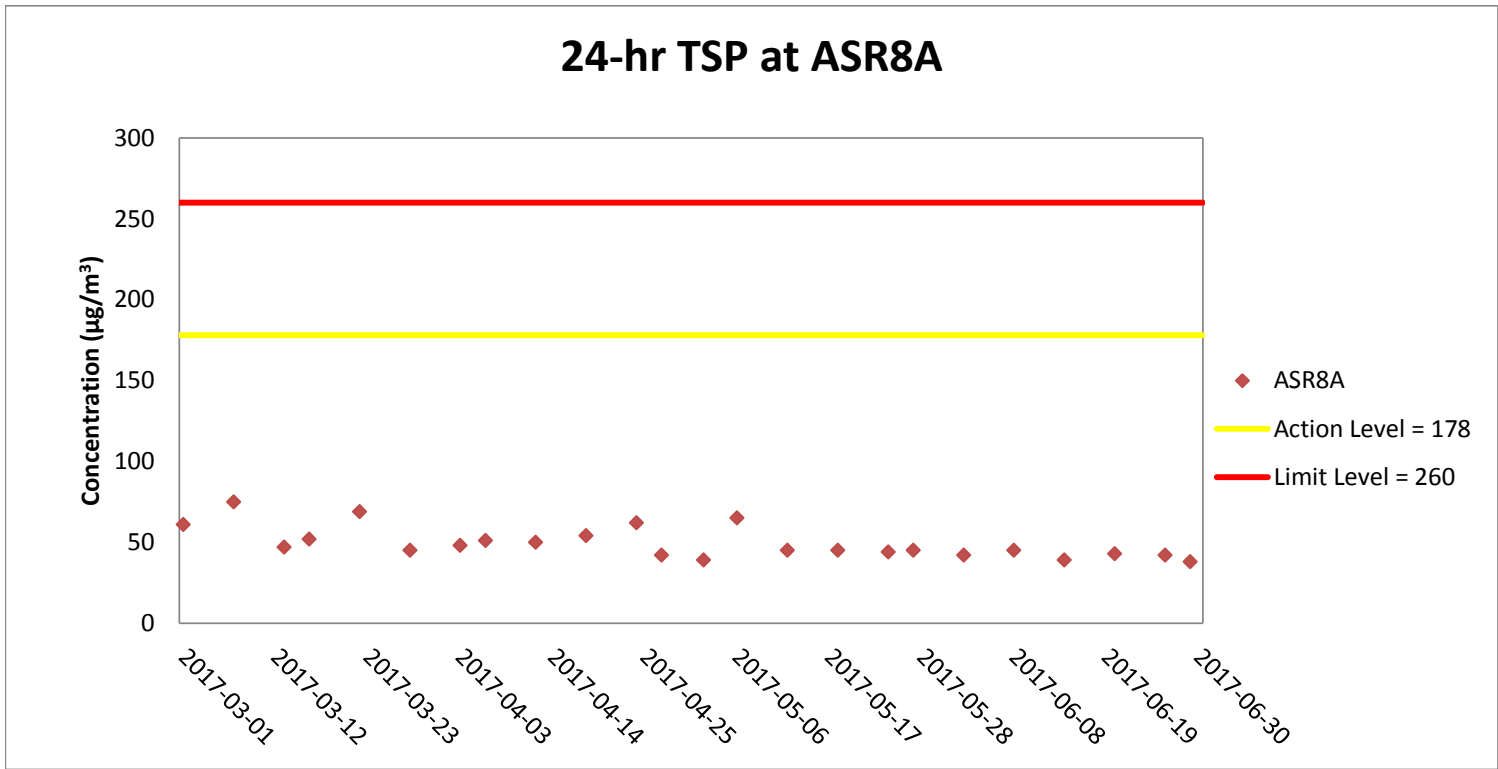

Weather condition within the reporting period varied between sunny to rainy.

Major construction works undertaken within the reporting period include Pier construction; Re-alignment of Cheung Tung Road; Road works along North Lantau Highway;; Installation of pier head and deck segments; and Slope work of Viaducts A, B & C.

Marine works within the reporting period include Construction and installation of pile caps; Uninstallation of marine piling platform; Pier construction; Launching gantry operation; Installation of deck segment and pier head segment; and Construction of underslung truss scheme (no additional seabed will be occupied other than those assumed in the approved EIA Report).
