


Appendix I-1 Noise Monitoring Results

Project	Works	Date (yyyy-mm-dd)	Station	Weather Condition	Time (hh:mm, 24hour)	Noise Level for 30-min, dB(A)			Limit Level dB(A)	Wind Speed (m/s)	Noise Meter Model/ID	Calibrator Model/ID
						Leq	L10	L90				
TMCLKL	HY/2012/07	2017-07-05	NSR1A	Sunny	9:29	62	64	58	75	0.3	RION NL31 (S/N 00603867)	RION NC73 (S/N 10486660)
TMCLKL	HY/2012/07	2017-07-11	NSR1A	Sunny	9:38	63	65	60	75	0.4	RION NL52 (S/N 01010406)	RION NC73 (S/N 10486660)
TMCLKL	HY/2012/07	2017-07-17	NSR1A	Cloudy	9:53	63	64	60	75	0.5	RION NL52 (S/N 01010406)	RION NC73 (S/N 10486660)
TMCLKL	HY/2012/07	2017-07-20	NSR1A	Sunny	10:09	63	65	60	75	2.7	RION NL52 (S/N 01010406)	RION NC73 (S/N 10486660)
TMCLKL	HY/2012/07	2017-07-26	NSR1A	Sunny	10:14	63	64	60	75	0.2	RION NL52 (S/N 01010406)	RION NC73 (S/N 10486660)
						Min.	62					
						Max.	63					
						Average	63					

Noise Monitoring Results at NSR 1A ($L_{eq, 30min}$)

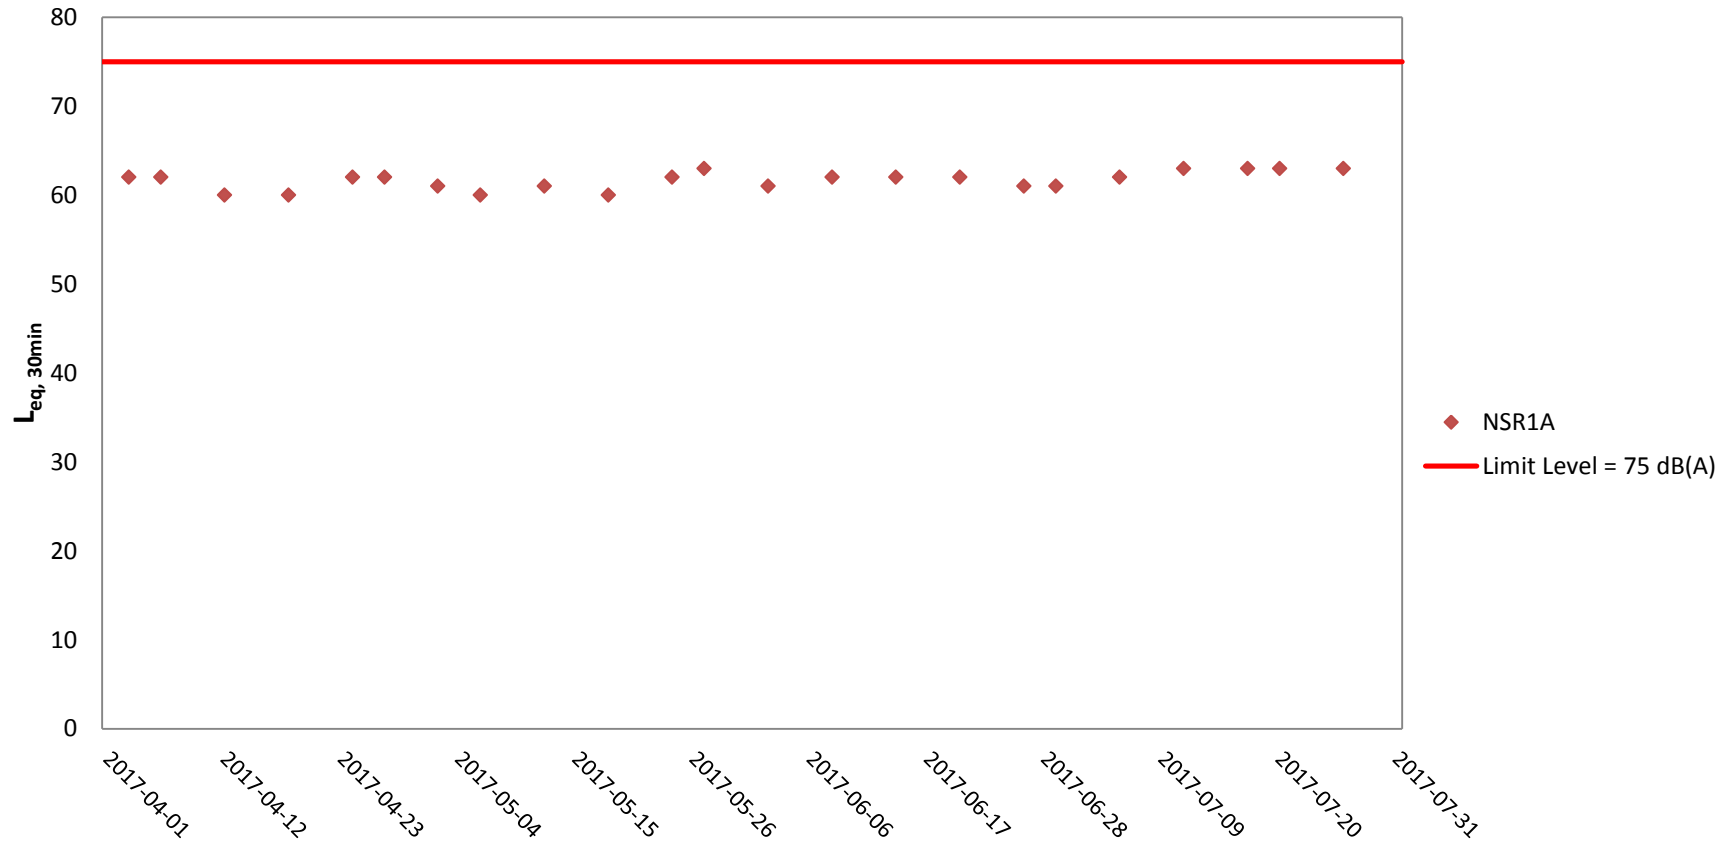

Weather condition within the reporting period varied between sunny to rainy.

Major construction works undertaken within the reporting period include Pier construction; Re-alignment of Cheung Tung Road; Road works along North Lantau Highway; Installation of pier head and deck segments; and Slope work of Viaducts A, B & C.

Marine works within the reporting period include Construction and installation of pile caps; Uninstallation of marine piling platform; Pier construction; Launching gantry operation; Installation of deck segment and pier head segment; and Construction of underslung truss scheme (no additional seabed will be occupied other than those assumed in the approved EIA Report).
