
Ducient	Works	Date (yyyy-mm-dd)	Station	Weather Condition	Time (hh:mm, 24hour)	Noise Level for 30-min, dB(A)			Limit Level	Wind Speed	Noise Meter	Calibrator
Project						Leq	L10	L90	dB(A)	(m/s)	Model/ID	Model/ID
TMCLKL	HY/2012/07	2017-10-03	NSR1A	Sunny	9:59	63	64	59	75	0.5	RION NL52	RION NC73
											(S/N 01010406)	(S/N 10486660)
TMCLKL	HY/2012/07	2017-10-09	NSR1A	Sunny	10:02	63	64	59	75	0.6	RION NL52	RION NC73
											(S/N 01010406)	(S/N 10486660)
TMCLKL	HY/2012/07	2017-10-12	NSR1A	Sunny	10:11	63	64	59	75	0.9	RION NL52	RION NC73
											(S/N 01010406)	(S/N 10486660)
TMCLKL	HY/2012/07	2017-10-18	NSR1A	Sunny	10:00	64	65	61	75	0.3	RION NL52	RION NC73
											(S/N 01010406)	(S/N 10486660)
TMCLKL	HY/2012/07	2017-10-24	NSR1A	Sunny	9:56	62	63	59	75	0.3	RION NL52	RION NC73
											(S/N 01010406)	(S/N 10486660)
TMCLKL	HY/2012/07	2017-10-30	NSR1A	Sunny	9:57	62	64	59	75	0.3	RION NL52	RION NC73
											(S/N 01010406)	(S/N 10486660)
					Min.	62						
					Max.	64						
					Average	63						

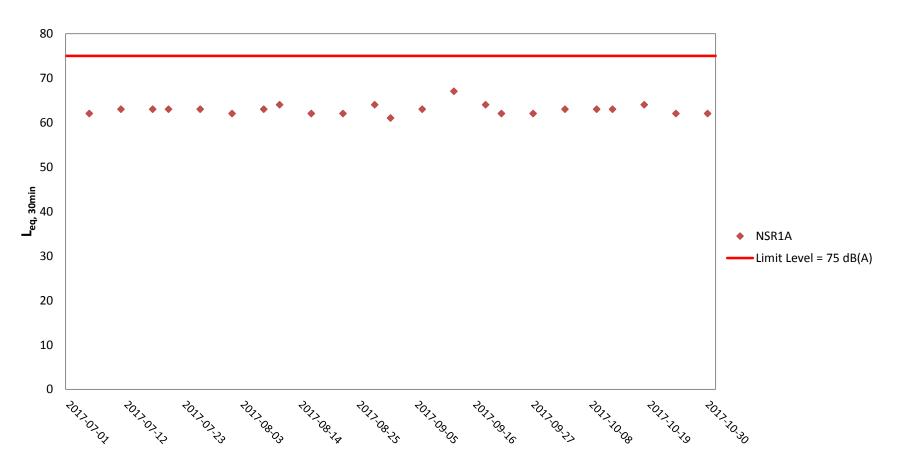

Noise Monitoring Results at NSR 1A ( $L_{eq, 30min}$ )

Weather condition within the reporting period varied between sunny to rainy.

Major construction works undertaken within the reporting period include Pier construction; Re-alignment of Cheung Tung Road; Road works along North Lantau Highway; Launching gantry operation; Installation of pier head and deck segments; and Slope work of Viaducts A, B & C.
