
Project	Works	Date (yyyy-mm-dd)	Station	Weather Condition	Time (hh:mm, 24hour)	Noise Level for 30-min, dB(A)			Limit Level	Wind Speed		Calibrator
						Leq	L10	L90	dB(A)	(m/s)	Noise Meter Model/ID	Model/ID
TMCLKL	HY/2012/07	2018-02-06	NSR1A	Sunny	10:06	63	64	59	75	0.2	RION NL52	RION NC73
											(S/N 01010406)	(S/N 10486660)
TMCLKL	HY/2012/07	2018-02-12	NSR1A	Sunny	10:05	63	64	59	75	0.3	RION NL52	RION NC73
											(S/N 01010406)	(S/N 10486660)
TMCLKL	HY/2012/07	2018-02-15	NSR1A	Cloudy	10:07	63	63	58	75	0.3	RION NL52	RION NC73
											(S/N 01010406)	(S/N 10486660)
TMCLKL	HY/2012/07	2018-02-21	NSR1A	Cloudy	9:20	62	63	59	75	0.9	RION NL52	RION NC73
											(S/N 01010406)	(S/N 10486660)
TMCLKL	HY/2012/07	2018-02-27	NSR1A	Cloudy	9:31	64	66	60	75	0.5	RION NL52	RION NC73
											(S/N 01010406)	(S/N 10486660)
					Min.	62						
					Max.	64						
					Average	63						

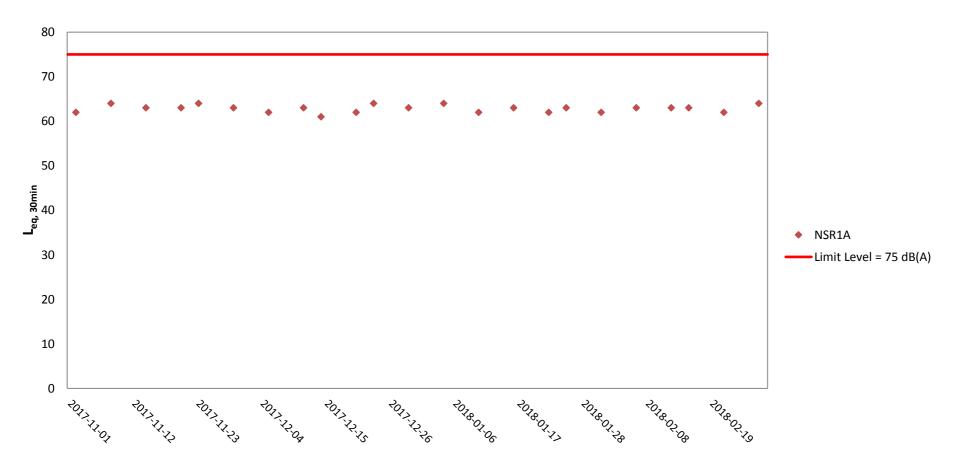

Noise Monitoring Results at NSR 1A ($L_{eq, 30min}$)

Weather condition within the reporting period varied between sunny to rainy.

Major construction works undertaken within the reporting period include Pier construction; Re-alignment of Cheung Tung Road; Road works along North Lantau Highway; Installation of pier head and deck segments; Asphalt paving; Sign gantries construction; Parapet installation; and Slope work of Viaducts A, B,C & D.
