

Appendix N1 Cumulative Statistics on Exceedances

		Total No. recorded in this reporting month	Total No. recorded since project commencement
1-Hr TSP	Action	0	0
	Limit	1	1
24-Hr TSP	Action	0	2
	Limit	0	0
Noise	Action	0	0
	Limit	0	0
Water Quality	Action	1	136
	Limit	0	15
Impact Dolphin Monitoring	Action	2	11
	Limit	0	11

Appendix N2 Cumulative Statistics on Complaints, Notifications of Summons and Successful Prosecutions

Reporting Period	Cumulative Statistics		
	Complaints	Notifications of Summons	Successful Prosecutions
This Reporting Month (February 2018)	0	0	0
Total No. received since project commencement	12	0	0

Email
message

Environmental
Resources
Management

To Ramboll Hong Kong, Limited (ENPO)

From ERM- Hong Kong, Limited

Ref/Project number Contract No. HY/2012/07
Tuen Mun – Chek Lap Kok Link – Southern
Connection Viaduct Section

Subject Notification of Exceedance for Air Quality Impact
Monitoring

Date 06 March 2018

16/F Berkshire House,
25 Westlands Road
Quarry Bay, Hong Kong
Telephone: (852) 2271 3113
Facsimile: (852) 2723 5660
E-mail: jovy.tam@erm.com



Dear Sir/ Madam,

Please find attached the Notification of Exceedance (NOE) of the following
Log no.:

Limit Level Exceedance
0215660_6 February 2018_1hrTSP_Station ASR9

A total of one (1) exceedance was recorded on 06 February 2018.

Regards,



Mr Jovy Tam
Environmental Team Leader

CONFIDENTIALITY NOTICE

This facsimile transmission is intended only for the use of the addressee and is confidential. If you are not the addressee it may be unlawful for you to read, copy, distribute, disclose or otherwise use the information in this facsimile. If you are not the intended recipient, please telephone or fax us immediately.



ERM-Hong Kong, Limited

CONTRACT NO. HY/2012/07

TUEN MUN – CHEK LAP KOK LINK –
SOUTHERN CONNECTION VIADUCT SECTION

Air Quality Impact Monitoring

Notification of Exceedance

Log No.	<p><u>Limit Level Exceedance</u> 0215660_6 February 2018_1hrTSP_Station ASR9</p> <p>[Total No. of Exceedances = 1]</p>	
Date	<p>6 February 2018 (Measured) 20 February 2018 (Results received by ERM)</p>	
Monitoring Station	ASR8A, ASR9	
Parameter(s) with Exceedance(s)	1-hr TSP	
Action Levels	1-hr TSP ($\mu\text{g}/\text{m}^3$)	ASR8A = 394 ASR9 = 393
Limit Levels	1-hr TSP ($\mu\text{g}/\text{m}^3$)	ASR8A and ASR9 = 500
Measured Levels	<p><u>Limit Level Exceedance</u> 1. 1-hr TSP at ASR9 ($680 \mu\text{g}/\text{m}^3$) during 09:42a.m.-10:42a.m.</p>	
Works Undertaken (at the time of monitoring event)	<p>Works undertaken under this Contract on 06 February 2018 included:</p> <ul style="list-style-type: none"> • Parapet installation at Viaduct B and Viaduct C, and • Slope work at Viaduct D 	
Possible Reason for Action or Limit Level Exceedance(s)	<p>The exceedance is unlikely to be due to the Project, in view of the following:</p> <ul style="list-style-type: none"> • According to the work record provided by the Contractor, major land-based works on 6 February 2018 included parapet installation at Viaduct B and Viaduct C and slope work at Viaduct D (see <i>Figure 1</i>). During the period of land-based construction works, the Contractor has implemented the required mitigation measures as per the EP, approved EIA and Updated EM&A Manual (e.g. water spraying on exposed soil within the Project site and associated works areas; exposed soil covered by tarpaulin sheets). • In addition, with reference to the recorded wind direction (ranged between 167° and 205°, blowing from a southerly direction) and low wind speed (ranged from 0.02 to 0.03 m/s) during the period of the observed 1-hr TSP exceedance, it is considered that the observed exceedance should not be due to the dust, if any, generated by the construction activities under this Contract. • Apart from one 1hr-TSP (09:42a.m.-10:42a.m.) at ASR9, other 1-hr TSP levels and all 24-hr TSP at ASR8A and ASR9 were in compliance with the Action and Limit Levels on the same day. • According to SOR & ET joint inspection on air quality monitoring on 6 February 2018, no particular observation was reported regarding the sampling procedures and monitoring area (see <i>Annex A</i>). • According to ET's weekly inspection on 7 and 14 February 2018, no particular finding was observed. Dust mitigation measures were observed at the site areas (see <i>Annex B</i>). <p>Based on the above, the exceedance is unlikely to be due to the Project.</p>	
Actions Taken / To Be Taken	<p>The Contractor has been reminded to ensure all dust suppression measures are implemented at the site area including water spraying at unpaved road/stockpiles and use of tarpaulin for stockpiles covering. The ET will monitor for future trends in exceedances.</p>	
Remarks	<p>The monitoring results and meteorological information on 6 February 2018 and locations of air quality monitoring stations are attached.</p>	

Results of Air Quality Monitoring

Project	Works	Date (yyyy-mm-dd)	Station	Time (hh:mm, 24hour)	Parameter	Results	Unit
TMCLKL	HY/2012/07	2018-02-06	ASR8A	8:30	1-hr TSP	183	ug/m3
TMCLKL	HY/2012/07	2018-02-06	ASR8A	9:32	1-hr TSP	115	ug/m3
TMCLKL	HY/2012/07	2018-02-06	ASR8A	10:45	1-hr TSP	96	ug/m3
TMCLKL	HY/2012/07	2018-02-06	ASR8A	11:47	24-hr TSP	76	ug/m3
TMCLKL	HY/2012/07	2018-02-06	ASR9	8:40	1-hr TSP	130	ug/m3
TMCLKL	HY/2012/07	2018-02-06	ASR9	9:42	1-hr TSP	680	ug/m3
TMCLKL	HY/2012/07	2018-02-06	ASR9	10:56	1-hr TSP	103	ug/m3
TMCLKL	HY/2012/07	2018-02-06	ASR9	11:58	24-hr TSP	100	ug/m3

Note: Indicates Exceedance of Action Level
Indicates Exceedance of Limit Level

Meteorological Information

Date	Time (HH)	Wind speed (m/s)	Wind direction (deg)
2018/2/6	0	0.02	155
2018/2/6	1	0.04	154
2018/2/6	2	0.02	139
2018/2/6	3	0.06	175
2018/2/6	4	0.02	174
2018/2/6	5	0.03	183
2018/2/6	6	0.03	185
2018/2/6	7	0.03	189
2018/2/6	8	0.08	129
2018/2/6	9	0.03	167
2018/2/6	10	0.03	205
2018/2/6	11	0.02	201
2018/2/6	12	0.03	199
2018/2/6	13	0.21	148
2018/2/6	14	0.87	128
2018/2/6	15	0.20	206
2018/2/6	16	0.09	189
2018/2/6	17	0.35	153
2018/2/6	18	0.43	183
2018/2/6	19	0.18	177
2018/2/6	20	0.17	179
2018/2/6	21	0.10	152
2018/2/6	22	0.17	153
2018/2/6	23	0.36	147

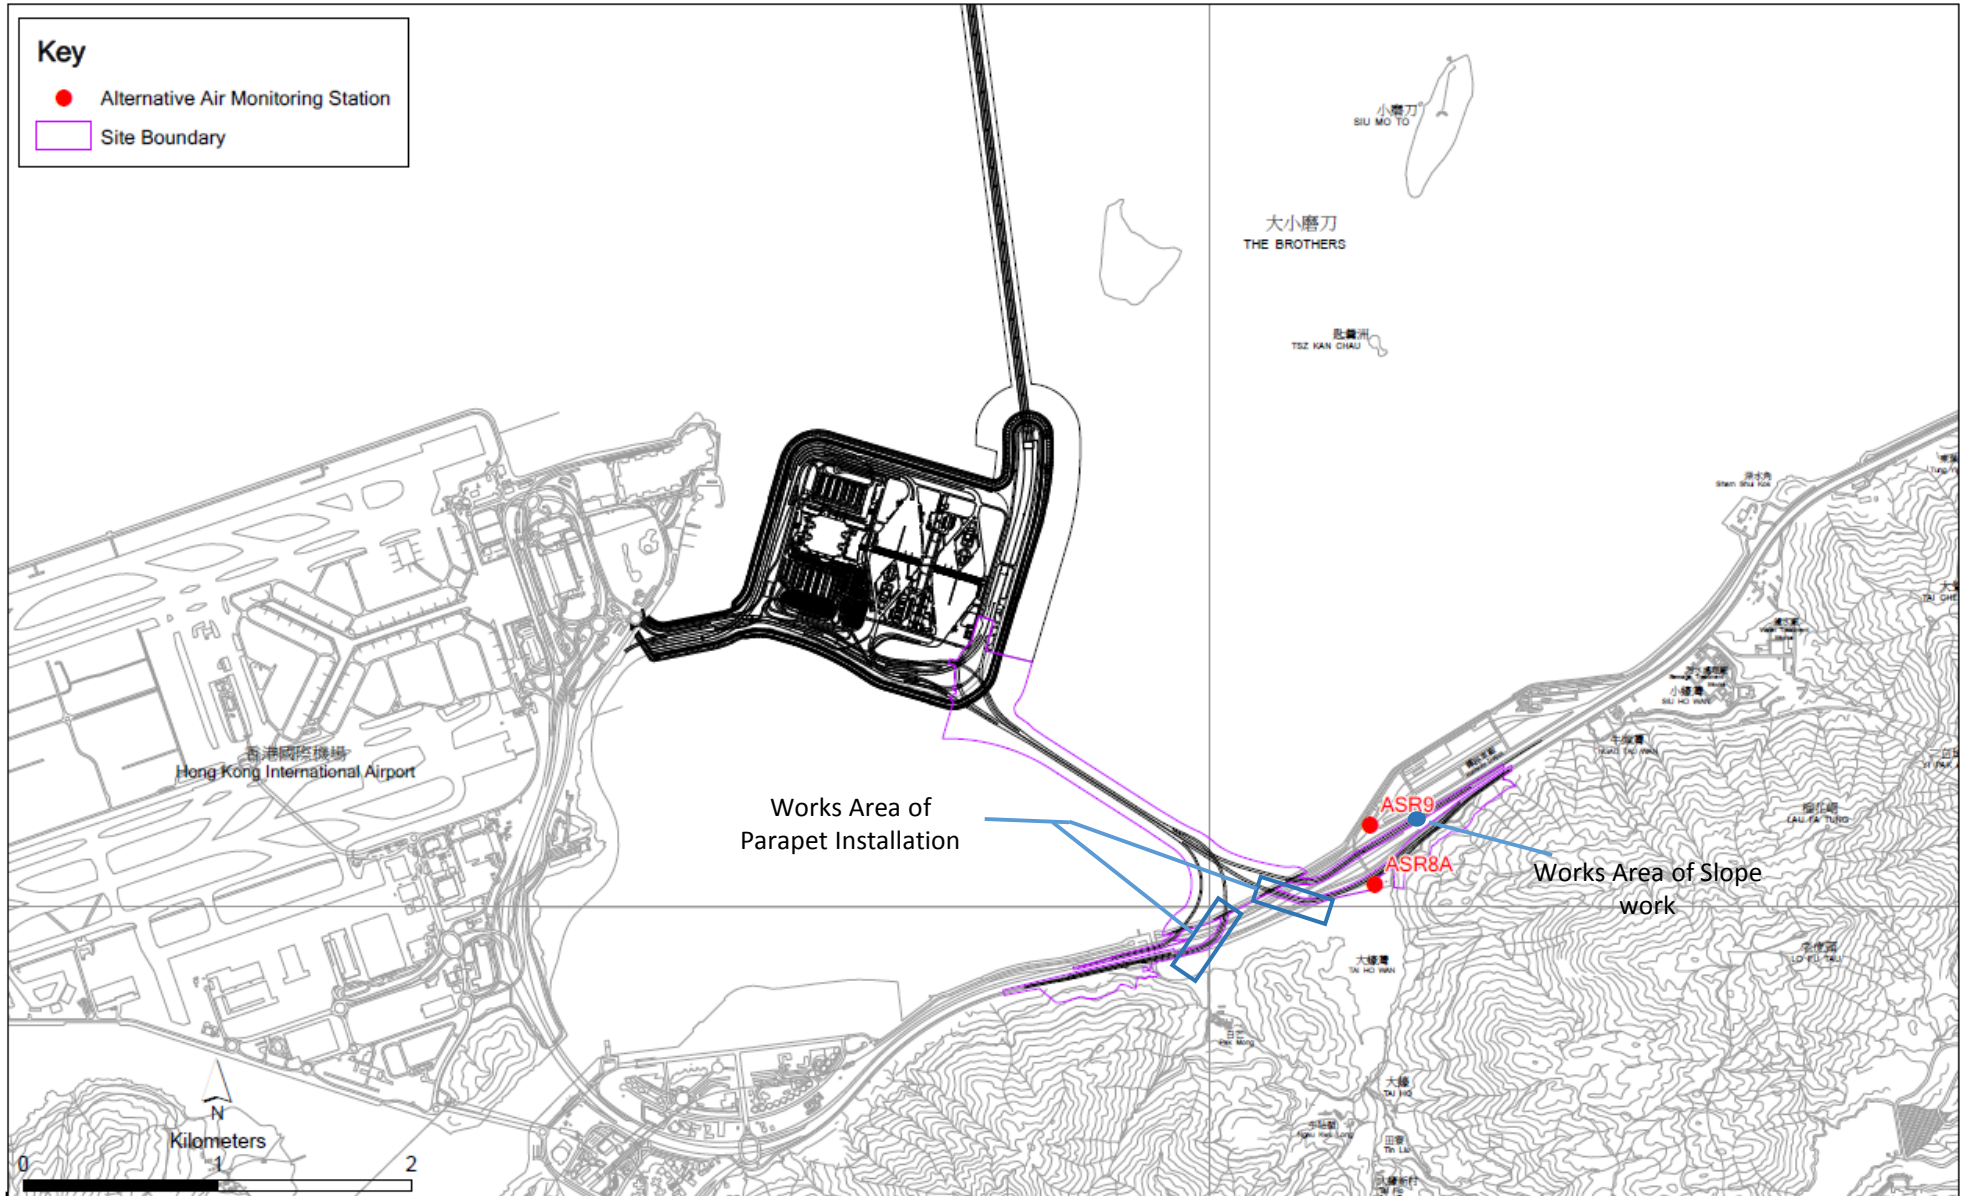


Figure 1

Locations of Air Quality Monitoring Stations

Annex A

Photo of AQM Inspection at
ASR9 on 6 February 2018

Photo 1 - ASR9 on 06 February 2018



Annex B

Photos of Site Inspection on
7 and 14 February 2018

Photo 1 - No debris or other materials were burnt on the works area (7 February 2018).



Photo 2 - Areas of exposed soil were covered by tarpaulin (14 February 2018).



Photo 3 - Watering programme was maintained on unpaved areas (14 February 2018).



Email
message

Environmental
Resources
Management

To Ramboll Hong Kong, Limited (ENPO)

From ERM- Hong Kong, Limited

Ref/Project number Contract No. HY/2012/07
Tuen Mun – Chek Lap Kok Link – Southern
Connection Viaduct Section

Subject Notification of Exceedance for Marine Water
Quality Impact Monitoring

Date 01 March 2018

16/F Berkshire House,
25 Westlands Road
Quarry Bay, Hong Kong
Telephone: (852) 2271 3113
Facsimile: (852) 2723 5660
E-mail: jovy.tam@erm.com



ERM

Dear Sir/ Madam,

Please find attached the Notification of Exceedance (NOE) of the following
Log no.:

Action Level Exceedance

0215660_21 February 2018_Depth-averaged SS_F_Station SR4a

A total of one (1) exceedance was recorded on 21 February 2018.

Regards,

A handwritten signature in black ink, appearing to be 'Jovy Tam'.

Mr Jovy Tam
Environmental Team Leader

CONFIDENTIALITY NOTICE

This facsimile transmission is intended only for the use of the addressee and is confidential. If you are not the addressee it may be unlawful for you to read, copy, distribute, disclose or otherwise use the information in this facsimile. If you are not the intended recipient, please telephone or fax us immediately.



ERM-Hong Kong, Limited

CONTRACT NO. HY/2012/07

TUEN MUN - CHEK LAP KOK LINK -
SOUTHERN CONNECTION VIADUCT SECTION

Marine Water Quality Impact Monitoring

Notification of Exceedance

Log No.	<p><u>Action Level Exceedance</u> 0215660_21 February 2018_Depth-averaged SS_F_Station SR4a</p> <p>[Total No. of Exceedances = 1]</p>	
Date	<p>21 February 2018 (Measured) 22 February 2018 (<i>In situ</i> results received by ERM) 01 March 2018 (Laboratory results received by ERM)</p>	
Monitoring Station	<p>CS(Mf)5, SR4a, SR4, IS8, IS(Mf)16, IS(Mf)9, CS(Mf)3(N)</p>	
Parameter(s) with Exceedance(s)	<p>Depth-averaged Suspended Solids (SS)</p>	
Action Levels for SS	<p>SS</p>	<p>120% of upstream control station at the same tide of the same day and 95%-ile of baseline data (i.e., 23.5 mg/L).</p>
Limit Levels for SS	<p>SS</p>	<p>130% of upstream control station at the same tide of the same day and 99%-ile of baseline data. (i.e., 34.4 mg/L)</p>
Measured Levels	<p><u>Action Level Exceedance</u> 1. Mid-flood at SR4a (Depth-averaged SS = 24.2mg/L).</p>	
Works Undertaken (at the time of monitoring event)	<p>No major marine works was undertaken under this Contract on 21 February 2018.</p>	
Possible Reason for Action or Limit Level Exceedance(s)	<p>The exceedances of depth-averaged SS are unlikely to be due to the Project, in view of the following:</p> <ul style="list-style-type: none"> • No marine works was undertaken under this Contract on 21 February 2018. • Apart from SR4a, depth-averaged SS levels at all other sensitive receiver stations and impact stations were in compliance with the Action and Limit Levels during both mid-flood and mid-ebb tides on the same day. • Depth-averaged Turbidity levels and average DO levels at all stations were in compliance with the Action and Limit Levels during both mid-ebb and mid-flood tides on the same day. • According to ET's site inspection on 21 February 2018, no particular finding was observed at SR4a (see <i>site photo record</i>). 	
Actions Taken/ To Be Taken	<p>No immediate action is considered necessary. The ET will monitor for future trends in exceedances.</p>	
Remarks	<p>The monitoring results on 21 February 2018 and locations of water quality monitoring stations are attached. Site photo record on 21 February 2018 is attached.</p>	

Project	Works	Date (yyyy-mm-dd)	Tide	Station	Start Time	Level	Replicate	Temperature (°C)	pH	Salinity (ppt)	DO (mg/L)	Average DO (mg/L)	Turbidity (NTU)	Depth-Averaged Turbidity	SS (mg/L)	Depth-Averaged SS
TMCLKL	HY/2012/07	2018-02-21	Mid-Ebb	CS(Mf)5	16:38	Surface	1	17.3	8.2	30.1	9.0	8.9	7.1	7.1	5.9	5.9
TMCLKL	HY/2012/07	2018-02-21	Mid-Ebb	CS(Mf)5	16:38	Surface	2	17.3	8.2	30.1	9.0		7.1		5.2	
TMCLKL	HY/2012/07	2018-02-21	Mid-Ebb	CS(Mf)5	16:38	Middle	1	17.2	8.2	30.2	8.7		7.4		5.3	
TMCLKL	HY/2012/07	2018-02-21	Mid-Ebb	CS(Mf)5	16:38	Middle	2	17.2	8.1	30.2	8.9		7.2		6.9	
TMCLKL	HY/2012/07	2018-02-21	Mid-Ebb	CS(Mf)5	16:38	Bottom	1	17.0	8.2	30.5	8.5		6.9		5.9	
TMCLKL	HY/2012/07	2018-02-21	Mid-Ebb	CS(Mf)5	16:38	Bottom	2	17.0	8.1	30.5	8.5	8.5	6.9	5.9		
TMCLKL	HY/2012/07	2018-02-21	Mid-Ebb	CS(Mf)3(N)	15:13	Surface	1	17.4	8.2	29.0	9.1	9.2	2.7	3.6	7.0	7.4
TMCLKL	HY/2012/07	2018-02-21	Mid-Ebb	CS(Mf)3(N)	15:13	Surface	2	17.3	8.2	29.0	9.2		2.5		8.1	
TMCLKL	HY/2012/07	2018-02-21	Mid-Ebb	CS(Mf)3(N)	15:13	Middle	1	17.2	8.2	30.1	9.1		2.7		6.7	
TMCLKL	HY/2012/07	2018-02-21	Mid-Ebb	CS(Mf)3(N)	15:13	Middle	2	17.1	8.2	30.1	9.2		2.5		7.0	
TMCLKL	HY/2012/07	2018-02-21	Mid-Ebb	CS(Mf)3(N)	15:13	Bottom	1	17.1	8.2	30.6	9.0		9.0		5.8	
TMCLKL	HY/2012/07	2018-02-21	Mid-Ebb	CS(Mf)3(N)	15:13	Bottom	2	17.0	8.2	30.6	9.0	9.0	5.5	7.8		
TMCLKL	HY/2012/07	2018-02-21	Mid-Ebb	IS(Mf)16	16:11	Surface	1	17.5	8.2	30.0	9.4	9.4	3.7	4.7	7.4	7.3
TMCLKL	HY/2012/07	2018-02-21	Mid-Ebb	IS(Mf)16	16:11	Surface	2	17.5	8.2	30.0	9.4		3.7		7.4	
TMCLKL	HY/2012/07	2018-02-21	Mid-Ebb	IS(Mf)16		Middle	1									
TMCLKL	HY/2012/07	2018-02-21	Mid-Ebb	IS(Mf)16		Middle	2									
TMCLKL	HY/2012/07	2018-02-21	Mid-Ebb	IS(Mf)16	16:11	Bottom	1	17.7	8.2	30.2	9.2		9.2		5.7	
TMCLKL	HY/2012/07	2018-02-21	Mid-Ebb	IS(Mf)16	16:11	Bottom	2	17.7	8.2	30.2	9.2	9.2	5.7	7.0		
TMCLKL	HY/2012/07	2018-02-21	Mid-Ebb	SR4a	15:59	Surface	1	17.4	8.2	30.0	9.0	9.0	10.7	10.8	8.6	8.5
TMCLKL	HY/2012/07	2018-02-21	Mid-Ebb	SR4a	15:59	Surface	2	17.4	8.2	30.0	9.0		10.7		8.2	
TMCLKL	HY/2012/07	2018-02-21	Mid-Ebb	SR4a		Middle	1									
TMCLKL	HY/2012/07	2018-02-21	Mid-Ebb	SR4a		Middle	2									
TMCLKL	HY/2012/07	2018-02-21	Mid-Ebb	SR4a	15:59	Bottom	1	17.4	8.2	30.0	8.9		8.9		11.0	
TMCLKL	HY/2012/07	2018-02-21	Mid-Ebb	SR4a	15:59	Bottom	2	17.4	8.2	30.0	8.9	8.9	10.9	9.1		
TMCLKL	HY/2012/07	2018-02-21	Mid-Ebb	SR4	15:54	Surface	1	17.6	8.2	30.1	8.9	8.9	7.0	7.1	11.1	13.4
TMCLKL	HY/2012/07	2018-02-21	Mid-Ebb	SR4	15:54	Surface	2	17.6	8.2	30.1	8.9		7.0		12.9	
TMCLKL	HY/2012/07	2018-02-21	Mid-Ebb	SR4		Middle	1									
TMCLKL	HY/2012/07	2018-02-21	Mid-Ebb	SR4		Middle	2									
TMCLKL	HY/2012/07	2018-02-21	Mid-Ebb	SR4	15:54	Bottom	1	17.6	8.2	30.1	8.9		8.9		7.4	
TMCLKL	HY/2012/07	2018-02-21	Mid-Ebb	SR4	15:54	Bottom	2	17.6	8.2	30.2	8.9	8.9	7.0	14.2		
TMCLKL	HY/2012/07	2018-02-21	Mid-Ebb	IS8	15:47	Surface	1	17.8	8.2	30.3	9.1	9.1	4.4	4.6	7.9	7.8
TMCLKL	HY/2012/07	2018-02-21	Mid-Ebb	IS8	15:47	Surface	2	17.8	8.2	30.3	9.1		4.4		7.1	
TMCLKL	HY/2012/07	2018-02-21	Mid-Ebb	IS8		Middle	1									
TMCLKL	HY/2012/07	2018-02-21	Mid-Ebb	IS8		Middle	2									
TMCLKL	HY/2012/07	2018-02-21	Mid-Ebb	IS8	15:47	Bottom	1	17.8	8.2	30.3	9.1		9.1		4.7	
TMCLKL	HY/2012/07	2018-02-21	Mid-Ebb	IS8	15:47	Bottom	2	17.8	8.3	30.3	9.1	9.1	4.7	8.1		
TMCLKL	HY/2012/07	2018-02-21	Mid-Ebb	IS(Mf)9	15:39	Surface	1	17.7	8.2	30.2	9.2	9.2	5.1	5.0	8.8	10.1
TMCLKL	HY/2012/07	2018-02-21	Mid-Ebb	IS(Mf)9	15:39	Surface	2	17.7	8.3	30.2	9.2		5.0		7.5	
TMCLKL	HY/2012/07	2018-02-21	Mid-Ebb	IS(Mf)9		Middle	1									
TMCLKL	HY/2012/07	2018-02-21	Mid-Ebb	IS(Mf)9		Middle	2									
TMCLKL	HY/2012/07	2018-02-21	Mid-Ebb	IS(Mf)9	15:39	Bottom	1	17.7	8.2	30.2	9.2		9.2		4.9	
TMCLKL	HY/2012/07	2018-02-21	Mid-Ebb	IS(Mf)9	15:39	Bottom	2	17.7	8.3	30.2	9.2	9.2	4.9	12.9		

Project	Works	Date (yyyy-mm-dd)	Tide	Station	Start Time	Level	Replicate	Temperature (°C)	pH	Salinity (ppt)	DO (mg/L)	Average DO (mg/L)	Turbidity (NTU)	Depth-Averaged Turbidity	SS (mg/L)	Depth-Averaged SS
TMCLKL	HY/2012/07	2018-02-21	Mid-Flood	CS(Mf)5	9:12	Surface	1	17.3	8.2	29.8	8.9	8.9	2.9	5.3	7.2	6.2
TMCLKL	HY/2012/07	2018-02-21	Mid-Flood	CS(Mf)5	9:12	Surface	2	17.3	8.2	29.8	8.9		2.7		6.6	
TMCLKL	HY/2012/07	2018-02-21	Mid-Flood	CS(Mf)5	9:12	Middle	1	17.3	8.2	29.9	8.8		3.4		5.8	
TMCLKL	HY/2012/07	2018-02-21	Mid-Flood	CS(Mf)5	9:12	Middle	2	17.3	8.2	29.9	8.8	8.6	3.2	5.3	5.9	6.2
TMCLKL	HY/2012/07	2018-02-21	Mid-Flood	CS(Mf)5	9:12	Bottom	1	17.1	8.2	30.3	8.5		9.8		5.7	
TMCLKL	HY/2012/07	2018-02-21	Mid-Flood	CS(Mf)5	9:12	Bottom	2	17.1	8.2	30.3	8.6	8.7	9.6	3.6	6.2	6.7
TMCLKL	HY/2012/07	2018-02-21	Mid-Flood	CS(Mf)3(N)	11:07	Surface	1	17.5	8.2	29.2	8.7		2.9		6.9	
TMCLKL	HY/2012/07	2018-02-21	Mid-Flood	CS(Mf)3(N)	11:07	Surface	2	17.4	8.2	29.2	8.7		3.0		6.1	
TMCLKL	HY/2012/07	2018-02-21	Mid-Flood	CS(Mf)3(N)	11:07	Middle	1	17.5	8.2	29.2	8.7	8.7	3.2	3.6	6.8	6.7
TMCLKL	HY/2012/07	2018-02-21	Mid-Flood	CS(Mf)3(N)	11:07	Middle	2	17.3	8.2	29.2	8.7		3.1		5.8	
TMCLKL	HY/2012/07	2018-02-21	Mid-Flood	CS(Mf)3(N)	11:07	Bottom	1	17.5	8.2	29.3	8.7	8.7	4.6	3.6	7.3	6.7
TMCLKL	HY/2012/07	2018-02-21	Mid-Flood	CS(Mf)3(N)	11:07	Bottom	2	17.3	8.2	29.3	8.7		4.5		7.0	
TMCLKL	HY/2012/07	2018-02-21	Mid-Flood	IS(Mf)16	9:39	Surface	1	17.4	8.2	30.1	8.8	8.9	4.8	4.9	5.2	8.1
TMCLKL	HY/2012/07	2018-02-21	Mid-Flood	IS(Mf)16	9:39	Surface	2	17.4	8.2	30.1	8.9		4.8		6.9	
TMCLKL	HY/2012/07	2018-02-21	Mid-Flood	IS(Mf)16		Middle	1									
TMCLKL	HY/2012/07	2018-02-21	Mid-Flood	IS(Mf)16		Middle	2					8.8		4.9		8.1
TMCLKL	HY/2012/07	2018-02-21	Mid-Flood	IS(Mf)16	9:39	Bottom	1	17.5	8.2	30.2	8.8		5.0		10.3	
TMCLKL	HY/2012/07	2018-02-21	Mid-Flood	IS(Mf)16	9:39	Bottom	2	17.5	8.2	30.2	8.8	8.7	5.1	14.8	10.0	24.2
TMCLKL	HY/2012/07	2018-02-21	Mid-Flood	SR4a	9:48	Surface	1	17.3	8.2	30.0	8.7		15.8		23.4	
TMCLKL	HY/2012/07	2018-02-21	Mid-Flood	SR4a	9:48	Surface	2	17.3	8.2	30.0	8.7		15.5		23.0	
TMCLKL	HY/2012/07	2018-02-21	Mid-Flood	SR4a		Middle	1					8.7		14.8		24.2
TMCLKL	HY/2012/07	2018-02-21	Mid-Flood	SR4a		Middle	2									
TMCLKL	HY/2012/07	2018-02-21	Mid-Flood	SR4a	9:48	Bottom	1	17.3	8.2	30.0	8.7	8.7	14.1	14.8	24.7	24.2
TMCLKL	HY/2012/07	2018-02-21	Mid-Flood	SR4a	9:48	Bottom	2	17.3	8.2	30.0	8.7		13.8		25.7	
TMCLKL	HY/2012/07	2018-02-21	Mid-Flood	SR4	9:52	Surface	1	17.4	8.2	30.0	8.8	8.8	4.3	4.5	6.0	4.9
TMCLKL	HY/2012/07	2018-02-21	Mid-Flood	SR4	9:52	Surface	2	17.4	8.2	30.0	8.8		4.6		4.7	
TMCLKL	HY/2012/07	2018-02-21	Mid-Flood	SR4		Middle	1									
TMCLKL	HY/2012/07	2018-02-21	Mid-Flood	SR4		Middle	2					8.8		4.5		4.9
TMCLKL	HY/2012/07	2018-02-21	Mid-Flood	SR4	9:52	Bottom	1	17.4	8.2	30.0	8.8		4.3		4.7	
TMCLKL	HY/2012/07	2018-02-21	Mid-Flood	SR4	9:52	Bottom	2	17.4	8.2	30.0	8.8	9.0	4.7	7.6	4.3	12.4
TMCLKL	HY/2012/07	2018-02-21	Mid-Flood	IS8	10:06	Surface	1	17.5	8.2	30.1	9.0		7.3		12.2	
TMCLKL	HY/2012/07	2018-02-21	Mid-Flood	IS8	10:06	Surface	2	17.5	8.2	30.1	9.0		7.3		11.9	
TMCLKL	HY/2012/07	2018-02-21	Mid-Flood	IS8		Middle	1					9.0		7.6		12.4
TMCLKL	HY/2012/07	2018-02-21	Mid-Flood	IS8		Middle	2									
TMCLKL	HY/2012/07	2018-02-21	Mid-Flood	IS8	10:06	Bottom	1	17.5	8.2	30.1	9.0	9.0	7.9	7.6	13.2	12.4
TMCLKL	HY/2012/07	2018-02-21	Mid-Flood	IS8	10:06	Bottom	2	17.4	8.2	30.0	9.0		8.0		12.2	
TMCLKL	HY/2012/07	2018-02-21	Mid-Flood	IS(Mf)9	10:14	Surface	1	17.6	8.2	30.2	9.0	9.1	5.3	5.2	5.4	6.3
TMCLKL	HY/2012/07	2018-02-21	Mid-Flood	IS(Mf)9	10:14	Surface	2	17.6	8.2	30.2	9.1		4.9		6.4	
TMCLKL	HY/2012/07	2018-02-21	Mid-Flood	IS(Mf)9		Middle	1									
TMCLKL	HY/2012/07	2018-02-21	Mid-Flood	IS(Mf)9		Middle	2					9.1		5.2		6.3
TMCLKL	HY/2012/07	2018-02-21	Mid-Flood	IS(Mf)9	10:14	Bottom	1	17.6	8.2	30.2	9.0		5.3		6.9	
TMCLKL	HY/2012/07	2018-02-21	Mid-Flood	IS(Mf)9	10:14	Bottom	2	17.6	8.2	30.2	9.1	9.1	5.2	5.2	6.3	

Note: Indicates Exceedance of Action Level
Indicates Exceedance of Limit Level

Photo 1 - Mid-Flood at SR4a on 21 February 2018

