

1-hour TSP Monitoring Results at Air Quality Monitoring Station ASR8A

Project	Works	Date(yyyy-mm-dd)	Station	Time (hh:mm, 24hour)	Parameter	Results (ug/m3)	Action Level (ug/m3)	Limit Level (ug/m3)		
TMCLKL	HY/2012/07	2018-03-05	ASR8A	8:10	1-hr TSP	44	394	500		
TMCLKL	HY/2012/07	2018-03-05	ASR8A	9:12	1-hr TSP	13				
TMCLKL	HY/2012/07	2018-03-05	ASR8A	10:14	1-hr TSP	13				
TMCLKL	HY/2012/07	2018-03-08	ASR8A	8:20	1-hr TSP	36				
TMCLKL	HY/2012/07	2018-03-08	ASR8A	9:22	1-hr TSP	39				
TMCLKL	HY/2012/07	2018-03-08	ASR8A	10:44	1-hr TSP	25				
TMCLKL	HY/2012/07	2018-03-14	ASR8A	8:05	1-hr TSP	24				
TMCLKL	HY/2012/07	2018-03-14	ASR8A	9:07	1-hr TSP	43				
TMCLKL	HY/2012/07	2018-03-14	ASR8A	10:10	1-hr TSP	28				
TMCLKL	HY/2012/07	2018-03-20	ASR8A	8:00	1-hr TSP	77				
TMCLKL	HY/2012/07	2018-03-20	ASR8A	9:02	1-hr TSP	91				
TMCLKL	HY/2012/07	2018-03-20	ASR8A	10:08	1-hr TSP	88				
TMCLKL	HY/2012/07	2018-03-26	ASR8A	8:00	1-hr TSP	137				
TMCLKL	HY/2012/07	2018-03-26	ASR8A	9:02	1-hr TSP	108				
TMCLKL	HY/2012/07	2018-03-26	ASR8A	10:05	1-hr TSP	101				
TMCLKL	HY/2012/07	2018-03-29	ASR8A	8:40	1-hr TSP	96				
TMCLKL	HY/2012/07	2018-03-29	ASR8A	9:42	1-hr TSP	56				
TMCLKL	HY/2012/07	2018-03-29	ASR8A	10:50	1-hr TSP	95				
				Average		62				
				Min.		13				
				Max.		137				

1-hour TSP Monitoring Results at Air Quality Monitoring Station ASR9



Project	Works	Date(yyyy-mm-dd)	Station	Time (hh:mm, 24hour)	Parameter	Results (ug/m3)	Action Level (ug/m3)	Limit Level (ug/m3)		
TMCLKL	HY/2012/07	2018-03-05	ASR9	8:21	1-hr TSP	261	393	500		
TMCLKL	HY/2012/07	2018-03-05	ASR9	9:23	1-hr TSP	165				
TMCLKL	HY/2012/07	2018-03-05	ASR9	10:25	1-hr TSP	157				
TMCLKL	HY/2012/07	2018-03-08	ASR9	8:30	1-hr TSP	86				
TMCLKL	HY/2012/07	2018-03-08	ASR9	9:32	1-hr TSP	28				
TMCLKL	HY/2012/07	2018-03-08	ASR9	10:55	1-hr TSP	20				
TMCLKL	HY/2012/07	2018-03-14	ASR9	8:15	1-hr TSP	83				
TMCLKL	HY/2012/07	2018-03-14	ASR9	9:17	1-hr TSP	52				
TMCLKL	HY/2012/07	2018-03-14	ASR9	10:22	1-hr TSP	40				
TMCLKL	HY/2012/07	2018-03-20	ASR9	8:10	1-hr TSP	179				
TMCLKL	HY/2012/07	2018-03-20	ASR9	9:12	1-hr TSP	70				
TMCLKL	HY/2012/07	2018-03-20	ASR9	10:20	1-hr TSP	86				
TMCLKL	HY/2012/07	2018-03-26	ASR9	8:10	1-hr TSP	169				
TMCLKL	HY/2012/07	2018-03-26	ASR9	9:12	1-hr TSP	85				
TMCLKL	HY/2012/07	2018-03-26	ASR9	10:16	1-hr TSP	90				
TMCLKL	HY/2012/07	2018-03-29	ASR9	8:32	1-hr TSP	129				
TMCLKL	HY/2012/07	2018-03-29	ASR9	9:54	1-hr TSP	88				
TMCLKL	HY/2012/07	2018-03-29	ASR9	11:02	1-hr TSP	147				
				Average		108				
				Min.		20				
				Max.		261				

24-hour TSP Monitoring Results at Air Quality Monitoring Station ASR8A

Project	Works	Date(yyyy-mm-dd)	Station	Time (hh:mm, 24hour)	Parameter	Results (ug/m3)	Action Level (ug/m3)	Limit Level (ug/m3)
TMCLKL	HY/2012/07	2018-03-05	ASR8A	11:16	24-hr TSP	35	178	260
TMCLKL	HY/2012/07	2018-03-08	ASR8A	11:46	24-hr TSP	43		
TMCLKL	HY/2012/07	2018-03-14	ASR8A	11:12	24-hr TSP	50		
TMCLKL	HY/2012/07	2018-03-20	ASR8A	11:10	24-hr TSP	86		
TMCLKL	HY/2012/07	2018-03-26	ASR8A	11:07	24-hr TSP	82		
TMCLKL	HY/2012/07	2018-03-29	ASR8A	11:52	24-hr TSP	48		
						Average	57	
						Min.	35	
						Max.	86	



24-hour TSP Monitoring Results at Air Quality Monitoring Station ASR9

Project	Works	Date(yyyy-mm-dd)	Station	Time (hh:mm, 24hour)	Parameter	Results (ug/m3)	Action Level (ug/m3)	Limit Level (ug/m3)
TMCLKL	HY/2012/07	2018-03-05	ASR9	11:27	24-hr TSP	57	178	260
TMCLKL	HY/2012/07	2018-03-08	ASR9	11:57	24-hr TSP	47		
TMCLKL	HY/2012/07	2018-03-14	ASR9	11:24	24-hr TSP	66		
TMCLKL	HY/2012/07	2018-03-20	ASR9	11:22	24-hr TSP	65		
TMCLKL	HY/2012/07	2018-03-26	ASR9	11:18	24-hr TSP	100		
TMCLKL	HY/2012/07	2018-03-29	ASR9	12:04	24-hr TSP	52		
						Average	65	
						Min.	47	
						Max.	100	

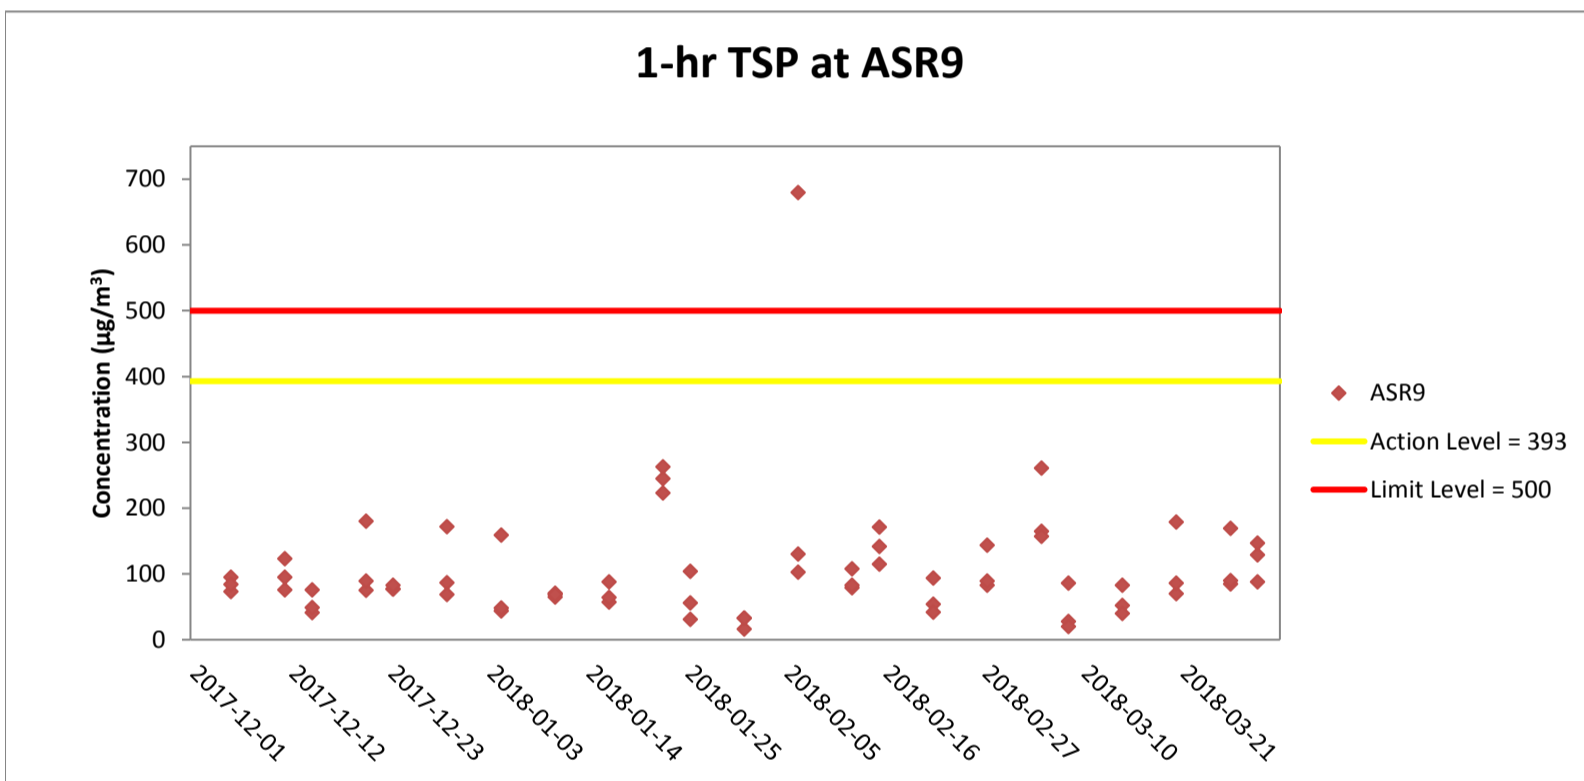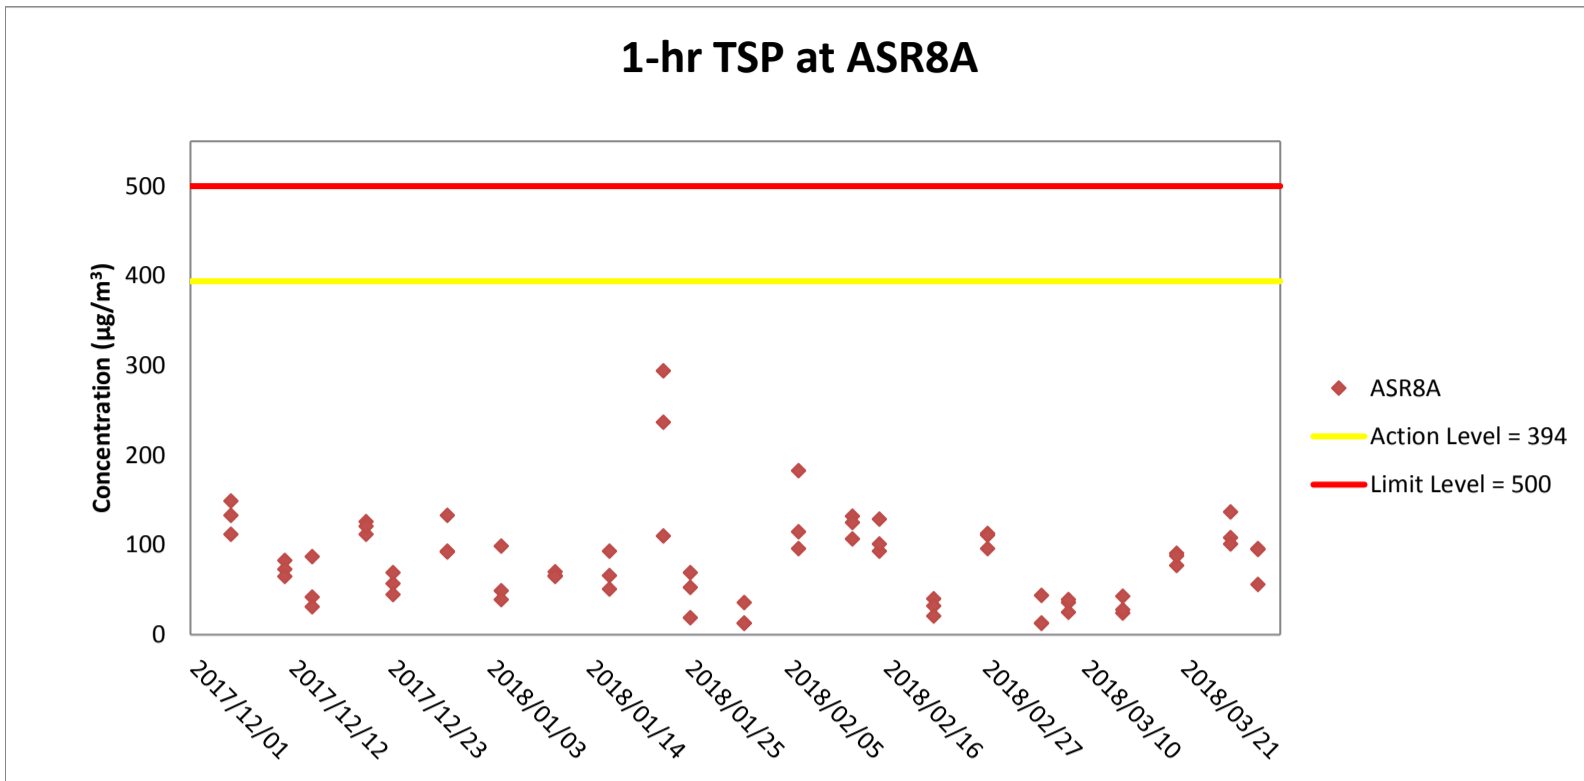

Weather condition within the reporting period varied between sunny to rainy.

Major construction works undertaken within the reporting period include Pier construction; Re-alignment of Cheung Tung Road; Road works along North Lantau Highway; Installation of pier head and deck segments; Asphalt paving; Sign gantries construction; Parapet installation; and Slope work of Viaducts A, B, C & D.

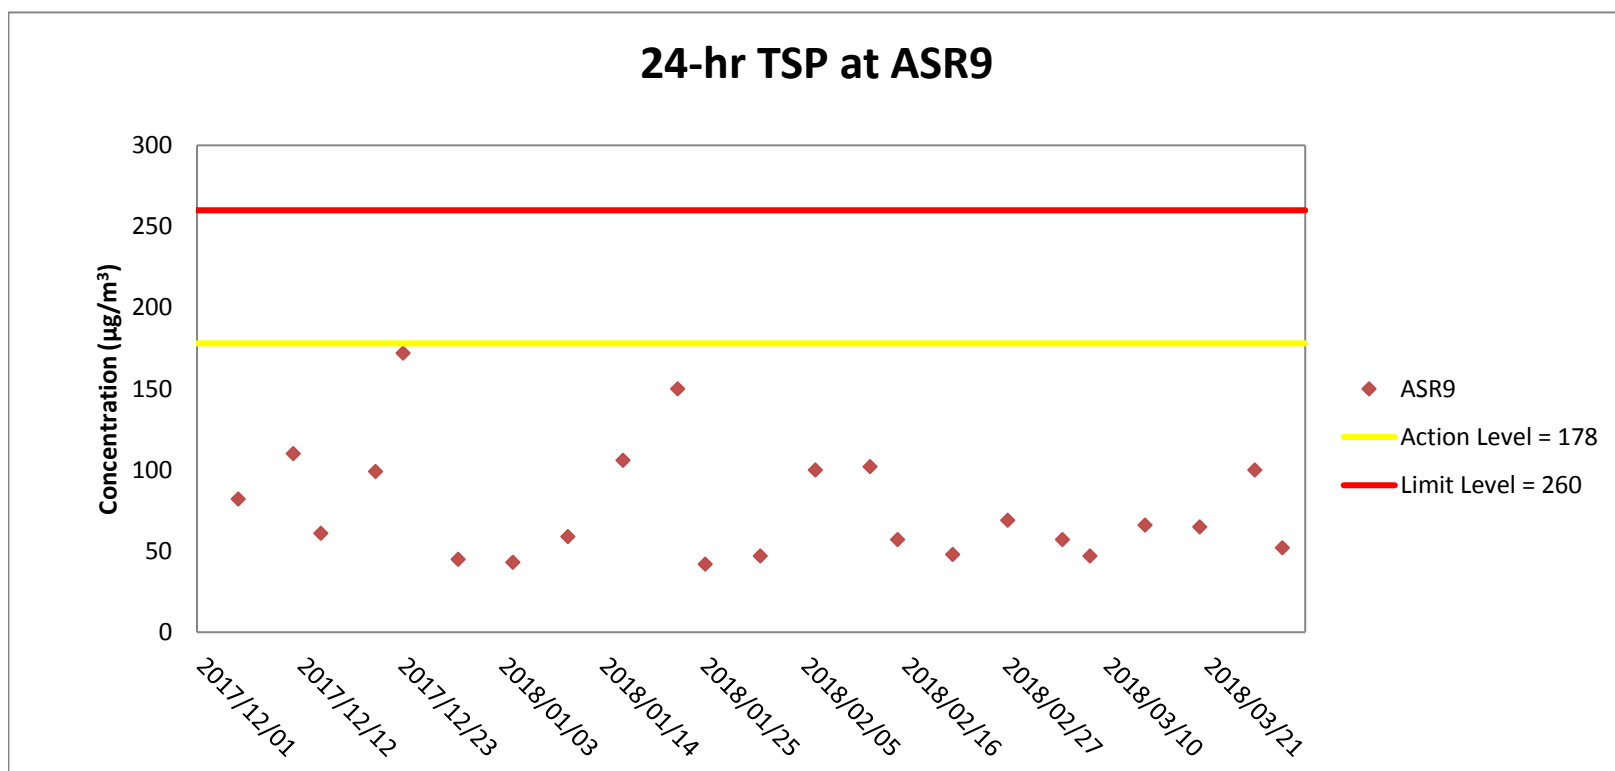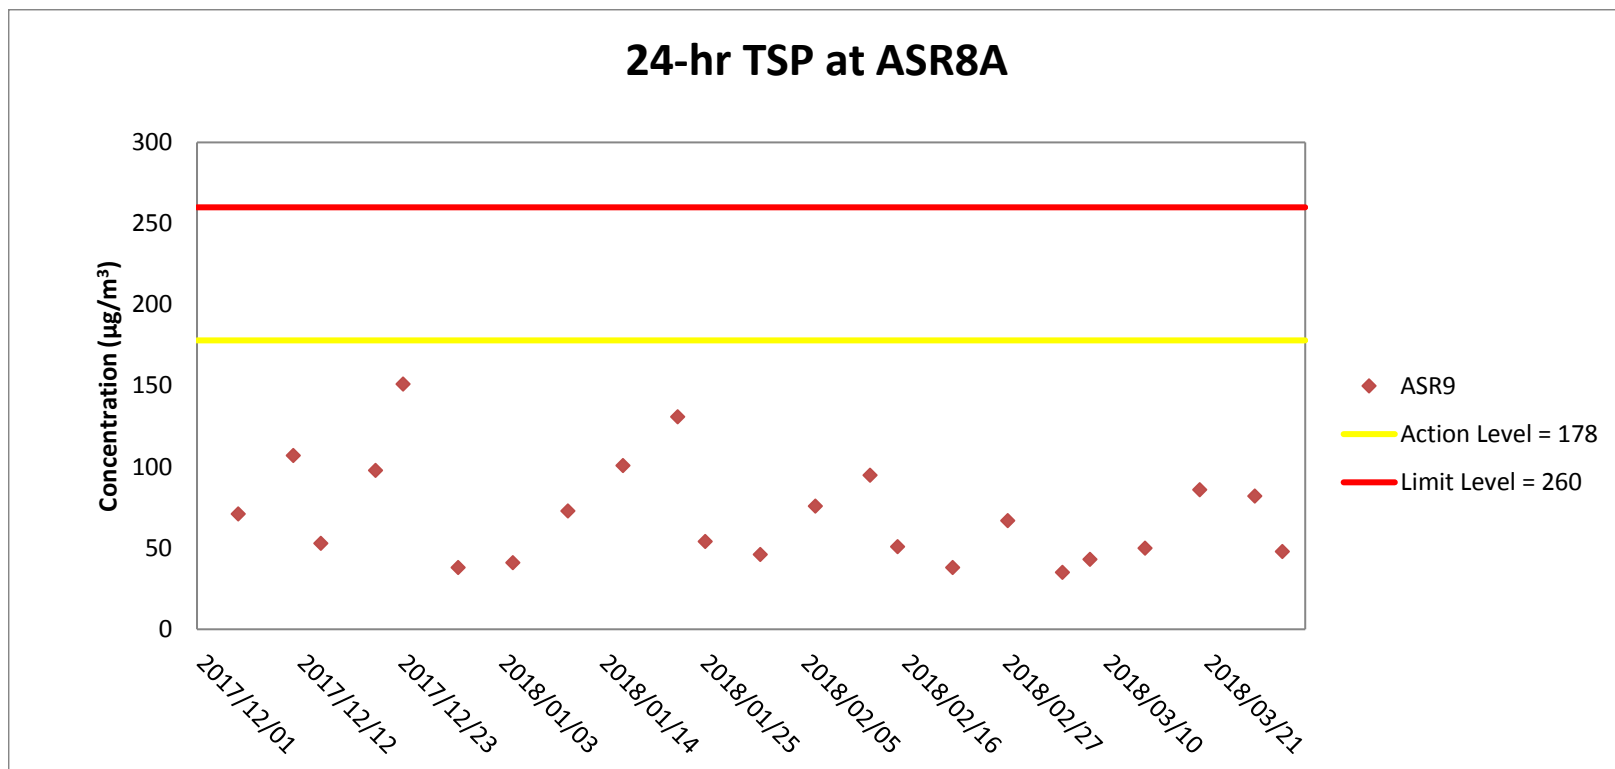

Weather condition within the reporting period varied between sunny to rainy.

Major construction works undertaken within the reporting period include Pier construction; Re-alignment of Cheung Tung Road; Road works along North Lantau Highway; Installation of pier head and deck segments; Asphalt paving; Sign gantries construction; Parapet installation; and Slope work of Viaducts A, B,C & D.
