
Project	Works	Date (yyyy-mm-dd)	Station	Weather Condition	Time (hh:mm, 24hour)	Noise Level for 30-min, dB(A)			Limit Level	Wind Speed		Calibrator
						Leq	L10	L90	dB(A)	(m/s)	Noise Meter Model/ID	Model/ID
TMCLKL	HY/2012/07	2018-08-02	NSR1A	Sunny	9:50	63	64	60	75	0.3	RION NL52	RION NC73
											(00131628)	(S/N 10486660)
TMCLKL	HY/2012/07	2018-08-08	NSR1A	Sunny	9:50	63	64	61	75	0.2	RION NL52	RION NC73
											(00131628)	(S/N 10486660)
TMCLKL	HY/2012/07	2018-08-14	NSR1A	Cloudy	9:55	66	67	64	75	0.5	RION NL52	RION NC73
											(00131628)	(S/N 10486660)
TMCLKL	HY/2012/07	2018-08-20	NSR1A	Cloudy	9:44	64	65	62	75	0.2	RION NL52	RION NC73
											(00131628)	(S/N 10486660)
TMCLKL	HY/2012/07	2018-08-23	NSR1A	Cloudy	10:00	64	65	61	75	0.3	RION NL52	RION NC73
											(00131628)	(S/N 10486660)
TMCLKL	HY/2012/07	2018-08-29	NSR1A	Cloudy	10:01	63	64	60	75	0.3	RION NL52	RION NC73
											(00131628)	(S/N 10486660)
					Min.	63						
					Max.	66						
					Average	64						

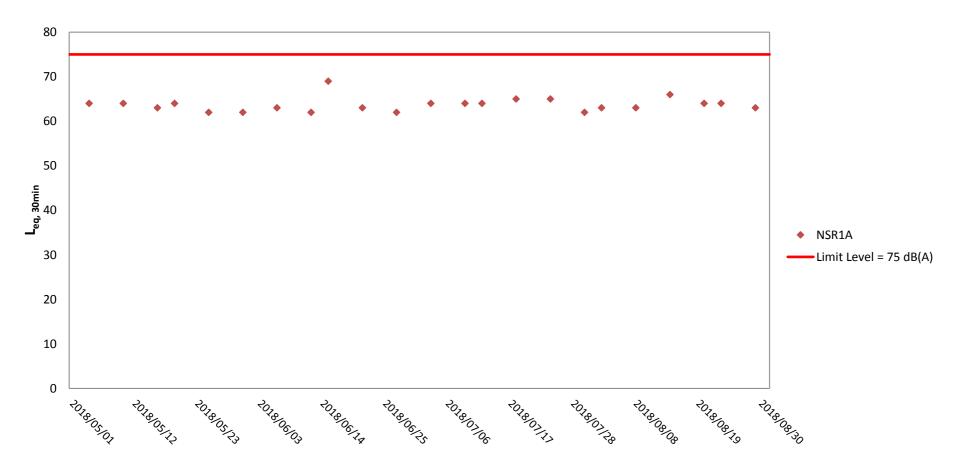

Noise Monitoring Results at NSR 1A ($L_{eq, 30min}$)

Weather condition within the reporting period varied between sunny to rainy.

Major construction works undertaken within the reporting period include Pier construction; Re-alignment of Cheung Tung Road; Road works along North Lantau Highway; Installation of pier head and deck segments; Asphalt paving; Sign gantries construction; Parapet installation; and Slope work of Viaducts A, B,C & D.
