Activity ID	Activity Name	Orig Dur	Planned Start	Planned Finish	Current Start	Current Finish
TMCLK - Northern Connection Sub-Sea Tunnel Section		361	25-Oct-13	07-Nov-14	25-Oct-13 A	15-Jan-15
Construction		361	25-Oct-13	07-Nov-14	25-Oct-13 A	15-Jan-15
Northern Landfall		361	25-Oct-13	07-Nov-14	25-Oct-13 A	15-Jan-15
North Reclamation (Phase 1)		224	25-Oct-13	18-Jun-14	25-Oct-13 A	02-Aug-14
Construction		224	25-Oct-13	18-Jun-14	25-Oct-13 A	02-Aug-14
Milestones		144	20-Jan-14	06-Jun-14	02-Apr-14 A	22-Jul-14
NRC10020	200m Leading Seawall for Reclamation: 100-150 (Zone E)	0	20-Jan-14		02-Apr-14 A	
NRC10030	200m Leading Seawall for Reclamation: 150-205 (Zone E)	0	28-Jan-14		17-Apr-14 A	
NRC10040	200m Leading Seawall for Reclamation: 200-250 (Zone D1)	0	12-Feb-14		28-Apr-14	
NRC10050	200m Leading Seawall for Reclamation: 250-300 (Zone D1)	0	20-Feb-14		29-Apr-14	
NRC10060	200m Leading Seawall for Reclamation: 300-350 (Zone D1)	0	03-Mar-14		02-May-14	
NRC10070	200m Leading Seawall for Reclamation: 350-400 (Zone D2)	0	13-Mar-14		14-May-14	
NRC10080	200m Leading Seawall for Reclamation: 400-450 (Zone D2)	0	24-Mar-14		24-May-14	
NRC10090	200m Leading Seawall for Reclamation: 450-500 (Zone C1)	0	29-Mar-14		30-May-14	
NRC10100	200m Leading Seawall for Reclamation: 500-550 (Zone C1)	0	04-Apr-14		18-Jun-14	
NRC10110	200m Leading Seawall for Reclamation: 550-600 (Zone C2)	0	11-Apr-14		10-Jul-14	
NRC10120	200m Leading Seawall for Reclamation: 600-650 (Zone B)	0	28-Apr-14		22-Jul-14	
NRC13140	Completion of Zone E Reclamation up to +10mPD	0		30-Apr-14		13-Jun-14
NRC13150	Completion of Zone D1 Reclamation up to +5.0mPD	0		16-May-14		30-Jun-14
NRC13170	Completion of Zone D2 Relamation up tp +5.0mPD	0		06-Jun-14		22-Jul-14
Ground Investigation		138	25-Oct-13	30-Apr-14	25-Oct-13 A	10-May-14
DDP09010	Ground Investigation (Phase 2) - Northern Landfall & Sub-sea Tunnel	138	25-Oct-13	30-Apr-14	25-Oct-13 A	10-May-14
Zone E		135	16-Dec-13	13-Jun-14	15-Feb-14 A	13-Jun-14
Vertical Seawall		135	16-Dec-13	13-Jun-14	15-Feb-14 A	13-Jun-14
NRC10340	VS - Rockfill Type A- Zone E - (CH100 to 150)	3	16-Dec-13	18-Dec-13	15-Feb-14 A	03-Apr-14 A
NRC10350	VS - Rockfill Type A- Zone E - (CH150 to 205)	4	28-Dec-13	02-Jan-14	20-Feb-14 A	09-Apr-14 A
NRC10380	VS - Geotextile - Zone E - (CH100 to 150)	2	19-Dec-13	20-Dec-13	22-Feb-14 A	03-Apr-14 A
NRC10390	VS - Geotextile - Zone E - (CH150 to 205)	2	03-Jan-14	04-Jan-14	03-Mar-14 A	09-Apr-14 A
NRC10420	VS - Granular Filter - Zone E - (CH100 to 150)	4	31-Dec-13	04-Jan-14	15-Feb-14 A	03-Apr-14 A
NRC10430	VS - Granular Filter - Zone E - (CH150 to 205)	5	06-Jan-14	10-Jan-14	06-Mar-14 A	09-Apr-14 A
NRC10480	VS - Mass Concrete Coping - Zone E - (CH0 to 50)	8	02-May-14	12-May-14	02-May-14*	12-May-14
NRC10490	VS - Mass Concrete Coping - Zone E - (CH50 to 100)	8	13-May-14	21-May-14	13-May-14	21-May-14
NRC10500	VS - Mass Concrete Coping - Zone E - (CH100 to 150)	8	22-May-14	30-May-14	22-May-14	30-May-14
NRC10510	VS - Mass Concrete Coping - Zone E - (CH150 to 205)	11	31-May-14	13-Jun-14	31-May-14	13-Jun-14
Reclamation		95	15-Feb-14	30-Apr-14	05-Mar-14 A	13-Jun-14
NRC10590	Reclamation - Sand Blanket - Zone E - (CH150 to 205)	2	28-Feb-14	01-Mar-14	05-Mar-14 A	29-Mar-14 A
NRC10620	Reclamation - Band Drain - Zone E - (CH100 to 150)	4	24-Feb-14	27-Feb-14	07-Mar-14 A	04-Apr-14 A
NRC10630	Reclamation - Band Drain - Zone E - (CH150 to 205)	2	03-Mar-14	06-Mar-14	01-Apr-14 A	29-Apr-14
NRC10640	Public Fill - Zone E - (CH0 to 50) to -2.5mPD	5	15-Feb-14	20-Feb-14	21-Mar-14 A	21-Apr-14 A
NRC10650	Public Fill - Zone E - (CH50 to 100) to -2.5mPD	2	21-Feb-14	26-Feb-14	14-Apr-14 A	30-Apr-14
NRC10660	Public Fill - Zone E - (CH100 to 150) to -2.5mPD	1	07-Mar-14	11-Mar-14	21-Apr-14 A	07-May-14
NRC10670	Public Fill - Zone E - (CH150 to 205) to -2.5mPD	4	28-Mar-14	01-Apr-14	16-May-14	20-May-14
NRC10680	Public Fill - Zone E - (CH0 to 50) to +2.5mPD	6	27-Feb-14	06-Mar-14	18-Mar-14 A	02-May-14
NRC10690	Public Fill - Zone E - (CH50 to 100) to +2.5mPD	6	12-Mar-14	19-Mar-14	22-Mar-14 A	08-May-14
NRC10700	Public Fill - Zone E - (CH100 to 150) to +2.5mPD	2	20-Mar-14	27-Mar-14	18-Apr-14 A	15-May-14
NRC10710	Public Fill - Zone E - (CH150 to 205) to +2.5mPD	7	02-Apr-14	10-Apr-14	17-May-14	24-May-14
NRC10720	Public Fill - Zone E - (CH0 to 50) to +6.0mPD	4	20-Mar-14	27-Mar-14	21-Mar-14 A	13-May-14
NRC10730	Public Fill - Zone E - (CH50 to 100) to +6.0mPD	1	02-Apr-14	10-Apr-14	01-Apr-14 A	27-May-14
NRC10740	Public Fill - Zone E - (CH100 to 150) to +6.0mPD	7	11-Apr-14	22-Apr-14	28-May-14	05-Jun-14
NRC10750	Public Fill - Zone E - (CH150 to 205) to +6.0mPD	7	23-Apr-14	30-Apr-14	06-Jun-14	13-Jun-14
Zone D1		142	16-Dec-13	09-Jun-14	18-Mar-14 A	05-Jul-14
Vertical Seawall		110	20-Jan-14	09-Jun-14	18-Mar-14 A	05-Jul-14
NRC10980	VS - Seawall Block - Zone D1 - (CH305 to 355)	7	20-Jan-14	27-Jan-14	18-Mar-14 A	02-Apr-14 A
NRC11010	VS - Rockfill Type A- Zone D1 - (CH205 to 255)	5	20-Jan-14	25-Jan-14	18-Mar-14 A	28-Apr-14
NRC11020	VS - Rockfill Type A- Zone D1 - (CH255 to 305)	2	27-Jan-14	29-Jan-14	26-Mar-14 A	29-Apr-14
NRC11030	VS - Rockfill Type A- Zone D1 - (CH305 to 355)	2	30-Jan-14	08-Feb-14	01-Apr-14 A	30-Apr-14
NRC11060	VS - Geotextile - Zone D1 - (CH205 to 255)	3	30-Jan-14	08-Feb-14	21-Mar-14 A	30-Apr-14
NRC11070	VS - Geotextile - Zone D1 - (CH255 to 305)	2	10-Feb-14	11-Feb-14	25-Mar-14 A	02-May-14
NRC11080	VS - Geotextile - Zone D1 - (CH305 to 355)	2	12-Feb-14	13-Feb-14	02-Apr-14 A	03-May-14
NRC11140	VS - Granular Filter - Zone D1 - (CH205 to 255)	6	12-Feb-14	19-Feb-14	24-Mar-14 A	03-May-14
NRC11210	VS - Granular Filter - Zone D1 - (CH255 to 305)	3	20-Feb-14	24-Feb-14	27-Mar-14 A	05-May-14
NRC11280	VS - Granular Filter - Zone D1 - (CH305 to 355)	2	25-Feb-14	28-Feb-14	03-Apr-14 A	08-May-14
NRC11720	VS - Mass Concrete Coping - Zone D1 - (CH205 to 255)	15	02-May-14	20-May-14	29-May-14*	17-Jun-14
NRC11790	VS - Mass Concrete Coping - Zone D1 - (CH255 to 305)	8	21-May-14	29-May-14	17-Jun-14	25-Jun-14
NRC11860	VS - Mass Concrete Coping - Zone D1 - (CH305 to 355)	8	30-May-14	09-Jun-14	26-Jun-14	05-Jul-14
Sloping Seawall		140	16-Dec-13	19-May-14	25-Mar-14 A	03-Jul-14
NRC1202090	VS - Mass Concrete Coping - Zone D1 - RTT	4	26-Apr-14	02-May-14	12-Jun-14	17-Jun-14
NRC13610	SS - Armour Rock Underlayer - Zone D1 - (CH255 to 305)	5	27-Dec-13	02-Jan-14	28-Apr-14	03-May-14
NRC13690	SS - Armour Rock Underlayer - Zone D1 - (CH305 to 355)	5	03-Jan-14	08-Jan-14	05-May-14	10-May-14
NRC14070	SS - Armour Rock - Zone D1 - (CH255 to 305)	4	03-Jan-14	07-Jan-14	05-May-14	09-May-14
NRC14080	SS - Armour Rock - Zone D1 - (CH305 to 355)	4	08-Jan-14	11-Jan-14	10-May-14	14-May-14
NRC14120	SS - Mass Concrete Coping - Zone D1 - (CH255 to 305)	7	02-May-14	10-May-14	17-Jun-14	24-Jun-14
NRC14130	SS - Mass Concrete Coping - Zone D1 - (CH305 to 355)	7	12-May-14	19-May-14	25-Jun-14	03-Jul-14
NRC14170	Sloping - Rockfill Type A- Zone D1 - (CH255 to 305)	1	16-Dec-13	16-Dec-13	01-Apr-14 A	02-Apr-14 A
NRC14180	Sloping - Rockfill Type A- Zone D1 - (CH305 to 355)	1	27-Dec-13	27-Dec-13	01-Apr-14 A	02-Apr-14 A
NRC14220	Sloping - Geotextile - Zone D1 - (CH255 to 305)	1	17-Dec-13	17-Dec-13	29-Mar-14 A	31-Mar-14 A
NRC14230	Sloping - Geotextile - Zone D1 - (CH305 to 355)	1	28-Dec-13	28-Dec-13	01-Apr-14 A	02-Apr-14 A
NRC14270	Sloping - Granular Filter - Zone D1 - (CH255 to 305)	2	18-Dec-13	19-Dec-13	01-Apr-14 A	03-Apr-14 A
NRC14280	Sloping - Granular Filter - Zone D1 - (CH305 to 355)	2	30-Dec-13	31-Dec-13	04-Apr-14 A	08-Apr-14 A
NRC14320	Reclamation - Geotextile - Zone D1 - (CH255 to 305)	6	07-Mar-14	13-Mar-14	25-Mar-14 A	01-Apr-14 A
NRC14330	Reclamation - Geotextile - Zone D1 - (CH305 to 355)	6	14-Mar-14	20-Mar-14	02-Apr-14 A	10-Apr-14 A
NRC14360	Reclamation - Sand Blanket - Zone D1 - (CH205 to 255)	2	07-Mar-14	08-Mar-14	31-Mar-14 A	04-Apr-14 A
NRC14370	Reclamation - Sand Blanket - Zone D1 - (CH255 to 305)	1	14-Mar-14	15-Mar-14	01-Apr-14 A	28-Apr-14
NRC14380	Reclamation - Sand Blanket - Zone D1 - (CH305 to 355)	1	21-Mar-14	22-Mar-14	07-Apr-14 A	28-Apr-14
NRC14410	Reclamation - Band Drain - Zone D1 - (CH205 to 255)	5	10-Mar-14	14-Mar-14	30-Apr-14	07-May-14
NRC14420	Reclamation - Band Drain - Zone D1 - (CH255 to 305)	5	17-Mar-14	21-Mar-14	08-May-14	13-May-14
NRC14430	Reclamation - Band Drain - Zone D1 - (CH305 to 355)	5	24-Mar-14	28-Mar-14	14-May-14	19-May-14
Reclamation		34	02-Apr-14	16-May-14	21-May-14	30-Jun-14
NRC13260	Compacted Sandfill - Zone D1 - (CH205 to 255) to -2.5mPD	3	02-Apr-14	04-Apr-14	21-May-14	23-May-14
NRC13270	Compacted Sandfill - Zone D1 - (CH255 to 305) to -2.5mPD	3	07-Apr-14	09-Apr-14	24-May-14	27-May-14
NRC13280	Compacted Sandfill - Zone D1 - (CH305 to 355) to -2.5mPD	3	10-Apr-14	12-Apr-14	28-May-14	30-May-14
NRC13290	Public Fill - Zone D1 - (CH205 to 255) to -2.5mPD	1	07-Apr-14	07-Apr-14	24-May-14	24-May-14
NRC13300	Public Fill - Zone D1 - (CH255 to 305) to -2.5mPD	2	10-Apr-14	11-Apr-14	28-May-14	29-May-14
NRC13310	Public Fill - Zone D1 - (CH305 to 355) to -2.5mPD	2	14-Apr-14	15-Apr-14	31-May-14	03-Jun-14
NRC13320	Compacted Sandfill - Zone D1 - (CH205 to 255) to +2.5mPD	3	08-Apr-14	10-Apr-14	26-May-14	28-May-14
NRC13340	Compacted Sandfill - Zone D1 - (CH255 to 305) to +2.5mPD	3	12-Apr-14	15-Apr-14	30-May-14	03-Jun-14
NRC13350	Compacted Sandfill - Zone D1 - (CH305 to 355) to +2.5mPD	3	16-Apr-14	22-Apr-14	04-Jun-14	06-Jun-14
NRC13360	Public Fill - Zone D1 - (CH205 to 255) to +2.5mPD	4	11-Apr-14	15-Apr-14	29-May-14	03-Jun-14
NRC13370	Public Fill - Zone D1 - (CH255 to 305) to +2.5mPD	4	16-Apr-14	23-Apr-14	04-Jun-14	07-Jun-14
NRC13380	Public Fill - Zone D1 - (CH305 to 355) to +2.5mPD	4	24-Apr-14	28-Apr-14	09-Jun-14	12-Jun-14
NRC13390	Compacted Sandfill - Zone D1 - (CH205 to 255)to +5.0mPD	2	16-Apr-14	17-Apr-14	14-Jun-14	16-Jun-14
NRC13400	Compacted Sandfill - Zone D1 - (CH255 to 305) to +5.0mPD	2	24-Apr-14	25-Apr-14	17-Jun-14	18-Jun-14
NRC13410	Compacted Sandfill - Zone D1 - (CH305 to 355) to +5.0mPD	2	29-Apr-14	30-Apr-14	19-Jun-14	20-Jun-14
NRC13420	Public Fill - Zone D1 - (CH205 to 255) to +5.0mPD	4	02-May-14	07-May-14	17-Jun-14	20-Jun-14
NRC13430	Public Fill - Zone D1 - (CH255 to 305) to +5.0mPD	4	08-May-14	12-May-14	21-Jun-14	25-Jun-14
NRC13450	Public Fill - Zone D1 - (CH305 to 355) to +5.0mPD	4	13-May-14	16-May-14	26-Jun-14	30-Jun-14
Zone D2		130	08-Jan-14	06-Jun-14	31-Mar-14 A	22-Jul-14
Vertical Seawall		126	09-Jan-14	03-Jun-14	31-Mar-14 A	18-Jul-14

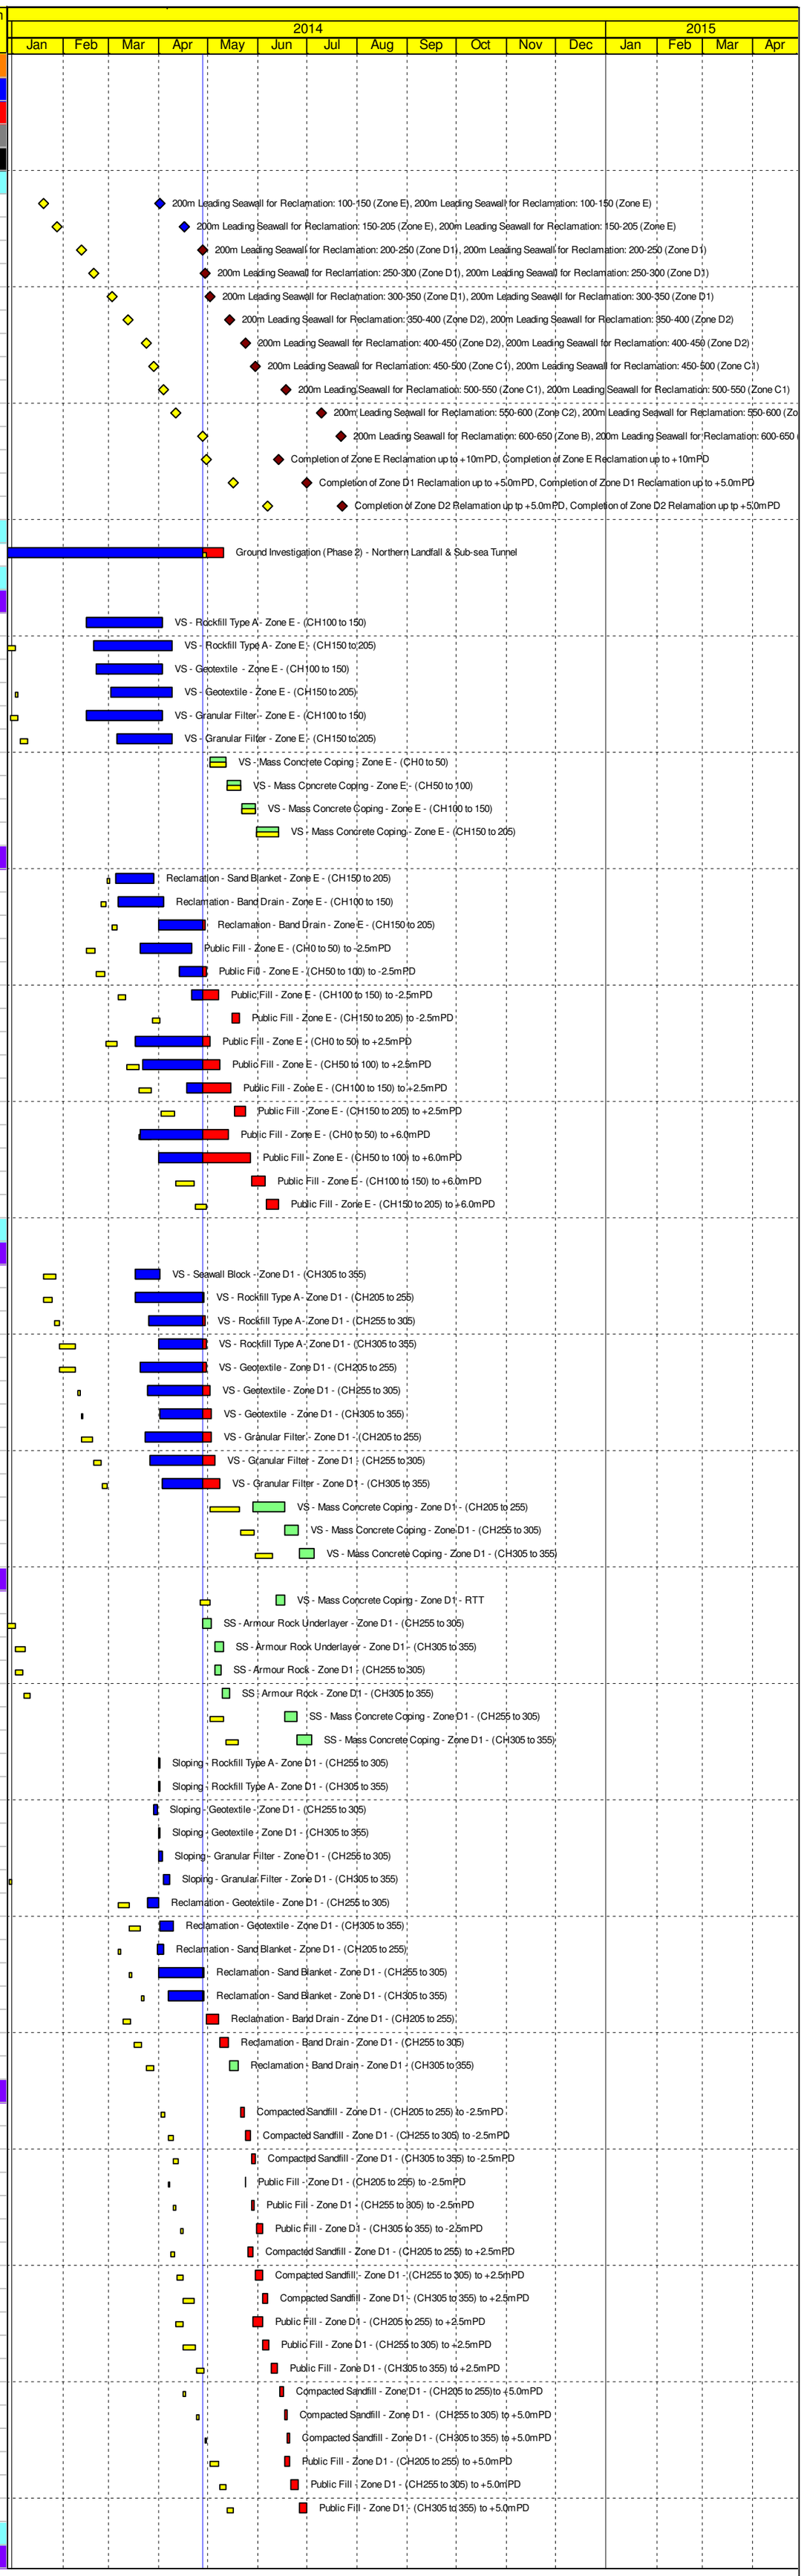

Current Bar
Current Bar - Critical
Planned Bar
Planned Milestone
Current Milestone
Progress Milestone
Progress Bar

TMCLK - Northern Connection Sub-Sea Tunnel Section

3-Months Rolling Programme - Construction

As of 28-Apr-14 Progress

香港寶嘉 Dragages HongKong

A member of the Bouygues Construction group

Dragages - Bouygues Joint Venture 寶嘉 - 布依格聯營

BOUYGUES TRAVAUX PUBLICS

Date	Revision	Checked	Approved
12-Feb-14	TMCLK/DBJ/GEN/PRG/98507	SPa	WYu

Activity ID	Activity Name	Orig Dur	Planned Start	Planned Finish	Current Start	Current Finish
NRC10950	VS - Levelling Stone - Zone D2 - (CH405 to 443)	4	09-Jan-14	13-Jan-14	31-Mar-14 A	02-Apr-14 A
NRC10990	VS - Seawall Block - Zone D2 - (CH355 to 405)	7	28-Jan-14	11-Feb-14	05-Apr-14 A	17-Apr-14 A
NRC11000	VS - Seawall Block - Zone D2 - (CH405 to 443)	6	12-Feb-14	19-Feb-14	08-Apr-14 A	28-Apr-14
NRC11040	VS - Rockfill Type A- Zone D2 - (CH355 to 405)	1	12-Feb-14	14-Feb-14	16-Apr-14 A	03-May-14
NRC11050	VS - Rockfill Type A- Zone D2 - (CH405 to 443)	1	20-Feb-14	22-Feb-14	22-Apr-14 A	07-May-14
NRC11090	VS - Geotextile - Zone D2 - (CH355 to 405)	1	15-Feb-14	17-Feb-14	10-Apr-14 A	05-May-14
NRC11100	VS - Geotextile - Zone D2 - (CH405 to 443)	2	24-Feb-14	25-Feb-14	08-May-14	09-May-14
NRC11350	VS - Granular Filter - Zone D2 - (CH355 to 405)	1	01-Mar-14	05-Mar-14	16-Apr-14 A	12-May-14
NRC11390	VS - Granular Filter - Zone D2 - (CH405 to 443)	1	06-Mar-14	10-Mar-14	13-May-14	13-May-14
NRC11930	VS - Mass Concrete Coping - Zone D2 - (CH355 to 405)	8	12-May-14	21-May-14	26-Jun-14	07-Jul-14
NRC11980	VS - Mass Concrete Coping - Zone D2 - (CH405 to 443)	8	23-May-14	03-Jun-14	09-Jul-14	18-Jul-14
Sloping Seawall		123	08-Jan-14	05-Jun-14	15-Apr-14 A	19-Jul-14
NRC13770	SS - Armour Rock Underlayer - Zone D2 - (CH355 to 405)	5	09-Jan-14	14-Jan-14	12-May-14	16-May-14
NRC13880	SS - Armour Rock Underlayer - Zone D2 - (CH405 to 443)	5	15-Jan-14	20-Jan-14	17-May-14	22-May-14
NRC14090	SS - Armour Rock - Zone D2 - (CH355 to 405)	4	13-Jan-14	16-Jan-14	15-May-14	19-May-14
NRC14100	SS - Armour Rock - Zone D2 - (CH405 to 443)	4	17-Jan-14	21-Jan-14	20-May-14	23-May-14
NRC14140	SS - Mass Concrete Coping - Zone D2 - (CH355 to 405)	7	20-May-14	27-May-14	04-Jul-14	11-Jul-14
NRC14150	SS - Mass Concrete Coping - Zone D2 - (CH405 to 443)	7	28-May-14	05-Jun-14	12-Jul-14	19-Jul-14
NRC14190	Sloping - Rockfill Type A- Zone D2 - (CH355 to 405)	1	08-Jan-14	08-Jan-14	15-Apr-14 A	28-Apr-14
NRC14200	Sloping - Rockfill Type A- Zone D2 - (CH405 to 443)	1	17-Jan-14	17-Jan-14	21-Apr-14 A	28-Apr-14
NRC14240	Sloping - Geotextile - Zone D2 - (CH355 to 405)	1	09-Jan-14	09-Jan-14	29-Apr-14	29-Apr-14
NRC14250	Sloping - Geotextile - Zone D2 - (CH405 to 443)	1	18-Jan-14	18-Jan-14	29-Apr-14	29-Apr-14
NRC14290	Sloping - Granular Filter - Zone D2 - (CH355 to 405)	2	10-Jan-14	11-Jan-14	30-Apr-14	02-May-14
NRC14300	Sloping - Granular Filter - Zone D2 - (CH405 to 443)	2	20-Jan-14	21-Jan-14	30-Apr-14	02-May-14
Reclamation		91	21-Mar-14	06-Jun-14	10-Apr-14 A	22-Jul-14
NRC13490	Compacted Sandfill- Zone D2 - (CH355 to 405) to -2.5mPD	3	14-Apr-14	16-Apr-14	04-Jun-14	06-Jun-14
NRC13500	Compacted Sandfill - Zone D2 - (CH405 to 443) to -2.5mPD	2	17-Apr-14	22-Apr-14	07-Jun-14	09-Jun-14
NRC13510	Public Fill - Zone D2 - (CH355 to 405) to -2.5mPD	4	17-Apr-14	24-Apr-14	07-Jun-14	11-Jun-14
NRC13520	Public Fill - Zone D2 - (CH405 to 443) to -2.5mPD	4	25-Apr-14	29-Apr-14	12-Jun-14	16-Jun-14
NRC13540	Compacted Sandfill - Zone D2 - (CH355 to 405) to +2.5mPD	6	25-Apr-14	02-May-14	12-Jun-14	18-Jun-14
NRC13550	Compacted Sandfill - Zone D2 - (CH405 to 443) to +2.5mPD	5	03-May-14	09-May-14	19-Jun-14	24-Jun-14
NRC13560	Public Fill - Zone D2 - (CH355 to 405) to +2.5mPD	10	03-May-14	15-May-14	19-Jun-14	30-Jun-14
NRC13570	Public Fill - Zone D2 - (CH405 to 443) to +2.5mPD	10	16-May-14	27-May-14	02-Jul-14	12-Jul-14
NRC13580	Compacted Sandfill - Zone D2 - (CH355 to 405) to +5.0mPD	4	16-May-14	20-May-14	02-Jul-14	05-Jul-14
NRC13590	Compacted Sandfill - Zone D2 - (CH405 to 443) to +5.0mPD	4	28-May-14	31-May-14	14-Jul-14	17-Jul-14
NRC13600	Public Fill - Zone D2 - (CH355 to 405) to +5.0mPD	4	21-May-14	24-May-14	07-Jul-14	10-Jul-14
NRC13620	Public Fill - Zone D2 - (CH405 to 443) to +5.0mPD	4	03-Jun-14	06-Jun-14	18-Jul-14	22-Jul-14
NRC14340	Reclamation - Geotextile - Zone D2 - (CH355 to 405)	5	21-Mar-14	27-Mar-14	10-Apr-14 A	13-May-14
NRC14350	Reclamation - Geotextile - Zone D2 - (CH405 to 443)	6	28-Mar-14	03-Apr-14	14-May-14	20-May-14
NRC14390	Reclamation - Sand Blanket - Zone D2 - (CH355 to 405)	2	28-Mar-14	29-Mar-14	14-May-14	15-May-14
NRC14400	Reclamation - Sand Blanket - Zone D2 - (CH405 to 443)	2	04-Apr-14	07-Apr-14	21-May-14	22-May-14
NRC14440	Reclamation - Band Drain - Zone D2 - (CH355 to 405)	5	31-Mar-14	04-Apr-14	20-May-14	24-May-14
NRC14450	Reclamation - Band Drain - Zone D2 - (CH405 to 443)	5	08-Apr-14	12-Apr-14	26-May-14	30-May-14
Zone C1		130	04-Jan-14	18-Jun-14	10-Jan-14 A	02-Aug-14
Vertical Seawall		130	04-Jan-14	18-Jun-14	10-Mar-14 A	02-Aug-14
NRC14500	VS - Rock Grade 400 - Zone C1 - (CH493 to 543)	7	04-Jan-14	08-Jan-14	10-Mar-14 A	03-Apr-14 A
NRC14520	VS - Levelling Stone - Zone C1 - (CH443 to 493)	4	14-Jan-14	17-Jan-14	05-Apr-14 A	09-Apr-14 A
NRC14530	VS - Levelling Stone - Zone C1 - (CH493 to 543)	4	18-Jan-14	22-Jan-14	09-Apr-14 A	11-Apr-14 A
NRC14550	VS - Seawall Block - Zone C1 - (CH443 to 493)	7	20-Feb-14	01-Mar-14	10-Apr-14 A	30-Apr-14
NRC14560	VS - Seawall Block - Zone C1 - (CH493 to 543)	9	03-Mar-14	12-Mar-14	02-May-14	13-May-14
NRC14580	VS - Rockfill Type A- Zone C1 - (CH443 to 493)	1	13-Mar-14	15-Mar-14	17-Apr-14 A	15-May-14
NRC14590	VS - Rockfill Type A- Zone C1 - (CH493 to 543)	3	17-Mar-14	19-Mar-14	16-May-14	19-May-14
NRC14610	VS - Geotextile - Zone C1 - (CH443 to 493)	2	20-Mar-14	21-Mar-14	20-May-14	21-May-14
NRC14620	VS - Geotextile - Zone C1 - (CH493 to 543)	2	22-Mar-14	24-Mar-14	22-May-14	23-May-14
NRC14640	VS - Granular Filter - Zone C1 - (CH443 to 493)	1	25-Mar-14	28-Mar-14	22-May-14 A	27-May-14
NRC14650	VS - Granular Filter - Zone C1 - (CH493 to 543)	4	29-Mar-14	02-Apr-14	28-May-14	31-May-14
NRC14700	VS - Mass Concrete Coping - Zone C1 - (CH443 to 493)	8	10-Jun-14	18-Jun-14	24-Jul-14	02-Aug-14
Sloping Seawall		104	27-Jan-14	18-Jun-14	10-Jan-14 A	02-Aug-14
NRC14770	SS - Rock Grade 400 - Zone C1 - (CH493 to 543) to +2.5mPD	15	27-Jan-14	11-Feb-14	10-Jan-14 A	08-Apr-14 A
NRC14820	SS - Armour Rock Underlayer - Zone C1 - (CH443 to 493)	5	27-Jan-14	07-Feb-14	23-May-14	28-May-14
NRC14830	SS - Armour Rock Underlayer - Zone C1 - (CH493 to 543)	5	12-Feb-14	17-Feb-14	29-May-14	04-Jun-14
NRC14850	SS - Armour Rock - Zone C1 - (CH443 to 493)	4	27-Feb-14	03-Mar-14	11-Jun-14	14-Jun-14
NRC14860	SS - Armour Rock - Zone C1 - (CH493 to 543)	4	04-Mar-14	07-Mar-14	16-Jun-14	19-Jun-14
NRC14880	SS - Mass Concrete Coping - Zone C1 - (CH443 to 493)	7	10-Jun-14	18-Jun-14	25-Jul-14	02-Aug-14
NRC14910	Sloping - Rockfill Type A- Zone C1 - (CH443 to 493)	1	27-Jan-14	27-Jan-14	29-Apr-14	29-Apr-14
NRC14920	Sloping - Rockfill Type A- Zone C1 - (CH493 to 543)	1	12-Feb-14	12-Feb-14	30-Apr-14	30-Apr-14
NRC14940	Sloping - Geotextile - Zone C1 - (CH443 to 493)	1	28-Jan-14	28-Jan-14	30-Apr-14	30-Apr-14
NRC14950	Sloping - Geotextile - Zone C1 - (CH493 to 453)	1	13-Feb-14	13-Feb-14	02-May-14	02-May-14
NRC14970	Sloping - Granular Filter - Zone C1 - (CH443 to 493)	3	29-Jan-14	07-Feb-14	03-May-14	07-May-14
NRC14980	Sloping - Granular Filter - Zone C1 - (CH493 to 543)	3	14-Feb-14	17-Feb-14	08-May-14	10-May-14
Reclamation		58	04-Apr-14	13-Jun-14	21-May-14	29-Jul-14
NRC13650	Compacted Sandfill - Zone C1 - (CH443 to 493) to -2.5mPD	2	28-May-14	29-May-14	14-Jul-14	15-Jul-14
NRC13660	Compacted Sandfill - Zone C1 - (CH493 to 543) to -2.5mPD	2	30-May-14	31-May-14	16-Jul-14	17-Jul-14
NRC13670	Public Fill - Zone C1 - (CH443 to 493) to -2.5mPD	2	30-May-14	31-May-14	16-Jul-14	17-Jul-14
NRC13680	Public Fill - Zone C1 - (CH493 to 543) to -2.5mPD	2	03-Jun-14	04-Jun-14	18-Jul-14	19-Jul-14
NRC13700	Compacted Sandfill - Zone C1 - (CH443 to 493) to +2.5mPD	5	03-Jun-14	07-Jun-14	18-Jul-14	23-Jul-14
NRC13710	Compacted Sandfill - Zone C1 - (CH493 to 543) to +2.5mPD	5	09-Jun-14	13-Jun-14	24-Jul-14	29-Jul-14
NRC13720	Public Fill - Zone C1 - (CH443 to 493) to +2.5mPD	4	09-Jun-14	12-Jun-14	24-Jul-14	28-Jul-14
NRC15000	Reclamation - Geotextile - Zone C1 - (CH443 to 493)	4	04-Apr-14	09-Apr-14	21-May-14	24-May-14
NRC15010	Reclamation - Geotextile - Zone C1 - (CH493 to 543)	4	10-Apr-14	14-Apr-14	26-May-14	29-May-14
NRC15030	Reclamation - Sand Blanket - Zone C1 - (CH443 to 493)	2	10-Apr-14	11-Apr-14	26-May-14	27-May-14
NRC15040	Reclamation - Sand Blanket - Zone C1 - (CH493 to 543)	2	15-Apr-14	16-Apr-14	30-May-14	31-May-14
NRC15060	Reclamation - Band Drain - Zone C1 - (CH443 to 493)	4	14-Apr-14	17-Apr-14	31-May-14	05-Jun-14
NRC15070	Reclamation - Band Drain - Zone C1 - (CH493 to 543)	4	22-Apr-14	25-Apr-14	06-Jun-14	10-Jun-14
Zone C2		117	09-Jan-14	10-Jun-14	06-Mar-14 A	25-Jul-14
Vertical Seawall		76	09-Jan-14	08-Apr-14	06-Mar-14 A	06-Jun-14
NRC14510	VS - Rock Grade 400 - Zone C2 - (CH543 to 598)	8	09-Jan-14	13-Jan-14	06-Mar-14 A	16-Apr-14 A
NRC14540	VS - Levelling Stone - Zone C2 - (CH543 to 598)	4	23-Jan-14	27-Jan-14	15-Apr-14 A	20-Apr-14 A
NRC14570	VS - Seawall Block - Zone C2 - (CH543 to 598)	9	13-Mar-14	22-Mar-14	14-May-14	23-May-14
NRC14600	VS - Rockfill Type A- Zone C2 - (CH543 to 598)	3	20-Mar-14	22-Mar-14	20-May-14	22-May-14
NRC14630	VS - Geotextile - Zone C2 - (CH543 to 598)	2	25-Mar-14	26-Mar-14	24-May-14	26-May-14
NRC14660	VS - Granular Filter - Zone C2 - (CH543 to 598)	4	03-Apr-14	08-Apr-14	03-Jun-14	06-Jun-14
Sloping Seawall		57	12-Feb-14	12-Mar-14	18-Mar-14 A	24-Jun-14
NRC14780	SS - Rock Grade 400 - Zone C2 - (CH543 to 598) to +2.5mPD	3	12-Feb-14	20-Feb-14	18-Mar-14 A	13-May-14
NRC14840	SS - Armour Rock Underlayer - Zone C2 - (CH543 to 598)	5	21-Feb-14	26-Feb-14	05-Jun-14	10-Jun-14
NRC14870	SS - Armour Rock - Zone C2 - (CH543 to 598)	4	08-Mar-14	12-Mar-14	20-Jun-14	24-Jun-14
NRC14930	Sloping - Rockfill Type A- Zone C2 - (CH543 to 598)	1	21-Feb-14	21-Feb-14	14-May-14	14-May-14
NRC14960	Sloping - Geotextile - Zone C2 - (CH543 to 598)	1	22-Feb-14	22-Feb-14	15-May-14	15-May-14
NRC14990	Sloping - Granular Filter - Zone C2 - (CH543 to 598)	3	24-Feb-14	26-Feb-14	16-May-14	19-May-14
Reclamation		47	15-Apr-14	10-Jun-14	30-May-14	25-Jul-14
NRC15020	Reclamation - Geotextile - Zone C2 - (CH543 to 598)	4	15-Apr-14	22-Apr-14	30-May-14	04-Jun-14
NRC15050	Reclamation - Sand Blanket - Zone C2 - (CH543 to 598)	2	23-Apr-14	24-Apr-14	05-Jun-14	06-Jun-14
NRC15080	Reclamation - Band Drain - Zone C2 - (CH543 to 598)	4	26-Apr-14	30-Apr-14	11-Jun-14	14-Jun-14
NRC15090	Public Fill - Zone C2 - (CH543 to 598) to -2.5mPD	2	09-Jun-14	10-Jun-14	24-Jul-14	25-Jul-14
Zone B		112	14-Jan-14	16-May-14	13-Mar-14 A	29-Jul-14
Vertical Seawall		89	14-Jan-14	05-May-14	13-Mar-14 A	02-Jul-14
NRC11150	VS - Rock Grade 400 - Zone B - (CH598 to 648)	9	14-Jan-14	18-Jan-14	13-Mar-14 A	22-Apr-14 A
NRC11160	VS - Rock Grade 400 - Zone B - (CH648 to 698)	6	20-Jan-14	24-Jan-14	17-Mar-14 A	30-Apr-14

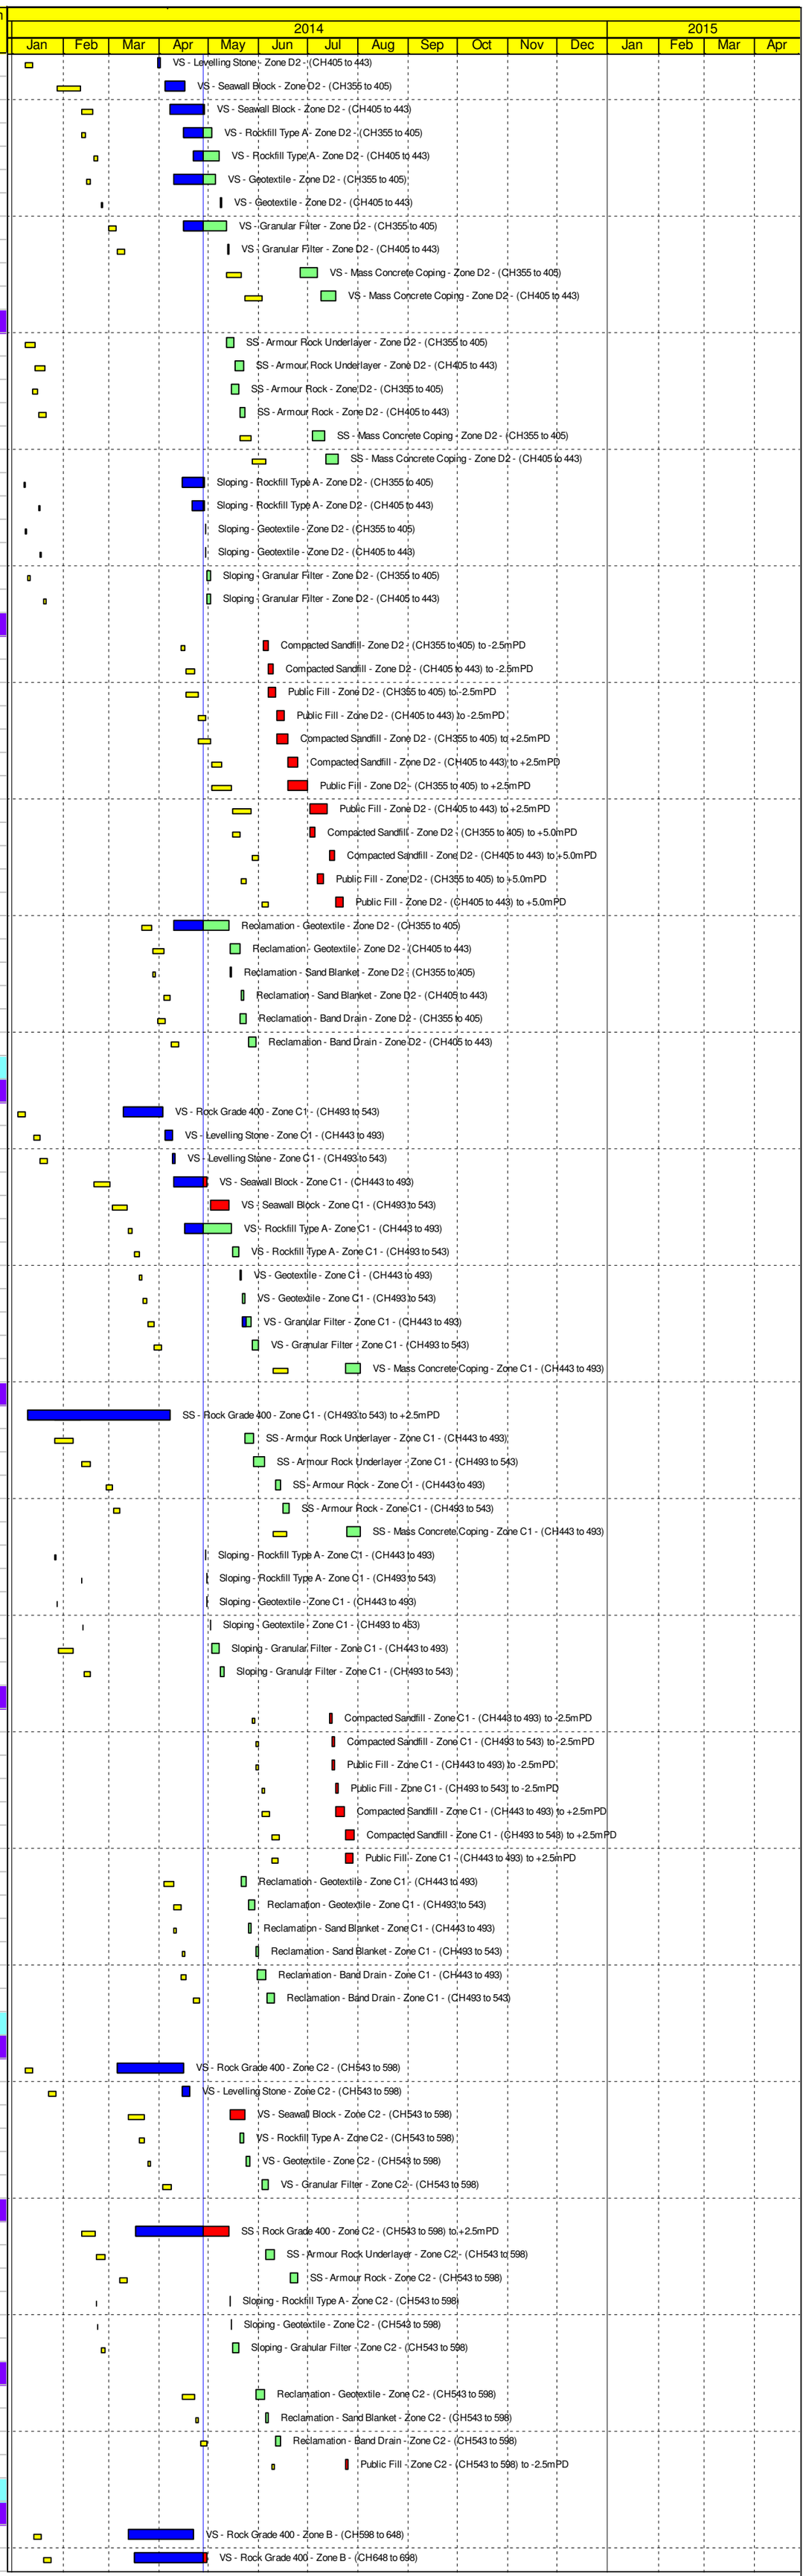

Project ID: TMCLK_I0.0-101 - B1-1 - B3-5 - B4-44

Data Date: 28-Apr-14

Current Bar
Current Bar - Critical
Planned Bar
Planned Milestone
Current Milestone
Progress Milestone
Progress Bar

TMCLK - Northern Connection Sub-Sea Tunnel Section

3-Months Rolling Programme - Construction

As of 28-Apr-14 Progress

香港寶嘉 Dragages HongKong
A member of the Bouygues Construction group
Dragages - Bouygues Joint Venture 寶嘉 - 布依格聯營

BOUYGUES TRAVAUX PUBLICS

Date	Revision	Checked	Approved
12-Feb-14	TMCLK/DBJ/GEN/PRG/98507	SPa	WYu

Activity ID	Activity Name	Orig Dur	Planned Start	Planned Finish	Current Start	Current Finish
NRC11170	VS - Rock Grade 400 - Zone B - (CH698 to 738)	3	25-Jan-14	30-Jan-14	24-Mar-14 A	09-May-14
NRC11180	VS - Levelling Stone - Zone B - (CH598 to 648)	4	28-Jan-14	07-Feb-14	02-May-14	07-May-14
NRC11190	VS - Levelling Stone - Zone B - (CH648 to 698)	4	08-Feb-14	12-Feb-14	08-May-14	12-May-14
NRC11200	VS - Levelling Stone - Zone B - (CH698 to 738)	4	13-Feb-14	17-Feb-14	13-May-14	16-May-14
NRC11220	VS - Seawall Block - Zone B - (CH598 to 648)	5	24-Mar-14	28-Mar-14	24-May-14	29-May-14
NRC11230	VS - Seawall Block - Zone B - (CH648 to 698)	5	29-Mar-14	03-Apr-14	30-May-14	05-Jun-14
NRC11240	VS - Seawall Block - Zone B - (CH698 to 738)	5	04-Apr-14	10-Apr-14	06-Jun-14	11-Jun-14
NRC11250	VS - Rockfill Type A - Zone B - (CH598 to 648)	3	04-Apr-14	08-Apr-14	06-Jun-14	09-Jun-14
NRC11260	VS - Rockfill Type A - Zone B - (CH648 to 698)	3	09-Apr-14	11-Apr-14	10-Jun-14	12-Jun-14
NRC11270	VS - Rockfill Type A - Zone B - (CH698 to 738)	3	12-Apr-14	15-Apr-14	13-Jun-14	16-Jun-14
NRC11290	VS - Geotextile - Zone B - (CH598 to 648)	2	12-Apr-14	14-Apr-14	13-Jun-14	14-Jun-14
NRC11300	VS - Geotextile - Zone B - (CH648 to 698)	2	15-Apr-14	16-Apr-14	16-Jun-14	17-Jun-14
NRC11310	VS - Geotextile - Zone B - (CH698 to 738)	2	17-Apr-14	22-Apr-14	18-Jun-14	19-Jun-14
NRC11320	VS - Granular Filter - Zone B - (CH598 to 648)	4	17-Apr-14	24-Apr-14	18-Jun-14	21-Jun-14
NRC11330	VS - Granular Filter - Zone B - (CH648 to 698)	4	25-Apr-14	29-Apr-14	23-Jun-14	26-Jun-14
NRC11340	VS - Granular Filter - Zone B - (CH698 to 738)	4	30-Apr-14	05-May-14	27-Jun-14	02-Jul-14
Sloping Seawall		71	21-Feb-14	15-Apr-14	15-Mar-14 A	29-Jul-14
NRC11450	SS - Dredging - Zone B - (CH648 to 698)	3	28-Feb-14	03-Mar-14	15-Mar-14 A	17-May-14 A
NRC11460	SS - Dredging - Zone B - (CH698 to 738)	4	10-Mar-14	13-Mar-14	17-Mar-14 A	25-Apr-14 A
NRC11470	SS - Rock Grade 400 - Zone B - (CH598 to 648) to +2.5mPD	2	21-Feb-14	03-Mar-14	26-Mar-14 A	29-May-14
NRC11480	SS - Rock Grade 400 - Zone B - (CH648 to 698) to +2.5mPD	2	04-Mar-14	13-Mar-14	02-Apr-14 A	17-Jun-14
NRC11490	SS - Rock Grade 400 - Zone B - (CH698 to 738) to +2.5mPD	18	14-Mar-14	25-Mar-14	18-Jun-14	09-Jul-14
NRC11540	SS - Armour Rock Underlayer - Zone B - (CH598 to 648)	5	04-Mar-14	08-Mar-14	11-Jun-14	16-Jun-14
NRC11550	SS - Armour Rock Underlayer - Zone B - (CH648 to 698)	5	14-Mar-14	19-Mar-14	18-Jun-14	23-Jun-14
NRC11560	SS - Armour Rock Underlayer - Zone B - (CH698 to 738)	5	26-Mar-14	31-Mar-14	10-Jul-14	15-Jul-14
NRC11580	SS - Armour Rock - Zone B - (CH598 to 648)	4	01-Apr-14	04-Apr-14	16-Jul-14	19-Jul-14
NRC11590	SS - Armour Rock - Zone B - (CH648 to 698)	4	07-Apr-14	10-Apr-14	21-Jul-14	24-Jul-14
NRC11600	SS - Armour Rock - Zone B - (CH698 to 738)	4	11-Apr-14	15-Apr-14	25-Jul-14	29-Jul-14
NRC11650	Sloping - Rockfill Type A - Zone B - (CH598 to 648)	1	04-Mar-14	04-Mar-14	30-May-14	30-May-14
NRC11660	Sloping - Rockfill Type A - Zone B - (CH648 to 698)	1	14-Mar-14	14-Mar-14	18-Jun-14	18-Jun-14
NRC11670	Sloping - Rockfill Type A - Zone B - (CH698 to 738)	1	26-Mar-14	26-Mar-14	10-Jul-14	10-Jul-14
NRC11690	Sloping - Geotextile - Zone B - (CH598 to 648)	1	05-Mar-14	05-Mar-14	31-May-14	31-May-14
NRC11700	Sloping - Geotextile - Zone B - (CH648 to 698)	1	15-Mar-14	15-Mar-14	19-Jun-14	19-Jun-14
NRC11710	Sloping - Geotextile - Zone B - (CH698 to 738)	1	27-Mar-14	27-Mar-14	11-Jul-14	11-Jul-14
NRC11730	Sloping - Granular Filter - Zone B - (CH598 to 648)	2	06-Mar-14	07-Mar-14	03-Jun-14	04-Jun-14
NRC11740	Sloping - Granular Filter - Zone B - (CH648 to 698)	3	17-Mar-14	19-Mar-14	20-Jun-14	23-Jun-14
NRC11750	Sloping - Granular Filter - Zone B - (CH698 to 738)	3	28-Mar-14	31-Mar-14	12-Jul-14	15-Jul-14
Reclamation		44	23-Apr-14	16-May-14	05-Jun-14	26-Jul-14
NRC11760	Reclamation - Geotextile - Zone B - (CH598 to 648)	4	23-Apr-14	26-Apr-14	05-Jun-14	09-Jun-14
NRC11770	Reclamation - Geotextile - Zone B - (CH488 to 698)	4	28-Apr-14	02-May-14	24-Jun-14	27-Jun-14
NRC11780	Reclamation - Geotextile - Zone B - (CH598 to 738)	4	03-May-14	08-May-14	16-Jul-14	19-Jul-14
NRC11800	Reclamation - Sand Blanket - Zone B - (CH598 to 648)	2	28-Apr-14	29-Apr-14	10-Jun-14	11-Jun-14
NRC11810	Reclamation - Sand Blanket - Zone B - (CH648 to 698)	2	03-May-14	05-May-14	28-Jun-14	30-Jun-14
NRC11820	Reclamation - Sand Blanket - Zone B - (CH698 to 738)	2	09-May-14	10-May-14	21-Jul-14	22-Jul-14
NRC11830	Reclamation - Band Drain - Zone B - (CH598 to 648)	4	02-May-14	07-May-14	16-Jun-14	19-Jun-14
NRC11840	Reclamation - Band Drain - Zone B - (CH648 to 698)	4	08-May-14	12-May-14	02-Jul-14	05-Jul-14
NRC11850	Reclamation - Band Drain - Zone B - (CH698 to 738)	4	13-May-14	16-May-14	23-Jul-14	26-Jul-14
Zone A1		87	28-Jan-14	10-May-14	18-Mar-14 A	28-Jul-14
Vertical Seawall		69	28-Jan-14	10-May-14	18-Mar-14 A	07-Jul-14
NRC12020	VS - Dredging - Zone A1 - (CH738 to 793)	3	28-Jan-14	30-Jan-14	18-Mar-14 A	02-Apr-14 A
NRC12040	VS - Rock Grade 400 - Zone A1 - (CH738 to 793)	3	07-Feb-14	12-Feb-14	01-Apr-14 A	16-May-14
NRC12050	VS - Levelling Stone - Zone A1 - (CH738 to 793)	4	18-Feb-14	21-Feb-14	17-May-14	21-May-14
NRC12060	VS - Seawall Block - Zone A1 - (CH738 to 793)	11	11-Apr-14	26-Apr-14	12-Jun-14	24-Jun-14
NRC12080	VS - Rockfill Type A - Zone A1 - (CH738 to 793)	3	28-Apr-14	30-Apr-14	25-Jun-14	27-Jun-14
NRC12090	VS - Geotextile - Zone A1 - (CH738 to 793)	2	02-May-14	03-May-14	28-Jun-14	30-Jun-14
NRC12100	VS - Granular Filter - Zone A1 - (CH738 to 793)	4	07-May-14	10-May-14	03-Jul-14	07-Jul-14
Sloping Seawall		24	20-Mar-14	08-Apr-14	18-Mar-14 A	28-Jul-14
NRC12140	SS - Dredging - Zone A1 - (CH738 to 793)	3	20-Mar-14	25-Mar-14	18-Mar-14 A	09-Jul-14
NRC12150	SS - Rock Grade 400 - Zone A1 - (CH738 to 793) to +2.5mPD (4k/d)	10	26-Mar-14	31-Mar-14	10-Jul-14	21-Jul-14
NRC12180	SS - Armour Rock Underlayer - Zone A1 - (CH738 to 793)	5	01-Apr-14	07-Apr-14	22-Jul-14	26-Jul-14
NRC12220	Sloping - Rockfill Type A - Zone A1 - (CH738 to 793)	1	01-Apr-14	01-Apr-14	22-Jul-14	22-Jul-14
NRC12230	Sloping - Geotextile - Zone A1 - (CH738 to 793)	2	02-Apr-14	03-Apr-14	23-Jul-14	24-Jul-14
NRC12250	Sloping - Granular Filter - Zone A1 - (CH738 to 793)	3	04-Apr-14	08-Apr-14	25-Jul-14	28-Jul-14
Zone A2		82	28-Jan-14	05-Jun-14	26-Mar-14 A	01-Aug-14
Vertical Seawall		81	28-Jan-14	05-Jun-14	26-Mar-14 A	31-Jul-14
NRC12350	VS - Dredging - Zone A2 - (CH793 to 843)	2	28-Jan-14	30-Jan-14	26-Mar-14 A	16-May-14
NRC12360	VS - Dredging - Zone A2 - (CH843 to 893)	3	07-Feb-14	11-Feb-14	06-Apr-14 A	23-May-14
NRC12370	VS - Dredging - Zone A2 - (CH893 to 956)	11	12-Feb-14	24-Feb-14	24-May-14	06-Jun-14
NRC12380	VS - Rock Grade 400 - Zone A2 - (CH793 to 843)	2	13-Feb-14	18-Feb-14	15-Apr-14 A	24-May-14
NRC12390	VS - Rock Grade 400 - Zone A2 - (CH843 to 893)	10	19-Feb-14	24-Feb-14	26-May-14	06-Jun-14
NRC12400	VS - Rock Grade 400 - Zone A2 - (CH893 to 956)	30	25-Feb-14	14-Mar-14	07-Jun-14	12-Jul-14
NRC12410	VS - Levelling Stone - Zone A2 - (CH793 to 843)	4	25-Feb-14	28-Feb-14	07-Jun-14	11-Jun-14
NRC12420	VS - Levelling Stone - Zone A2 - (CH843 to 893)	4	01-Mar-14	05-Mar-14	12-Jun-14	16-Jun-14
NRC12440	VS - Levelling Stone - Zone A2 - (CH893 to 956)	9	06-Mar-14	15-Mar-14	17-Jun-14	26-Jun-14
NRC12450	VS - Seawall Block - Zone A2 - (CH793 to 843)	7	28-Apr-14	07-May-14	25-Jun-14	03-Jul-14
NRC12460	VS - Seawall Block - Zone A2 - (CH843 to 893)	7	08-May-14	15-May-14	04-Jul-14	11-Jul-14
NRC12470	VS - Seawall Block - Zone A2 - (CH893 to 956)	17	16-May-14	05-Jun-14	12-Jul-14	31-Jul-14
NRC12480	VS - Rockfill Type A - Zone A2 - (CH793 to 843)	3	16-May-14	19-May-14	12-Jul-14	15-Jul-14
Sloping Seawall		18	25-Mar-14	08-Apr-14	17-Apr-14 A	01-Aug-14
NRC12630	SS - Dredging - Zone A2 - (CH793 to 843)	2	25-Mar-14	29-Mar-14	17-Apr-14 A	21-Jul-14
NRC12640	SS - Dredging - Zone A2 - (CH843 to 893)	6	31-Mar-14	07-Apr-14	26-Jul-14	01-Aug-14
NRC12660	SS - Rock Grade 400 - Zone A2 - (CH793 to 843) to +2.5mPD (4k/d)	10	01-Apr-14	08-Apr-14	22-Jul-14	01-Aug-14
Zone F		157	10-Jan-14	25-Apr-14	22-Feb-14 A	28-Jul-14
CH137 to CH184		121	10-Jan-14	08-Mar-14	22-Feb-14 A	14-Jun-14
A6416030	F - Marine Sheet Piling (H2) - CH137 to CH184	3	10-Jan-14	13-Jan-14	22-Feb-14 A	28-Apr-14
A6416035	F - Marine Sheet Piling (H1) - CH137 to CH184	2	14-Jan-14	15-Jan-14	25-Mar-14 A	21-Apr-14 A
A6416100	F - Backfilling up to -7.5mPD & T1 Installation - CH137 to CH184	4	16-Jan-14	19-Jan-14	29-Apr-14	02-May-14
A6416110	F - Backfilling up to -4.5mPD - CH137 to CH184	2	20-Jan-14	21-Jan-14	03-May-14	04-May-14
A6416115	F - Backfilling up to +0.5mPD & T3 Installation - CH137 to CH184	6	22-Jan-14	27-Jan-14	05-May-14	10-May-14
A6416118	F - Backfilling up to +3.0mPD - CH137 to CH184	2	28-Jan-14	29-Jan-14	11-May-14	12-May-14
A6416120	F - Backfilling up to +6.0mPD - CH137 to CH184	2	30-Jan-14	31-Jan-14	13-May-14	14-May-14
A6416320	F - Anchor Wall Installation - CH160 to CH184	2	07-Mar-14	08-Mar-14	13-Jun-14	14-Jun-14
CH184 to CH231		124	16-Jan-14	21-Mar-14	25-Apr-14 A	27-Jun-14
A6416040	F - Marine Sheet Piling (H2) - CH184 to CH231	3	16-Jan-14	18-Jan-14	29-Apr-14	02-May-14
A6416050	F - Marine Sheet Piling (H1) - CH184 to CH231	1	20-Jan-14	22-Jan-14	25-Apr-14 A	05-May-14
A6416060	F - Backfilling up to -7.5mPD & T1 Installation - CH184 to CH231	4	23-Jan-14	26-Jan-14	06-May-14	09-May-14
A6416070	F - Backfilling up to -4.5mPD - CH184 to CH231	2	27-Jan-14	28-Jan-14	10-May-14	11-May-14
A6416080	F - Backfilling up to +0.5mPD & T3 Installation - CH184 to CH231	6	29-Jan-14	03-Feb-14	12-May-14	17-May-14
A6416085	F - Backfilling up to +3.0mPD - CH184 to CH231	2	04-Feb-14	05-Feb-14	18-May-14	19-May-14
A6416090	F - Backfilling up to +6.0mPD - CH184 to CH231	2	06-Feb-14	07-Feb-14	20-May-14	21-May-14
A6416230	F - Anchor wall Installation - CH184 to CH231	4	10-Mar-14	13-Mar-14	16-Jun-14	19-Jun-14
A6416290	F - Backfilling up to 0.0mPD & G2 Installation to Anchor Wall - CH184 to CH231	3	14-Mar-14	16-Mar-14	20-Jun-14	22-Jun-14
A6416295	F - Backfilling up to +3.0mPD & G1 Installation to Anchor Wall - CH184 to CH231	2	17-Mar-14	18-Mar-14	23-Jun-14	24-Jun-14
A6416300	F - Backfilling up to +6.0mPD to Anchor Wall - CH184 to CH231	2	19-Mar-14	20-Mar-14	25-Jun-14	26-Jun-14
A6416400	F - Backfilling to +6.0mPD to Existing Seawall - CH184 to CH231	1	21-Mar-14	21-Mar-14	27-Jun-14	27-Jun-14
CH231 to CH278		67	23-Jan-14	18-Apr-14	07-May-14	25-Jul-14
A6416240	F - Marine Sheet Piling (H1) - CH231 to CH278	4	23-Jan-14	27-Jan-14	07-May-14	10-May-14
A6416250	F - Marine Sheet Piling (H2) - CH231 to CH278	4	18-Mar-14	21-Mar-14	24-Jun-14	27-Jun-14

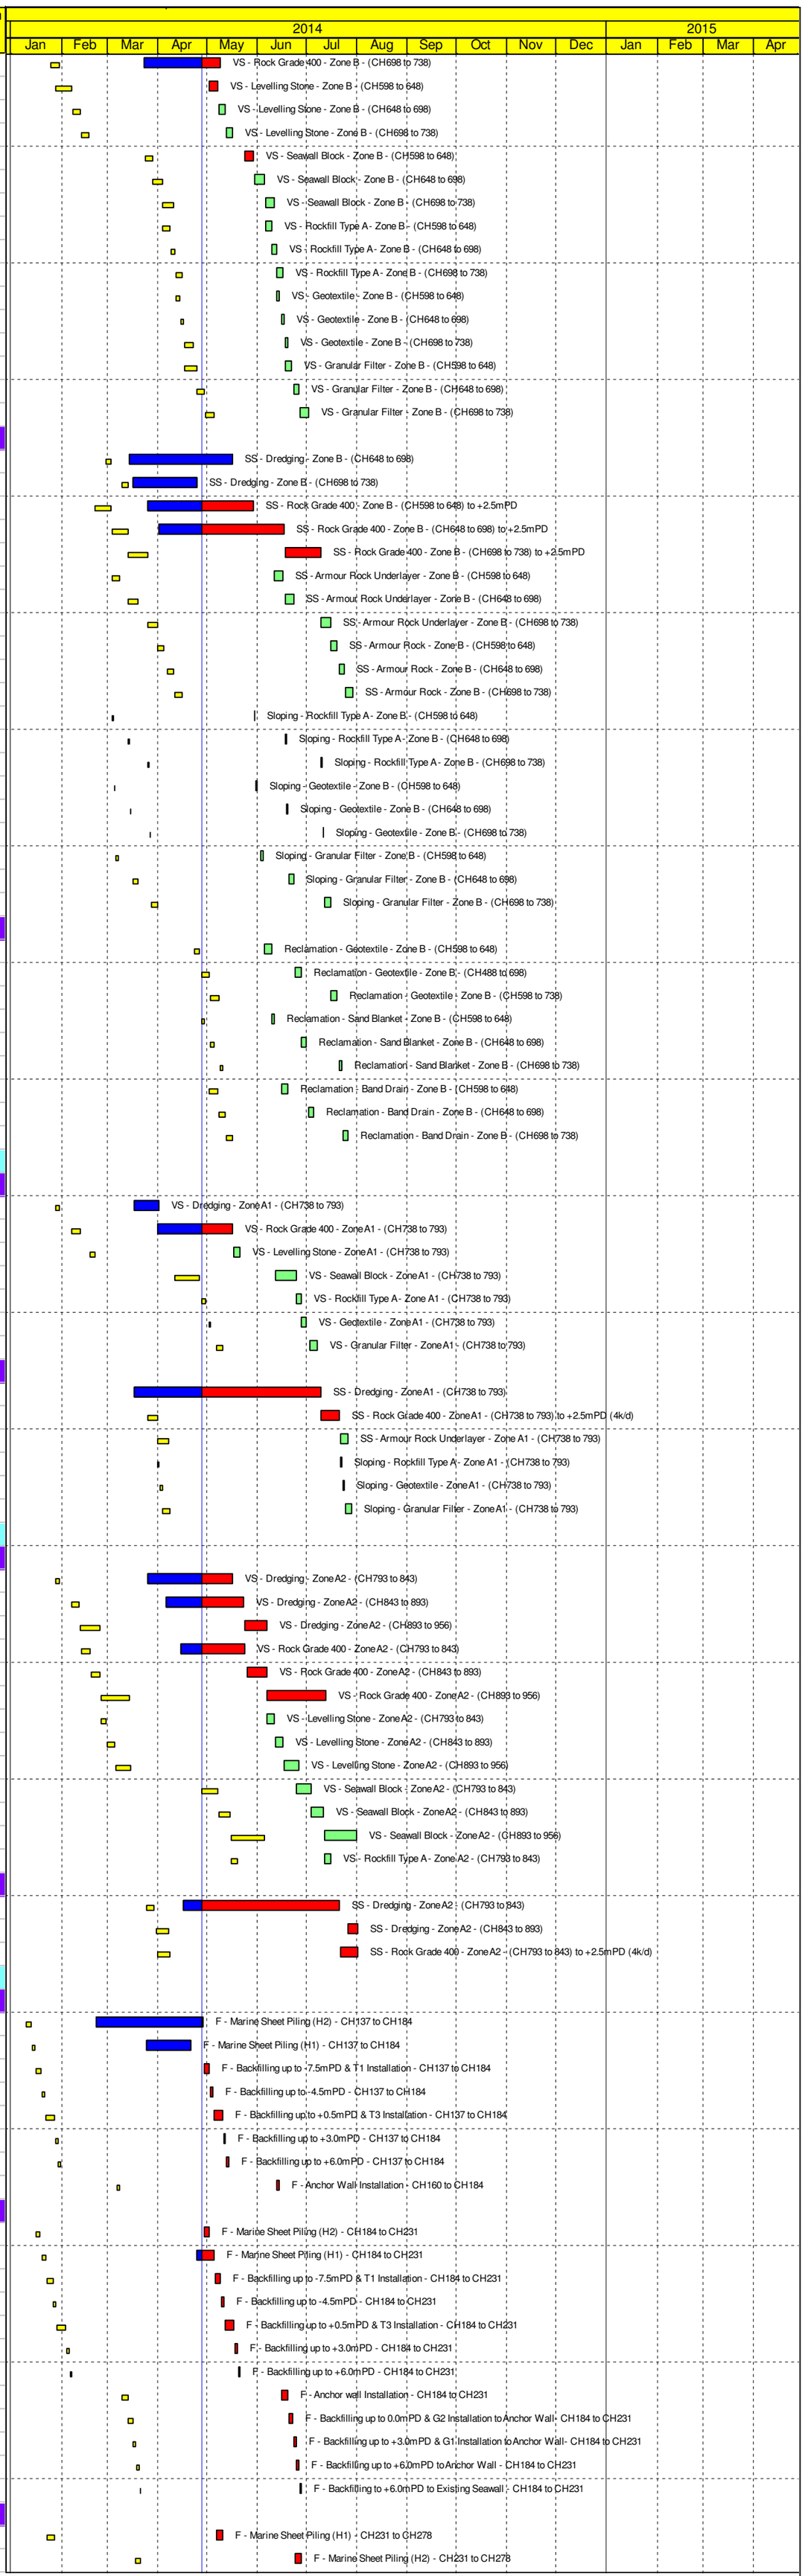

Current Bar
Current Bar - Critical
Planned Bar
Planned Milestone
Current Milestone
Progress Milestone
Progress Bar

TMCLK - Northern Connection Sub-Sea Tunnel Section

3-Months Rolling Programme - Construction

As of 28-Apr-14 Progress

Dragages HongKong 香港寶嘉
A member of the Bouygues Construction group
Dragages - Bouygues Joint Venture 寶嘉 - 布依格聯營

BOUYGUES TRAVAUX PUBLICS

Date	Revision	Checked	Approved
12-Feb-14	TMCLK/DBJ/GEN/PRG/98507	SPa	WYu

Activity ID	Activity Name	Orig Dur	Planned Start	Planned Finish	Current Start	Current Finish
A6416260	F - Backfilling up to -7.5mPD & T1 Installation - CH231 to CH278	4	22-Mar-14	25-Mar-14	28-Jun-14	01-Jul-14
A6416270	F - Backfilling up to -4.5mPD - CH231 to CH278	2	26-Mar-14	27-Mar-14	02-Jul-14	03-Jul-14
A6416273	F - Backfilling up to +0.5mPD & T3 Installation - CH231 to CH278	6	28-Mar-14	02-Apr-14	04-Jul-14	09-Jul-14
A6416278	F - Backfilling up to +3.0mPD - CH231 to CH278	2	03-Apr-14	04-Apr-14	10-Jul-14	11-Jul-14
A6416280	F - Backfilling up to +6.0mPD - CH231 to CH278	2	05-Apr-14	06-Apr-14	12-Jul-14	13-Jul-14
A6416310	F - Anchor wall Installation - CH231 to CH278	4	07-Apr-14	10-Apr-14	14-Jul-14	17-Jul-14
A6416480	F - Backfilling up to 0.0mPD & G2 Installation to Anchor Wall- CH231 to CH278	3	11-Apr-14	13-Apr-14	18-Jul-14	20-Jul-14
A6416490	F - Backfilling up to +3.0mPD & G1 Installation to Anchor Wall - CH231 to CH278	2	14-Apr-14	15-Apr-14	21-Jul-14	22-Jul-14
A6416500	F - Backfilling up to +6.0mPD to Anchor Wall - CH231 to CH278	2	16-Apr-14	17-Apr-14	23-Jul-14	24-Jul-14
A6416510	F - Backfilling to +6.0mPD to Existing Seawall - CH231 to CH278	1	18-Apr-14	18-Apr-14	25-Jul-14	25-Jul-14
CH278 to CH327		65	28-Jan-14	21-Apr-14	12-May-14	28-Jul-14
A6416180	F - Pre-boring for Marine Sheet Pile - CH278 to CH327	6	28-Jan-14	10-Feb-14	12-May-14	17-May-14
A6416190	F - Marine Sheet Piling (H1) - CH278 to CH327	5	25-Feb-14	01-Mar-14	03-Jun-14	07-Jun-14
A6416195	F - Marine Sheet Piling (H2) - CH278 to CH327	5	12-Mar-14	17-Mar-14	18-Jun-14	23-Jun-14
A6416200	F - Backfilling up to -3.5mPD & T2 Installation - CH278 to CH327	5	18-Mar-14	22-Mar-14	24-Jun-14	28-Jun-14
A6416210	F - Backfilling up to +0.5mPD - CH278 to CH327	4	23-Mar-14	26-Mar-14	29-Jun-14	02-Jul-14
A6416215	F - Backfilling up to +3.0mPD & T4 Installation - CH278 to CH327	5	27-Mar-14	31-Mar-14	03-Jul-14	07-Jul-14
A6416220	F - Backfilling up to +6.0mPD - CH278 to CH327	2	01-Apr-14	02-Apr-14	08-Jul-14	09-Jul-14
A6416340	F - Anchor wall Installation - CH278 to CH327	4	11-Apr-14	15-Apr-14	18-Jul-14	22-Jul-14
A6416520	F - Backfilling up to 0.0mPD & G2 Installation to Anchor Wall - CH278 to CH327	3	16-Apr-14	18-Apr-14	23-Jul-14	25-Jul-14
A6416530	F - Backfilling up to +3.0mPD & G1 Installation to Anchor Wall - CH278 to CH327	3	19-Apr-14	21-Apr-14	26-Jul-14	28-Jul-14
CH327 to CH381		59	11-Feb-14	25-Apr-14	19-May-14	28-Jul-14
A6416130	F - Pre-boring for Marine Sheet Pile - CH327 to CH381	6	11-Feb-14	17-Feb-14	19-May-14	24-May-14
A6416140	F - Marine Sheet Piling (H1) - CH327 to CH381	4	03-Mar-14	06-Mar-14	09-Jun-14	12-Jun-14
A6416145	F - Marine Sheet Piling (H2) - CH327 to CH381	4	07-Mar-14	11-Mar-14	13-Jun-14	17-Jun-14
A6416150	F - Backfilling up to -3.5mPD & T2 Installation - CH327 to CH381	4	12-Mar-14	15-Mar-14	18-Jun-14	21-Jun-14
A6416155	F - Backfilling up to+ 0.5mPD - CH327 to CH381	3	16-Mar-14	18-Mar-14	22-Jun-14	24-Jun-14
A6416160	F - Backfilling up to +3.0mPD & T4 Installation - CH327 to CH381	5	19-Mar-14	23-Mar-14	25-Jun-14	29-Jun-14
A6416170	F - Backfilling up to +6.0mPD - CH327 to CH381	3	24-Mar-14	26-Mar-14	30-Jun-14	02-Jul-14
A6416370	F - Anchor wall Installation - CH327 to CH381	3	16-Apr-14	22-Apr-14	23-Jul-14	25-Jul-14
A6416560	F - Backfilling up to 0.0mPD & G2 Installation to Anchor Wall - CH327 to CH381	3	23-Apr-14	25-Apr-14	26-Jul-14	28-Jul-14
Box Culvert Extension		203	07-Feb-14	13-Oct-14	15-May-14	15-Jan-15
Construction		203	07-Feb-14	13-Oct-14	15-May-14	15-Jan-15
CH000 to CH137		120	02-May-14	23-Sep-14	14-Jun-14	05-Nov-14
A6416600	Predrilling - CH27 to CH137	24	02-May-14	30-May-14	14-Jun-14	12-Jul-14
A6416670	Bored Pile Construction - A43 to A62 (4 Rigs) & Land Sheet Piling	96	31-May-14	23-Sep-14	14-Jul-14	05-Nov-14
CH137 to CH184		184	07-Feb-14	19-Sep-14	15-May-14	20-Dec-14
A6416610	Predrilling - CH137 to CH184	24	07-Feb-14	06-Mar-14	15-May-14	12-Jun-14
A6416720	Bored Pile Construction - A42 to A35	160	07-Mar-14	19-Sep-14	13-Jun-14	20-Dec-14
CH184 to CH231		156	22-Mar-14	30-Sep-14	28-Jun-14	03-Jan-15
A6416620	Predrilling - CH184 to CH231	24	22-Mar-14	23-Apr-14	28-Jun-14	26-Jul-14
A6416730	Bored Pile Construction - A34 to A27	156	22-Mar-14	30-Sep-14	28-Jun-14	03-Jan-15
CH231 to CH278		143	22-Apr-14	13-Oct-14	26-Jul-14	15-Jan-15
A6416630	Predrilling - CH231 to CH278	24	22-Apr-14	21-May-14	26-Jul-14	22-Aug-14
A6416740	Bored Pile Construction - A26 to A19	143	22-Apr-14	13-Oct-14	26-Jul-14	15-Jan-15
CH381 to CH399 (Box Culvert Connection)		58	18-Feb-14	30-Apr-14	26-May-14	02-Aug-14
A6416660	F - Prebored H-piles for CKS Temporary Land Access	6	18-Feb-14	24-Feb-14	26-May-14	31-May-14
A6417000	F - Steel Bridge Installation for Land Access to Zone E	52	25-Feb-14	30-Apr-14	03-Jun-14	02-Aug-14
North Shafts Construction & Tunnel Structure		106	28-Mar-14	07-Jul-14	14-May-14	17-Sep-14
Construction		106	28-Mar-14	07-Jul-14	14-May-14	17-Sep-14
North Launching Shaft ELS Foundation & Capping Beam (Cell 1 to 3)		106	28-Mar-14	07-Jul-14	14-May-14	17-Sep-14
NSH1180	E - Setup for Launching Shaft ELS	18	28-Mar-14	22-Apr-14	14-May-14	04-Jun-14
NSH1340	E - Cell 1-3 - Diaphragm Wall & Toe Grouting - Shaft ELS	54	02-May-14	07-Jul-14	16-Jul-14	17-Sep-14
North Launching Shaft ELS Foundation & Capping Beam		21	02-May-14	27-May-14	14-Jun-14	09-Jul-14
NSH1210	E - Cell 4 to 6 - Prebored H-piles - Perm	21	02-May-14	27-May-14	14-Jun-14	09-Jul-14
CLP Temporary Substation		268	31-Dec-13	07-Nov-14	08-Mar-14A	28-Nov-14
Construction		268	31-Dec-13	07-Nov-14	08-Mar-14A	28-Nov-14
DDP12540	Gazette & Traffic Advice Application	27	31-Dec-13	08-Feb-14	07-Apr-14A	29-Apr-14
DDP12550	RMO Application for TTMS Implementation	6	10-Feb-14	15-Feb-14	29-Apr-14	08-May-14
DDP12560	TTMS Implementation	0	17-Feb-14		08-May-14	
DDP12720	Trench Excavation & Service Connection	60	17-Feb-14	17-May-14	08-May-14	19-Jul-14
DDP1274040	200mm thk on-grade Slab & Cable Trench - Rebar, Fwk	6			08-Mar-14A	01-Apr-14A
DDP1274045	200mm thk on-grade Slab & Cable Trench - Concreting	0				02-Apr-14A
DDP1274047	200mm thk on-grade Slab & Cable Trench - Remove Fwk	2			03-Apr-14A	03-Apr-14A
DDP1274050	Concrete Plinth - Rebar, Fwk & Concreting	6			17-Apr-14A	17-Apr-14A
DDP1274060	Concrete Plinth - Concreting	0				17-Apr-14A
DDP1275040	Outerwall & Water Tank up to +7.7mPD - Rebar, Fwk	4			18-Mar-14A	02-Apr-14A
DDP1275050	Outerwall & Water Tank up to +7.7mPD - Concreting	0				02-Apr-14A
DDP1275055	Outerwall & Water Tank up to +7.7mPD - Remove Fwk	2			03-Apr-14A	03-Apr-14A
DDP1275060	Outerwall & Water Tank up to +9.0mPD - Rebar, Fwk	4			07-Apr-14A	16-Apr-14A
DDP1275070	Outerwall & Water Tank up to +9.0mPD - Concreting	0				16-Apr-14A
DDP1275075	Outerwall & Water Tank up to +9.0mPD - Remove Fwk	2			16-Apr-14A	19-Apr-14A
DDP127507540	Internal Wall up to +10.14mPD - Rebar, Fwk	5			24-Mar-14A	17-Apr-14A
DDP127507550	Internal Wall up to +10.14mPD - Concreting	0				17-Apr-14A
DDP127507560	Internal Wall up to +10.14mPD - Fwk Removal	2			15-Apr-14A	17-Apr-14A
DDP1275080	Substation - Roof Structure - Rebar, Fwk	4			17-Apr-14A	21-Apr-14A
DDP1275090	Substation - Roof Strucuture - Concreting	0				23-Apr-14A
DDP1275095	Substation - Roof Strucuture - Fwk Removal	2			21-Apr-14A	23-Apr-14A
DDP1275100	Internal Wall up to +13.14mPD - Rebar, Fwk	8			17-Apr-14A	23-Apr-14A
DDP1275110	Internal Wall up to +13.14mPD - Concreting	0				25-Apr-14A
DDP1275120	Internal Wall up to +13.14 - Fwk Removal	2			26-Apr-14A	28-Apr-14A
DDP1275130	BYME Possession to CLP Substation	0			25-Apr-14A	
DDP1275140	CLP Substation - E&M, BS Installation	46			28-Apr-14	23-Jun-14
DDP1276010	Substation - ABWF works	2			26-Apr-14A	10-May-14
DDP1276020	Substation - Metal works & Remaining civil works	18			12-May-14	31-May-14
DDP1276030	Substation - E&M works	46			28-Apr-14	23-Jun-14
DDP12780	Pre-Electrical Access Inspection	0		31-May-14		23-Jun-14
DDP12790	Electrical Access	0		30-Jun-14		22-Jul-14
DDP12800	1st Batch - CLP Installation & Commissioning	108	02-Jul-14	07-Nov-14	23-Jul-14	28-Nov-14
North Surface works for TBM Tunnelling		92	08-May-14	05-Aug-14	21-Jun-14	20-Sep-14
Construction		92	08-May-14	05-Aug-14	21-Jun-14	20-Sep-14
Zone D1		70	08-May-14	15-Jul-14	21-Jun-14	29-Aug-14
NRC13940	Zone D1 - Vibro-compaction (CH205 to 255)	60	08-May-14	06-Jul-14	21-Jun-14	19-Aug-14
NRC13950	Zone D1 - Vibro-compaction (CH255 to 305)	60	13-May-14	11-Jul-14	26-Jun-14	24-Aug-14
NRC13960	Zone D1 - Vibro-compaction (CH305 to 355)	60	17-May-14	15-Jul-14	01-Jul-14	29-Aug-14
Zone D2		72	25-May-14	05-Aug-14	11-Jul-14	20-Sep-14
NRC13970	Zone D2 - Vibro-compaction (CH355 to 405)	60	25-May-14	23-Jul-14	11-Jul-14	08-Sep-14
NRC13980	Zone D2 - Vibro-compaction (CH405 to 443)	60	07-Jun-14	05-Aug-14	23-Jul-14	20-Sep-14

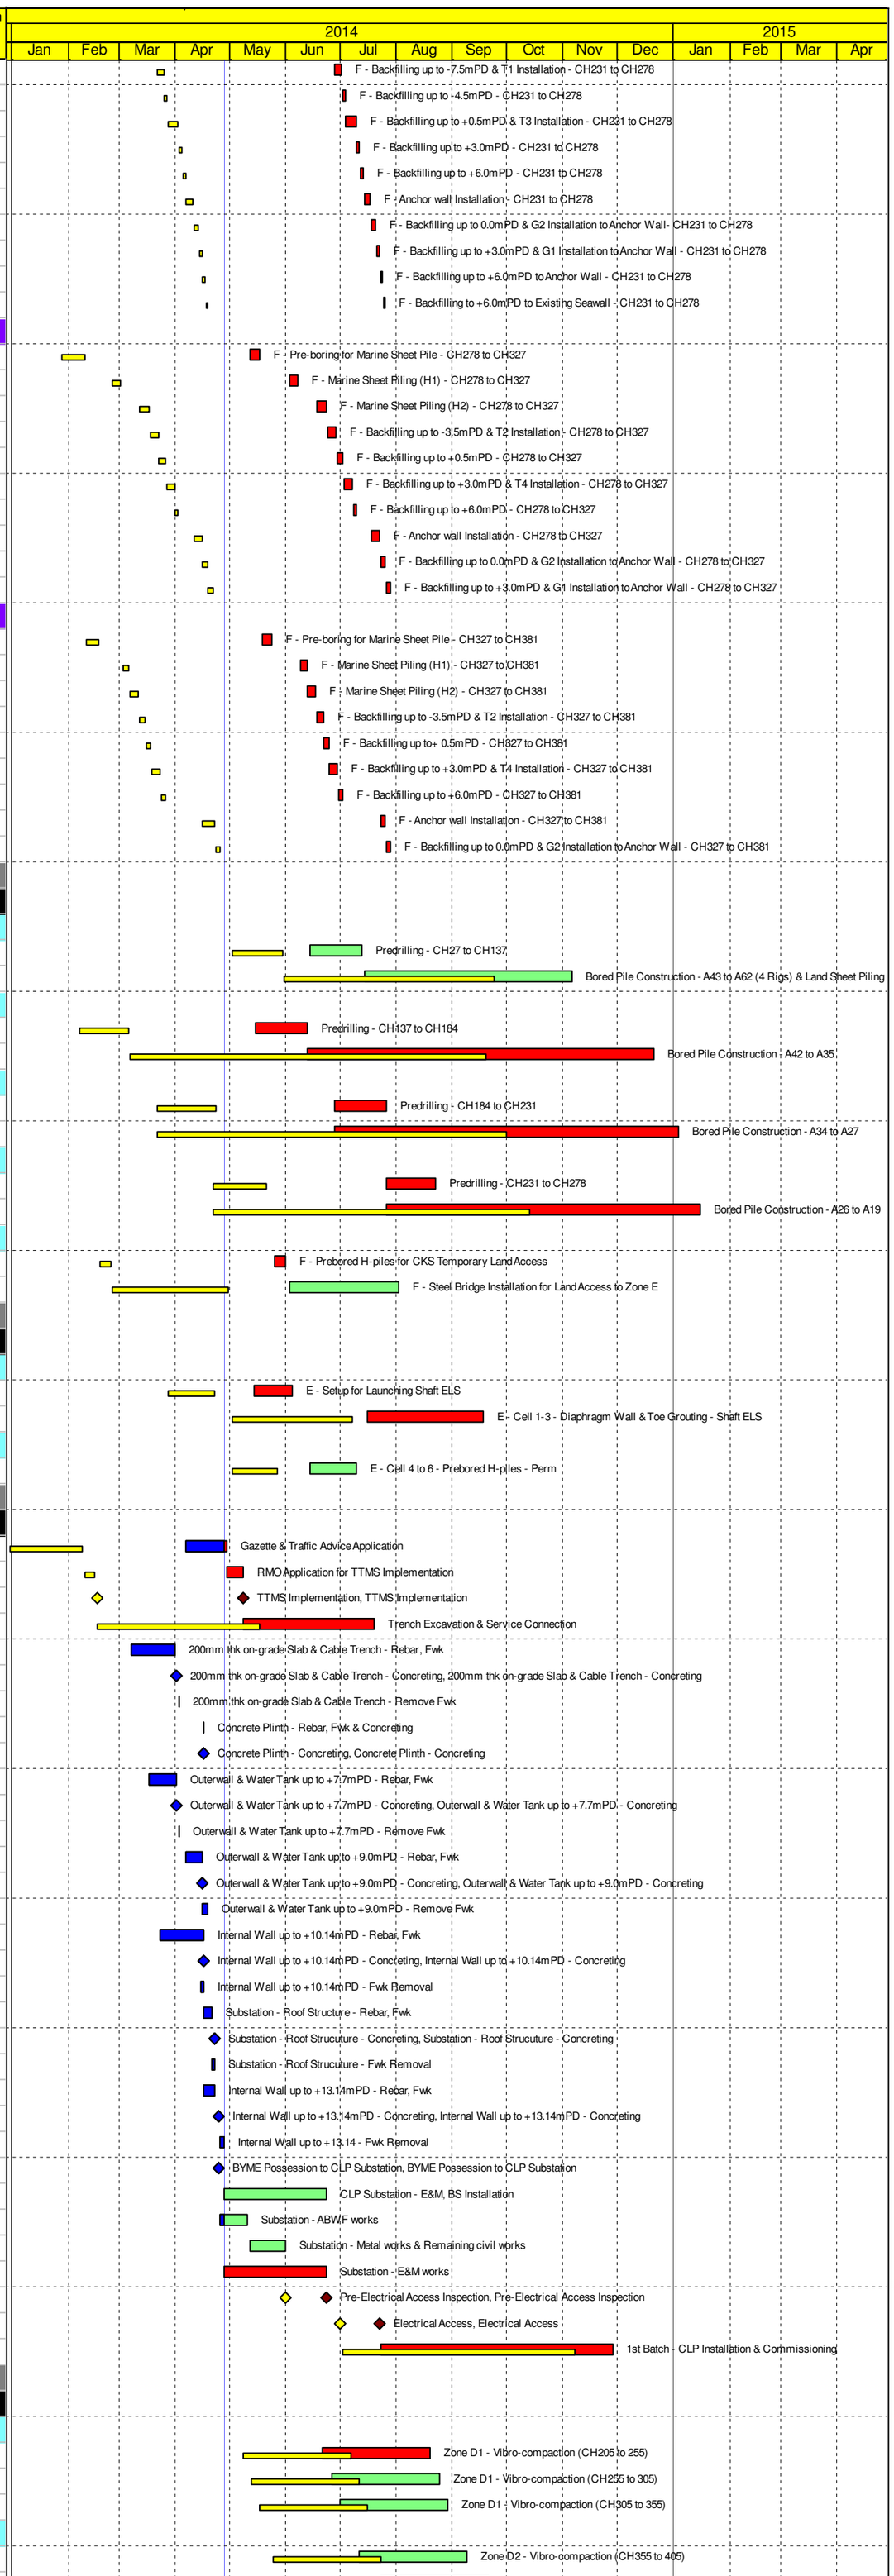

Current Bar
Current Bar - Critical
Planned Bar
Planned Milestone
Current Milestone
Progress Milestone
Progress Bar

TMCLK - Northern Connection Sub-Sea Tunnel Section

3-Months Rolling Programme - Construction

As of 28-Apr-14 Progress

Dragages HongKong 香港寶嘉
A member of the Bouygues Construction group
Dragages - Bouygues Joint Venture 寶嘉 - 布依格聯營

BOUYGUES TRAVAUX PUBLICS

Date	Revision	Checked	Approved
12-Feb-14	TMCLK/DBJ/GEN/PRG/98507	SPa	WYu
